




ภาคผนวก 7ข

แผนการก่อสร้างโครงการ

PROJECT : MP6&MP7

WEEKLY REPORT, WEEK 19th

2 - 8 January, 2023

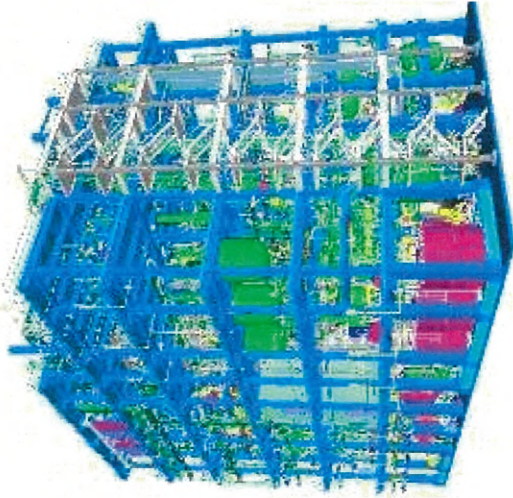


N.K.G. PLUS CO., LTD.

PROJECT : MP6&MP7

WEEKLY REPORT, WEEK 19th
2 - 8 January, 2023



Installation the steel column line E/6 MP7
to level +19.50.

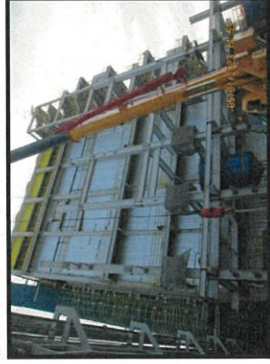

Installation the steel column line E/6 MP7
to level +19.50.



Welding the pipe rack at steel column.



Installation the scaffolding for concrete encasing column
at MP7.



Installation the steel column line E/6 MP7
to level +19.50.



Installation the beam support at level +13.50 MP7.



Welding the pipe rack at steel column.



Installation the formwork for concrete encasing column
at MP6.



WEEKLY REPORT, WEEK 19th

2 - 8 January, 2023



Metal deck slab on site 6 Jan.23




Metal deck slab on site 6 Jan.23



Installation the beam frame at level +13.50.



Installation the premixed asphalt of tank foundation no. T-9501.

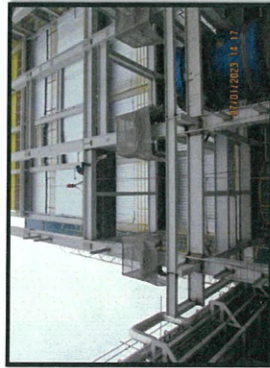

Installation the steel column to +19.50 at MP7.



Installation the metal deck slab level +7.50 at MP7.



Installation the scaffolding for concrete encasing column



Installation the scaffolding for concrete encasing column

WEEKLY REPORT, WEEK 19th

2 - 8 January, 2023



Steel beam on site 8 Jan, 23



Steel handrail on site 8 Jan, 23



Steel columns on site 8 Jan, 23



Installation the steel column MP6



Installation the tempo.handrail for metal deck slab work level +7.50.



Installation the tempo.handrail for metal deck slab work level +7.50.



Installation the tempo.handrail for metal deck slab work level +7.50.



Installation the tempo.handrail for metal deck slab work level +7.50.



Installation the formwork for concrete encasing column at MP7.



Installation the formwork for concrete encasing column at MP7.



N.K.G.®

Project: MP6 & MP7

Position Date		Jan-23																													
		2 Mon	3 Tue	4 Wed	5 Thu	6 Fri	7 Sat	8 Sun	9 Mon	10 Tue	11 Wed	12 Thu	13 Fri	14 Sat	15 Sun	16 Mon	17 Tue	18 Wed	19 Thu	20 Fri	21 Sat	22 Sun	23 Mon	24 Tue	25 Wed	26 Thu	27 Fri	28 Sat	29 Sun	30 Mon	31 Tue
Project Manager					1	1	1	-																							
Site Engineer					1	1	1	1																							
Safety officer					1	1	1	1																							
Supervisor					1	1	1	1																							
Foreman					2	2	2	2																							
Surveyor					1	1	1	-																							
Admin					1	1	1	-																							
Pick up Driver					1	1	1	1																							
NKG staff		-	-	-	9	9	9	6	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Head man					1	1	1	1																							
Carpenter																															
Mason					13	13	13	13																							
Steel fixer																															
Labour					5	5	5	5																							
General Labour					1	1	1	1																							
Store , Checker-maid					2	2	2	2																							
NKG worker		-	-	-	22	22	22	22	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
SUB CONTRACTOR																															
Machine Operator					1	1	1	1																							
Scaffolding work					6		7																								
Liquid floor hardener																															
Drainage work					4	4																									
Steel Structure					11	11	13	13																							
Aluminum work																															
Air condition work																															
Electrical Work																															
Total sub contract		-	-	-	22	16	21	14	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Total Manpower		-	-	-	53	47	52	42	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
MACHINE & EQUIPMENT																															
6 wheels dump truck																															
10 wheels dump truck																															
Backhoe PC120																															
MOBILE CRANE 50 T					1	1	1	1																							
Pick Up truck (NKG)					1	1	1	1																							

WEEK 19th 2-8 Jan. 23

JANUARY, 2023

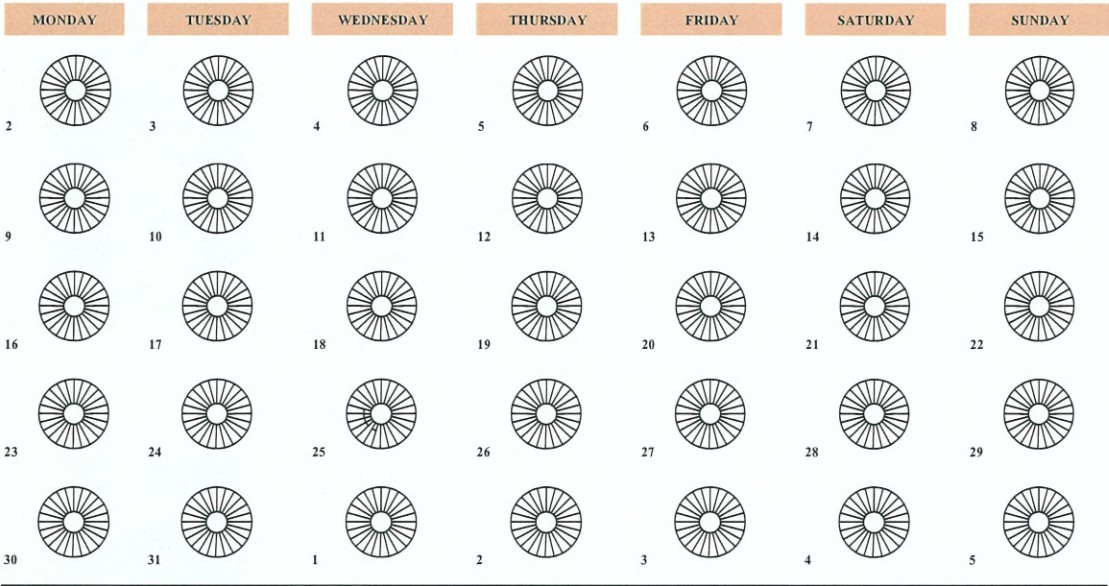

Day type	This week (days)	Accumulate to Last month	Accumulate to this month	Remark
Working day	4	111	115	
Holiday	3	12	15	
Total	7	116	130	
Summary Rain hours.				
Clear				
Rain	-	75	75	
Hard rain	-	4	4	
Total Rain hours	0	79	79	



WORK OBSTRUCTION

WEEKLY REPORT, WEEK 19th

2 - 8 January, 2023


DATE	Description	Number of working days delayed
	Accumulated number of delayed working days	6



PROJECT : MP6&MP7

WEEKLY REPORT,WEEK 24th

6 - 12 February 2023

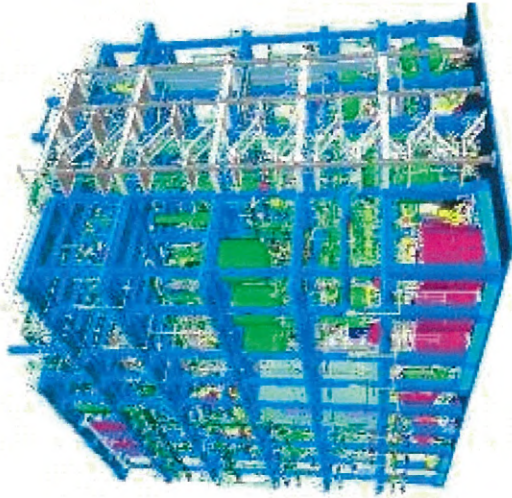

N.K.G. PLUS CO.,LTD.

PROJECT : MP6&MP7


WEEKLY REPORT,WEEK 24th
6 - 12 February 2023




Installation the metal deck slab level +19.50 at MP7.



Installation the metal deck slab level +19.50 at MP7.

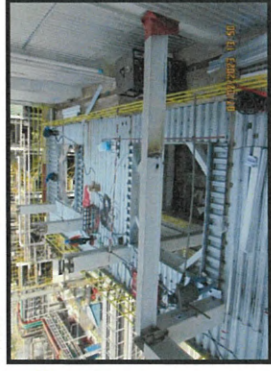

Welding shear stud at metal deck slab level +19.50 at MP7.

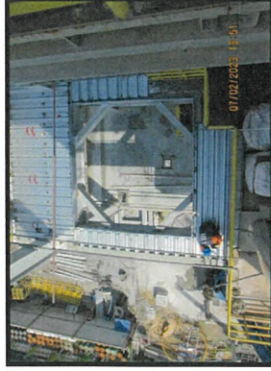


Welding shear stud at metal deck slab level +19.50 at MP7.



Installation the metal deck slab level +19.50 at MP7.



Installation the metal deck slab level +19.50 at MP7.

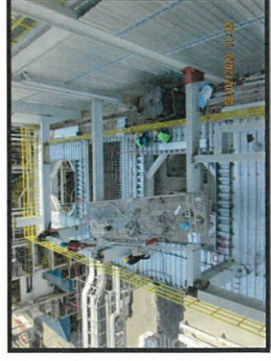

Installation wiremesh reinforcement level +19.50 at MP7.



Installation wiremesh reinforcement level +19.50 at MP7.



Welding shear stud at metal deck slab level +19.50 at MP7.



Installation wiremesh reinforcement level +19.50 at MP7.



Pouring concrete slab level +19.50 MP7.




Pouring concrete slab level +19.50 MP7.



Pouring concrete slab level +19.50 MP7.



Pouring concrete slab level +19.50 MP7.

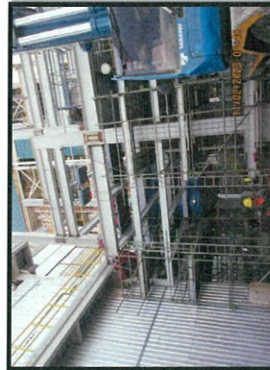

Installation the pipe rack level +4.60, +5.80.



Installation the beam level +19.5 and metal deck slab level +7.50 MP6.



Installation the beam level +22.25 at MP7.



Pouring the concrete kerb level +13.50 MP7.



Pouring the concrete kerb level +13.50 MP7.



Pouring the concrete kerb level +19.50 MP7.



Installation the scaffolding for wall of MCC room and DCS room.



Pouring the concrete kerb level +13.50 MP7.



Pouring the concrete kerb level +13.50 MP7.



Pouring the concrete kerb level +19.50 MP7.



Material from steamer factory on site 10 Feb.23



Installation the steel handrail and line marking for block out slab level +7.50 MP6.



Installation the metal deck slab level +7.50 MP6.



Installation the steel beam level +19.50



Installation the steel handrail and line marking for block out slab level +7.50 MP6.



Installation the metal deck slab level +7.50 MP6.

Daily Manpower Report

Company : N.K.G. PLUS CO.,LTD.


Project: MP6 & MP7



Position	Date	Feb-23																												
		30 Mon	31 Tue	1 Wed	2 Thu	3 Fri	4 Sat	5 Sun	6 Mon	7 Tue	8 Wed	9 Thu	10 Fri	11 Sat	12 Sun	13 Mon	14 Tue	15 Wed	16 Thu	17 Fri	18 Sat	19 Sun	20 Mon	21 Tue	22 Wed	23 Thu	24 Fri	25 Sat	26 Sun	27 Mon
Project Manager		-	1	1	1	1	1	1	1	1	1	1	1	1	1															
Site Engineer		1	1	1	1	1	1	1	1	1	1	1	1	1	-															
Safety officer		1	1	1	1	1	1	1	1	1	1	1	1	1	1															
Supervisor		1	1	1	1	1	1	1	1	1	1	1	1	1	1															
Foreman		2	2	2	2	-	2	2	2	2	2	2	2	2	2															
Surveyor		1	1	1	1	1	1	-	1	1	1	1	1	1	-															
Admin		1	1	1	1	1	1	-	1	1	1	-	-	-	-															
Pick up Driver		1	1	1	1	1	1	1	1	1	1	1	1	1	1															
NKG staff		8	9	9	9	7	9	7	9	9	9	8	8	8	6	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Head man		1	1	1	1	1	1	1	1	1	1	1	1	1	1															
Carpenter																														
Mason		13	13	13	13	13	13	13	13	13	13	13	13	13	13															
Steel fixer																														
Labour		5	5	5	5	5	5	5	5	5	5	5	4	4	4															
General Labour		1	1	1	1	1	1	1	1	1	1	1	1	1	1															
Store , Checker-maid		2	2	2	2	2	2	2	2	2	2	2	2	2	2															
NKG worker		22	22	22	22	22	22	22	22	22	22	22	21	21	21	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
SUB CONTRACTOR																														
Machine Operator		2	2	2	3	2	2	2	2	2	2	1	2	2																
Scaffolding work		5		4	5	4	5	6	4	5	5	6																		
Shear stud of metal deck work																														
Drainage work		6	5	4	6		5	6	5	4		4	4	8	4															
Steel Structure		16	16	16	16	16	16	16	16	16	16	15	16	16																
Aluminum work																														
Air condition work																														
Electrical Work																														
Total sub contract		29	23	26	30	22	28	30	27	27	23	26	22	26	4	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Total Manpower		59	54	57	61	51	59	59	58	58	54	56	51	55	31	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
MACHINE & EQUIPMENT																														
6 wheels dump truck																														
10 wheels dump truck																														
Backhoe PC120																														
MOBILE CRANE 5 T					1																									
MOBILE CRANE 70 T																														
MOBILE CRANE 50 T		2	2	2	2	2	2	2	2	2	2	2	2	2																
Pick Up truck (NKG)		1	1	1	1	1	1	1	1	1	1	1	1	1	1															

WEEK 24th 6-12 Feb. 23

FEBRUARY, 2023

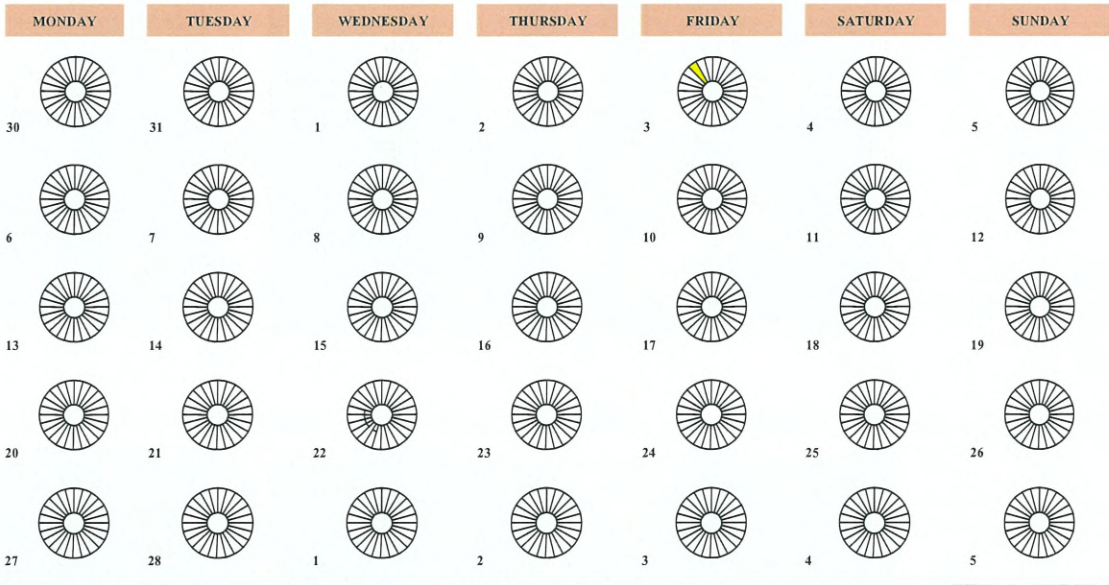

Day type	This week (days)	Accumulate to Last month	Accumulate to this month	Remark
Working day	7	143	150	
Holiday	-	15	15	
Total	7	158	165	
Summary Rain hours.				
Clear				
Rain	-	80	80	
Hard rain	-	4	4	
Total Rain hours	0	84	84	



WORK OBSTRUCTION

WEEKLY REPORT, WEEK 24th

6 - 12 February 2023


Date	Description	Number of working days delayed
	Accumulated number of delayed working days	13



PROJECT : MP6&MP7

WEEKLY REPORT,WEEK 28th

6 - 12 March 2023

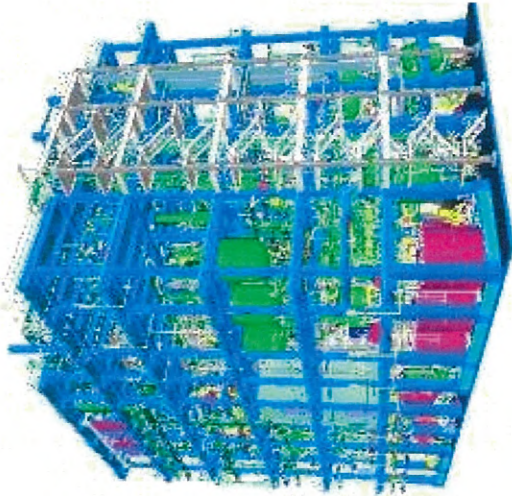


N.K.G. PLUS CO.,LTD.

PROJECT : MP6&MP7

WEEKLY REPORT,WEEK 28th

6 - 12 March 2023

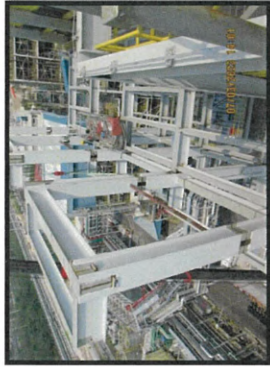

Installation the cantiliver beam frame level +32.50 MP7.



Installation the metal deck level +26.50 MP7.



Welding the shear stud for metal deck slab level +26.50



Welding the shear stud for metal deck slab level +26.50 MP7.



Installation the cantiliver beam frame level +32.50 MP7.



Installation the metal deck level +26.50 MP7.



Welding the shear stud for metal deck slab level +26.50



Installation the steel handrail for slab level +26.50 MP7.



Installation the beam level +32.50 MP6.



Installation the beam level +32.50 MP6.




Installation the metal deck&handrail level +32.50 MP6.



Installation the beam level +26.50 MP6.



Welding the shear stud for metal deck slab level +12.50&+13.50 MP6.

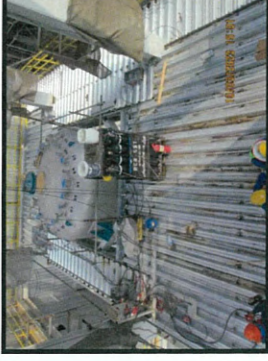

Welding the shear stud for metal deck slab level +19.50 MP6.



Installation the wiremesh for slab level +12.50&+13.50 MP6.



Installation the wiremesh for slab level +19.50 MP6.



Pouring the concrete wall of DCS room level +13.50 MP7 on 7 March 23.



Pouring the concrete wall of DCS room level +13.50 MP7 on 9 March 23.



Installation the wall formworks of DCS room level +13.50 MP7.



Pouring the concrete wall of DCS room level +13.50 MP7 on 11 March 23.



Installation the wall formworks of DCS room level +13.50 MP7.



Installation the wall formworks of DCS room level +13.50 MP7.

Daily Manpower Report

Company : N.K.G. PLUS CO.,LTD.

Project: MP6 & MP7



Position	Date	Mar-23																															
		27 Mon	28 Tue	1 Wed	2 Thu	3 Fri	4 Sat	5 Sun	6 Mon	7 Tue	8 Wed	9 Thu	10 Fri	11 Sat	12 Sun	13 Mon	14 Tue	15 Wed	16 Thu	17 Fri	18 Sat	19 Sun	20 Mon	21 Tue	22 Wed	23 Thu	24 Fri	25 Sat	26 Sun	27 Mon	28 Tue	29 Wed	30 Thu
Project Manager		1	1	1	1	1	1	-	1	1	1	1	1	1																			
Site Engineer		1	1	1	1	1	1	1	1	1	1	1	1	1																			
Safety officer		1	1	1	1	1	1		1	1	1	1	1	1																			
Supervisor		1	1	1	1	1	1	1	1	1	1	1	1	1																			
Foreman		2	2	2	2	2	2	2	1	2	2	2	2	2																			
Surveyor		1	1	1	1	1	1		1	1	1	1	1	1																			
Admin		1	1	1	1	1	1		1	1	1	1	1	1																			
Pick up Driver		1	1	1	1	1	1	1	1	1	1	1	1	1																			
NKG staff		9	9	9	9	9	9	5	7	9	9	9	9	9	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Head man		1	1	1	1	1	1	1	1	1	1	1	1	1																			
Carpenter																																	
Mason		13	13	13	13	13	13	13	13	13	13	13	13	13																			
Steel fixer													1	1																			
Labour		4	4	4	4	4	4	4	3	3	3	4	4	4																			
General Labour		2	2	2	3	3	3	3	4	4	4	4	4	4																			
Store , Checker-maid		2	2	2	2	2	2	2	2	2	2	2	2	2																			
NKG worker		22	22	22	23	23	23	23	23	23	23	24	25	25	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
SUB CONTRACTOR																																	
Machine Operator		2	2	2	2	2	2	-	-	2	2	2	2	2																			
Steel Structure		18	17	17	17	17	13	-	-	18	18	18	18	18																			
Shear stud of metal deck work																																	
Scaffolding work																																	
Aluminum work																																	
Air condition work																																	
Electrical Work																																	
Total sub contract		20	19	19	19	19	15	-	-	20	20	20	20	20	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Total Manpower		51	50	50	51	51	47	28	30	52	52	53	54	54	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
MACHINE & EQUIPMENT																																	
6 wheels dump truck																																	
10 wheels dump truck																																	
Backhoe PC120																																	
MOBILE CRANE 5 T																																	
MOBILE CRANE 75 T			1																														
MOBILE CRANE 50 T		2	2	2	2	2	2	-	-	2	2	2	2	2																			
Pick Up truck (NKG)		1	1	1	1	1	1	-	-	1	1	1	1	1																			

WEATHER REPORT

WEEK 28th 6-12 March 23

MARCH, 2023


MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY	SUNDAY
27	28	1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31	1	2

Day type	This week (days)	Accumulate to Last month	Accumulate to this month	Remark
Working day	7	170	177	
Holiday	-	16	16	
Total	7	186	193	
Summary Rain hours.				
Clear				
Rain	-	80	80	
Hard rain	3	4	7	
Total Rain hours	3	84	87	






Date	Description	Number of working days delayed
10/Mar/23	Stop all steel structure work for installation the equipment tank no.R-8121A level +19.50 at MP7 and lift up tank no.D-8122&D-8122B. Lost working time 1 day.	1
	Accumulated number of delayed working days	18

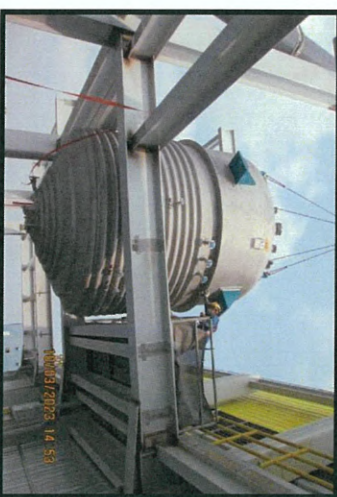

PROJECT : MP6&MP7

WEEKLY REPORT, WEEK 32nd

3 - 9 April 2023

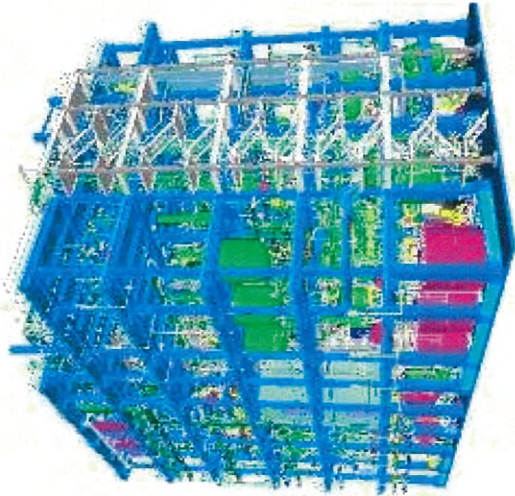

N.K.G. PLUS CO.,LTD.

WEEKLY REPORT, WEEK 32nd

3 - 9 April 2023


PROJECT : MP6&MP7



Installation the wiremesh slab level +38.375 MP7.



Installation the wiremesh slab level +38.375 MP7.

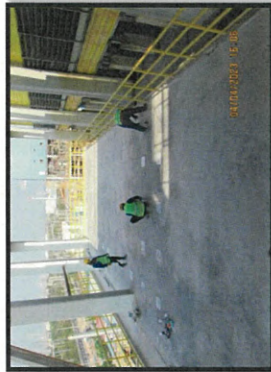

Line marking cooling tower support location level +32.50 MP7.



Installation pipe rack beam level +29.60, +30.80 MP7.



Pouring concrete pump foundation level +26.50 MP7.



Pouring concrete pump foundation level +26.50 MP7.



Remove the wall formworks of DCS room level +13.50 MP7.



Remove the wall formworks of DCS room level +13.50 MP7.



Installation column rebar with epoxy



Installation column rebar with epoxy




Installation the beam support for tank




Installation the pipe rack level +24.80 +23.60



Installation column rebar with epoxy



Installation column rebar with epoxy



Installation the metal deck level +13.50.+19.50 MP6.



Installation the pipe rack level +24.80, +23.60



Daily Manpower Report


Company : N.K.G. PLUS CO.,LTD.

Project: MP6 & MP7

Date						
Position	Mon	Tue	Wed	Thu	Fri	Sat
Project Manager	1	1	1	1	1	1
Site Engineer	1	1	1	1	1	1
Safety officer	-	1	1	-	-	1
Supervisor	-	1	1	-	-	-
Foreman	2	2	2	2	2	-
Servicior	1	1	1	1	1	-
Admin	1	1	1	1	1	1
Pick up Driver	1	9	8	8	5	-
NKG staff	8	9	9	8	8	5
Head man	1	1	1	-	-	-
Carpenter	11	11	11	9	5	4
Mason	11	11	11	9	5	4
Steel fixer	1	1	1	1	1	1
Labour	4	4	4	4	4	5
General Labour	4	4	4	4	4	2
Store , Checker-maid	2	2	2	-	-	-
NKG worker	23	23	23	18	13	12
SUB CONTRACTOR						
Concrete pump boom operator						
Mobile crane operator	2	2	2	2	2	14
Shear stud of metal deck work	15	15	15	13	13	14
Scalloiding work						
Aluminium work						
Total sub contract	17	17	17	15	16	-
Total Manpower	48	49	49	41	36	33
MACHINE & EQUIPMENT						
CONCRETE PUMP BOOM						
STATIONARY CONCRETE PUMP						
MOBILE CRANE 75 T	1	1	1	1	1	1
MOBILE CRANE 50 T	1	1	1	1	1	1
Pick Up truck (NKG)	1	1	1	1	1	1

WEEK 32nd 3-9 April 23

APRIL, 2023

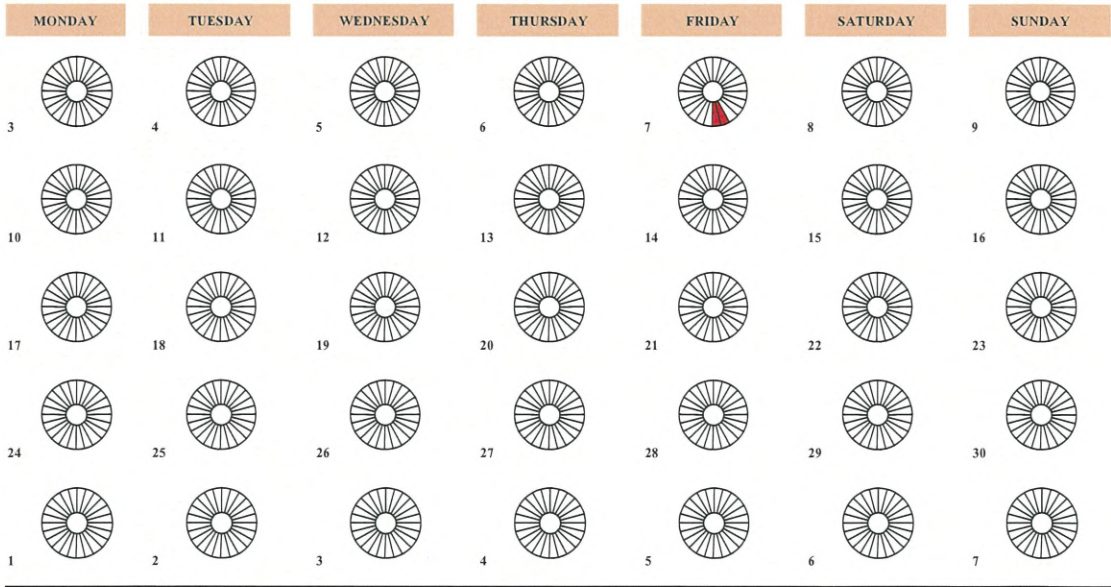

Day type	This week (days)	Accumulate to Last month	Accumulate to this month	Remark
Working day	7	197	204	
Holiday	0	17	17	
Total	7	214	221	
Summary Rain hours.				
Clear				
Rain	-	80	80	
Hard rain	2	10	12	
Total Rain hours	2	90	92	



WORK OBSTRUCTION

WEEKLY REPORT WEEK 32nd

3 - 9 April 2023




Date	Description	Number of working days delayed
6/Apr/23	Stop all steel structure work for installation the equipment tank no.D-9552 level +7.50 MP6. Lost working time 1 day.	1
4/7/2023	Heavy rain. Lost working time 1 day. Accumulated number of delayed working days	1 20



PROJECT : MP6&MP7

WEEKLY REPORT,WEEK 38th

15 - 21 May 2023

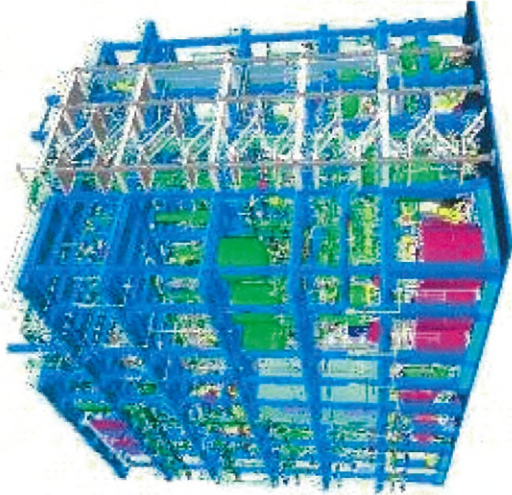

N.K.G. PLUS CO.,LTD.


PROJECT : MP6&MP7

WEEKLY REPORT,WEEK 38th

15 - 21 May 2023




Installation wiremesh slab level +13.50 m. MP6.

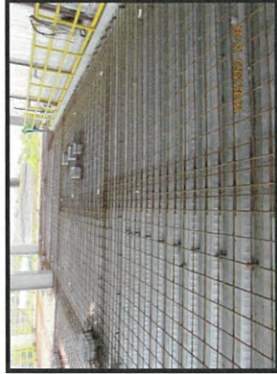

Installation wiremesh slab level +13.50 m. MP6.



Pouring concrete slab level +13.50 m. MP6.

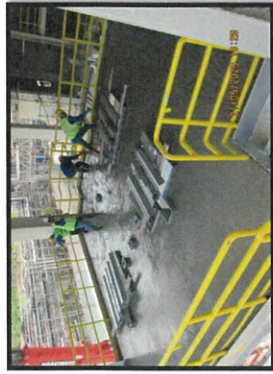

Pouring concrete slab level +10.25 m. MP6.



Installation wiremesh slab level +13.50 m. MP6.



Pouring concrete slab level +13.50 m. MP6.



Pouring concrete slab level +13.50 m. MP6.



Installation pipe rack frame +35.608+36.80 m.MP6.

Daily Manpower Report

Company : N.K.G. PLUS CO.,LTD.

Project: MP6 & MP7


Date	Position	May-23																												
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	
	Project Manager				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	Site Engineer				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	Safety officer				2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2
	Supervisor				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	Foreman				2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2
	Servyor				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	Admin				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	Pick up Driver				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	NKG staff	-			10	10	10	10	10	10	10	11	11	10	3	10	9	9	9	9	9	9	9	7	-	-	-	-	-	-
	Head man				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	Carpenter																													
	Mason				11	10	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11
	Steel fixer				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	General Labour				4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	3	3	3	3	3	3	3	3
	Store , Checker-maid				2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2
	NKG worker	-			21	20	21	21	21	21	21	21	21	21	21	21	21	21	21	21	21	21	18	-	-	-	-	-	-	-
	SUB CONTRACTOR																													
	Mobile crane operator				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	6							
	Concrete pump boom operator				1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
	Steel Structure				15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15	15
	Shear stud of metal deck work																													
	Liquid floor hardener																													
	Scaffolding work																													
	Total sub contract	-			16	16	16	16	16	16	16	16	16	16	16	16	16	16	16	16	16	16	22	-	-	-	-	-	-	-
	Total Manpower	-			47	46	47	47	47	47	47	47	47	47	47	47	47	47	47	47	47	47	47	-	-	-	-	-	-	-
	CACHINE & EQUIPMENT																													
	CONCRETE PUMP BOOM																													
	Stationary Pump Concrete																													
	Backhoe SK 200																													
	MOBILE CRANE 75 T																													
	MOBILE CRANE 70 T																													
	Pick Up Truck (NKG)																													



Installation metal deck level +32.50 m. MP6.



Installation angle bar for gutter at ground floor.

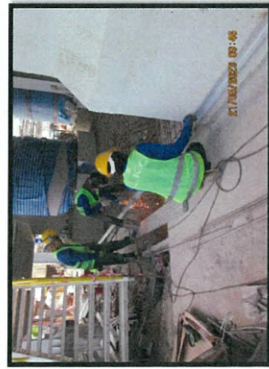

Installation angle bar for gutter at ground floor.



Installation metal deck level +32.50 m. MP6.



Installation angle bar for gutter at ground floor.




External wall painting of MCC room level +7.50 m



WEEK 38th 15-21 May 23

MAY, 2023

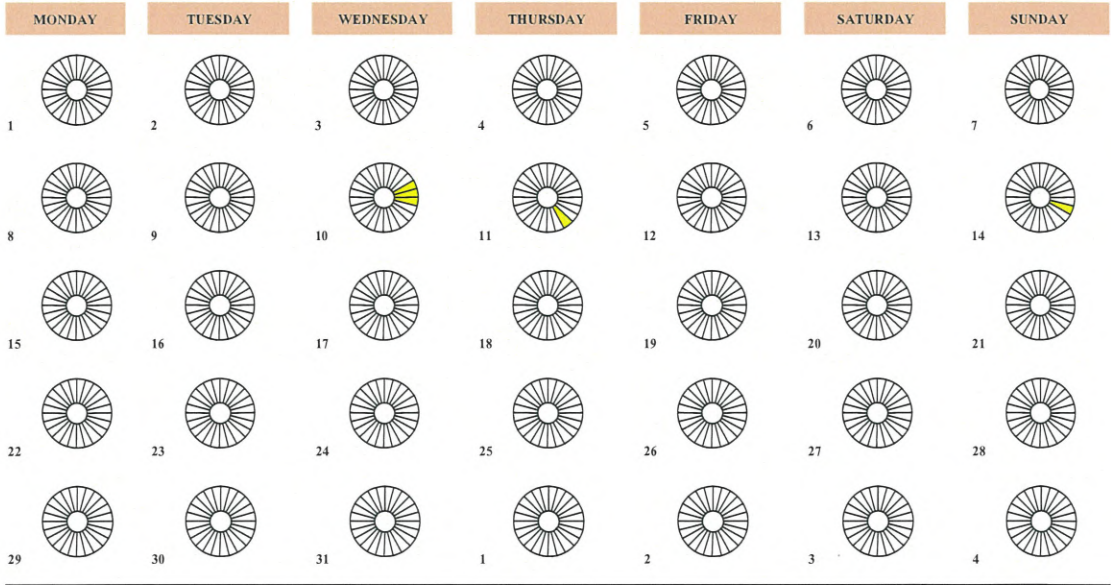

Day type	This week (days)	Accumulate to Last month	Accumulate to this month	Remark
Working day	7	233	240	
Holiday	-	23	23	
Total	7	249	263	
Summary Rain hours.				
Clear				
Rain	-	87	87	
Hard rain	-	12	12	
Total Rain hours	0	94	99	



WORK OBSTRUCTION

WEEKLY REPORT WEEK 38th

15 - 21 May 2023


Date	Description	Number of working days delayed
	Accumulated number of delayed working days	21



PROJECT : MP6&MP7

WEEKLY REPORT,WEEK 40th

29 - 4 June 2023

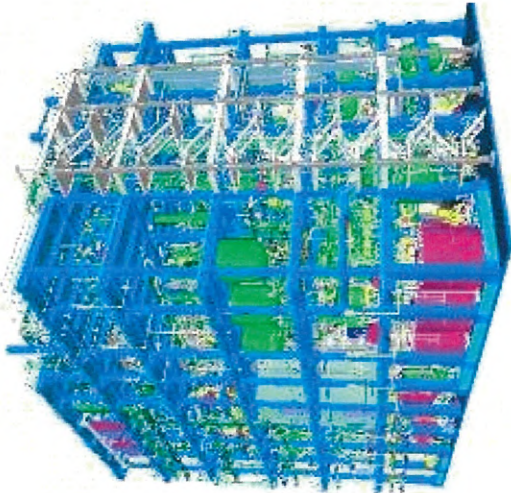

N.K.G. PLUS CO.,LTD.

PROJECT : MP6&MP7

WEEKLY REPORT,WEEK 40th
29 - 4 June 2023




Installation gutter formwork level +32.50 m. MP6.



Pouring concrete slab level +26.50 m. MP6.



Installation rebar and formwork pump foundation level +26.50 m. MP6.

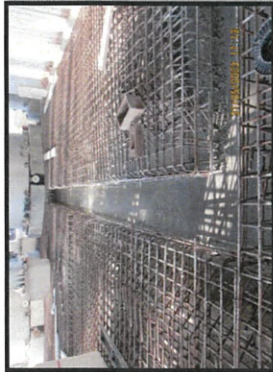

Pouring concrete gutter slab level +0.25 m. MP6.




Installation gutter formwork level +32.50 m. MP6.




Pouring concrete slab level +26.50 m. MP6.



Installation rebar and formwork pump foundation level +26.50 m. MP6.

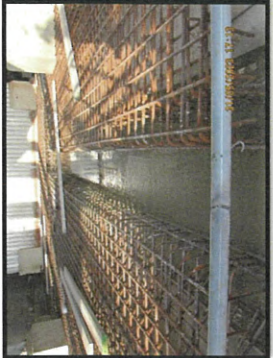


Pouring concrete gutter slab level +0.25 m. MP6.

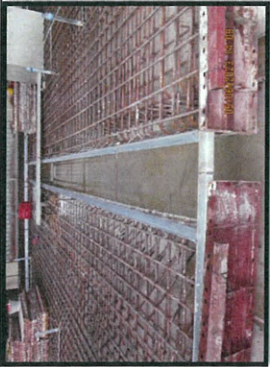


Pouring concrete gutter slab level +0.25 m. MP6.



Installation angle bar of gutter level +0.25 m. MP6.

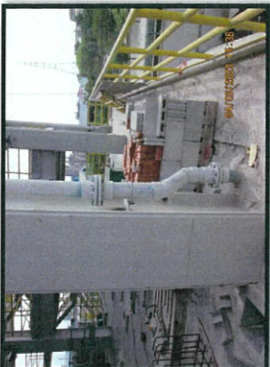

Installation pipe rainage level +7.50 m. MP6.

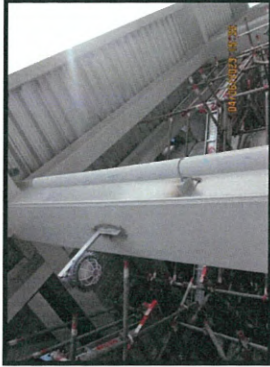


Installation pipe rainage level +13.50 m. MP6.



Installation angle bar of gutter level +0.25 m. MP6.



Pouring sand cement of landing and tread of staircase ST3 MP6.

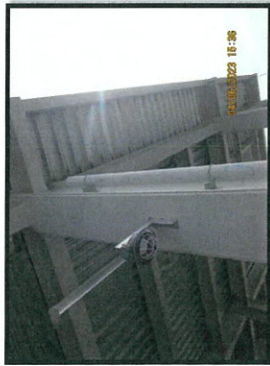

Installation pipe rainage level +7.50 m. MP6.



Installation pipe rainage level +13.50 m. MP6.



Installation aluminum glass window of DCS room and MCC room MP7.

Daily Manpower Report

Company : N.K.G. PLUS CO.,LTD.

Project: MP6 & MP7



Position	Date	Ji. 01. -23																											
		29 Mon	30 Tue	31 Wed	1 Thu	2 Fri	3 Sat	4 Sun	5 Mon	6 Tue	7 Wed	8 Thu	9 Fri	10 Sat	11 Sun	12 Mon	13 Tue	14 Wed	15 Thu	16 Fri	17 Sat	18 Sun	19 Mon	20 Tue	21 Wed	22 Thu	23 Fri	24 Sat	25 Sun
Project Manager		1	1	1	1	1	1	1																					
Site Engineer		1	1	1	1	1	1	1																					
Safety officer		2	2	2	2	2	2	1																					
Supervisor		1	1	1	1	1	1	1																					
Foreman		3	3	3	3	3	3	3																					
Surveyor		1	1	1	1	1	1	1																					
Admin		1	1	1	1	1	1	1																					
Pick up Driver		1	1	1	1	1	1	1																					
NKG staff		11	11	11	11	11	11	8	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Head man		1	1	1	1	1	1	1																					
Carpenter																													
Mason		11	11	11	11	11	11	11																					
Steel fixer		1	1	1	1	1	1	5	5																				
Labour		3	4	3	3	3	7	5																					
General Labour		3	3	3	3	3	3	2																					
Daily chart labour		6	9	6	4	6																							
Store , Checker-maid		2	2	2	2	2	2	2																					
NKG worker		27	31	27	25	27	29	26	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
SUB CONTRACTOR																													
Concrete pump operator				5																									
Mobile crane operator				1																									
Steel Structure		16	8																										
Pipe drainage work					5	5	3	3																					
Cutting slab work																													
Liquid floor hardener																													
Scaffolding work		3																											
Total sub contract		19	8	6	5	5	3	3	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Total Manpower		57	50	44	41	43	43	37	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
MACHINE & EQUIPMENT																													
Pump boom concrete																													
Stationary Pump Concrete				1																									
Backhoe SK 200																													
MOBILE CRANE 75 T																													
MOBILE CRANE 70 T		1																											
MOBILE CRANE 60 T				1																									
Pick Up truck (NKG)		1	1	1	1	1	1	1																					

WEATHER REPORT

WEEK 40th 29-4 June 23

JUNE, 2023

MONDAY	TUESDAY	WEDNESDAY	THURSDAY	FRIDAY	SATURDAY	SUNDAY
29	30	31	1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	1	1

Day type	This week (days)	Accumulate to Last month	Accumulate to this month	Remark
Working day	7	246	253	
Holiday	-	24	24	
Total	7	270	277	
Summary Rain hours.				
Clear				
Rain	-	87	87	
Hard rain	-	12	12	
Total Rain hours	0	94	99	



WORK OBSTRUCTION

WEEKLY REPORT, WEEK 40th

29 - 4 June 2023




Date	Description	Number of working days delayed
	Accumulated number of delayed working days	21

PROJECT : MP6&MP7

WEEKLY REPORT, WEEK 41st

5 - 11 June 2023

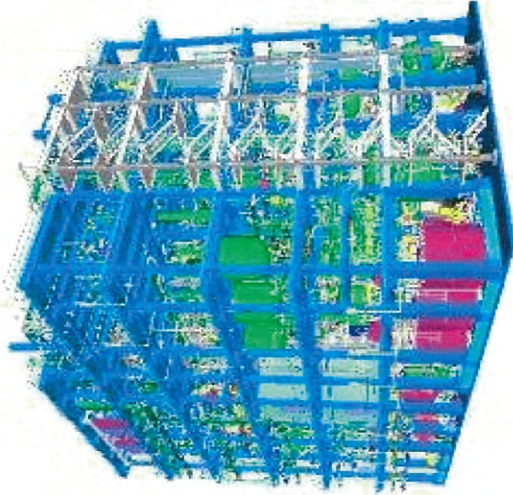

N.K.G. PLUS CO.,LTD.

PROJECT : MP6&MP7

WEEKLY REPORT, WEEK 41st
5 - 11 June 2023



Pouring concrete slab level +32.50 m. MP6.



Pouring concrete slab level +32.50 m. MP6.



Pouring concrete slab level +32.50 m. MP6.



Pouring concrete slab level +32.50 m. MP6.



Pouring concrete slab level +0.25 m. MP6.



Pouring concrete slab level +0.25 m. MP6.




Pouring concrete slab level +0.25 m. MP6.



Pouring concrete slab level +0.25 m. MP6.



Pouring concrete pump foundation P-9561 level +7.50 m. MP6.

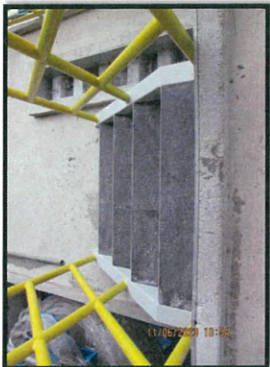

Installation granito floor tile at staircase to level +12.50 m. MP6.



Installation granito floor tile at staircase to level +12.50 m. MP6.



Pouring concrete kerb level +32.50 m. MP6.



Pouring concrete pump foundation V-9558,V-9559 level +26.50 m. MP6.



Installation granito floor tile at staircase to level +12.50 m. MP6.



Installation grating tread of staircase to platform level +9.10 m. MP6.



Pouring concrete kerb level +32.50 m. MP6.



Remove formwork of pump foundation level +26.50 m. MP6.



Installation pipe drainage level +19.50 m. +26.50 m. MP7.



Pouring concrete kerb level +26.50 m. MP6.



Installation pipe drainage level +19.50 m. +26.50 m. MP7.

Daily Manpower Report

Company : N.K.G. PLUS CO.,LTD.

Project: MP6 & MP7




Position	Date	Ji. 0. -23																											
		29 Mon	30 Tue	31 Wed	1 Thu	2 Fri	3 Sat	4 Sun	5 Mon	6 Tue	7 Wed	8 Thu	9 Fri	10 Sat	11 Sun	12 Mon	13 Tue	14 Wed	15 Thu	16 Fri	17 Sat	18 Sun	19 Mon	20 Tue	21 Wed	22 Thu	23 Fri	24 Sat	25 Sun
Project Manager		1	1	1	1	1	1	1	1	1	1	1	1	1	1														
Site Engineer		1	1	1	1	1	1	1	1	1	1	1	1	1	1														
Safety officer		2	2	2	2	2	2	1	1	1	1	1	2	2	1														
Supervisor		1	1	1	1	1	1	1	1	1	1	1	1	1	1														
Foreman		3	3	3	3	3	3	3	3	3	3	3	3	3	3														
Surveyor		1	1	1	1	1	1	-	1	1	1	1	1	1	1														
Admin		1	1	1	1	1	1	-	1	1	1	1	1	1	1														
Pick up Driver		1	1	1	1	1	1	1	1	1	1	1	1	1	1														
NKG staff		11	11	11	11	11	11	8	10	10	10	10	11	11	6	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Head man		1	1	1	1	1	1	1	1	1	1			1															
Carpenter																													
Mason		11	11	11	11	11	11	11	11	11	11	11	11	11	11														
Steel fixer		1	1	1	1	1	5	5	6	6	6	6	6	6	3														
Labour		3	4	3	3	3	7	5	6	5	6	6	6	6	3														
General Labour		3	3	3	3	3	3	2	3	3	3	3	3	3	3														
Daily chart labour		6	9	6	4	6																							
Store ,Checker-maid		2	2	2	2	2	2	2	2	2	2				2														
NKG worker		27	31	27	25	27	29	26	29	28	29	26	26	26	23	-	-	-	-	-	-	-	-	-	-	-	-	-	-
SUB CONTRACTOR																													
Concrete pump operator				5							3			5															
Mobile crane operator				1																									
Steel Structure		16	8									8	7	7															
Pipe drainage work					5	5	3	3	4					3	3														
Cutting slab work																													
Liquid floor hardener																													
Scaffolding work		3																											
Total sub contract		19	8	6	5	5	3	3	4	-	3	8	7	15	3	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Total Manpower		57	50	44	41	43	43	37	43	38	42	44	44	52	32	-	-	-	-	-	-	-	-	-	-	-	-	-	-
MACHINE & EQUIPMENT																													
Pump boom concrete											1																		
Stationary Pump Concrete				1										1															
Backhoe SK 200																													
MOBILE CRANE 75 T																													
MOBILE CRANE 70 T		1																											
MOBILE CRANE 60 T				1																									
Pick Up truck (NKG)		1	1	1	1	1	1	1	1	1	1	1	1	1	1														

WEATHER REPORT

WEEK 41st 5-11 June 23

JUNE, 2023

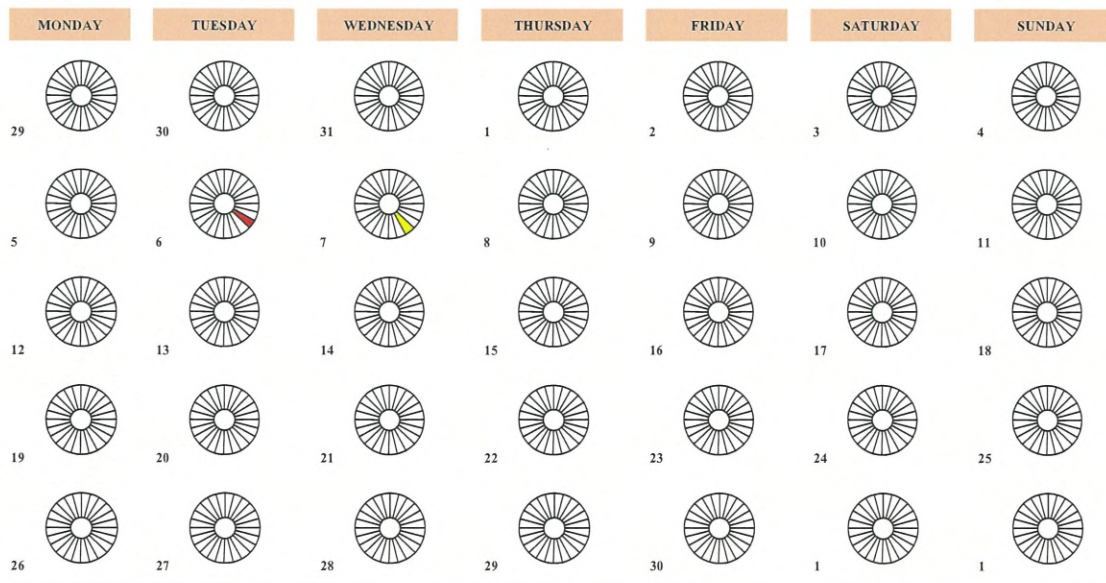

Day type	This week (days)	Accumulate to Last month	Accumulate to this month	Remark
Working day	7	253	260	
Holiday	-	24	24	
Total	7	270	284	
Summary Rain hours.				
Clear				
Rain	1	87	88	
Hard rain	1	12	13	
Total Rain hours	2	94	101	



WORK OBSTRUCTION

WEEKLY REPORT, WEEK 41st

5 - 11 June 2023




Date	Description	Number of working days delayed
	Accumulated number of delayed working days	21

PROJECT : MP6&MP7

WEEKLY REPORT,WEEK 42nd

12 - 18 June 2023

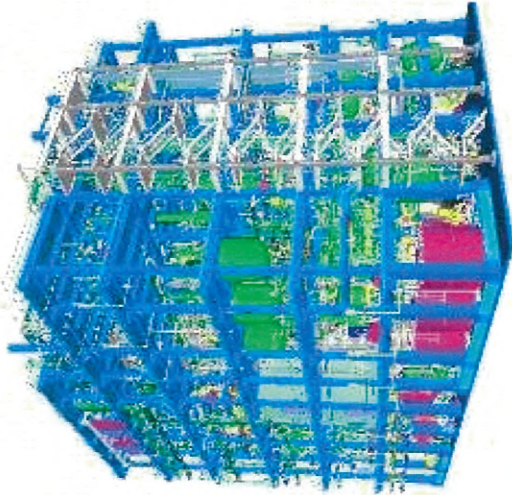

N.K.G. PLUS CO.,LTD.

PROJECT : MP6&MP7

WEEKLY REPORT,WEEK 42nd
12 - 18 June 2023




Remove gutter formwork level +32.50 m. MP6.



Pump foundation level +32.50 m. MP6.



Pouring concrete pump foundation level +26.50 m. MP6.

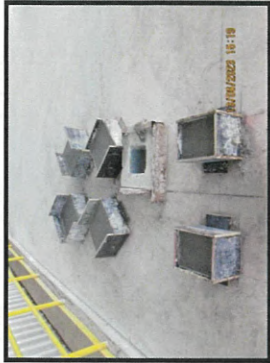

Pouring concrete pump foundation level +26.50 m. MP6.



Pouring concrete pump foundation level +19.50 m. MP6.



Installation scaffolding for column to 6 meters level +0.25 m. MP6.



Pouring concrete column to 6 meters +0.25 m. MP6.



Installation column formwork to 6 meters +0.25 m. MP6.



Liquid floor hardner level +0.25 m. MP6.



Liquid floor hardner level +7.50 m. MP6.



Liquid floor hardner level +19.50 m. MP6.



Liquid floor hardner level +10.25 m. MP6.



Liquid floor hardner level +0.25 m. MP6.



Liquid floor hardner level +7.50 m. MP6.



Liquid floor hardner level +19.50 m. MP6.



Liquid floor hardner level +26.50 m. MP6.



Liquid floor hardner level +26.50 m. MP6.



Installation galvanized steel grating +0.25 m. MP6.



Installation galvanized steel grating +0.25 m. MP6.



Pump foundation level +0.25 m. MP6.



Liquid floor hardner level +26.50 m. MP6.



Installation galvanized steel grating +0.25 m. MP6.



Pump foundation level +0.25 m. MP6.



Pump foundation level +0.25 m. MP6.



Pump foundation level +0.25 m. MP6.



Installation granito floor tile of staircase to level +26.50 m. MP6.




Clearing material for slab around building MP6.



Pump foundation level +0.25 m. MP6.



Installation granito floor tile of staircase to level +26.50 m. MP6.

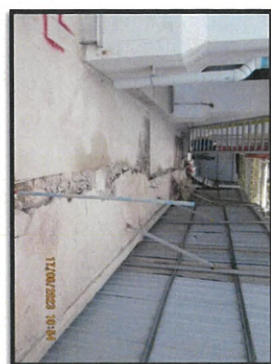

Clearing material for slab around building MP6.

Daily Manpower Report

Company : N.K.G. PLUS CO.,LTD.

Project: MP6 & MP7




Position	Date	ปี.บ.-23																											
		29 Mon	30 Tue	31 Wed	1 Thu	2 Fri	3 Sat	4 Sun	5 Mon	6 Tue	7 Wed	8 Thu	9 Fri	10 Sat	11 Sun	12 Mon	13 Tue	14 Wed	15 Thu	16 Fri	17 Sat	18 Sun	19 Mon	20 Tue	21 Wed	22 Thu	23 Fri	24 Sat	25 Sun
Project Manager		1	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	-	1	1	-	1						
Site Engineer		1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	-							
Safety officer		2	2	2	2	2	2	1	1	1	1	1	2	2	1	2	2	2	2	2	2	1							
Supervisor		1	1	1	1	1	1	1	1	1	1	1	1	1		1	1	1	1	1	1	1	1						
Foreman		3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	2	3	3	3	3	3						
Serveyor		1	1	1	1	1	1	-	1	1	1	1	1	1		1	1	1	1	1	1	1	-						
Admin		1	1	1	1	1	1	-	1	1	1	1	1	1		1	1	1	1	1	1	-							
Pick up Driver		1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1						
NKG staff		11	11	11	11	11	11	8	10	10	10	10	11	11	6	11	10	10	11	11	10	7	-	-	-	-	-	-	
Head man		1	1	1	1	1	1	1	1	1	1				1	1	1	1	1	1	1	1							
Carpenter																													
Mason		11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	10	10	10							
Steel fixer		1	1	1	1	1	5	5	6	6	6	6	6	6	3	7	7	7	7	7	7	6							
Labour		3	4	3	3	3	7	5	6	5	6	6	6	6	3	9	10	11	11	11	11	9							
General Labour		3	3	3	3	3	3	2	3	3	3	3	3	3	3	3	3	3	3	3	3	3							
Daily chart labour		6	9	6	4	6																							
Store , Checker-maid		2	2	2	2	2	2	2	2	2	2				2	2	2	2	2	2	2	2							
NKG worker		27	31	27	25	27	29	26	29	28	29	26	26	26	23	33	34	35	35	34	34	31	-	-	-	-	-	-	
SUB CONTRACTOR																													
Concrete pump operator				5							3			5															
Mobile crane operator				1																									
Steel Structure		16	8									8	7	7		7	7	7											
Pipe drainage work					5	5	3	3	4					3	3			3											
Cutting slab work																													
Liquid floor hardener																		4	4	4									
Scaffolding work		3														5	4												
Total sub contract		19	8	6	5	5	3	3	4	-	3	8	7	15	3	12	11	14	4	4	-	-	-	-	-	-	-		
Total Manpower		57	50	44	41	43	43	37	43	38	42	44	44	52	32	56	55	59	50	49	44	38	-	-	-	-	-		
MACHINE & EQUIPMENT																													
Pump boom concrete											1																		
Stationary Pump Concrete				1										1															
Backhoe SK 200																													
MOBILE CRANE 75 T																													
MOBILE CRANE 70 T		1																											
MOBILE CRANE 60 T				1																									
Pick Up truck (NKG)		1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1							

WEATHER REPORT

WEEK 42nd 12-18 June 23

JUNE, 2023

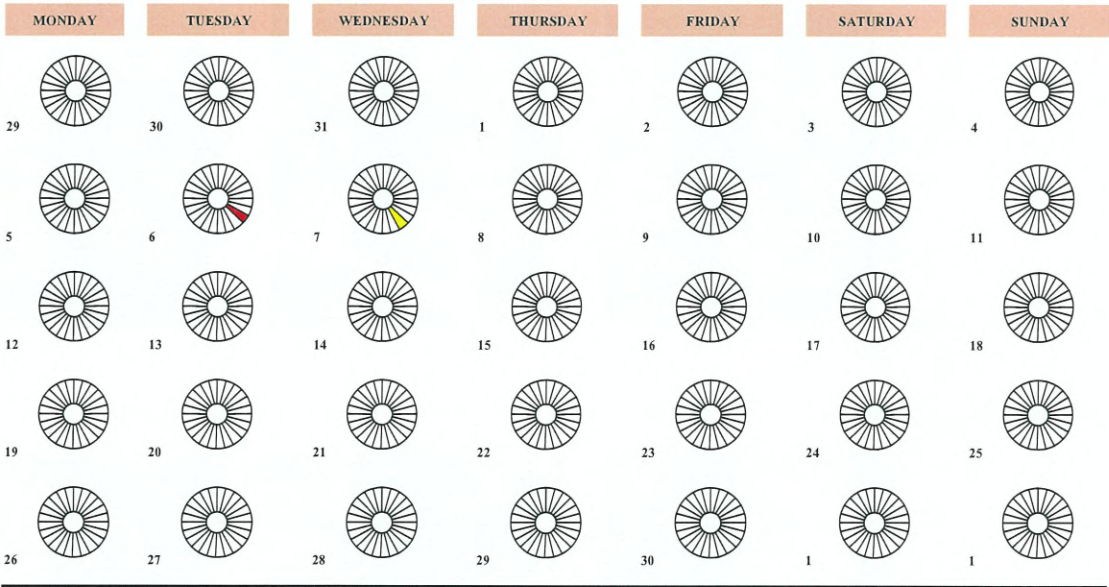

Day type	This week (days)	Accumulate to Last month	Accumulate to this month	Remark
Working day	7	260	267	
Holiday	-	24	24	
Total	7	284	291	
Summary Rain hours.				
Clear				
Rain	-	88	88	
Hard rain	-	13	13	
Total Rain hours	0	101	101	



WORK OBSTRUCTION

WEEKLY REPORT WEEK 42nd

12 - 18 June 2023


Date	Description	Number of working days delayed
	Accumulated number of delayed working days	21



PROJECT : MP6&MP7

WEEKLY REPORT, WEEK 43rd

19 - 25 June 2023

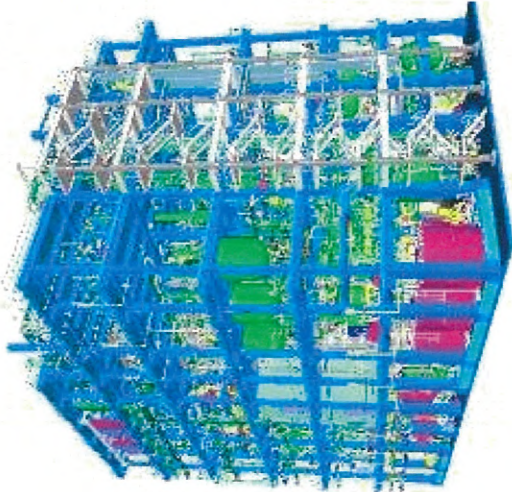

N.K.G. PLUS CO.,LTD.

PROJECT : MP6&MP7


WEEKLY REPORT, WEEK 43rd
19 - 25 June 2023



Pouring concrete column to 6 meters at level +0.25 m. MP6.



Remove column formwork and skim coating level +0.25 m. MP6.

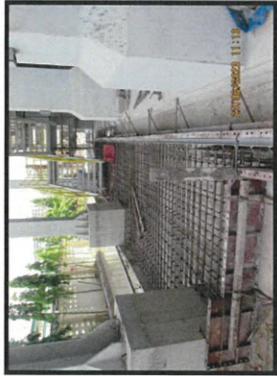

Installation rebar and formwork of slab under staircase ST-3 level +0.25m. MP6.



Setting angle bar, rebar and formwork of gutter level +0.25 m. MP6.



Breaking existing concrete slab for slab around MP6.



Breaking existing concrete slab for slab around MP6.



Pouring concrete kerb for bund wall MP6.





Installation PVC pipe rainage level +7.50 m. MP6.



Installation granito floor tile level +32.50 m. MP6.



Granito floor tile grouting of staircase ST-3 level +32.50 m. to +26.50 m. MP6.



Welding pipe rainage support level +32.50 m. to +26.50 m. MP6.

to +26.50 m. MP6.

to +7.50 m. MP7.

Daily Manpower Report

Company : N.K.G. PLUS CO.,LTD.


Project: MP6 & MP7

Date	Position	11.11.23																												
		29 Mon	30 Tue	31 Wed	1 Thu	2 Fri	3 Sat	4 Sun	5 Mon	6 Tue	7 Wed	8 Thu	9 Fri	10 Sat	11 Sun	12 Mon	13 Tue	14 Wed	15 Thu	16 Fri	17 Sat	18 Sun	19 Mon	20 Tue	21 Wed	22 Thu	23 Fri	24 Sat	25 Sun	
	Project Manager	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
	Site Engineer	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
	Safety Officer	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	
	Supervisor	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
	Foreman	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	
	Surveyor	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
	Admin	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
	Pick up Driver	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
	NKG staff	11	11	11	11	11	11	8	10	10	10	10	10	10	10	6	11	10	10	10	10	7	11	11	11	11	11	11	11	
	Head man	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
	Carpenter																													
	Mason	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	11	10	10	10	10	10	10	10	10	10	
	Steel fixer	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
	Labour	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	
	General Labour	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	
	Daily chart labour	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	6	
	Store , Checker-maid	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	
	NKG worker	27	31	27	27	25	27	29	26	29	28	29	26	29	26	23	33	34	35	35	34	34	31	34	34	35	34	34	32	-
	SUB CONTRACTOR																													
	Concrete pump operator																													
	Mobile crane operator																													
	Steel Structure	16	8																											
	Pipe drainage work																													
	Cutting slab work																													
	Liquid floor hardener	3																												
	Scaffolding work																													
	Total sub contract	19	8	6	5	5	3	3	3	3	4	3	3	3	3	3	5	4	15	7	3	3	3	5	4	11	3	3	3	
	Total Manpower	57	50	44	41	43	43	43	37	43	38	42	44	44	52	32	56	55	59	50	49	44	38	45	48	49	48	46	5	
	MACHINE & EQUIPMENT																													
	Stationary Pump Concrete																													
	Pump boom concrete																													
	Backhoe SK 200																													
	MOBILE CRANE 75 T																													
	MOBILE CRANE 70 T																													
	MOBILE CRANE 60 T																													
	Pick Up truck (NKG)																													

WEATHER REPORT

WEEK 43rd 19-25 June 23

JUNE, 2023

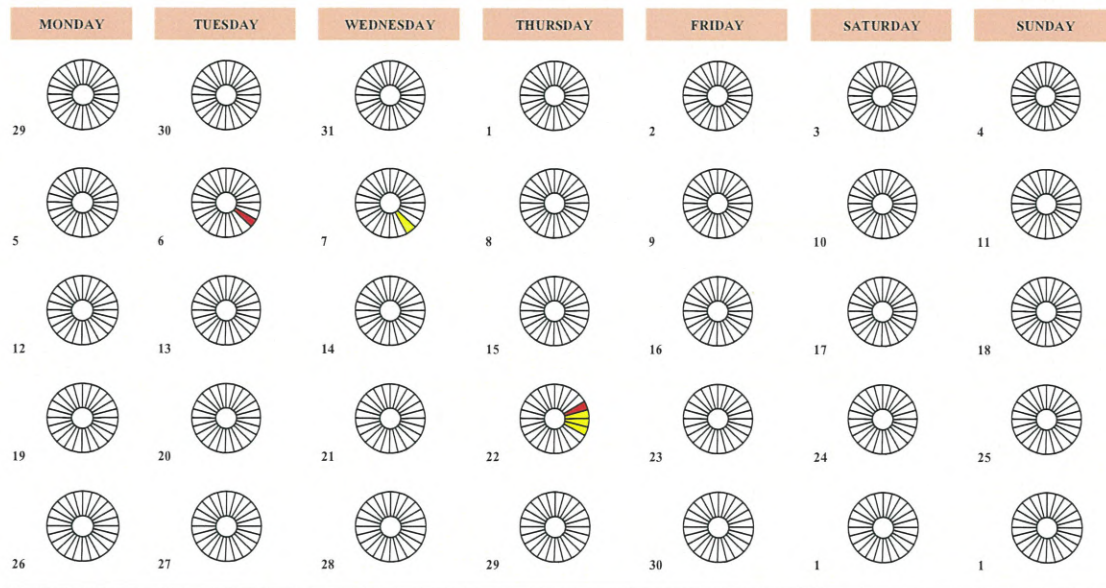

Day type	This week (days)	Accumulate to Last month	Accumulate to this month	Remark
Working day	7	260	267	
Holiday	-	24	24	
Total	7	284	291	
Summary Rain hours.				
Clear				
Rain	3	88	91	
Hard rain	1	13	14	
Total Rain hours	4	101	105	



WORK OBSTRUCTION

WEEKLY REPORT, WEEK 43rd

19 - 25 June 2023

Date	Description	Number of working days delayed
	Accumulated number of delayed working days	21

