

ภาคผนวก ค

เอกสารการปฏิบัติตามมาตรการป้องกันและลดผลกระทบสิ่งแวดล้อม

- ค1 ใบเสร็จค่าเก็บขยะ
- ค2 ใบเสร็จขายของเก่า
- ค3 ใบเสร็จกำจัดสิ่งปฏิกูล
- ค4 เอกสารการตรวจสอบถังดับเพลิง
- ค5 เอกสารทดสอบสัญญาณ Fire Alarm
- ค6 เอกสารตรวจสอบตู้สายดับเพลิง Fire hose Cabinet
- ค7 เอกสารตรวจสอบตู้และสายส่งน้ำดับเพลิง
- ค8 เอกสารตรวจสอบตู้สำหรับเก็บชุดและอุปกรณ์ดับเพลิง
- ค9 เอกสารการบำรุงรักษาไฟฉุกเฉินและไฟทางออก
- ค10 เอกสารตรวจสอบไฟฉุกเฉินและไฟทางออก
- ค11 เอกสารตรวจสอบหัวจ่ายน้ำดับเพลิง
- ค12 เอกสารบันทึกการตรวจสอบ Sprinkler Alarm
- ค13 เอกสารตรวจสอบบันไดหนีไฟ
- ค14 เอกสารตรวจสอบประตูทางออกฉุกเฉิน
- ค15 เอกสารทดสอบการทำงานของปั้มน้ำดับเพลิง
- ค16 เอกสารตรวจสอบห้องเครื่องสูบน้ำดับเพลิง
- ค17 เอกสารทดสอบการทำงานของเครื่องกำเนิดไฟ



ภาคผนวก ค

เอกสารการปฏิบัติตามมาตรการป้องกันและลดผลกระทบสิ่งแวดล้อม (ต่อ)

- ค18 เอกสารตรวจสอบกล้อง CCTV Monthly Inspection
- ค19 เอกสารตรวจสอบกล้องปฐมพยาบาล
- ค20 บันทึกการตรวจสอบสระว่ายน้ำ
- ค21 การตรวจสอบระบบไฟฟ้าแสงสว่าง
- ค22 เอกสารการตรวจสอบระบบระบายน้ำ รางระบายน้ำ
- ค23 เอกสารตรวจสอบ LPG Log sheet
- ค24 เอกสารตรวจสอบบันทึกเครื่องทำความเย็น Chiller Log Sheet
- ค25 เอกสารตรวจสอบบันทึกห้องแช่แข็งและห้องเย็น
- ค26 เอกสารบันทึกการตรวจสอบ Heat Pump
- ค27 ทส.1 และ ทส.2
- ค28 เอกสารตรวจสอบห้องบันทึกห้องเครื่องกำเนิดไฟ
- ค29 รายงานสำรวจโครงสร้าง อีสตินตัน เชียงใหม่
- ค30 เอกสารตรวจสอบถังเก็บน้ำประปา
- ค31 Master Key Control
- ค32 เอกสารใบตรวจเช็คถังดับเพลิง
- ค33 ซ่อมอพยพหนีไฟประจำปี 2568



ภาคผนวก ค1

ใบเสร็จค่าเก็บขยะ



ใบเสร็จรับเงินค่ามูลฝอย

สำนักงาน

เล่มที่ 3882

เลขที่ 5

เทศบาลนครเชียงใหม่

ได้รับเงินค่ามูลฝอยอัตรา.....300.....ลิตร 1..... เดือน

ประจำเดือน..... (English).....

บ้านเลขที่

อำเภอ.....

ไว้แล้ว แ

(นางสาวพยอม ใจวงศ์)

เจ้าพนักงานจัดเก็บรายได้ปฏิบัติงาน

ใบเสร็จรับเงินค่ามูลฝอย

สำนักงาน

เล่มที่ 3890

เลขที่ 6

เทศบาลนครเชียงใหม่

ได้รับเงินค่ามูลฝอยอัตรา 300 ลิตร 1 เดือน

ประจำเดือน สิงหาคม 2568 จาก บจก. คีนะบุ (Eastin.)

บ้านเลขที่ 171

อำเภอ ฝาง

ไว้แล้ว แต่



จังหวัดเชียงใหม่

ใบเสร็จรับเงินค่ามูลฝอย

สำนักงาน

เล่มที่ 3898

เลขที่ 11

เทศบาลนครเชียงใหม่

ได้รับเงินค่ามูลฝอยอัตรา 300 ลิตร เดือน

ประจำเดือน กย 68 จาก ขวัญ บ้านเลขที่ 68 (Ersting)

บ้านเลขที่...

อำเภอ...

ไว้แล้ว แต่

หัวหน้างานจัดเก็บรายได้ศรีวิชัย

ใบเสร็จรับเงินค่ามูลฝอย

สำนักงาน

เล่มที่ 3912

เลขที่ 5

เทศบาลนครเชียงใหม่

ได้รับเงินค่ามูลฝอยอัตรา 300 ลิตร 1 เดือน

ประจำเดือน ตุลาคม 2568 จาก ขก.พันธ์ (Eastin)

บ้านเลขที่ 171

อำเภอ...

ไว้แล้ว



ใบเสร็จรับเงินค่ามูลฝอย

สำนักงาน

เล่มที่ 3921
(โครงการ Eastin)

เลขที่ 23

เทศบาลนครเชียงใหม่


ได้รับเงินค่ามูลฝอยอัตรา.....300.....ลิตร.....1.....เดือน

ประจำเดือน.....พฤษภาคม 2568.....จาก.....รพช.พิษณุโลก รหัสที่ ๐๐๐๐๑

บ้านเลข

อำเภอ.....

ไว้แล้ว



ใบเสร็จรับเงินค่ามุลฝอย

สำนักงาน

เล่มที่ 3935

เลขที่ 39

(โครงการ Eastin)

เทศบาลนครเชียงใหม่

ได้รับเงินค่ามุลฝอยอัตรา 300 ลิตร 1 เดือน

ประจำเดือน ธันวาคม 2568 จาก ขจก.ตำบ.ราช อำเภอ 00002

บ้านเลขที่

อำเภอ

ไว้แล้ว แ



ภาคผนวก ค2

ใบเสร็จขายของเก่า



เลขที่ใบเสร็จ: OVKN-WDGG-VYE1

วันที่: 4 ธันวาคม 2025

ลูกค้า: บริษัท ต้นบุญ จำกัด สาขาที่ 00002


ที่อยู่: 171 ถ. ห้วยแก้ว ต. สุเทพ อ. เมืองเชียงใหม่ จ. เชียงใหม่ 50200 Tax ID : 0 1055 52003 12 7

รายการสินค้า	น้ำหนัก (กก.)	ราคา (บาท/กก.)	ราคารวม (บาท)
กระดาดลึง	38.00		
กระดาดจับจั่ว	8.00		
กระป๋องเหล็ก	4.00		
กระป๋องอลูมิเนียม	2.00		
ขวด PET ไม่เกาะ	16.00		
พลาสติกขวดขุน	11.00		

ยอดรวม



กระดาษ 46.00 กิโลกรัม
260.98 kgCO2eq



พลาสติก 27.00 กิโลกรัม
27.84 kgCO2eq



อะลูมิเนียม 2.00 กิโลกรัม
18.25 kgCO2eq



เหล็ก 4.00 กิโลกรัม
7.33 kgCO2eq

bilนี้ลดคาร์บอนได้รวมทั้งหมด 314.40 kgCO2eq เทียบเท่าการปลูกต้นไม้ 20 ต้น (ภายใน 1 ปี)



ប្រាសាទបាវ

วันที่ 05/09/2025

[illegible]

รวมใจ

ตายในร้านค้า

៩/១១ ដើម
ដើម

เลขที่ใบเสร็จ: 8MGR-D1XD-H10G


วันที่: 7 ธันวาคม 2025

ลูกค้า: บริษัท ต้นบุญ จำกัด สาขา 00002

ที่อยู่: 171 ถ.ห้วยแก้ว ต.สุเทพ อ.เมืองเชียงใหม่ จ.เชียงใหม่ 50200 Tax ID: 0 1055 52003 12 7

รายการสินค้า	น้ำหนัก (กก.)	ราคา (บาท/กก.)	ราคารวม (บาท)
กระดาษลัง	25.00		
กระดาษจับจ้ว	12.00		
พลาสติกขุดขุ่น	9.00		
พลาสติกกรวม	2.00		
แก้วรวมสี่	6.00		
กระป๋องเหล็ก	1.00		
พลาสติกถุง/ฟิล์ม	2.00		
กระป๋องอลูมิเนียม	1.00		
ขวด PET ไม่แกะ	10.00		

ยอดรวม



กระดาษ 37.00 กิโลกรัม
209.92 kgCO₂eq



พลาสติก 23.00 กิโลกรัม
23.71 kgCO₂eq



อะลูมิเนียม 1.00 กิโลกรัม
9.13 kgCO₂eq



เหล็ก 1.00 กิโลกรัม
1.83 kgCO₂eq



แก้ว 6.00 กิโลกรัม
1.66 kgCO₂eq

ปริมาณคาร์บอนได้รวมทั้งหมด 246.25 kgCO₂eq เทียบเท่าการปลูกต้นไม้ 16 ต้น (ภายใน 1 ปี)


เลขที่ใบเสร็จ: Y003-WBHC-B10Z

วันที่: 13 กันยายน 2025

ลูกค้า: บริษัท ต้นบุญ จำกัด สาขา 00002

ที่อยู่: 171 ถ.ห้วยแก้ว ต.สุเทพ อ.เมืองเชียงใหม่ จ.เชียงใหม่ 50200 Tax ID: 0-1055-52003-12-7


รายการสินค้า	น้ำหนัก (กก.)	ราคา (บาท/กก.)	ราคารวม (บาท)
กระดาษลัง	13.00		
กระดาษจับจีว	2.00		
พลาสติกรวม	1.00		
พลาสติกขูดขุ่น	2.00		
แก้วรวมสี	4.00		
กระป๋องอลูมิเนียม	1.00		
พลาสติกถุง/ฟิล์ม	2.00		
ขวด PET ไม่แกะ	35.00		
			ยอดรวม



กระดาษ 15 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 85.1 kgCO₂eq
 พลาสติก 40 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 41.24 kgCO₂eq
 อะลูมิเนียม 1 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 9.13 kgCO₂eq
 แก้ว 4 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 1.1 kgCO₂eq
 มีผลลดการปล่อยก๊าซเรือนกระจก 136.57 กิโลกรัมคาร์บอนไดออกไซด์
 เทียบเท่ากับการปลูกต้นไม้ 9 ต้น (ใน 1 ปี)

เลขที่ใบเสร็จ: LAMR-SC3U-L4BG
วันที่: 4 กันยายน 2025
ลูกค้า: บริษัท ต้นบุญ จำกัด สาขาที่ 00002
ที่อยู่: 171 ถนนห้วยแก้ว อ.สุเทพ อ.เมืองเชียงใหม่ จ.เชียงใหม่ 50200 tax ID: 0-1055-52003-12-7

รายการสินค้า	น้ำหนัก (กก.)	ราคา (บาท/กก.)	ราคารวม (บาท)
กระดาษลัง	10.00		
ขวด PET ไม่แกะ	35.00		
พลาสติกถุง/ฟิล์ม	2.00		
แก้วรวมสี่	18.00		
กระป๋องอะลูมิเนียม	2.00		
พลาสติกขวดขุ่น	2.00		
พลาสติกทรวม	1.00		
กระดาษจันฉี	1.00		
ยอดรวม			



กระดาษ 11 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 62.41 kgCO2eq
พลาสติก 40 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 41.24 kgCO2eq
อะลูมิเนียม 2 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 18.25 kgCO2eq
แก้ว 18 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 4.97 kgCO2eq
มีผลลดการปล่อยก๊าซเรือนกระจก 126.87 กิโลกรัมคาร์บอนไดออกไซด์
เทียบเท่ากับการปลูกต้นไม้ 8 ต้น (ใน 1 ปี)

เลขที่ใบเสร็จ: CSY3-X7BU-DF07

วันที่: 9 กันยายน 2025

ลูกค้า: บริษัท ดินบุญ จำกัด สาขา 00002

ที่อยู่: 171 ถนนพหลโยธิน อ.เมืองเชียงใหม่ จ.เชียงใหม่ 50200 Tax ID: 0105552003127

รายการสินค้า	น้ำหนัก (กก.)	ราคา (บาท/กก.)	ราคารวม (บาท)
กระดาษลัง	26.00		
ลังเบียร์ช้าง	100		
พลาสติกขวดชุ่น	2.00		
แก้วรวมสี	2.00		
ขวด PET ไม่แกะ	30.00		
กระป๋องอะลูมิเนียม	150		
พลาสติกรวม	2.00		
ยอดรวม			



กระดาษ 26 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 147.51 kgCO2eq
พลาสติก 34 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 35.05 kgCO2eq
อะลูมิเนียม 15 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 13.69 kgCO2eq
แก้ว 3 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 0.83 kgCO2eq
มีผลลดการปล่อยก๊าซเรือนกระจก 197.08 กิโลกรัมคาร์บอนไดออกไซด์
เทียบเท่ากับการปลูกต้นไม้ 13 ต้น (ใน 1 ปี)

เลขที่ใบเสร็จ: FDD7-QUSB-FXFK

วันที่: 15 สิงหาคม 2025

ลูกค้า: บริษัท ต้นบุญ จำกัด สาขาที่ 00002

ที่อยู่: 171 ถ.ห้วยแก้ว ต.สุเทพ อ.เมืองเชียงใหม่ จ.เชียงใหม่ 50200 Tax ID: 0-1055-52003-12-7

รายการสินค้า	น้ำหนัก (กก.)	ราคา (บาท/กก.)	ราคารวม (บาท)
ขวด PET ไม่แกะ (หักถุง 4 กิโล)	51.00		
กระดาษลัง	30.40		
กระดาษจับจีว	2.00		
กระป๋องอะลูมิเนียม	220		
แก้วรวมสี่	8.00		
พลาสติกรวม	120		
พลาสติกขวดขุ่น	3.80		
พลาสติกถุง/ฟิล์ม	3.40		
พลาสติกโฟม PS	0.20		
		ยอดรวม	



กระดาษ 32.4 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 183.82 kgCO₂eq
 พลาสติก 59.6 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 61.45 kgCO₂eq
 อะลูมิเนียม 22 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 20.08 kgCO₂eq
 แก้ว 8 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 2.21 kgCO₂eq

มีผลลดการปล่อยก๊าซเรือนกระจก 267.56 กิโลกรัมคาร์บอนไดออกไซด์
 เทียบเท่ากับการปลูกต้นไม้ 17 ต้น (ใน 1 ปี)


เลขที่ใบเสร็จ: CRVF-PF7I-BOKR

วันที่: 22 สิงหาคม 2025

ลูกค้า: บริษัท ต้นบุญ จำกัด สาขา 00002

ที่อยู่: 171 ถนนพหลโยธิน อ.เมืองเชียงใหม่ จ.เชียงใหม่ 50200 tax ID: 0-1055-52003-12-7

รายการสินค้า	น้ำหนัก (กก.)	ราคา (บาท/กก.)	ราคารวม (บาท)
กระดาษลัง	13.00		
แก้วรวมสี่	8.00		
กระป๋องอะลูมิเนียม	3.00		
กระดาษจับจี้	1.00		
พลาสติกทรม	1.00		
พลาสติกขวดขุน	1.00		
พลาสติกถุง/ฟิล์ม	2.00		
ขวด PET ไม่แกะ	35.00		
		ยอดรวม	



กระดาษ 14 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 79.43 kgCO₂eq
 พลาสติก 39 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 40.21 kgCO₂eq
 อะลูมิเนียม 3 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 27.38 kgCO₂eq
 แก้ว 8 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 2.21 kgCO₂eq

มีผลลดการปล่อยก๊าซเรือนกระจก 149.23 กิโลกรัมคาร์บอนไดออกไซด์
 เทียบเท่ากับการปลูกต้นไม้ 9 ต้น (ใน 1 ปี)



วันที่ 05/09/2025

รวมไว้

៩/១១ ដើម
ដើម



ร้านค้า บริษัท อรุณ อินโนเวชั่น จำกัด

เลขที่ใบเสร็จ: TVOC-JZEC-2W70

วันที่: 26 กันยายน 2025

ลูกค้า: บริษัท ต้นบุญ จำกัด สาขา 00002

ที่อยู่: 171 ถ.หัวขี้เหล็ก ต.สุเทพ อ.เมืองเชียงใหม่ จ.เชียงใหม่ 50200 Tax ID: O-1055-52003-12-7

รายการสินค้า	น้ำหนัก (กก.)	ราคา (บาท/กก.)	ราคารวม (บาท)
กระดาษลัง	14.00		
พลาสติกขวดปูน	2.00		
แก้วรวมสี่	5.00		
กระป๋องอลูมิเนียม	1.50		
พลาสติกรวม	1.00		
พลาสติกถุง/ฟิล์ม	2.00		
ขวด PET ไม่เกาะ	29.00		
		ยอดรวม	



กระดาษ 14 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 79.43 kgCO₂eq
พลาสติก 34 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 35.05 kgCO₂eq
อะลูมิเนียม 1.5 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 13.69 kgCO₂eq
แก้ว 5 กิโลกรัม ลดการปล่อยก๊าซเรือนกระจก 1.38 kgCO₂eq
มิลนี้ลดการปล่อยก๊าซเรือนกระจก 129.55 กิโลกรัมคาร์บอนไดออกไซด์
เทียบเท่ากับการปลูกต้นไม้ 8 ต้น (ใน 1 ปี)

ภาคผนวก ค3
ใบเสร็จการสุบสิ่งปฏิกูล



ใบเสร็จรับเงิน/ใบกำกับภาษี

บริษัท เชียงใหม่กำจัดปฏิกูล จำกัด (สำนักงานใหญ่)

เลขที่ 336/3 ถนนเจริญประเทศ ตำบลช้างคลาน อำเภอเมืองเชียงใหม่ จังหวัดเชียงใหม่ 50100
โทร. 053-820409, 053-281533, 053-818446 แฟกซ์. 053-818446

เล่มที่ **115**

เลขประจำตัวเสียภาษี 050 5525000 291

เลขที่ **5716**

อัตราภาษี ☒ ร้อยละ 7% ☐ อัตราศูนย์

วันที่ **1** เดือน **สิงหาคม** พ.ศ. **2568**

นาม **บริษัท ต้นบว จำกัด**

ที่อยู่ 12

เลขประจำตัวเสียภาษี

☐ สำนักงานใหญ่ ☐ สำนักงานสาขา

ลำดับ ที่	รายการ	จำนวน	ราคาต่อหน่วย	จำนวนเงิน	
				บาท	สต.
1.	ค่ากำจัดปฏิกูล	1	1,800.00	1,800.00	
2.	ค่ากำจัดปฏิกูล (ไนเตร)	1	2,000.00	2,000.00	
รวมราคาทั้งสิ้น				3,800.00	
จำนวนภาษีมูลค่า					
จำนวนเงินรวม				3,800.00	

จำนวนเงินรวมทั้ง
(ตัวอักษร)

ใบเสร็จรับเงิน/ใบกำกับภาษี

บริษัท เชียงใหม่กำจัดปฏิกูล จำกัด (สำนักงานใหญ่)

เลขที่ 336/3 ถนนเจริญประเทศ ตำบลช้างคลาน อำเภอเมืองเชียงใหม่ จังหวัดเชียงใหม่ 50100

โทร. 053-820409, 053-281533, 053-818446 แฟกซ์, 053-818446

เล่มที่ **117**

เลขประจำตัวผู้เสียภาษี 050 5525000 291

เลขที่ **5834**

อัตราภาษี ☒ ร้อยละ 7% ☐ อัตราศูนย์

วันที่ 5 เดือน กันยายน พ.ศ. 2568

นาม บริษัท เชียงใหม่กำจัดปฏิกูล จำกัด

ที่อยู่ เลขที่ 336/3 ถนนเจริญประเทศ ตำบลช้างคลาน อำเภอเมืองเชียงใหม่ จังหวัดเชียงใหม่ 50100

เลขประจำตัวผู้เสียภาษี 050 5525000 291

☐ สำนักงานใหญ่ ☒ สำนักงานสาขาเลขที่ 00002

ลำดับ ที่	รายการ	จำนวน	ราคาต่อหน่วย	จำนวนเงิน	
				บาท	สต.
1.	ค่ากำจัดปฏิกูล	1	1,		-
2.	ค่ากำจัดปฏิกูล (ใหม่)	1	2,		-
รวมราคาทั้งสิ้น					-
จำนวนภาษีมูลค่าเพิ่ม					-
จำนวนเงินรวมทั้งสิ้น				3,852	-
จำนวนเงินรวมทั้งสิ้น (ตัวอักษร)					

ผู้รับเงิน

ใบเสร็จรับเงิน/ใบกำกับภาษี

บริษัท เชียงใหม่กำจัดปฏิกูล จำกัด (สำนักงานใหญ่)

เลขที่ 336/3 ถนนเจริญประเทศ ตำบลช้างคลาน อำเภอเมืองเชียงใหม่ จังหวัดเชียงใหม่ 50100

โทร. 053-820409, 053-281533, 053-818446 แฟกซ์, 053-818446

เล่มที่ **117**

เลขประจำตัวเสียภาษี 050 5525000 291

เลขที่ **5834**

อัตราภาษี ☒ ร้อยละ 7% ☐ อัตราศูนย์

วันที่ 5 เดือน กันยายน พ.ศ. 2568

นาม...บริษัท ต้นบว จำกัด

ที่อยู่...

เลขประจำตัว...

☐ สำนักงานใหญ่ ☐ สำนักงานสาขาเลขที่ 0002

ลำดับ ที่	รายการ	จำนวน	ราคาต่อหน่วย	จำนวนเงิน	
				บาท	สต.
1.	ค่ากำจัดปฏิกูล	1			-
2.	ค่ากำจัดปฏิกูล (ใหม่)	1			
รวมราคาทั้ง					-
จำนวนภาษี					-
จำนวนเงินรวมทั้งสิ้น				5,834	-

จำนวนเงินรวม
(ตัวอักษร)

ใบเสร็จรับเงิน/ใบกำกับภาษี

บริษัท เชียงใหม่กำจัดปฏิกูล จำกัด (สำนักงานใหญ่)

เลขที่ 336/3 ถนนเจริญประเทศ ตำบลช้างคลาน อำเภอเมืองเชียงใหม่ จังหวัดเชียงใหม่ 50100
โทร. 053-820409, 053-281533, 053-818446 แฟกซ์. 053-818446

เล่มที่ **122**

เลขประจำตัวผู้เสียภาษี 050 5525000 291

เลขที่ **6098**

อัตราภาษี ☒ ร้อยละ 7% ☐ อัตราศูนย์

วันที่ 28 เดือน พฤษภาคม พ.ศ. 2568

นาม.....

ที่อยู่ 17.....

50200

เลขประจำตัว.....

☐ สำนัก.....

ลำดับ ที่	รายการ	จำนวน	ราคาต่อหน่วย	จำนวนเงิน	
				บาท	สต.
1.	ค่ากำจัดปฏิกูล	1	1		
2.	ค่ากำจัดปฏิกูล (โพรง)	1	2		
รวมราคาทั้งสิ้น					
จำนวนภาษีมูลค่าเพิ่ม					
จำนวนเงินรวมทั้งสิ้น				5,000	

จำนวนเงินรวมทั้งสิ้น

ลงชื่อ.....

ผู้รับเงิน

ใบเสร็จรับเงิน/ใบกำกับภาษี

บริษัท เชียงใหม่กำจัดปฏิกูล จำกัด (สำนักงานใหญ่)

เลขที่ 336/3 ถนนเจริญประเทศ ตำบลช้างคลาน อำเภอเมืองเชียงใหม่ จังหวัดเชียงใหม่ 50100
โทร. 053-820409, 053-281533, 053-818446 แฟกซ์. 053-818446

เล่มที่ **122**

เลขประจำตัวผู้เสียภาษี 050 5525000 291

เลขที่ **6098**

อัตราภาษี ☒ ร้อยละ 7% ☐ อัตราศูนย์

วันที่ 28 เดือน พฤษภาคม พ.ศ. 2568

นาม บริษัท

ที่อยู่ 171 200

เลขประจำตัว

☐ สำนักงาน

ลำดับ ที่	รายการ	จำนวน	ราคาต่อหน่วย	จำนวนเงิน	
				บาท	สต.
1.	ค่ากำจัดปฏิกูล	1	1		
2.	ค่ากำจัดปฏิกูล (โพรง)	1	2		
รวมราคาทั้งสิ้น					
จำนวนภาษีมูลค่าเพิ่ม					
จำนวนเงินรวม					

จำนวนเงินรวมทั้งสิ้น (ตัวอักษร)

ใบเสร็จรับเงิน/ใบกำกับภาษี

บริษัท เชียงใหม่กำจัดปฏิกูล จำกัด (สำนักงานใหญ่)

เลขที่ 336/3 ถนนเจริญประเทศ ตำบลช้างคลาน อำเภอเมืองเชียงใหม่ จังหวัดเชียงใหม่ 50100

โทร. 053-820409, 053-281533, 053-818446 แฟกซ์. 053-818446

เล่มที่ 127

เลขประจำตัวผู้เสียภาษี 050 5525000 291

เลขที่ 6318

อัตราภาษี ☒ ร้อยละ 7% ☐ อัตราศูนย์

วันที่.....เดือน.....ปี พ.ศ. 2568

นาย.....
ที่.....
เลข.....

☐ สำนักงานใหญ่ ☒ สำนักงานสาขาเลขที่ 00002

ลำดับ ที่	รายการ	จำนวน	ราคาต่อหน่วย	จำนวนเงิน	
				บาท	สต.
1.	ค่ากำจัดปฏิกูล	1			-
2.	ค่ากำจัดปฏิกูล (ใหม่)	1			-
รวมราคาทั้งสิ้น					-
จำนวนภาษี					-
จำนวนเงินรวม					-
จำนวนเงินรวม (ตัวอักษร)					

จำนวนเงินรวม (ตัวอักษร)

ผู้รับเงิน

ภาคผนวก ค4

เอกสารตรวจสอบถังดับเพลิง Extinguisher





EHCM FIRE EXTINGUISHERS INSPECTION

Month: July 2025

Items	Floor	Code	Location	Fire Extinguisher Type								Operable	Sealed	Checking Date	Remark
				DRY	Weight	CO2	Weight	WET	Weight	FOAM	Weight	Non-CFC	Weight		
1	B	B01-14	FHC-B-01 (Car Park B-2)	✓	10 lb									02/07/2025	
2		B02-14	FHC-B-02 (Front of Fire Staircase ST1)	✓	10 lb									02/07/2025	
3		B03-14	FHC-B-03 (Car Park B-1)	✓	10 lb									02/07/2025	
4		B04-14	FHC-B-04 (Front of Fire Staircase ST2)	✓	10 lb									02/07/2025	
5		B05-14	FHC-B-05 (Front of lift Service S1)	✓	10 lb									02/07/2025	
6		B07-14	Car Park 1	✓	10 lb									02/07/2025	
7		B08-14	Car Park 2	✓	10 lb									02/07/2025	
8		B09-14	Car Park 3	✓	10 lb									02/07/2025	
9		B10-14	Car Park 4	✓	10 lb									02/07/2025	
10		B11-14	Car Park 5	✓	10 lb									02/07/2025	หน้าปัดมีสีเขียว
11		B12-14	Car Park 6	✓	10 lb									02/07/2025	Refilled on March 21
12		B13-14	Canteen	✓		✓	10 lb							02/07/2025	13.25 kg.
13		B14-14	AC Office	✓	10 lb									02/07/2025	
14		B15-14	HR office	✓	10 lb									02/07/2025	
15		B16-14	Fire Fighting Cabinet	✓		✓	10 lb							02/07/2025	13.18 kg.
16	G	G01-14	FHC-G-01 (Front of Fire Staircase ST1)	✓	10 lb									02/07/2025	
17		G02-14	FHC-G-02 (Front of Lift Service S1)	✓	10 lb									02/07/2025	
18		G03-14	FHC-G-03 (Front of Fire Staircase ST2)	✓	10 lb									02/07/2025	หน้าปัดมีสีเขียว
19		G04-14	Main Entrance G floor	✓	10 lb									02/07/2025	
20		G05-14	Front of Luggage Room	✓	10 lb									02/07/2025	
21		G06-14	Car Park G floor	✓	10 lb									02/07/2025	
22		G07-14	Gas Station	✓	10 lb									02/07/2025	
23		G08-14	Gas Station	✓		✓	10 lb							02/07/2025	13.45 kg
24		G09-14	Control Room 1	✓	10 lb									02/07/2025	หน้าปัดมีสีเขียว
25		G10-14	Control Room 2	✓	10 lb									02/07/2025	
26	1	101-14	FHC-1-01 (Front of Fire Staircase ST1)	✓	10 lb									02/07/2025	
27		102-14	FHC-1-02 (Front of Lift Service S1)	✓	10 lb									02/07/2025	หน้าปัดมีสีเขียว
28		103 -02/11/23	Reservation Officer	✓	10 lb									02/07/2025	
29		104-14	FHC-1-03 (Front of Fire Staircase ST2)	✓	10 lb									02/07/2025	
30		105-14	Administrative Office	✓		✓	10 lb							02/07/2025	13.15 kg.
31		106-14	Kitchen (Entrance)	✓						✓	10 lb			02/07/2025	over
32		107-14	Kitchen (Entrance)	✓								✓	10 lb	02/07/2025	
33		108-14	Kitchen (Front of Dry Store)	✓		✓	10 lb							02/07/2025	11.54 kg.
34		109-14	Kitchen (Stove)	✓						✓	10 lb			02/07/2025	Transfer from UNCM
35		201-14	FHC-2-01 (Front of Fire Staircase ST1)	✓	10 lb									02/07/2025	Refilled on October 21
36	2	202-14	FHC-2-02 (Front of Lift Service S1)	✓	10 lb									02/07/2025	
37		203-14	FHC-2-03 (Front of Fire Staircase ST2)	✓	10 lb									02/07/2025	หน้าปัดมีสีเขียว
38		204-14	Generator Room	✓	10 lb									02/07/2025	
39		205-14	Generator Room	✓		✓	10 lb							02/07/2025	9.72 kg.
40		206-14	MDB Room	✓	10 lb									02/07/2025	
41		207-14	MDB Room	✓		✓	10 lb							02/07/2025	11.87 kg.
42		302-14	FHC-3-01 (Front of Fire Staircase ST1)	✓	10 lb									01/07/2025	
43	3	303-14	FHC-3-02 (Front of Lift Service S1)	✓	10 lb									01/07/2025	
44		304-14	FHC-3-03 (Front of Fire Staircase ST2)	✓	10 lb									01/07/2025	
45		401-14	FHC-4-01 (Front of Fire Staircase ST1)	✓	10 lb									01/07/2025	
46	4	402-14	FHC-4-02 (Front of Lift Service S1)	✓	10 lb									01/07/2025	
47		403-14	FHC-4-03 (Front of Fire Staircase ST2)	✓	10 lb									01/07/2025	หน้าปัดมีสีเขียว
48		501-14	FHC-5-01 (Front of Fire Staircase ST1)	✓	10 lb									01/07/2025	
49	5	502-14	FHC-5-02 (Front of Lift Service S1)	✓	10 lb									01/07/2025	หน้าปัดมีสีเขียว
50		503-14	FHC-5-03 (Front of Fire Staircase ST2)	✓	10 lb									01/07/2025	
51		601-14	FHC-6-01 (Front of Fire Staircase ST1)	✓	10 lb									01/07/2025	
52	6	602-14	FHC-6-02 (Front of Lift Service S1)	✓	10 lb									01/07/2025	หน้าปัดมีสีเขียว
53		603-14	FHC-6-03 (Front of Fire Staircase ST2)	✓	10 lb									01/07/2025	
54		701-14	FHC-7-01 (Front of Fire Staircase ST1)	✓	10 lb									01/07/2025	
55	7	702-14	FHC-7-02 (Front of Lift Service S1)	✓	10 lb									01/07/2025	
56		703-14	FHC-7-03 (Front of Fire Staircase ST2)	✓	10 lb									01/07/2025	หน้าปัดมีสีเขียว
57		801-14	FHC-8-01 (Front of Fire Staircase ST1)	✓	10 lb									01/07/2025	
58	8	802-14	FHC-8-02 (Front of Lift Service S1)	✓	10 lb									01/07/2025	
59		803-14	FHC-8-03 (Front of Fire Staircase ST2)	✓	10 lb									01/07/2025	
60		901-14	FHC-9-01 (Front of Fire Staircase ST1)	✓	10 lb									01/07/2025	
61	9	902-14	FHC-9-02 (Front of Lift Service S1)	✓	10 lb									01/07/2025	
62		903-14	FHC-9-03 (Front of Fire Staircase ST2)	✓	10 lb									01/07/2025	
63	10	1001-14	FHC-R-01 (Roof Top)	✓	10 lb									01/07/2025	
Grand Total				52		7		0		2		1			

Remark:

Yes = ✓ No = X

Check By: Mr.Pratchayarat Thongdee

(Security Officer)

Date: 02 July 2025

Review by: Mr. Prasit Inta

(Security Supervisor)

Date: 06 July 2025



EHCM FIRE EXTINGUISHERS INSPECTION

Month: August 2025

Items	Floor	Code	Location	Fire Extinguisher Type								Operable	Sealed	Checking Date	Remark
				DRY	Weight	CO2	Weight	WET	Weight	FOAM	Weight	Non-CFC	Weight		
1	B	B01-14	FHC-B-01 (Car Park B-2)	✓	10 lb									03/08/2025	
2		B02-14	FHC-B-02 (Front of Fire Staircase ST1)	✓	10 lb									03/08/2025	
3		B03-14	FHC-B-03 (Car Park B-1)	✓	10 lb									03/08/2025	
4		B04-14	FHC-B-04 (Front of Fire Staircase ST2)	✓	10 lb									03/08/2025	
5		B05-14	FHC-B-05 (Front of lift Service S1)	✓	10 lb									03/08/2025	
6		B07-14	Car Park 1	✓	10 lb									03/08/2025	
7		B08-14	Car Park 2	✓	10 lb									03/08/2025	
8		B09-14	Car Park 3	✓	10 lb									03/08/2025	
9		B10-14	Car Park 4	✓	10 lb									03/08/2025	
10		B11-14	Car Park 5	✓	10 lb									03/08/2025	หน้าปัดมีสีขึ้น
11		B12-14	Car Park 6	✓	10 lb									03/08/2025	Refilled on March 21
12		B13-14	Canteen	✓		✓	10 lb							03/08/2025	
13		B14-14	AC Office	✓	10 lb									03/08/2025	
14		B15-14	HR office	✓	10 lb									03/08/2025	
15		B16-14	Fire Fighting Cabinet	✓		✓	10 lb							03/08/2025	13.18 kg.
16	G	G01-14	FHC-G-01 (Front of Fire Staircase ST1)	✓	10 lb									03/08/2025	
17		G02-14	FHC-G-02 (Front of Lift Service S1)	✓	10 lb									03/08/2025	
18		G03-14	FHC-G-03 (Front of Fire Staircase ST2)	✓	10 lb									03/08/2025	หน้าปัดมีสีขึ้น
19		G04-14	Main Entrance G floor	✓	10 lb									03/08/2025	
20		G05-14	Front of Luggage Room	✓	10 lb									03/08/2025	
21		G06-14	Car Park G floor	✓	10 lb									03/08/2025	
22		G07-14	Gas Station	✓	10 lb									03/08/2025	
23		G08-14	Gas Station	✓		✓	10 lb							03/08/2025	13.45 kg
24		G09-14	Control Room 1	✓	10 lb									03/08/2025	หน้าปัดมีสีขึ้น
25		G10-14	Control Room 2	✓	10 lb									03/08/2025	
26	1	101-14	FHC-1-01 (Front of Fire Staircase ST1)	✓	10 lb									03/08/2025	
27		102-14	FHC-1-02 (Front of Lift Service S1)	✓	10 lb									03/08/2025	หน้าปัดมีสีขึ้น
28		103-02/11/23	Reservation Officer	✓	10 lb									03/08/2025	
29		104-14	FHC-1-03 (Front of Fire Staircase ST2)	✓	10 lb									03/08/2025	
30		105-14	Administrative Office	✓		✓	10 lb							03/08/2025	13.15 kg.
31		106-14	Kitchen (Entrance)	✓						✓	10 lb			03/08/2025	
32		107-14	Kitchen (Entrance)	✓								✓	10 lb	03/08/2025	
33		108-14	Kitchen (Front of Dry Store)	✓		✓	10 lb							03/08/2025	11.54 kg.
34		109-14	Kitchen (Stove)	✓						✓	10 lb			03/08/2025	Transfer from UNCM
35		201-14	FHC-2-01 (Front of Fire Staircase ST1)	✓	10 lb									03/08/2025	Refilled on October 21
36	2	202-14	FHC-2-02 (Front of Lift Service S1)	✓	10 lb									03/08/2025	
37		203-14	FHC-2-03 (Front of Fire Staircase ST2)	✓	10 lb									03/08/2025	หน้าปัดมีสีขึ้น
38		204-14	Generator Room	✓	10 lb									03/08/2025	
39		205-14	Generator Room	✓		✓	10 lb							03/08/2025	9.72 kg.
40		206-14	MDB Room	✓	10 lb									03/08/2025	
41		207-14	MDB Room	✓		✓	10 lb							03/08/2025	11.87 kg.
42	3	302-14	FHC-3-01 (Front of Fire Staircase ST1)	✓	10 lb									02/08/2025	
43		303-14	FHC-3-02 (Front of Lift Service S1)	✓	10 lb									02/08/2025	
44		304-14	FHC-3-03 (Front of Fire Staircase ST2)	✓	10 lb									02/08/2025	
45	4	401-14	FHC-4-01 (Front of Fire Staircase ST1)	✓	10 lb									02/08/2025	
46		402-14	FHC-4-02 (Front of Lift Service S1)	✓	10 lb									02/08/2025	
47		403-14	FHC-4-03 (Front of Fire Staircase ST2)	✓	10 lb									02/08/2025	หน้าปัดมีสีขึ้น
48	5	501-14	FHC-5-01 (Front of Fire Staircase ST1)	✓	10 lb									02/08/2025	
49		502-14	FHC-5-02 (Front of Lift Service S1)	✓	10 lb									02/08/2025	หน้าปัดมีสีขึ้น
50		503-14	FHC-5-03 (Front of Fire Staircase ST2)	✓	10 lb									02/08/2025	
51	6	601-14	FHC-6-01 (Front of Fire Staircase ST1)	✓	10 lb									02/08/2025	
52		602-14	FHC-6-02 (Front of Lift Service S1)	✓	10 lb									02/08/2025	หน้าปัดมีสีขึ้น
53		603-14	FHC-6-03 (Front of Fire Staircase ST2)	✓	10 lb									02/08/2025	
54	7	701-14	FHC-7-01 (Front of Fire Staircase ST1)	✓	10 lb									02/08/2025	
55		702-14	FHC-7-02 (Front of Lift Service S1)	✓	10 lb									02/08/2025	
56		703-14	FHC-7-03 (Front of Fire Staircase ST2)	✓	10 lb									02/08/2025	หน้าปัดมีสีขึ้น
57	8	801-14	FHC-8-01 (Front of Fire Staircase ST1)	✓	10 lb									02/08/2025	
58		802-14	FHC-8-02 (Front of Lift Service S1)	✓	10 lb									02/08/2025	
59		803-14	FHC-8-03 (Front of Fire Staircase ST2)	✓	10 lb									02/08/2025	
60	9	901-14	FHC-9-01 (Front of Fire Staircase ST1)	✓	10 lb									02/08/2025	
61		902-14	FHC-9-02 (Front of Lift Service S1)	✓	10 lb									02/08/2025	
62		903-14	FHC-9-03 (Front of Fire Staircase ST2)	✓	10 lb									02/08/2025	
63	10	1001-14	FHC-R-01 (Roof Top)	✓	10 lb									02/08/2025	
Grand Total				52		7		0		2		1			

Remark:

Yes = ✓ No = X

Check By: Mr.Pratchayarat Thongdee

(Security Officer)

Date: 02 August 2025

Review by: Mr. Prasit Inta

(Security Supervisor)

Date: 06 August 2025



EHCM FIRE EXTINGUISHERS INSPECTION

Month: September 2025

Items	Floor	Code	Location	Fire Extinguisher Type								Operable	Sealed	Checking Date	Remark
				DRY	Weight	CO2	Weight	WET	Weight	FOAM	Weight	Non-CFC	Weight		
1	B	B01-14	FHC-B-01 (Car Park B-2)	✓	10 lb									02/09/2025	
2		B02-14	FHC-B-02 (Front of Fire Staircase ST1)	✓	10 lb									02/09/2025	
3		B03-14	FHC-B-03 (Car Park B-1)	✓	10 lb									02/09/2025	
4		B04-14	FHC-B-04 (Front of Fire Staircase ST2)	✓	10 lb									02/09/2025	
5		B05-14	FHC-B-05 (Front of lift Service S1)	✓	10 lb									02/09/2025	
6		B07-14	Car Park 1	✓	10 lb									02/09/2025	
7		B08-14	Car Park 2	✓	10 lb									02/09/2025	
8		B09-14	Car Park 3	✓	10 lb									02/09/2025	
9		B10-14	Car Park 4	✓	10 lb									02/09/2025	
10		B11-14	Car Park 5	✓	10 lb									02/09/2025	หน้าปัดมีสีเขียว
11		B12-14	Car Park 6	✓	10 lb									02/09/2025	Refilled on March 21
12		B13-14	Canteen	✓		✓	10 lb							02/09/2025	13.25 kg.
13		B14-14	AC Office	✓	10 lb									02/09/2025	
14		B15-14	HR office	✓	10 lb									02/09/2025	
15		B16-14	Fire Fighting Cabinet	✓		✓	10 lb							02/09/2025	13.18 kg.
16	G	G01-14	FHC-G-01 (Front of Fire Staircase ST1)	✓	10 lb									02/09/2025	
17		G02-14	FHC-G-02 (Front of Lift Service S1)	✓	10 lb									02/09/2025	
18		G03-14	FHC-G-03 (Front of Fire Staircase ST2)	✓	10 lb									02/09/2025	หน้าปัดมีสีเขียว
19		G04-14	Main Entrance G floor	✓	10 lb									02/09/2025	
20		G05-14	Front of Luggage Room	✓	10 lb									02/09/2025	
21		G06-14	Car Park G floor	✓	10 lb									02/09/2025	
22		G07-14	Gas Station	✓	10 lb									02/09/2025	
23		G08-14	Gas Station	✓		✓	10 lb							02/09/2025	13.45 kg
24		G09-14	Control Room 1	✓	10 lb									02/09/2025	หน้าปัดมีสีเขียว
25		G10-14	Control Room 2	✓	10 lb									02/09/2025	
26	1	101-14	FHC-1-01 (Front of Fire Staircase ST1)	✓	10 lb									02/09/2025	
27		102-14	FHC-1-02 (Front of Lift Service S1)	✓	10 lb									02/09/2025	หน้าปัดมีสีเขียว
28		103 -02/11/23	Reservation Officer	✓	10 lb									02/09/2025	
29		104-14	FHC-1-03 (Front of Fire Staircase ST2)	✓	10 lb									02/09/2025	
30		105-14	Administrative Office	✓		✓	10 lb							02/09/2025	13.15 kg.
31		106-14	Kitchen (Entrance)	✓						✓	10 lb			02/09/2025	
32		107-14	Kitchen (Entrance)	✓								✓	10 lb	02/09/2025	
33		108-14	Kitchen (Front of Dry Store)	✓		✓	10 lb							02/09/2025	11.54 kg.
34		109-14	Kitchen (Stove)	✓						✓	10 lb			02/09/2025	Transfer from UNCM
35		201-14	FHC-2-01 (Front of Fire Staircase ST1)	✓	10 lb									02/09/2025	Refilled on October 21
36	2	202-14	FHC-2-02 (Front of Lift Service S1)	✓	10 lb									02/09/2025	
37		203-14	FHC-2-03 (Front of Fire Staircase ST2)	✓	10 lb									02/09/2025	หน้าปัดมีสีเขียว
38		204-14	Generator Room	✓	10 lb									02/09/2025	
39		205-14	Generator Room	✓		✓	10 lb							02/09/2025	9.72 kg.
40		206-14	MDB Room	✓	10 lb									02/09/2025	
41		207-14	MDB Room	✓		✓	10 lb							02/09/2025	11.87 kg.
42	3	302-14	FHC-3-01 (Front of Fire Staircase ST1)	✓	10 lb									03/09/2025	
43		303-14	FHC-3-02 (Front of Lift Service S1)	✓	10 lb									03/09/2025	
44		304-14	FHC-3-03 (Front of Fire Staircase ST2)	✓	10 lb									03/09/2025	
45	4	401-14	FHC-4-01 (Front of Fire Staircase ST1)	✓	10 lb									03/09/2025	
46		402-14	FHC-4-02 (Front of Lift Service S1)	✓	10 lb									03/09/2025	
47		403-14	FHC-4-03 (Front of Fire Staircase ST2)	✓	10 lb									03/09/2025	หน้าปัดมีสีเขียว
48	5	501-14	FHC-5-01 (Front of Fire Staircase ST1)	✓	10 lb									02/09/2025	
49		502-14	FHC-5-02 (Front of Lift Service S1)	✓	10 lb									02/09/2025	หน้าปัดมีสีเขียว
50		503-14	FHC-5-03 (Front of Fire Staircase ST2)	✓	10 lb									02/09/2025	
51	6	601-14	FHC-6-01 (Front of Fire Staircase ST1)	✓	10 lb									02/09/2025	
52		602-14	FHC-6-02 (Front of Lift Service S1)	✓	10 lb									02/09/2025	หน้าปัดมีสีเขียว
53		603-14	FHC-6-03 (Front of Fire Staircase ST2)	✓	10 lb									02/09/2025	
54	7	701-14	FHC-7-01 (Front of Fire Staircase ST1)	✓	10 lb									02/09/2025	
55		702-14	FHC-7-02 (Front of Lift Service S1)	✓	10 lb									02/09/2025	
56		703-14	FHC-7-03 (Front of Fire Staircase ST2)	✓	10 lb									02/09/2025	หน้าปัดมีสีเขียว
57	8	801-14	FHC-8-01 (Front of Fire Staircase ST1)	✓	10 lb									02/09/2025	
58		802-14	FHC-8-02 (Front of Lift Service S1)	✓	10 lb									02/09/2025	
59		803-14	FHC-8-03 (Front of Fire Staircase ST2)	✓	10 lb									02/09/2025	
60	9	901-14	FHC-9-01 (Front of Fire Staircase ST1)	✓	10 lb									02/09/2025	
61		902-14	FHC-9-02 (Front of Lift Service S1)	✓	10 lb									02/09/2025	
62		903-14	FHC-9-03 (Front of Fire Staircase ST2)	✓	10 lb									02/09/2025	
63	10	1001-14	FHC-R-01 (Roof Top)	✓	10 lb									02/09/2025	
Grand Total				52		7		0		2		1			

Remark:

Yes = ✓ No = X

Check By: Mr.Banbhot Sunyaphap

(Security Officer)

Date: 02 September 2025

Review by: Mr. Prasit Inta

(Security Supervisor)

Date: 05 September 2025



EHCM FIRE EXTINGUISHERS INSPECTION

Month: November 2025

Items	Floor	Code	Location	Fire Extinguisher Type								Operable	Sealed	Checking Date	Remark
				DRY	Weight	CO2	Weight	WET	Weight	FOAM	Weight	Non-CFC	Weight		
1	B	B01-14	FHC-B-01 (Car Park B-2)	✓	10 lb									03/11/2025	
2		B02-14	FHC-B-02 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
3		B03-14	FHC-B-03 (Car Park B-1)	✓	10 lb									03/11/2025	
4		B04-14	FHC-B-04 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	
5		B05-14	FHC-B-05 (Front of lift Service S1)	✓	10 lb									03/11/2025	
6		B07-14	Car Park 1	✓	10 lb									03/11/2025	
7		B08-14	Car Park 2	✓	10 lb									03/11/2025	
8		B09-14	Car Park 3	✓	10 lb									03/11/2025	
9		B10-14	Car Park 4	✓	10 lb									03/11/2025	
10		B11-14	Car Park 5	✓	10 lb									03/11/2025	หน้าปัดมีค่าขึ้น
11		B12-14	Car Park 6	✓	10 lb									03/11/2025	Refilled on March 21
12		B13-14	Canteen	✓		✓	10 lb							03/11/2025	13.25 kg.
13		B14-14	AC Office	✓	10 lb									03/11/2025	
14		B15-14	HR office	✓	10 lb									03/11/2025	
15		B16-14	Fire Fighting Cabinet	✓		✓	10 lb							03/11/2025	13.18 kg.
16	G	G01-14	FHC-G-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
17		G02-14	FHC-G-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	
18		G03-14	FHC-G-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	หน้าปัดมีค่าขึ้น
19		G04-14	Main Entrance G floor	✓	10 lb									03/11/2025	
20		G05-14	Front of Luggage Room	✓	10 lb									03/11/2025	
21		G06-14	Car Park G floor	✓	10 lb									03/11/2025	
22		G07-14	Gas Station	✓	10 lb									03/11/2025	
23		G08-14	Gas Station	✓		✓	10 lb							03/11/2025	13.45 kg
24		G09-14	Control Room 1	✓	10 lb									03/11/2025	หน้าปัดมีค่าขึ้น
25		101-14	FHC-1-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
26	1	102-14	FHC-1-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	หน้าปัดมีค่าขึ้น
27		103 -02/11/23	Reservation Officer	✓	10 lb									03/11/2025	
28		104-14	FHC-1-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	
29		105-14	Administrative Office	✓		✓	10 lb							03/11/2025	13.15 kg.
30		106-14	Kitchen (Entrance)							✓	10 lb			03/11/2025	
31		107-14	Kitchen (Entrance)									✓	10 lb	03/11/2025	
32		108-14	Kitchen (Front of Dry Store)			✓	10 lb							03/11/2025	11.54 kg.
33		109-14	Kitchen (Stove)							✓	10 lb			03/11/2025	Transfer from UNCM
34	2	201-14	FHC-2-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	Refilled on October 21
35		202-14	FHC-2-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	
36		203-14	FHC-2-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	หน้าปัดมีค่าขึ้น
37		204-14	Generator Room	✓	10 lb									03/11/2025	
38		205-14	Generator Room	✓		✓	10 lb							03/11/2025	9.72 kg.
39		206-14	MDB Room	✓	10 lb									03/11/2025	
40		207-14	MDB Room	✓		✓	10 lb							03/11/2025	11.87 kg.
41	3	302-14	FHC-3-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
42		303-14	FHC-3-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	
43		304-14	FHC-3-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	
44	4	401-14	FHC-4-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
45		402-14	FHC-4-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	
46		403-14	FHC-4-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	หน้าปัดมีค่าขึ้น
47	5	501-14	FHC-5-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
48		502-14	FHC-5-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	หน้าปัดมีค่าขึ้น
49		503-14	FHC-5-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	
50	6	601-14	FHC-6-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
51		602-14	FHC-6-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	หน้าปัดมีค่าขึ้น
52		603-14	FHC-6-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	
53	7	701-14	FHC-7-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
54		702-14	FHC-7-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	
55		703-14	FHC-7-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	หน้าปัดมีค่าขึ้น
56	8	801-14	FHC-8-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
57		802-14	FHC-8-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	
58		803-14	FHC-8-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	
59	9	901-14	FHC-9-01 (Front of Fire Staircase ST1)	✓	10 lb									03/11/2025	
60		902-14	FHC-9-02 (Front of Lift Service S1)	✓	10 lb									03/11/2025	
61		903-14	FHC-9-03 (Front of Fire Staircase ST2)	✓	10 lb									03/11/2025	
62	10	1001-14	FHC-R-01 (Roof Top)	✓	10 lb									03/11/2025	
Grand Total				52		7		0		2		1			

Remark:

Yes = ✓ No = X

Check By: Mr.Prasit Inta

(Security Supervisor)

Date: 03 November 2025

Review by: Mr. Prasit Inta

(Security Supervisor)

Date: 03 November 2025



EHCM FIRE EXTINGUISHERS INSPECTION

Month: October 2025

Items	Floor	Code	Location	Fire Extinguisher Type								Operable	Sealed	Checking Date	Remark
				DRY	Weight	CO2	Weight	WET	Weight	FOAM	Weight	Non-CFC	Weight		
1	B	B01-14	FHC-B-01 (Car Park B-2)	✓	10 lb									01/10/2025	
2		B02-14	FHC-B-02 (Front of Fire Staircase ST1)	✓	10 lb									01/10/2025	
3		B03-14	FHC-B-03 (Car Park B-1)	✓	10 lb									01/10/2025	
4		B04-14	FHC-B-04 (Front of Fire Staircase ST2)	✓	10 lb									01/10/2025	
5		B05-14	FHC-B-05 (Front of Lift Service S1)	✓	10 lb									01/10/2025	
6		B07-14	Car Park 1	✓	10 lb									01/10/2025	
7		B08-14	Car Park 2	✓	10 lb									01/10/2025	
8		B09-14	Car Park 3	✓	10 lb									01/10/2025	
9		B10-14	Car Park 4	✓	10 lb									01/10/2025	
10		B11-14	Car Park 5	✓	10 lb									01/10/2025	หน้าปัดมีค่าขึ้น
11		B12-14	Car Park 6	✓	10 lb									01/10/2025	Refilled on March 21
12		B13-14	Canteen	✓		✓	10 lb							01/10/2025	13.25 kg.
13		B14-14	AC Office	✓	10 lb									01/10/2025	
14		B15-14	HR office	✓	10 lb									01/10/2025	
15		B16-14	Fire Fighting Cabinet	✓		✓	10 lb							01/10/2025	13.18 kg.
16	G	G01-14	FHC-G-01 (Front of Fire Staircase ST1)	✓	10 lb									01/10/2025	
17		G02-14	FHC-G-02 (Front of Lift Service S1)	✓	10 lb									01/10/2025	
18		G03-14	FHC-G-03 (Front of Fire Staircase ST2)	✓	10 lb									01/10/2025	หน้าปัดมีค่าขึ้น
19		G04-14	Main Entrance G floor	✓	10 lb									01/10/2025	
20		G05-14	Front of Luggage Room	✓	10 lb									01/10/2025	
21		G06-14	Car Park G floor	✓	10 lb									01/10/2025	
22		G07-14	Gas Station	✓	10 lb									01/10/2025	
23		G08-14	Gas Station	✓		✓	10 lb							01/10/2025	13.45 kg
24		G09-14	Control Room 1	✓	10 lb									01/10/2025	หน้าปัดมีค่าขึ้น
25		G10-14	Control Room 2	✓	10 lb									01/10/2025	
26	1	101-14	FHC-1-01 (Front of Fire Staircase ST1)	✓	10 lb									02/10/2025	
27		102-14	FHC-1-02 (Front of Lift Service S1)	✓	10 lb									02/10/2025	หน้าปัดมีค่าขึ้น
28		103 -02/11/23	Reservation Officer	✓	10 lb									02/10/2025	
29		104-14	FHC-1-03 (Front of Fire Staircase ST2)	✓	10 lb									02/10/2025	
30		105-14	Administrative Office	✓		✓	10 lb							02/10/2025	13.15 kg.
31		106-14	Kitchen (Entrance)	✓						✓	10 lb			02/10/2025	
32		107-14	Kitchen (Entrance)	✓								✓	10 lb	02/10/2025	
33		108-14	Kitchen (Front of Dry Store)	✓		✓	10 lb							02/10/2025	11.54 kg.
34		109-14	Kitchen (Stove)	✓						✓	10 lb			02/10/2025	Transfer from UNCM
35		201-14	FHC-2-01 (Front of Fire Staircase ST1)	✓	10 lb									02/10/2025	Refilled on October 21
36	2	202-14	FHC-2-02 (Front of Lift Service S1)	✓	10 lb									02/10/2025	
37		203-14	FHC-2-03 (Front of Fire Staircase ST2)	✓	10 lb									02/10/2025	หน้าปัดมีค่าขึ้น
38		204-14	Generator Room	✓	10 lb									02/10/2025	
39		205-14	Generator Room	✓		✓	10 lb							02/10/2025	9.72 kg.
40		206-14	MDB Room	✓	10 lb									02/10/2025	
41		207-14	MDB Room	✓		✓	10 lb							02/10/2025	11.87 kg.
42		302-14	FHC-3-01 (Front of Fire Staircase ST1)	✓	10 lb									02/10/2025	
43	3	303-14	FHC-3-02 (Front of Lift Service S1)	✓	10 lb									02/10/2025	
44		304-14	FHC-3-03 (Front of Fire Staircase ST2)	✓	10 lb									02/10/2025	
45		401-14	FHC-4-01 (Front of Fire Staircase ST1)	✓	10 lb									02/10/2025	
46	4	402-14	FHC-4-02 (Front of Lift Service S1)	✓	10 lb									02/10/2025	
47		403-14	FHC-4-03 (Front of Fire Staircase ST2)	✓	10 lb									02/10/2025	หน้าปัดมีค่าขึ้น
48		501-14	FHC-5-01 (Front of Fire Staircase ST1)	✓	10 lb									01/10/2025	
49	5	502-14	FHC-5-02 (Front of Lift Service S1)	✓	10 lb									01/10/2025	หน้าปัดมีค่าขึ้น
50		503-14	FHC-5-03 (Front of Fire Staircase ST2)	✓	10 lb									01/10/2025	
51		601-14	FHC-6-01 (Front of Fire Staircase ST1)	✓	10 lb									01/10/2025	
52	6	602-14	FHC-6-02 (Front of Lift Service S1)	✓	10 lb									01/10/2025	หน้าปัดมีค่าขึ้น
53		603-14	FHC-6-03 (Front of Fire Staircase ST2)	✓	10 lb									01/10/2025	
54		701-14	FHC-7-01 (Front of Fire Staircase ST1)	✓	10 lb									01/10/2025	
55	7	702-14	FHC-7-02 (Front of Lift Service S1)	✓	10 lb									01/10/2025	
56		703-14	FHC-7-03 (Front of Fire Staircase ST2)	✓	10 lb									01/10/2025	หน้าปัดมีค่าขึ้น
57		801-14	FHC-8-01 (Front of Fire Staircase ST1)	✓	10 lb									01/10/2025	
58	8	802-14	FHC-8-02 (Front of Lift Service S1)	✓	10 lb									01/10/2025	
59		803-14	FHC-8-03 (Front of Fire Staircase ST2)	✓	10 lb									01/10/2025	
60		901-14	FHC-9-01 (Front of Fire Staircase ST1)	✓	10 lb									01/10/2025	
61	9	902-14	FHC-9-02 (Front of Lift Service S1)	✓	10 lb									01/10/2025	
62		903-14	FHC-9-03 (Front of Fire Staircase ST2)	✓	10 lb									01/10/2025	
63	10	1001-14	FHC-R-01 (Roof Top)	✓	10 lb									01/10/2025	
Grand Total				52		7		0		2		1			

Remark:

Yes = ✓ No = X

Check By: Mr.Banbhot Sunyaphap

(Security Officer)

Date: 01-2 October 2025

Review by: Mr. Prasit Inta

(Security Supervisor)

Date: 05 October 2025



EHCM FIRE EXTINGUISHERS INSPECTION

Month: December 2025

Items	Floor	Code	Location	Fire Extinguisher Type								Operable	Sealed	Checking Date	Remark
				DRY	Weight	CO2	Weight	WET	Weight	FOAM	Weight	Non-CFC	Weight		
1	B	B01-14	FHC-B-01 (Car Park B-2)	✓	10 lb									01/12/2025	
2		B02-14	FHC-B-02 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
3		B03-14	FHC-B-03 (Car Park B-1)	✓	10 lb									01/12/2025	
4		B04-14	FHC-B-04 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	
5		B05-14	FHC-B-05 (Front of Lift Service S1)	✓	10 lb									01/12/2025	
6		B07-14	Car Park 1	✓	10 lb									01/12/2025	
7		B08-14	Car Park 2	✓	10 lb									01/12/2025	
8		B09-14	Car Park 3	✓	10 lb									01/12/2025	
9		B10-14	Car Park 4	✓	10 lb									01/12/2025	
10		B11-14	Car Park 5	✓	10 lb									01/12/2025	หน้าปัดมีค่าขึ้น
11		B12-14	Car Park 6	✓	10 lb									01/12/2025	Refilled on March 21
12		B13-14	Canteen	✓		✓	10 lb							01/12/2025	13.25 kg.
13		B14-14	AC Office	✓	10 lb									01/12/2025	
14		B15-14	HR office	✓	10 lb									01/12/2025	
15		B16-14	Fire Fighting Cabinet	✓		✓	10 lb							01/12/2025	13.18 kg.
16	G	G01-14	FHC-G-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
17		G02-14	FHC-G-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	
18		G03-14	FHC-G-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	หน้าปัดมีค่าขึ้น
19		G04-14	Main Entrance G floor	✓	10 lb									01/12/2025	
20		G05-14	Front of Luggage Room	✓	10 lb									01/12/2025	
21		G06-14	Car Park G floor	✓	10 lb									01/12/2025	
22		G07-14	Gas Station	✓	10 lb									01/12/2025	
23		G08-14	Gas Station	✓		✓	10 lb							01/12/2025	13.45 kg
24		G09-14	Control Room 1	✓	10 lb									01/12/2025	หน้าปัดมีค่าขึ้น
25		101-14	FHC-1-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
26	1	102-14	FHC-1-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	หน้าปัดมีค่าขึ้น
27		103 -02/11/23	Reservation Officer	✓	10 lb									01/12/2025	
28		104-14	FHC-1-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	
29		105-14	Administrative Office	✓		✓	10 lb							01/12/2025	13.15 kg.
30		106-14	Kitchen (Entrance)							✓	10 lb			01/12/2025	
31		107-14	Kitchen (Entrance)									✓	10 lb	01/12/2025	
32		108-14	Kitchen (Front of Dry Store)			✓	10 lb							01/12/2025	11.54 kg.
33		109-14	Kitchen (Stove)							✓	10 lb			01/12/2025	Transfer from UNCM
34		201-14	FHC-2-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	Refilled on October 21
35	2	202-14	FHC-2-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	
36		203-14	FHC-2-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	หน้าปัดมีค่าขึ้น
37		204-14	Generator Room	✓	10 lb									01/12/2025	
38		205-14	Generator Room	✓		✓	10 lb							01/12/2025	9.72 kg.
39		206-14	MDB Room	✓	10 lb									01/12/2025	
40		207-14	MDB Room	✓		✓	10 lb							01/12/2025	11.87 kg.
41		302-14	FHC-3-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
42	3	303-14	FHC-3-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	
43		304-14	FHC-3-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	
44		401-14	FHC-4-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
45	4	402-14	FHC-4-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	
46		403-14	FHC-4-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	หน้าปัดมีค่าขึ้น
47		501-14	FHC-5-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
48	5	502-14	FHC-5-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	หน้าปัดมีค่าขึ้น
49		503-14	FHC-5-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	
50		601-14	FHC-6-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
51	6	602-14	FHC-6-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	หน้าปัดมีค่าขึ้น
52		603-14	FHC-6-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	
53		701-14	FHC-7-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
54	7	702-14	FHC-7-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	
55		703-14	FHC-7-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	หน้าปัดมีค่าขึ้น
56		801-14	FHC-8-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
57	8	802-14	FHC-8-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	
58		803-14	FHC-8-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	
59		901-14	FHC-9-01 (Front of Fire Staircase ST1)	✓	10 lb									01/12/2025	
60	9	902-14	FHC-9-02 (Front of Lift Service S1)	✓	10 lb									01/12/2025	
61		903-14	FHC-9-03 (Front of Fire Staircase ST2)	✓	10 lb									01/12/2025	
62	10	1001-14	FHC-R-01 (Roof Top)	✓	10 lb									01/12/2025	
Grand Total				52		7		0		2		1			

Remark:

Yes = ✓ No = X

Check By: Mr. Prasit Inta

(Security Supervisor)

Date: 01 December 2025

Review by: Mr. Prasit Inta

(Security Supervisor)

Date: 01 December 2025

ภาคผนวก ค5

เอกสารทดสอบสัญญาณ Fire Alarm





FIRE ALARM TESTING CHECKLIST


Activated by: ☐ / Automatic System ☐ Manual System

Date: 11 July 2025 Time: 14.00 hrs.

STEP Testing


1. Select location as required (Floor#2)
 - Room T-Quaterage - Room T-Quater 1 - Room T-Quater2/1
 - Room T-Quater2/2 - Elevator for customers F/2 - Lift service
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room T-Quaterage

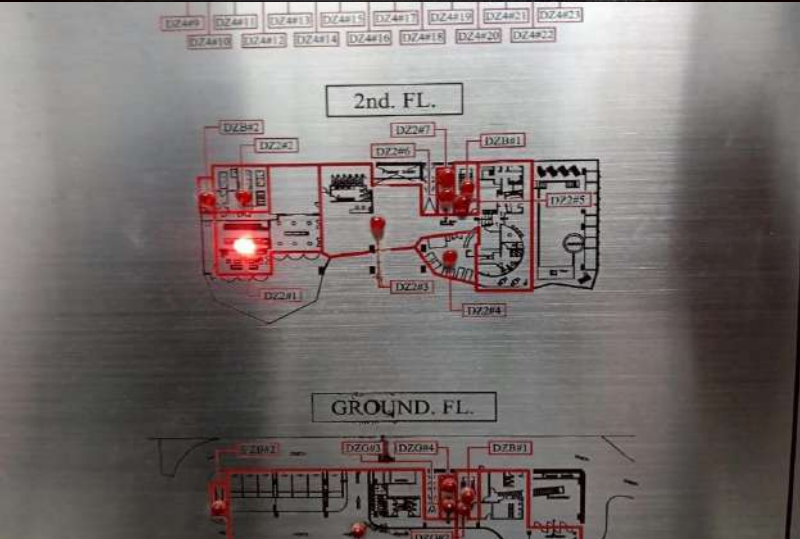Location / Dectector activated	
Fire Control Panel	
Annunciator	

Room T-Quater 1


**Location / Dectector
activated**

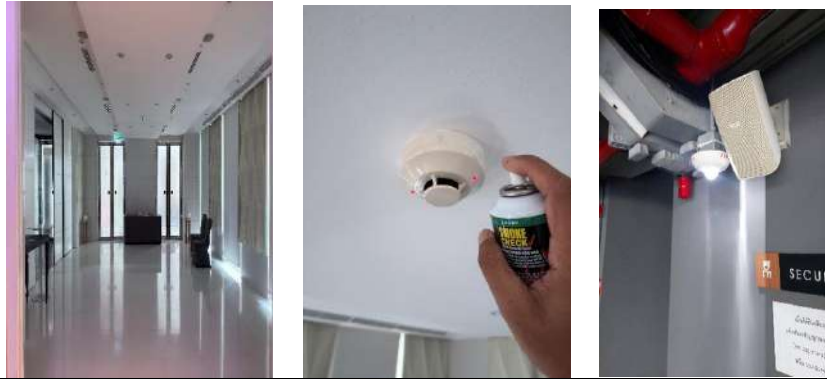

Fire Control Panel



Annunciator

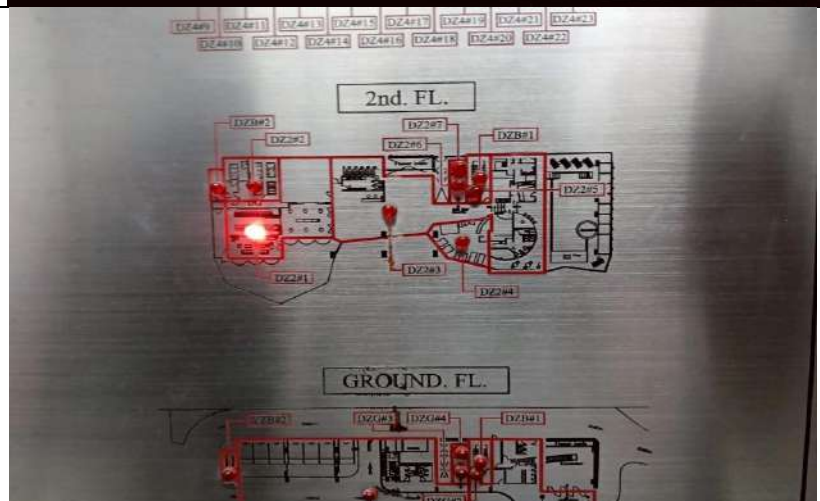

Room T-Quater2/2


Location / Dectector activated





Fire Control Panel





Annunciator

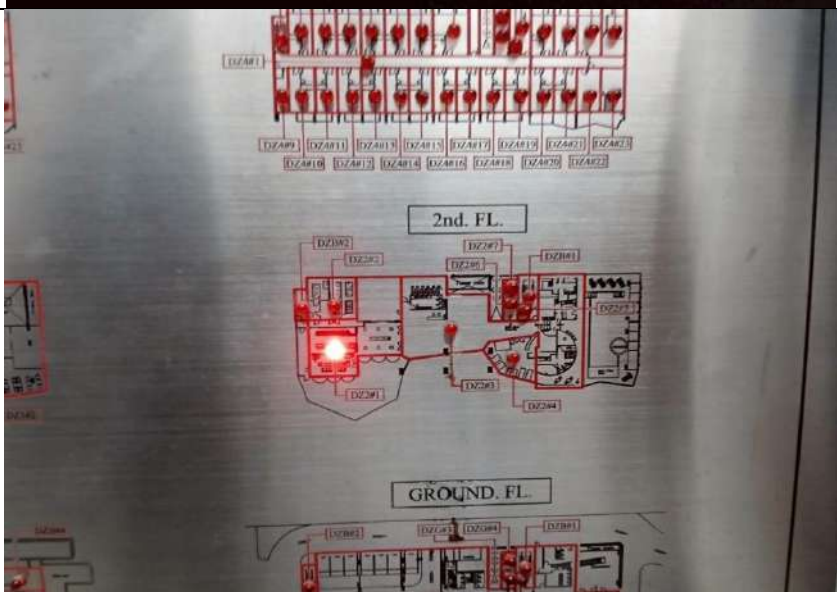

Room Elevator for customers F/2

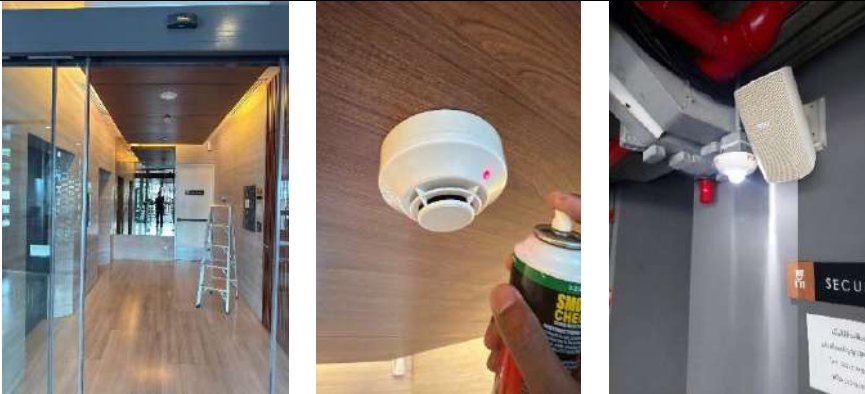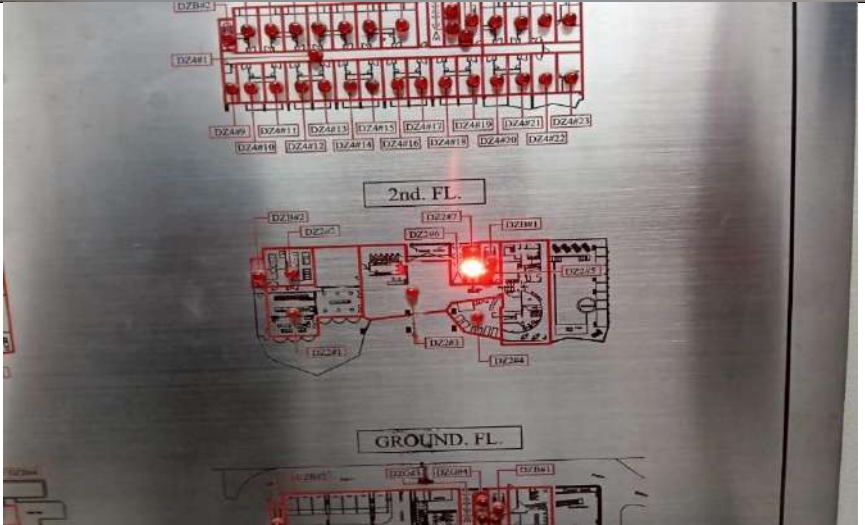Location / Dectector activated	
Fire Control Panel	
Annunciator	

Room Lift service

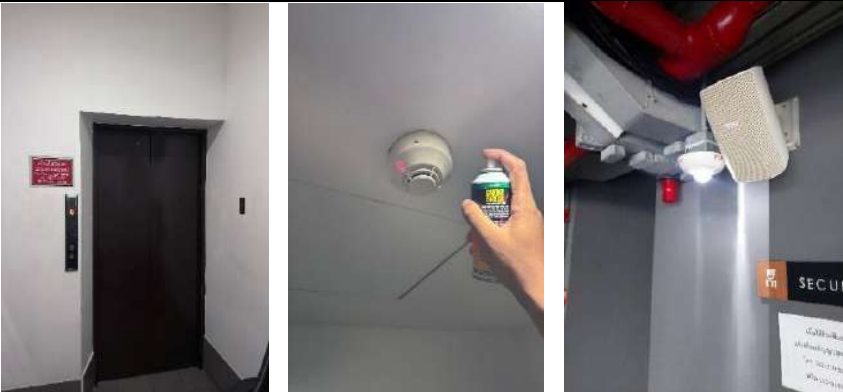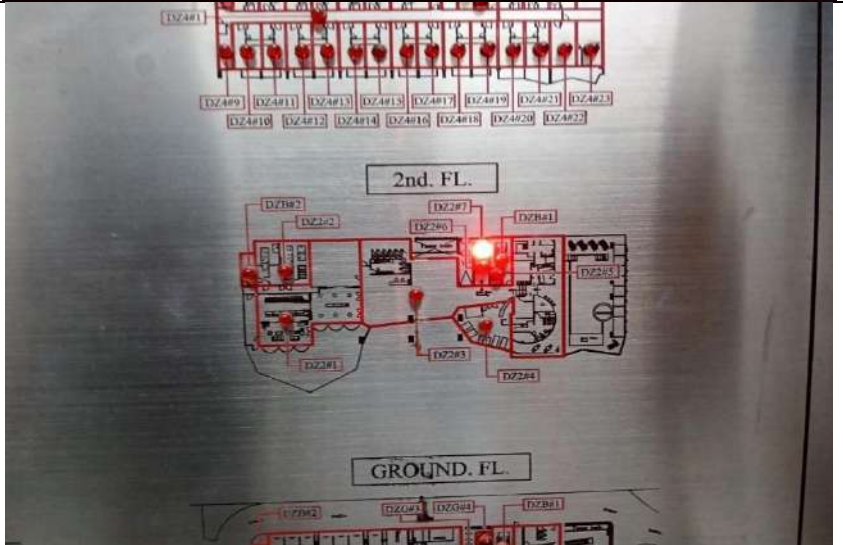Location / Dectector activated	
Fire Control Panel	
Annunciator	

Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
2	Room T-Quaterage	-	YES	-	-	
2	Room T-Quater 1	-	YES	-	-	
2	Room T-Quater2/1	-	YES	-	-	
2	Room T-Quater2/2	-	YES	-	-	
2	Elevator for customers F/2	-	YES	-	-	
2	Lift service	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ2#1	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ2#1	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ2#1	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ2#1	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ2#6	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ2#7	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Pratchayarat Thongdee (Security Officer)

Mr. Suvaroj Lorkeawnunthakul (Security Officer)

(11 July 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(11 July 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☐ / Automatic System ☐ Manual System

Date: 14 July 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor # 4 / 7)
 - Room 406 - Room 718
 - Room 714
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room 406


Location / Dectector
activated



Fire Control Panel



Annunciator

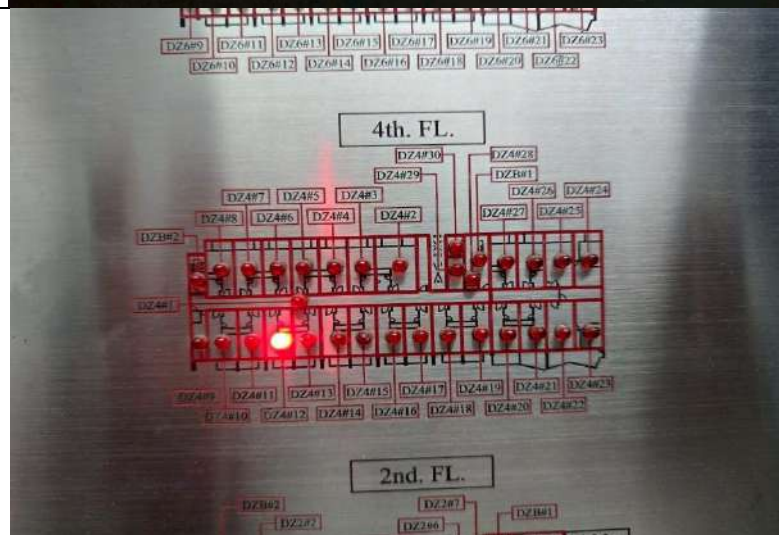

Room 714


Location / Dectector
activated



Fire Control Panel



Annunciator

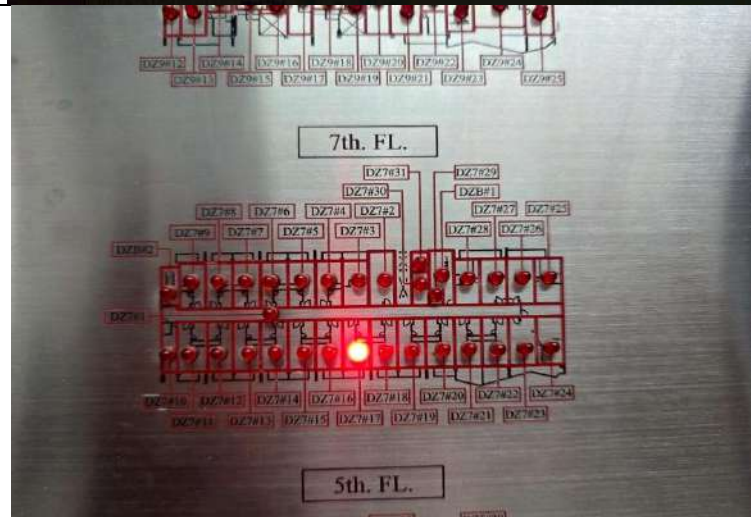

Room 718


**Location / Dectector
activated**



Fire Control Panel



Annunciator

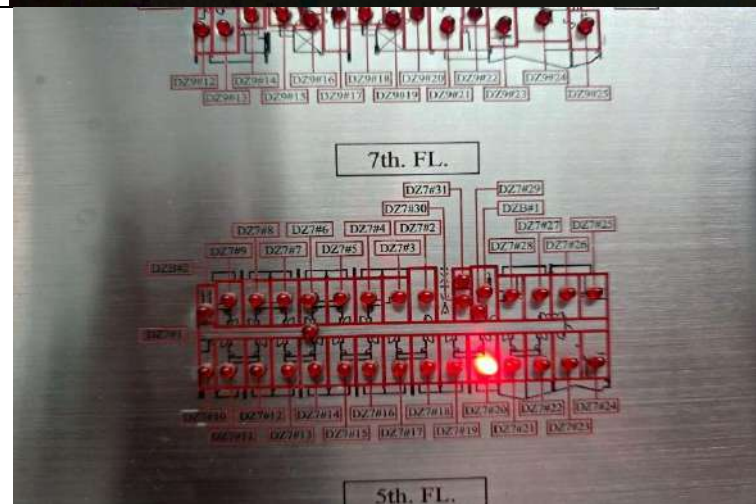



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
4	Room 406	-	YES	-	-	
7	Room 714	-	YES	-	-	
7	Room 718	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ4#12	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#17	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#20	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Banbhot Sunyaphap (Security Officer)

Mr . Adipong Pareesen (Security Supervisor)

(14 July 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(14 July 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☐ / Automatic System ☐ Manual System

Date: 21 July 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor # G / B)
 - Lift service FL.G - Lift staff FL.G - Lift staff FL.B
 - Dirty Linen room FL.B - Engineer office FL.B
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Lift Service FL.G


Location / Dectector
activated



Fire Control Panel



Annunciator

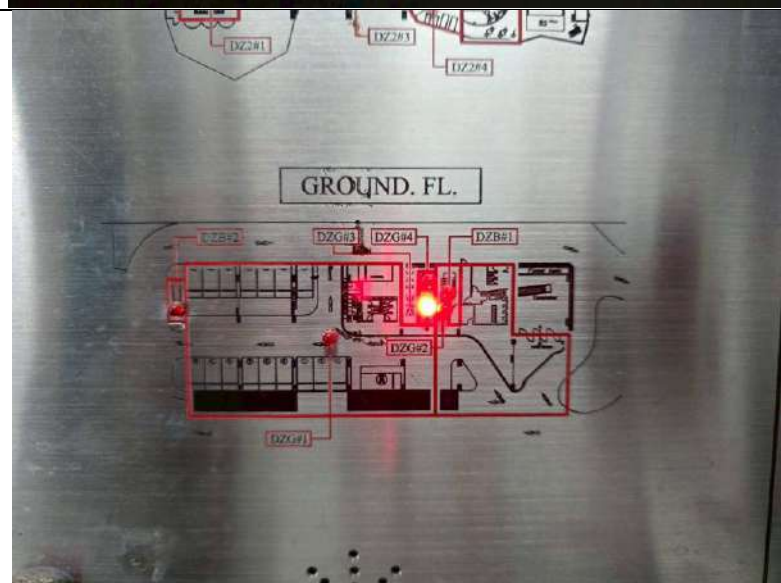

Lift Staff FL.G


**Location / Dectector
activated**



Fire Control Panel




Annunciator

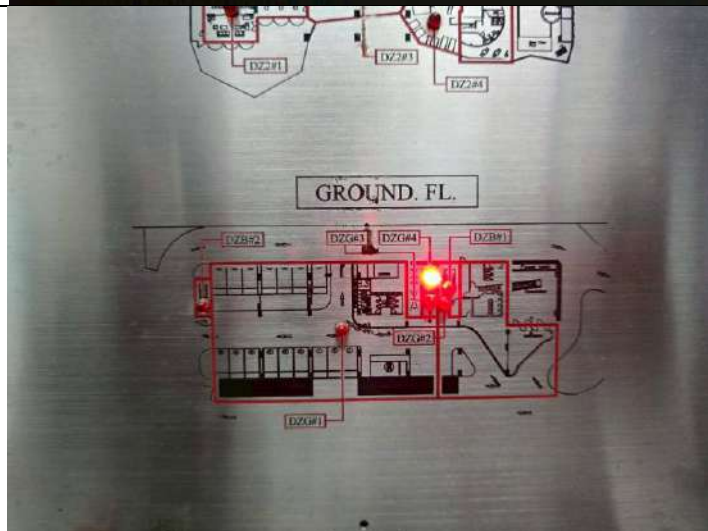

Lift Staff FL.B


**Location / Dectector
activated**

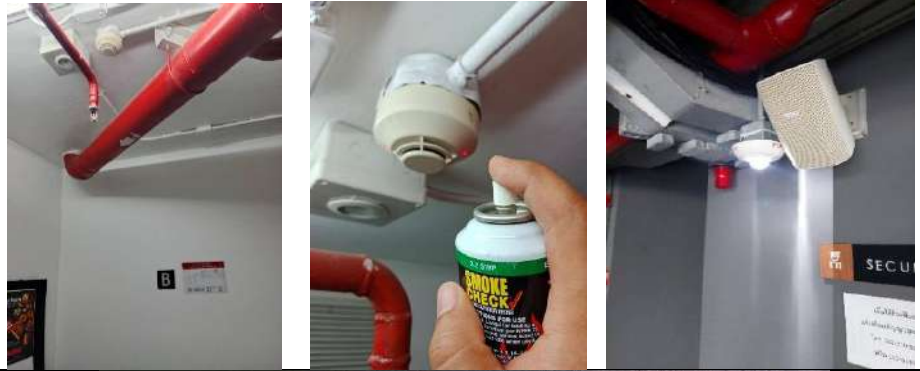

Fire Control Panel



Annunciator

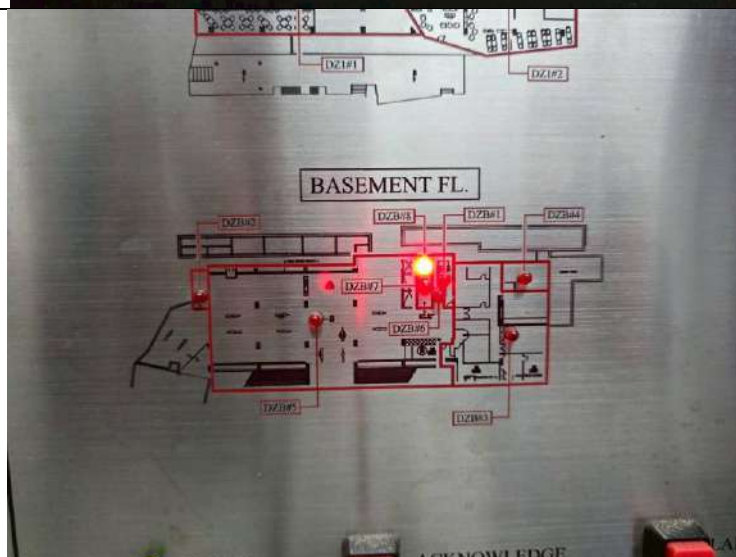

Dirty Linen FL.B


**Location / Dectector
activated**



Fire Control Panel



Annunciator

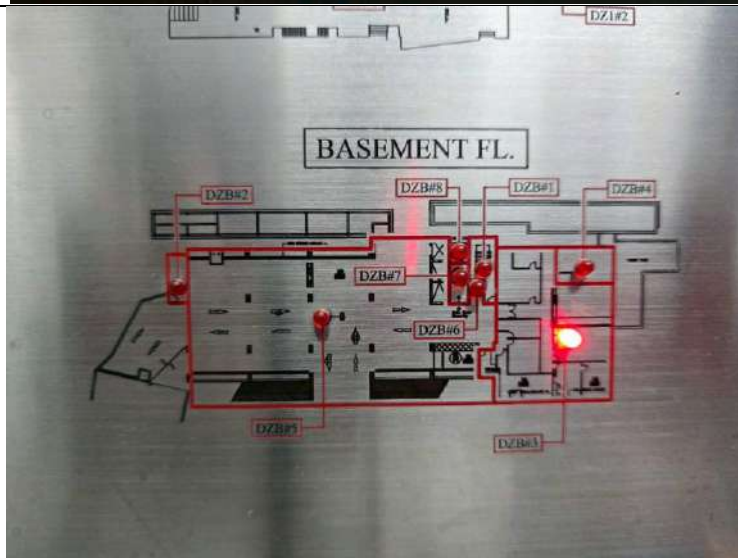

Engineer Office FL.B


**Location / Dectector
activated**



Fire Control Panel



Annunciator

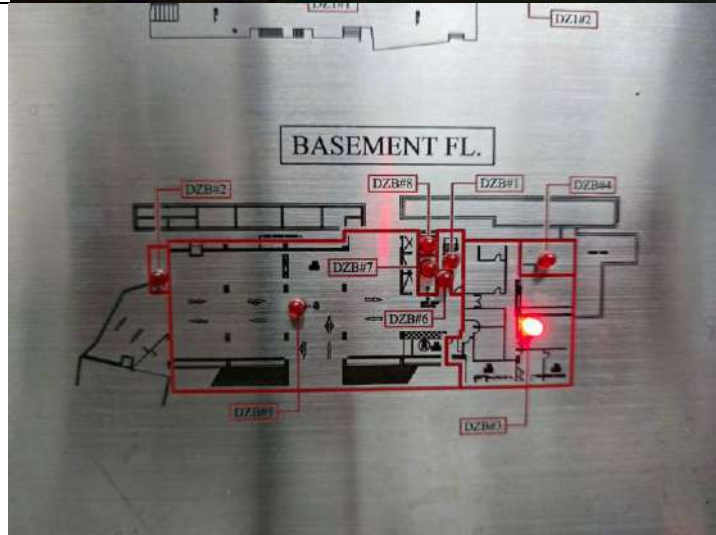

Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
G	Lift servive FL.G	-	YES	-	-	
G	Lift staff FL.G	-	YES	-	-	
B	Lift staff FL.B	-	YES	-	-	
B	Dirty Linen room FL.B	-	YES	-	-	
B	Engineer office FL.B	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZG#3	YES	YES	/	-	/	-	/	-	/	-	-	/
DZG#4	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#8	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Prasit Inta (Security Supervisor)

Mr . Adipong Pareesen (Security Supervisor)

(21 July 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(21 July 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 28 July 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#6)
 - Room 605 - Room 615/1 - Room 615/2
 - Room 621/1 - Room 621/2 - Room 622
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room 605


Location / Dectector
activated



Fire Control Panel



Annunciator

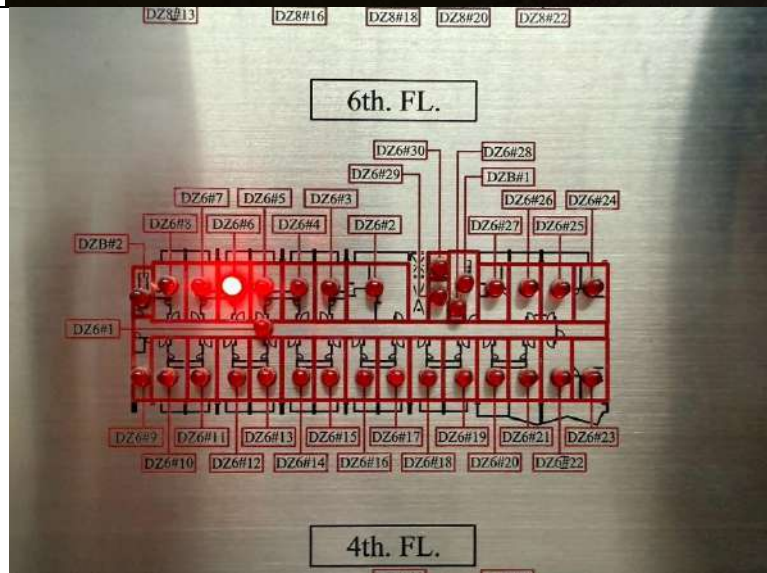

Room 615/1


Location / Dectector
activated



Fire Control Panel



Annunciator

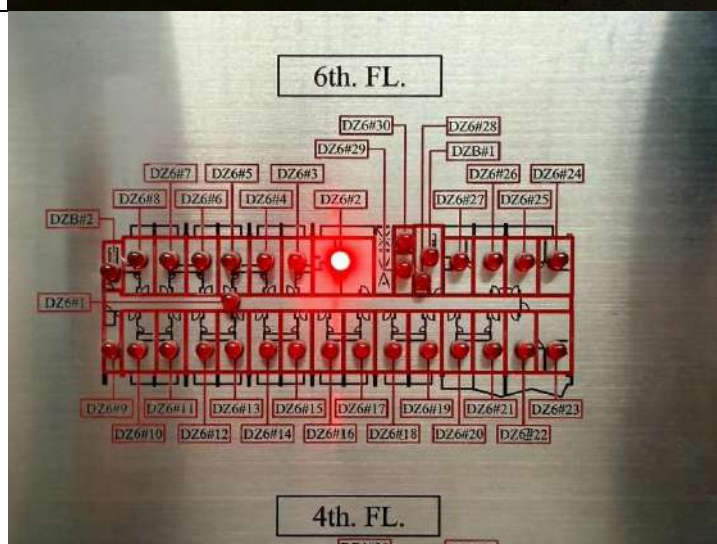

Room 615/2


Location / Dectector
activated



Fire Control Panel




Annunciator

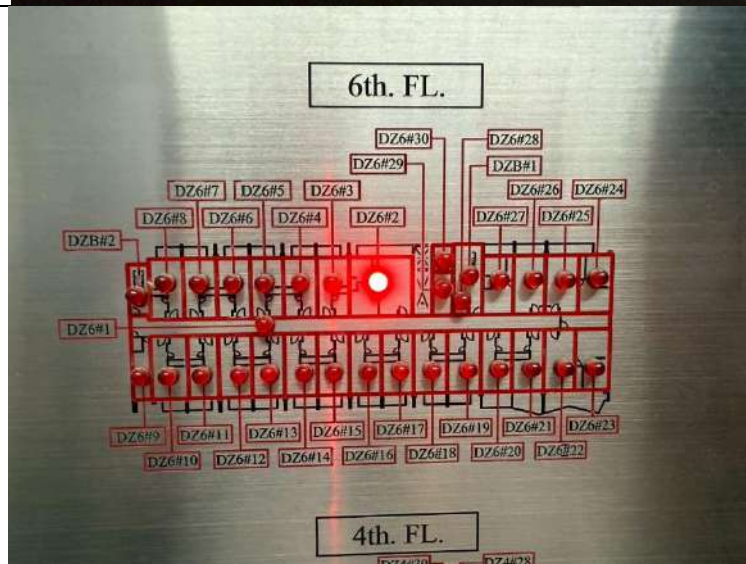

Room 621/1


**Location / Dectector
activated**

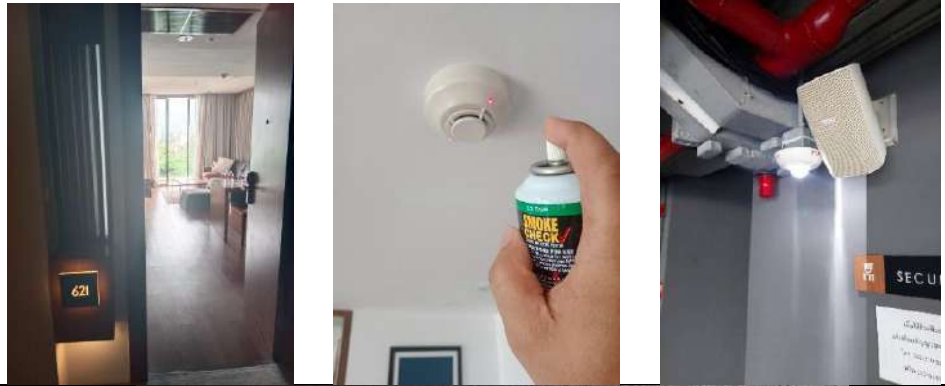

Fire Control Panel



Annunciator

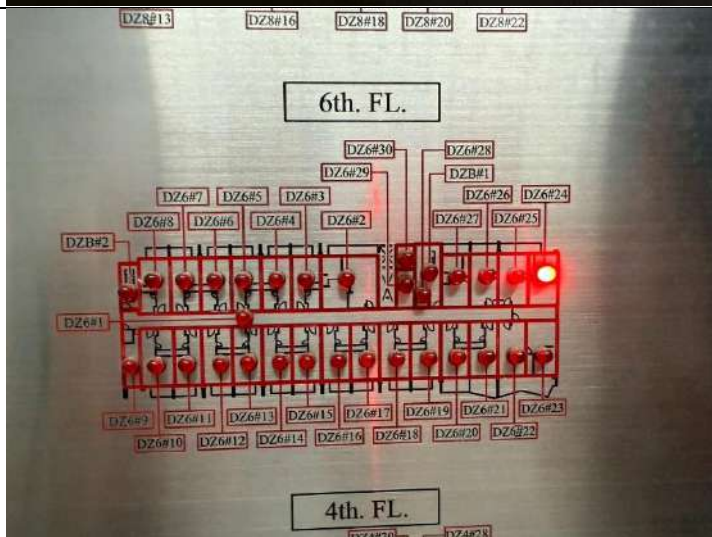

Room 621/2


Location / Dectector
activated



Fire Control Panel




Annunciator

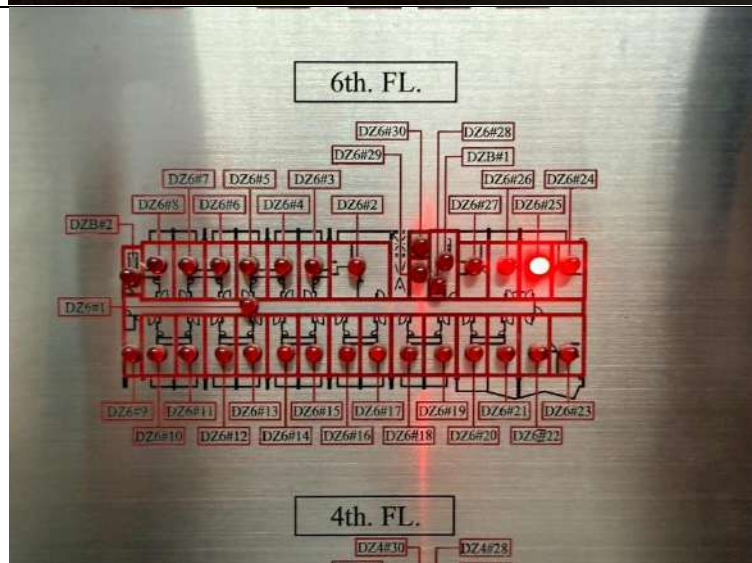

Room 622


Location / Dectector
activated



Fire Control Panel



Annunciator

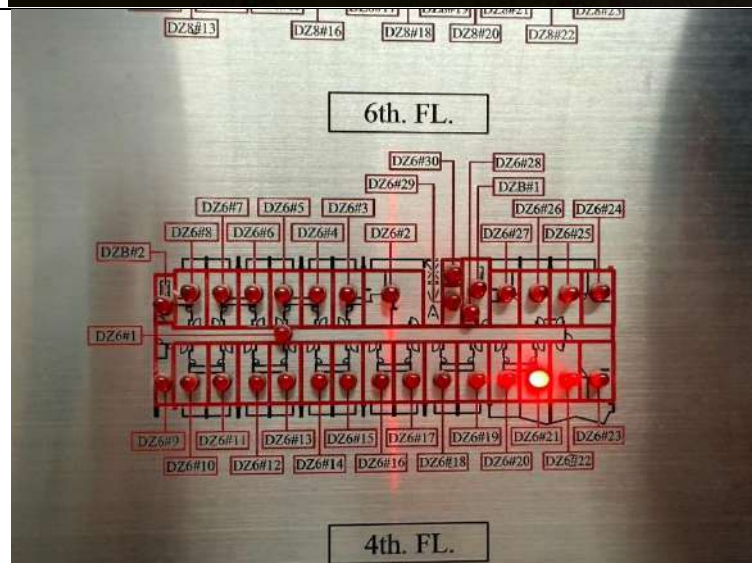



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
6	Room 605	-	YES	-	-	
6	Room 615/1	-	YES	-	-	
6	Room 615/2	-	YES	-	-	
6	Room 621/1	-	YES	-	-	
6	Room 621/2	-	YES	-	-	
6	Room 622	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ6#6	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ6#2	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ6#2	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ6#24	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ6#25	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ6#21	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Supanut Sikanta (Security Officer)

Mr . Prasit Inta (Security Supervisor)

(28 July 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(28 July 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ / Automatic System ☐ Manual System

Date: 04 August 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor # 3)
 - Room 318 - Room 320
 - Room 319
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room 318


Location / Dectector
activated



Fire Control Panel



Annunciator

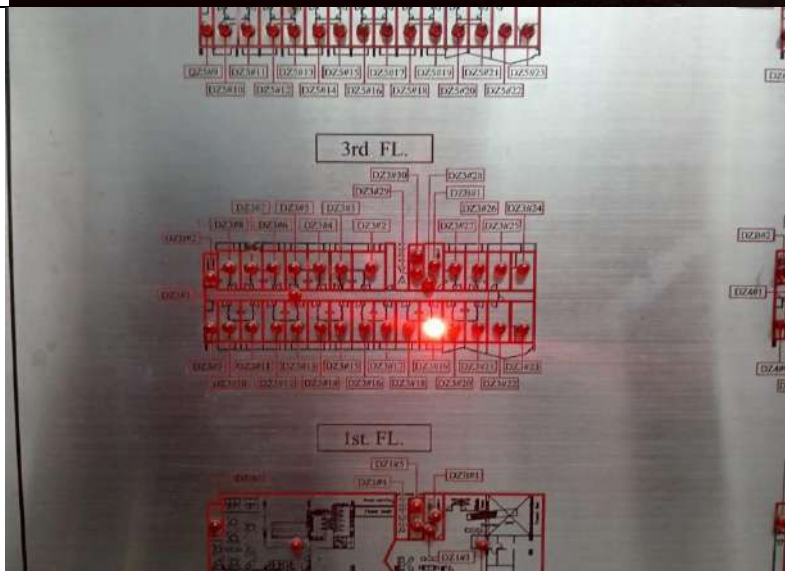

Room 319


Location / Dectector
activated



Fire Control Panel



Annunciator

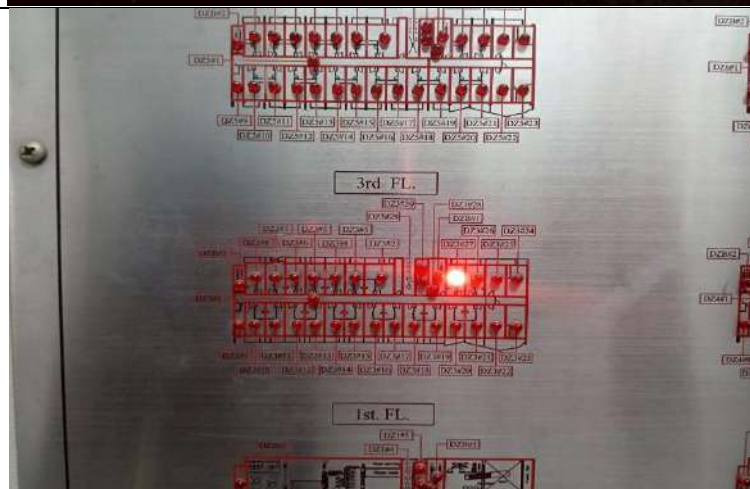

Room 320


Location / Dectector
activated



Fire Control Panel



Annunciator

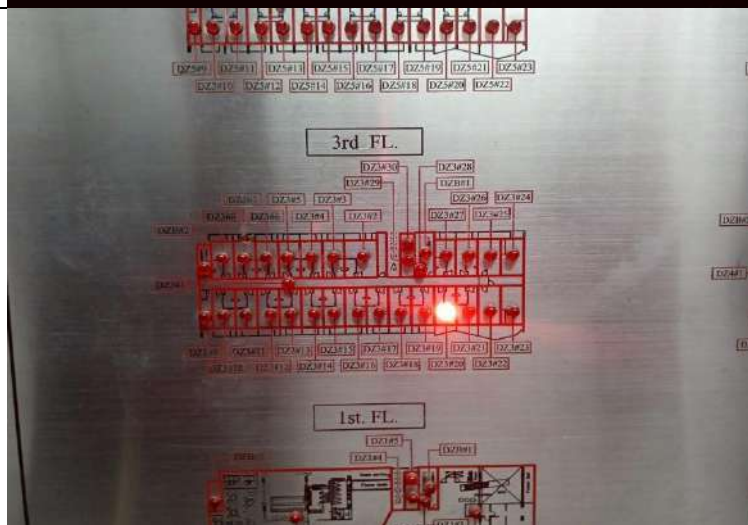



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
3	Room 318	-	YES	-	-	
3	Room 319	-	YES	-	-	
3	Room 320	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ3#19	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ3#27	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ3#20	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Banbhot Sunyaphap (Security Officer)

Mr . Suvaroj Lorkeawnunthakul (Security Officer)

(04 August 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(04 August 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 11 August 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#5/6/7/8)
 - Room 510 - Room 614 - Room 712 - Room 724/1
 - Room 724/2 - Room 803/1 - Room 803/2 - Room 803/2
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room 510


Location / Dectector
activated



Fire Control Panel




Annunciator

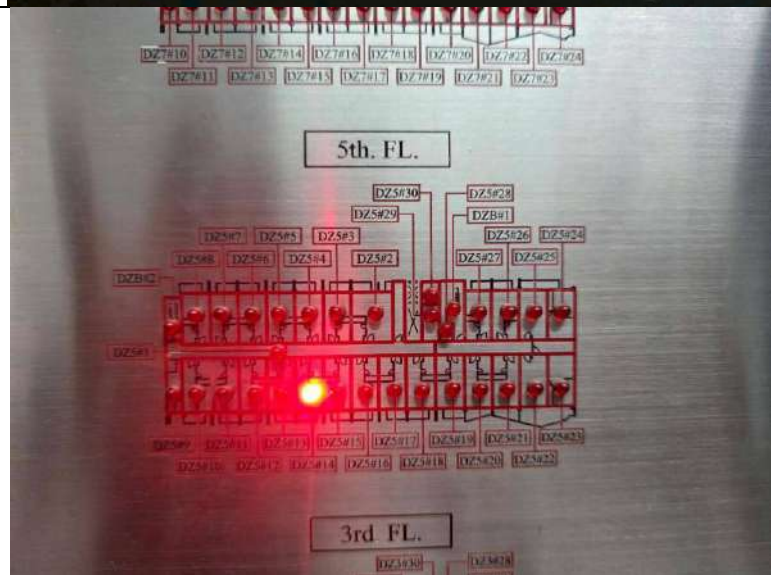

Room 614


Location / Dectector
activated



Fire Control Panel



Annunciator

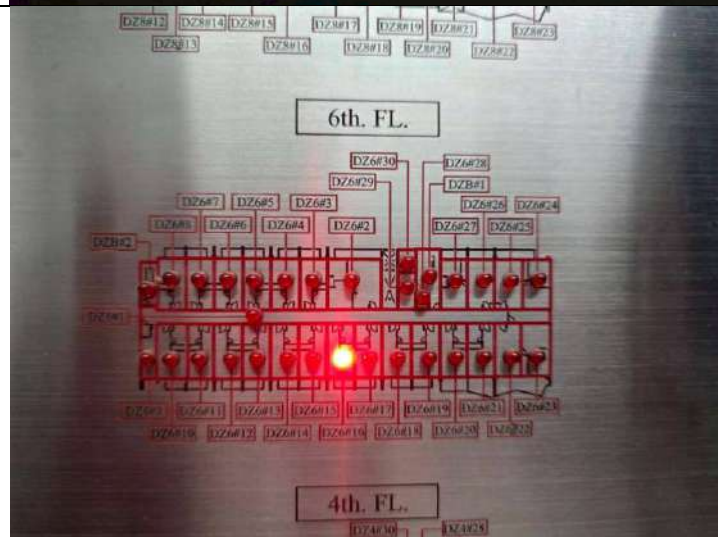

Room 712


Location / Dectector
activated



Fire Control Panel



Annunciator

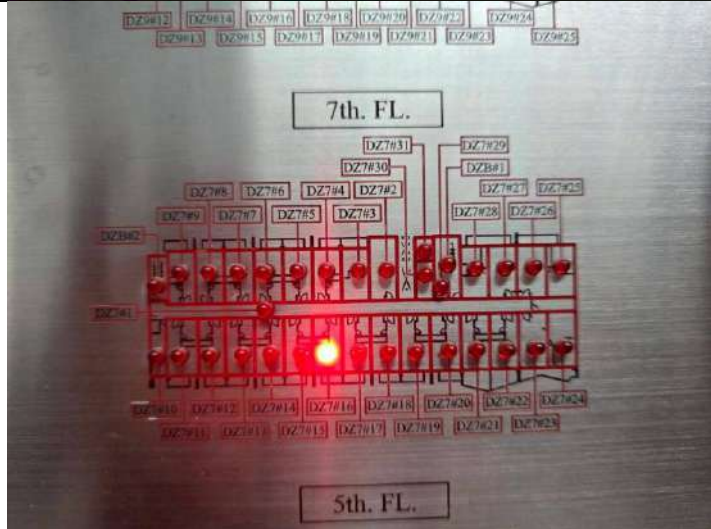

Room 724/1


Location / Dectector
activated



Fire Control Panel



Annunciator

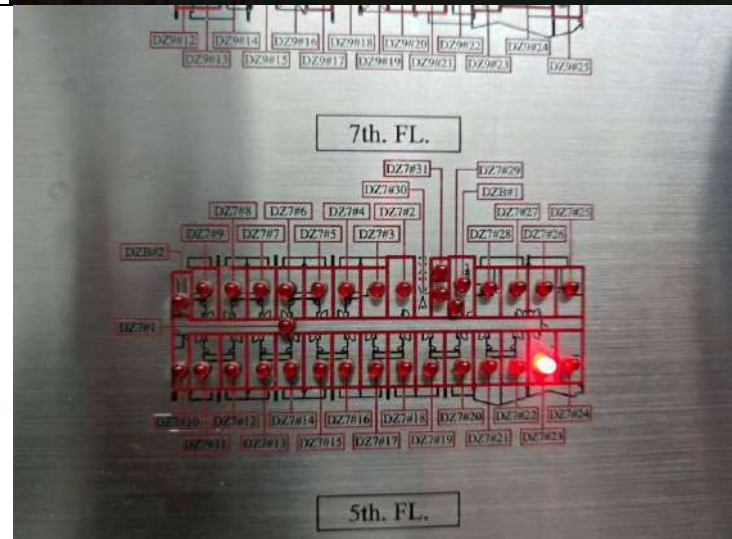

Room 724/2


**Location / Dectector
activated**



Fire Control Panel



Annunciator

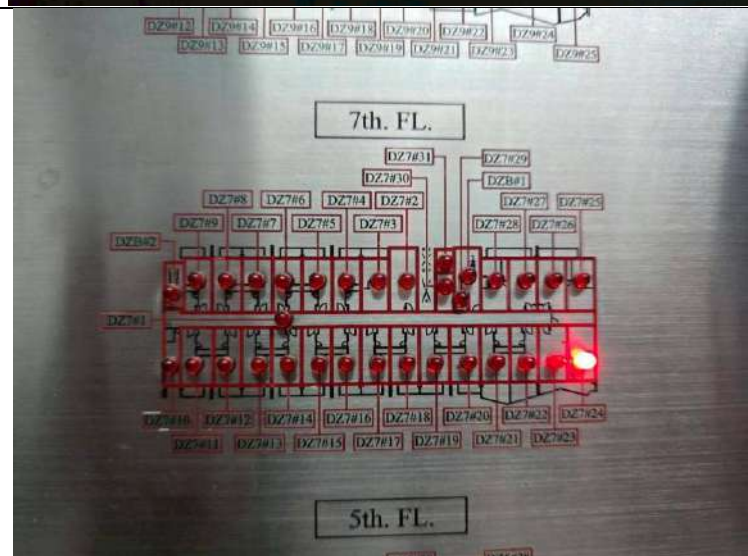

Room 803/1


**Location / Dectector
activated**



Fire Control Panel



Annunciator

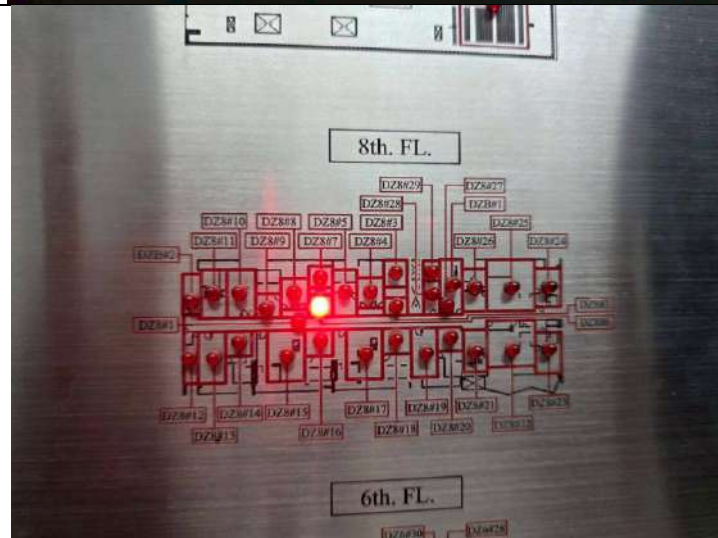

Room 803/2


Location / Dectector
activated



Fire Control Panel




Annunciator

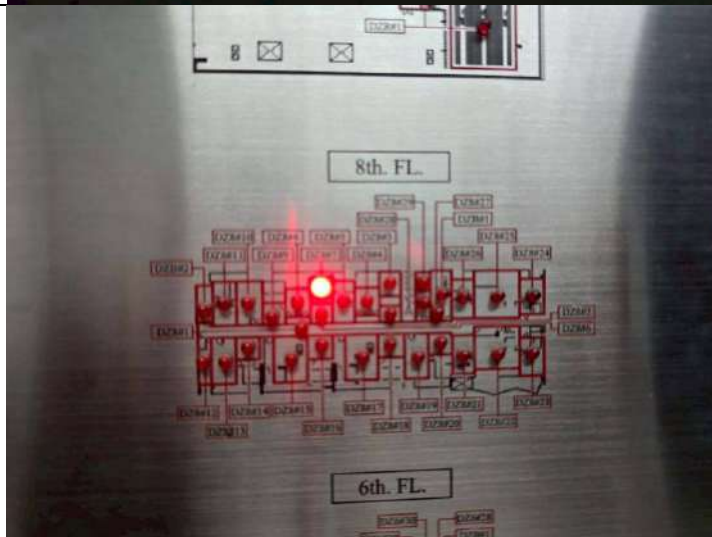

Room 803/3


Location / Dectector activated

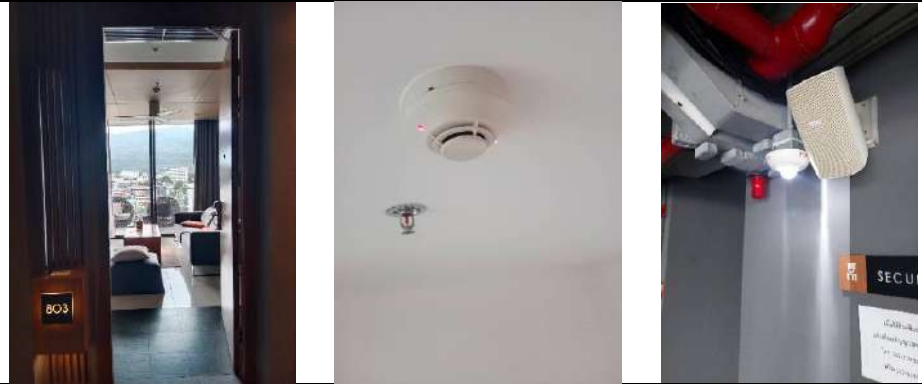

Fire Control Panel



Annunciator

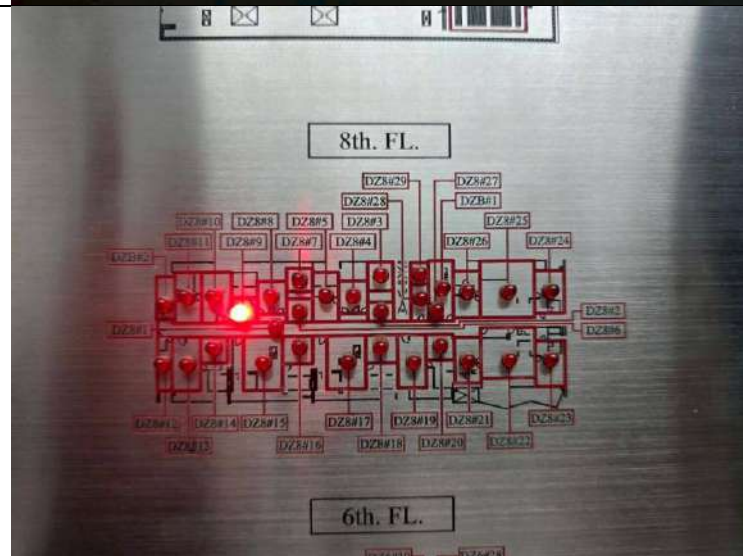



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
5	Room 510	-	YES	-	-	
6	Room 614	-	YES	-	-	
7	Room 712	-	YES	-	-	
7	Room 724/1	-	YES	-	-	
7	Room 724/2	-	YES	-	-	
8	Room 803/1	-	YES	-	-	
8	Room 803/2	-	YES	-	-	
8	Room 803/3	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ5#14	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ6#16	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#16	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#23	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#24	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ8#6	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ8#7	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ8#9	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Adipong Pareesen (Security Supervisor)

Mr. Prasit Inta (Security Supervisor)

(11 August 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(11 August 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 18 August 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Fire staircases ST1 ST2 Floor B-G-Fl.3)
 - Floor B. ST1- ST2. - Floor G. ST1 ST 2.
 - Floor 3. ST1- ST2.
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Fire Staircases B ST1


Location / Dectector
activated



Fire Control Panel



Annunciator

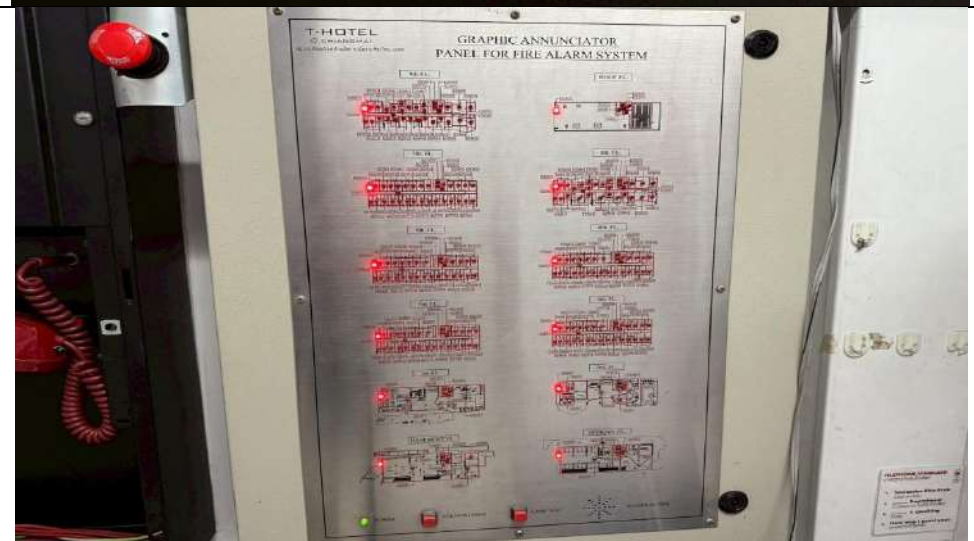

Fire Staircases B ST2

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Fire Staircases G ST1


Location / Dectector
activated



Fire Control Panel



Annunciator

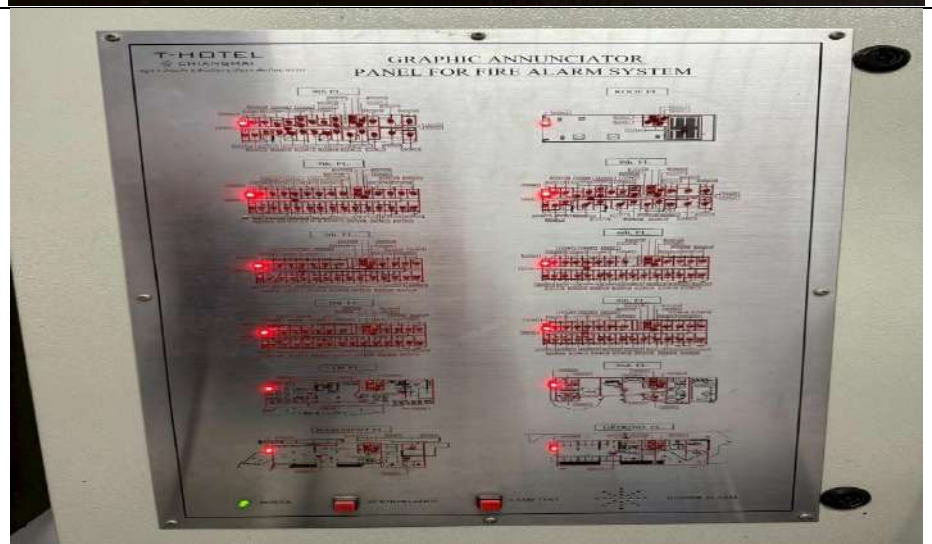

Fire Staircases G ST2

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Fire Staircases ST1 FL.3


Location / Dectector
activated



Fire Control Panel



Annunciator

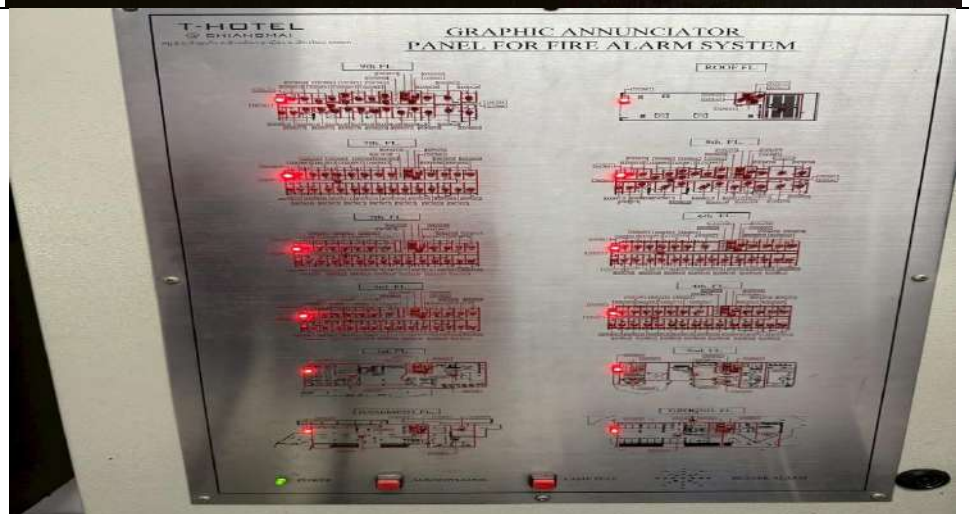

Fire Staircses ST2 FL.3

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
B	Fire Staircses B ST1	YES	YES	-	-	
B	Fire Staircses B ST2	YES	NO	-	-	ตู้ PCP Annunciator ไม่มีการแจ้งเตือน Alarm
G	Fire Staircses G ST1	YES	YES	-	-	
G	Fire Staircses G ST2	YES	NO	-	-	ตู้ PCP Annunciator ไม่มีการแจ้งเตือน Alarm
3	Fire Staircses Floor3 ST1	YES	YES	-	-	
3	Fire Staircses Floor3 ST2	YES	NO	-	-	ตู้ PCP- Annunciator ไม่มีการแจ้งเตือน Alarm

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZB#2	YES	YES	/	-	/	-	/	-	/	-	-	/
Fire Staircses B ST 2	NO	NO	-	-	-	-	-	-	-	-	-	-
DZB#2	YES	YES	/	-	/	-	/	-	/	-	-	/
Fire Staircses G ST 2	NO	NO	-	-	-	-	-	-	-	-	-	-
DZB#2	YES	YES	/	-	/	-	/	-	/	-	-	/
Fire Staircses FL.3 ST 2	NO	NO	-	-	-	-	-	-	-	-	-	-

Tested by: Mr. Banbhot Sunyaphap (Security Officer)

Mr . Supanut Sikanta (Security Officer)

(18 August 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(18 August 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 25 August 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Fire staircases ST1 ST2 Floor 4/5/6/7/8/9/10)
- Floor - 4/5/6/7/8/9/10 . ST1- ST2
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Fire Staircases 4 ST1


Location / Dectector
activated



Fire Control Panel



Annunciator

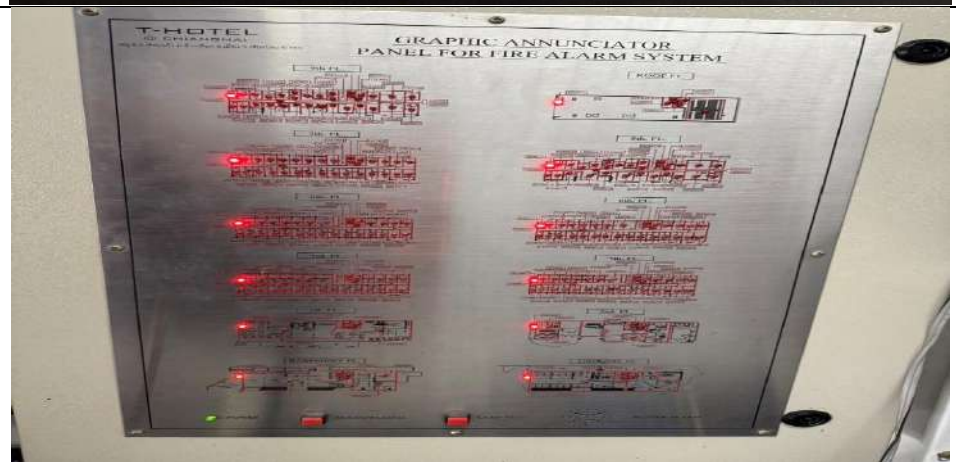

Fire Staircases 4 ST2

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Fire Staircases 5 ST1


Location / Dectector
activated



Fire Control Panel



Annunciator

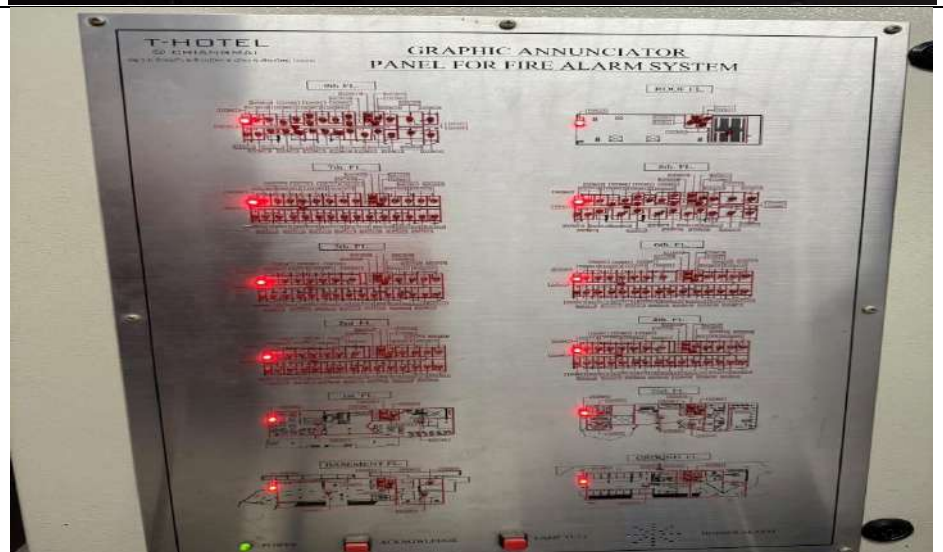

Fire Staircases 5 ST2

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Fire Staircases 6 ST1


**Location / Dectector
activated**



Fire Control Panel



Annunciator

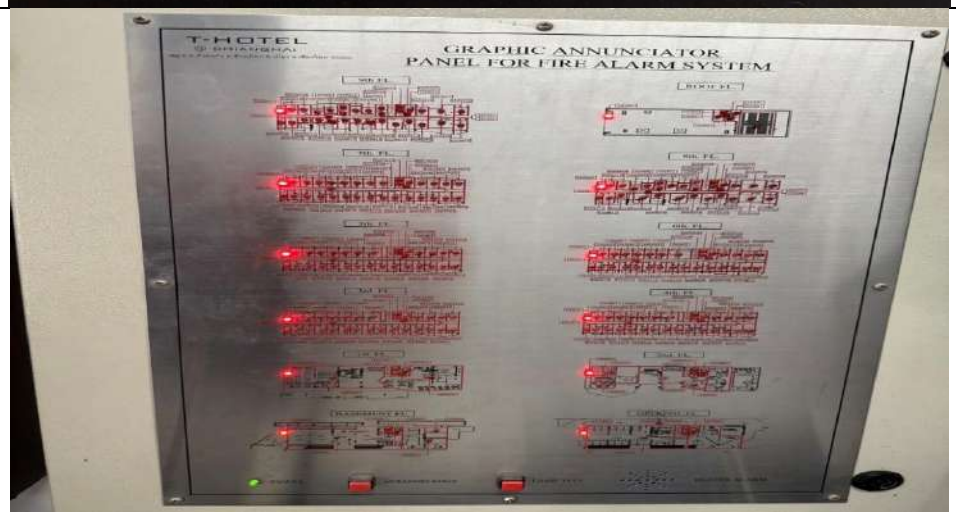

Fire Staircases 6 ST2

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Fire Staircases 7 ST1


Location / Dectector
activated



Fire Control Panel



Annunciator

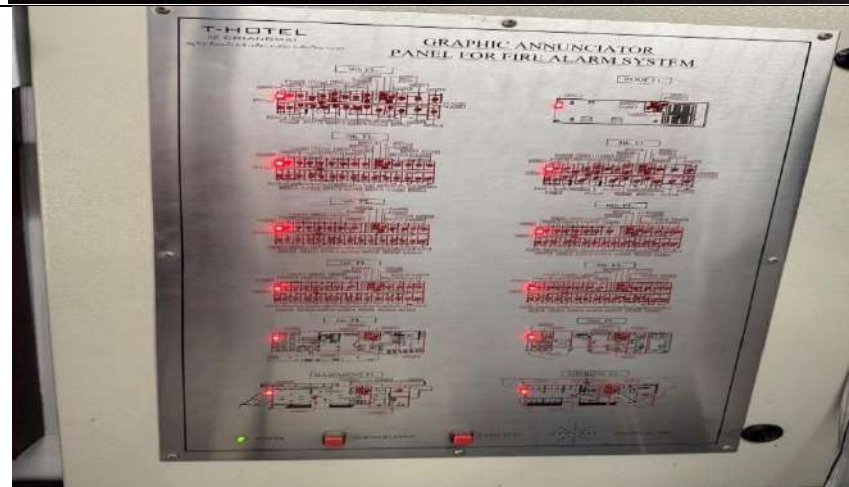

Fire Staircases 7 ST2

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Fire Staircases 8 ST1


Location / Dectector
activated



Fire Control Panel



Annunciator

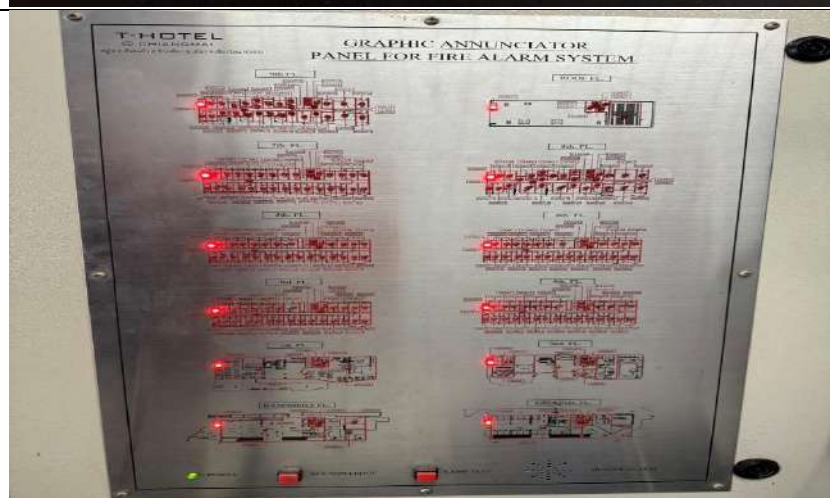

Fire Staircases 8 ST2

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Fire Staircases 9 ST1


Location / Dectector
activated



Fire Control Panel



Annunciator

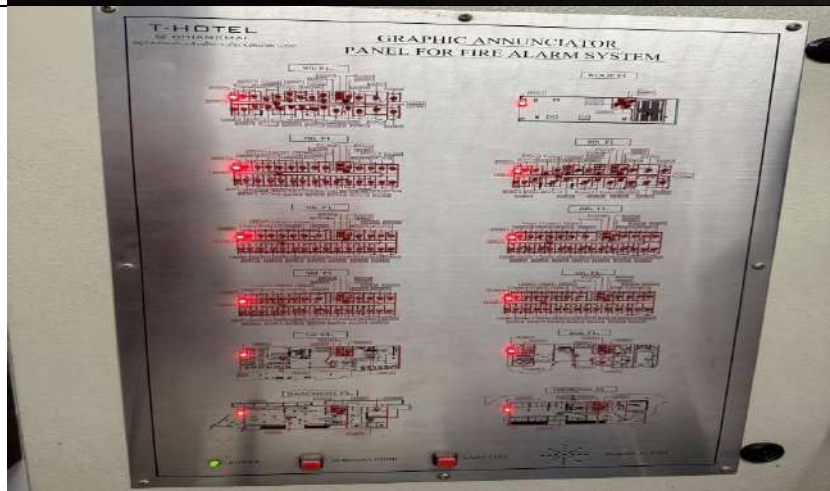

Fire Staircses 9 ST2

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Fire Staircases 10 ST1


Location / Dectector
activated



Fire Control Panel



Annunciator

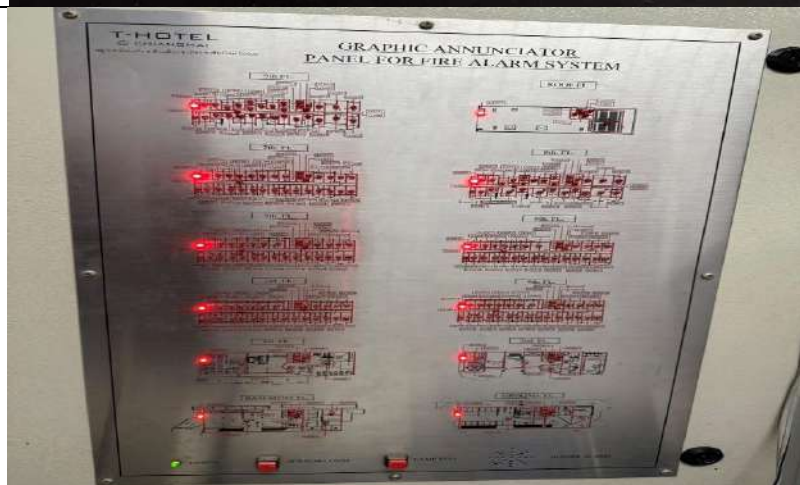

Fire Staircases 10 ST2

Location / Dectector activated	
Fire Control Panel	
Annunciator	

Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
4	Fire Staircases 4 ST1	YES	YES	-	-	
4	Fire Staircases 4 ST2	YES	NO	-	-	ตู้ -FCP Annunciator ไม่มีการแจ้งเตือน Alarm
5	Fire Staircases 5 ST1	YES	YES	-	-	
5	Fire Staircases 5 ST2	YES	NO	-	-	ตู้ - FCP Annunciator ไม่มีการแจ้งเตือน Alarm
6	Fire Staircases 6 ST1	YES	YES	-	-	
6	Fire Staircases 6 ST2	YES	NO	-	-	ตู้ – FCP Annunciator ไม่มีการแจ้งเตือน Alarm
7	Fire Staircases 7 ST1	YES	YES	-	-	

7	Fire Staircases 7 ST2	YES	NO	-	-	ตู้ - FCP Annunciator ไม่มีการแจ้งเตือน Alarm
8	Fire Staircases 8 ST1	YES	YES	-	-	
8	Fire Staircases 8 ST2	YES	NO	-	-	ตู้ - FCP Annunciator ไม่มีการแจ้งเตือน Alarm
9	Fire Staircases 9 ST1	YES	YES	-	-	
9	Fire Staircases 9 ST2	YES	NO	-	-	ตู้ - FCP Annunciator ไม่มีการแจ้งเตือน Alarm
10	Fire Staircases 10 ST1	YES	YES	-	-	
10	Fire Staircases 10 ST2	YES	NO	-	-	ตู้ - FCP Annunciator ไม่มีการแจ้งเตือน Alarm



EASTIN
TAN HOTEL
CHIANG MAI

[illegible]



DZB#2	YES	YES	/	-	/	-	/	-	/	-	-	/
Fire Staircases 9 ST 2	NO	NO	-	-	-	-	-	-	-	-	-	-
DZB#2	YES	YES	/	-	/	-	/	-	/	-	-	/
Fire Staircases 10 ST 2	NO	NO	-	-	-	-	-	-	-	-	-	-

Tested by: Mr. Banbhot Sunyaphap (Security Officer)

Mr . Supanut Sikanta (Security Officer)

(25 August 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(25 August 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 01 September 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#3/4/5/6)
 - Kids Club - Lift Staff-3 - Lift Staff-4
 - Lift Staff-5 - Lift Staff-6
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Kids Club


Location / Dectector
activated



Fire Control Panel



Annunciator

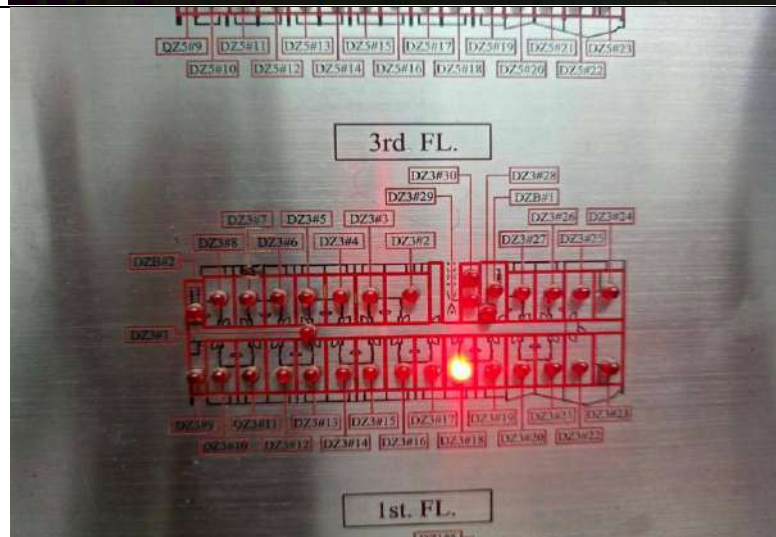

Lift Staff-3


**Location / Dectector
activated**



Fire Control Panel



Annunciator

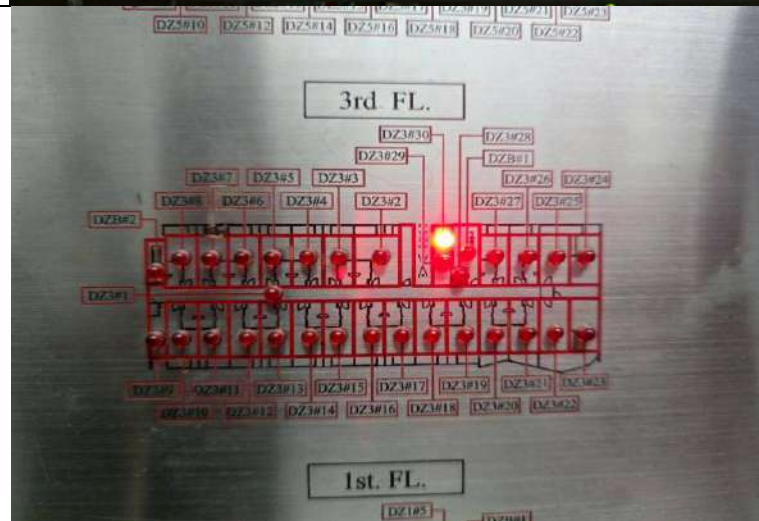

Lift Staff-4


**Location / Dectector
activated**



Fire Control Panel



Annunciator

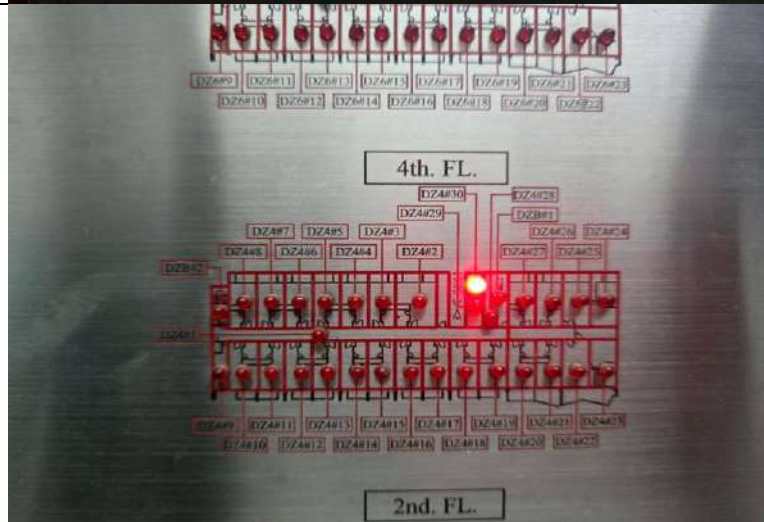

Lift Staff-6


Location / Dectector
activated



Fire Control Panel



Annunciator

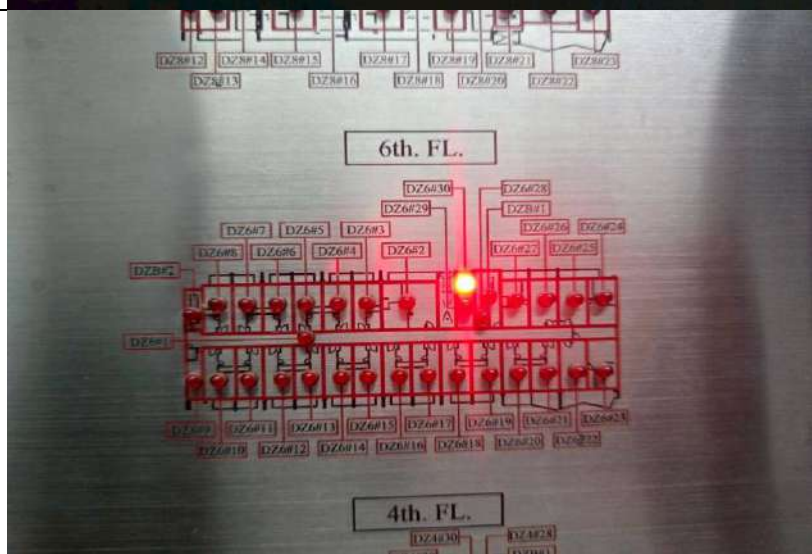



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
3	Kids Club	-	YES	-	-	
3	Lift Staff-3	-	YES	-	-	
4	Lift Staff-4	-	YES	-	-	
5	Lift Staff-5	-	YES	-	-	
6	Lift Staff-6	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ3#18	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ3#30	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ4#30	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ5#30	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ6#30	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Banbhot Sunyaphap (Security Officer)

Mr . Adipong Pareesen (Security Supervisor)

(01 September 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(01 September 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 08 September 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#7/8/9)
 - room 721/1 - room 721/2 - Lift Staff-7
 - Lift Staff-8 - Lift Staff-9
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

room 721/1


Location / Dectector
activated



Fire Control Panel



Annunciator

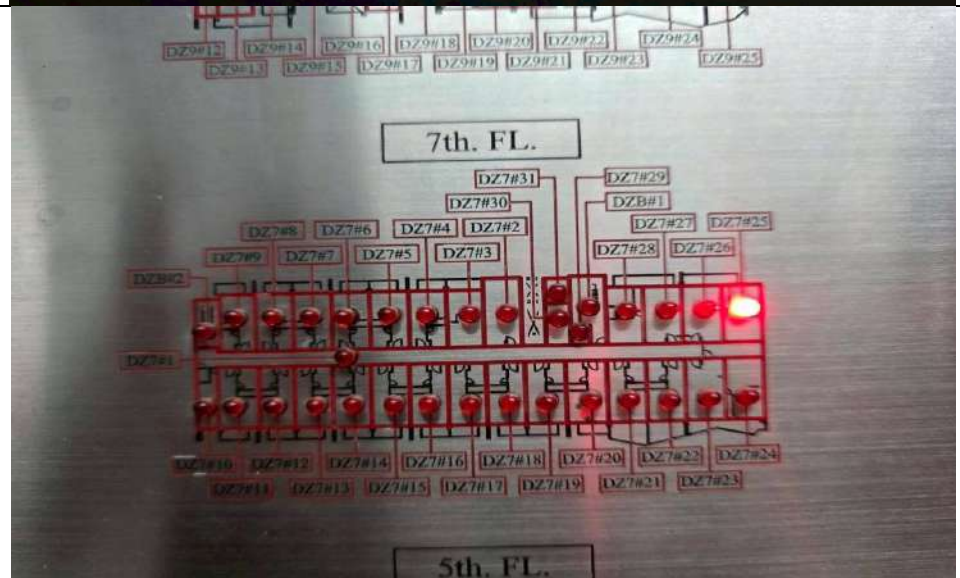

room 721/2


Location / Dectector
activated



Fire Control Panel



Annunciator

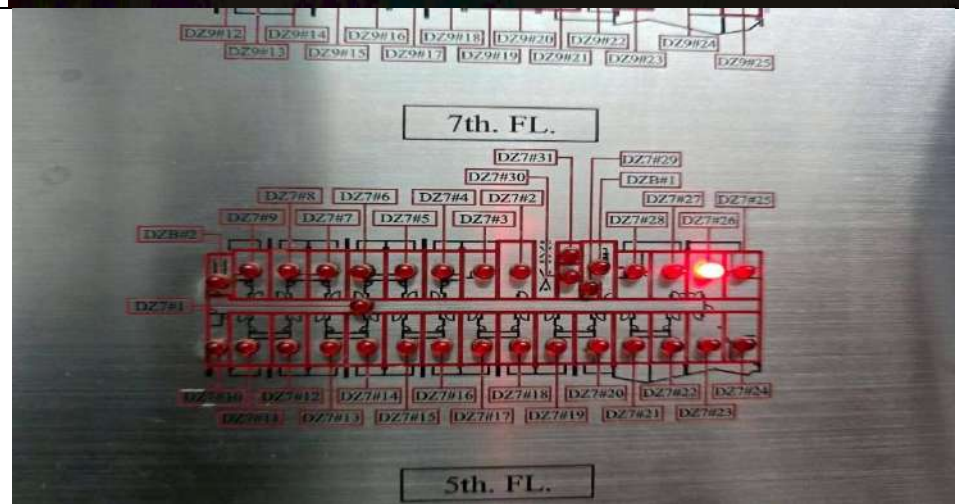

Lift Staff-7


Location / Dectector
activated



Fire Control Panel




Annunciator

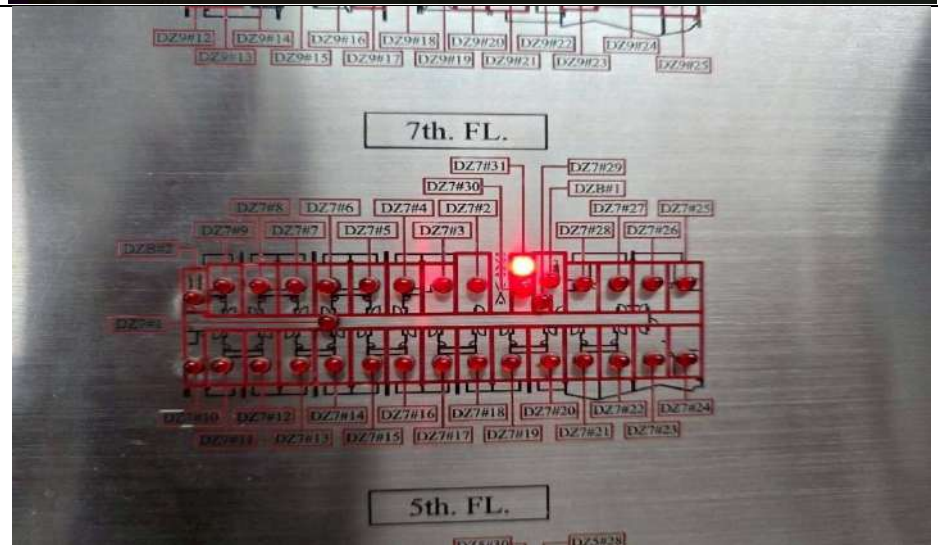

Lift Staff-8


Location / Dectector
activated

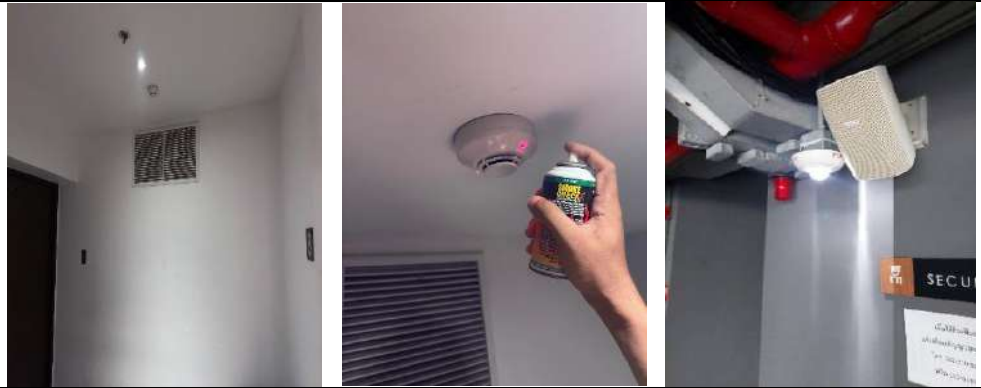

Fire Control Panel




Annunciator

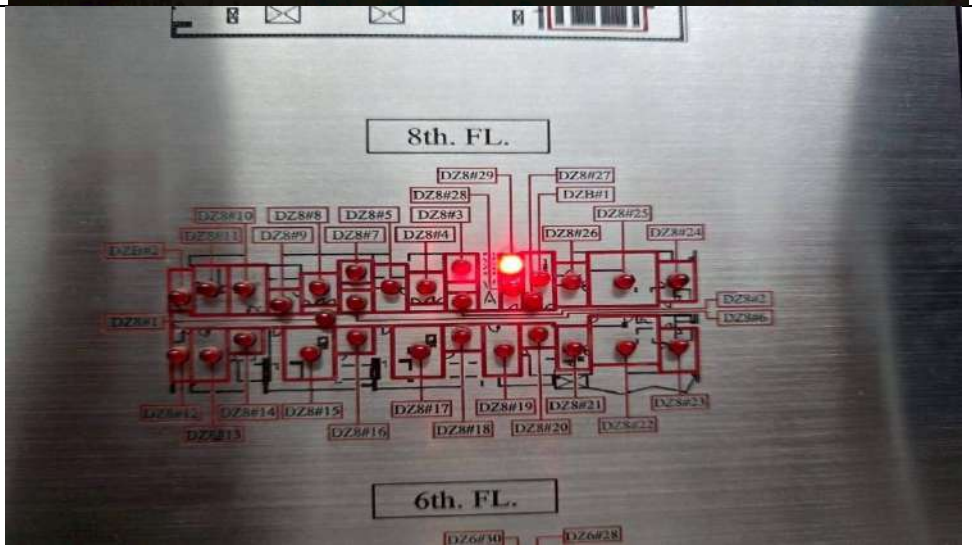

Lift Staff-9


Location / Dectector
activated

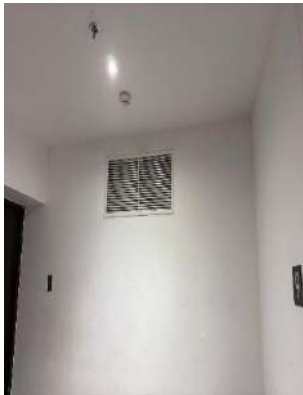

Fire Control Panel



Annunciator

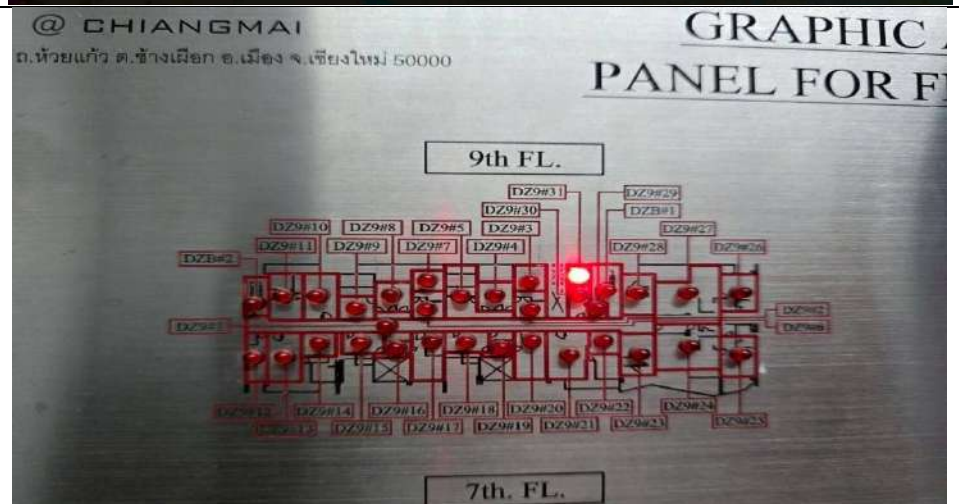



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
7	room 721/1	-	YES	-	-	
7	room 721/2	-	YES	-	-	
7	Lift Staff-7	-	YES	-	-	
8	Lift Staff-8	-	YES	-	-	
9	Lift Staff-9	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ7#25	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#26	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#31	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ8#29	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ9#31	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Pratchayarat Thongdee (Security Officer)

Mr . Adipong Pareesen (Security Supervisor)

(08 September 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(08 September 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System


Date: 08 September 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#7/8/9)
 - room 721/1 - room 721/2 - Lift Staff-7
 - Lift Staff-8 - Lift Staff-9
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

room 721/1


Location / Dectector
activated

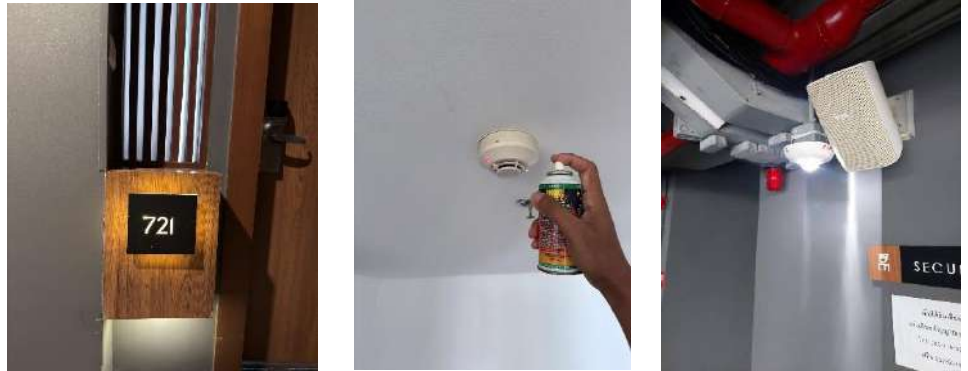

Fire Control Panel



Annunciator

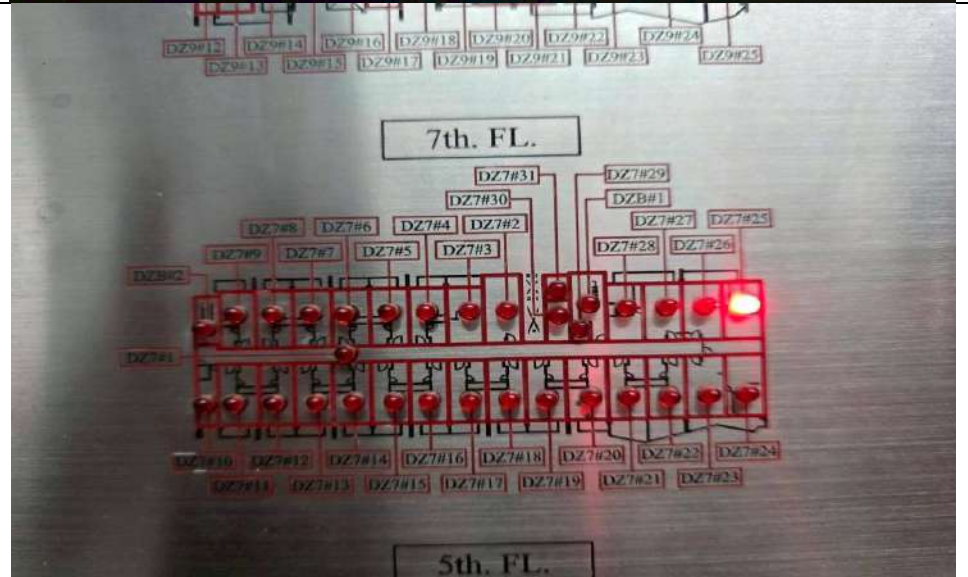

room 721/2


Location / Dectector
activated



Fire Control Panel



Annunciator

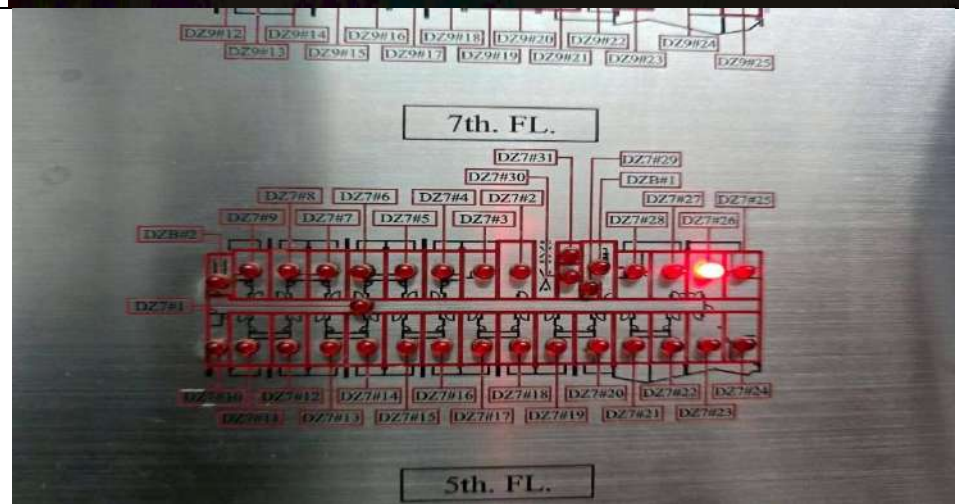

Lift Staff-7


Location / Dectector
activated



Fire Control Panel




Annunciator

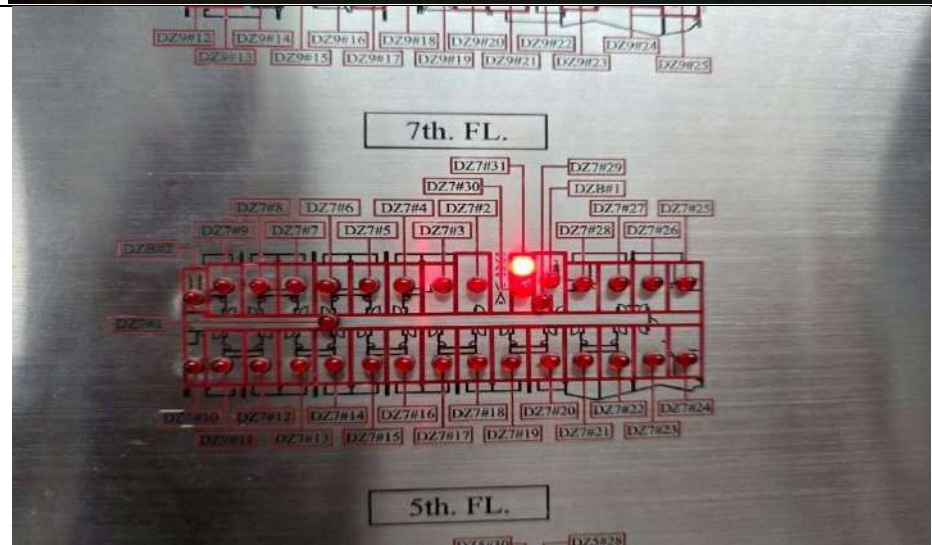

Lift Staff-8


Location / Dectector
activated

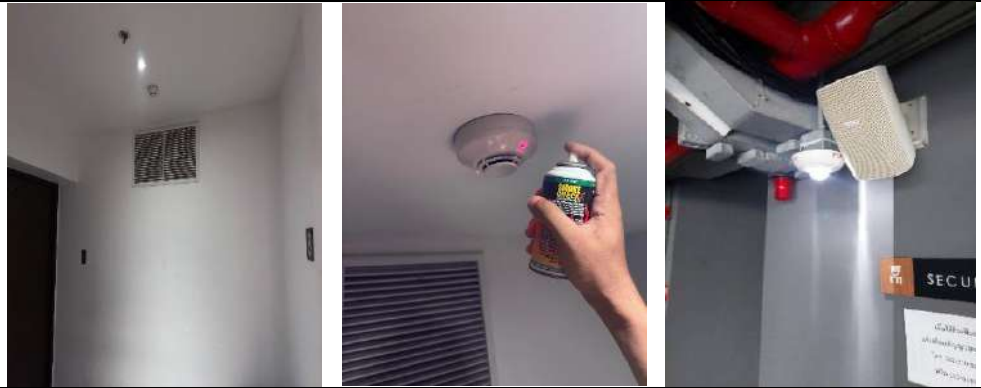

Fire Control Panel




Annunciator

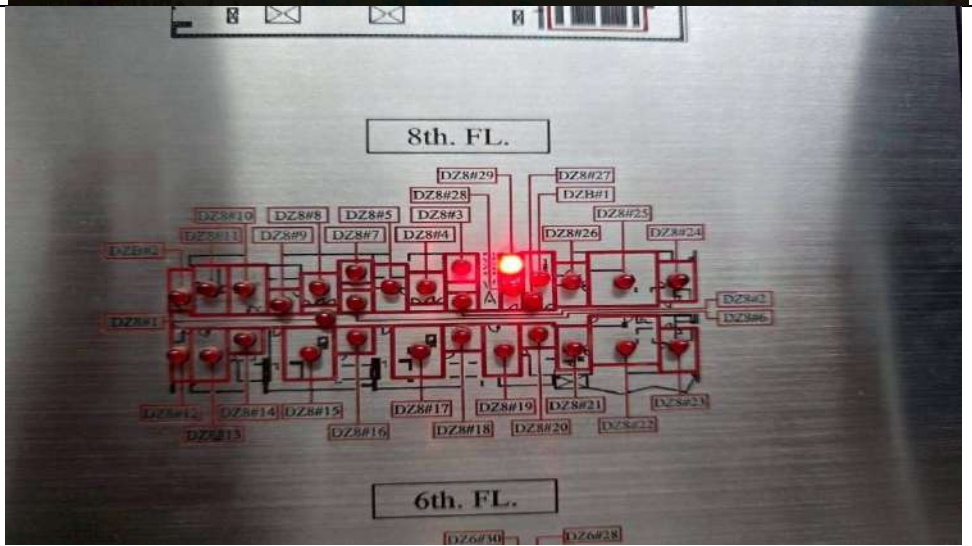

Lift Staff-9


Location / Dectector
activated

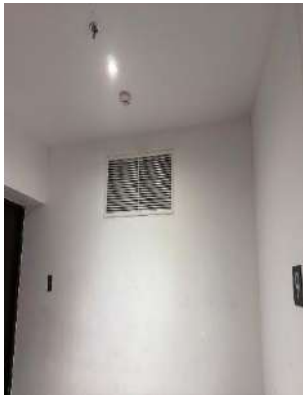

Fire Control Panel



Annunciator

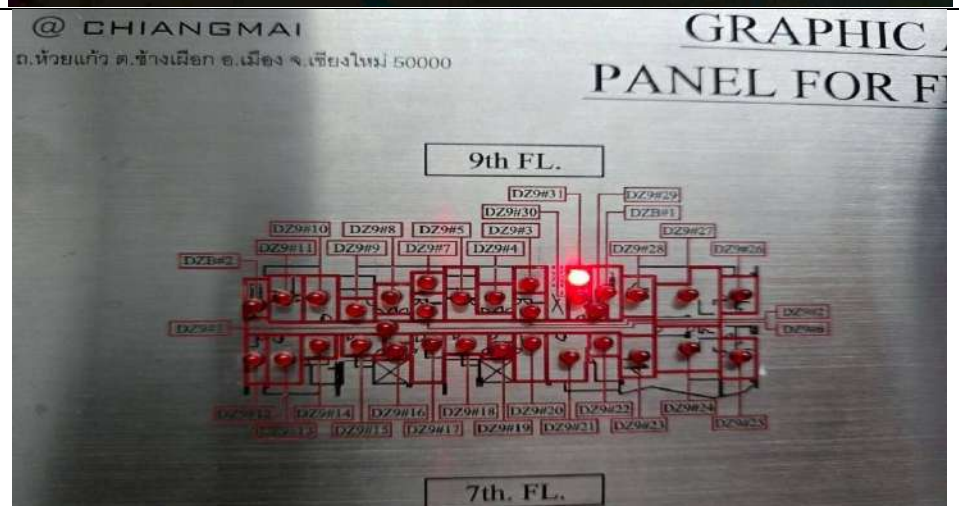



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
7	room 721/1	-	YES	-	-	
7	room 721/2	-	YES	-	-	
7	Lift Staff-7	-	YES	-	-	
8	Lift Staff-8	-	YES	-	-	
9	Lift Staff-9	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ7#25	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#26	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#31	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ8#29	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ9#31	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Pratchayarat Thongdee (Security Officer)

Mr . Adipong Pareesen (Security Supervisor)

(08 September 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(08 September 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 14 September 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#4/5/7)
 - room 402 - room 505 - room 507
 - room 703 - room 706
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

room 402


Location / Dectector
activated



Fire Control Panel



Annunciator

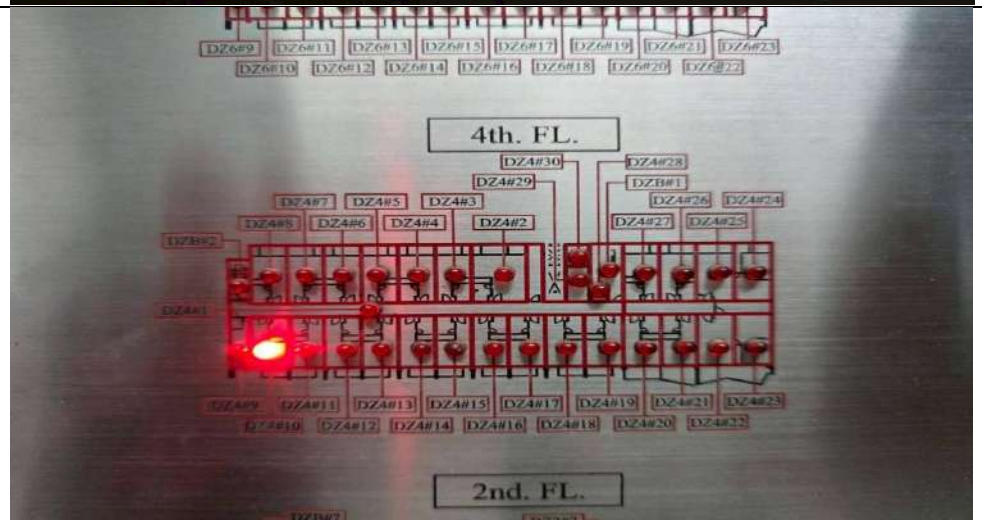

room 505


**Location / Dectector
activated**



Fire Control Panel




Annunciator

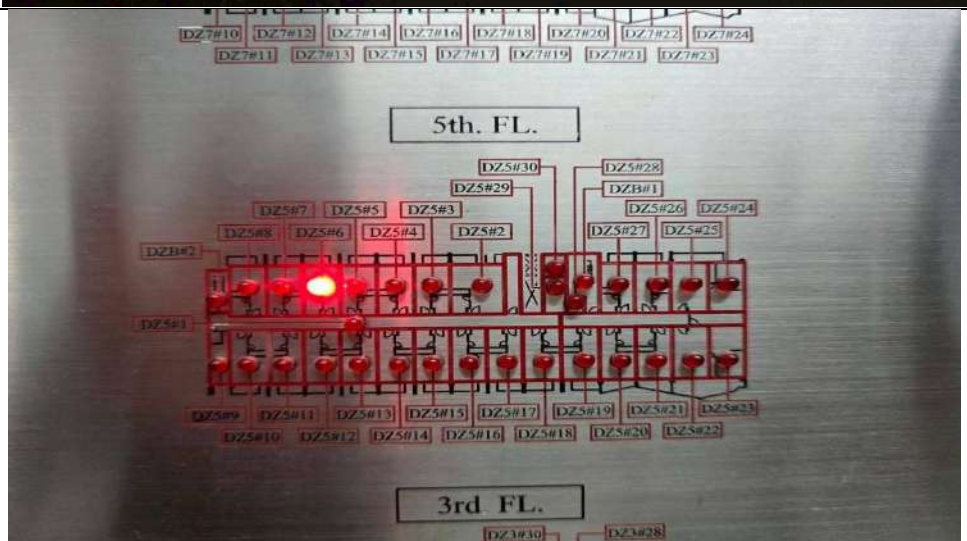

Room 507


Location / Detector activated

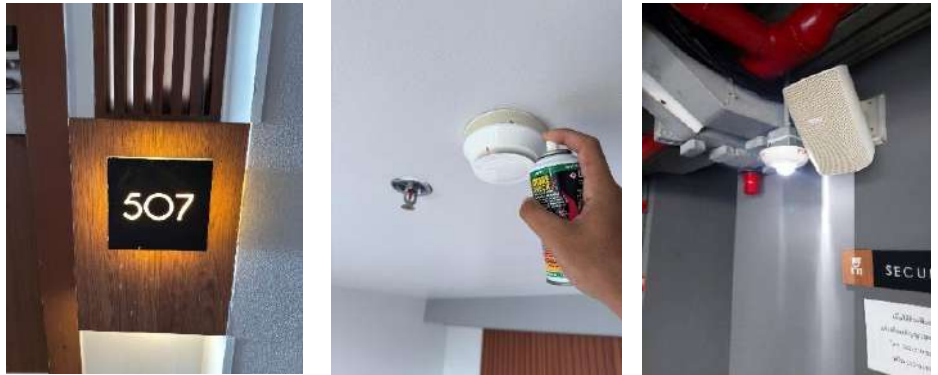

Fire Control Panel



Annunciator

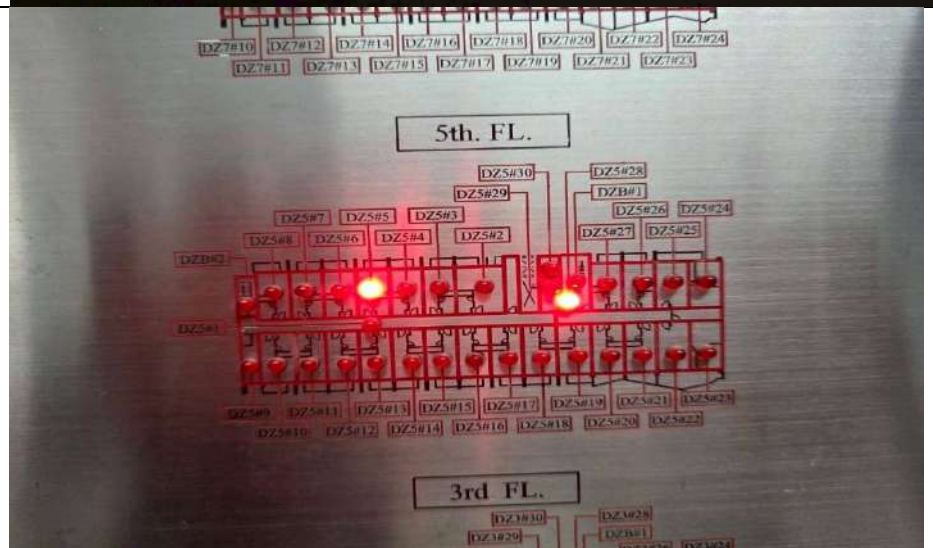

Room 703


Location / Dectector activated



Fire Control Panel



Annunciator

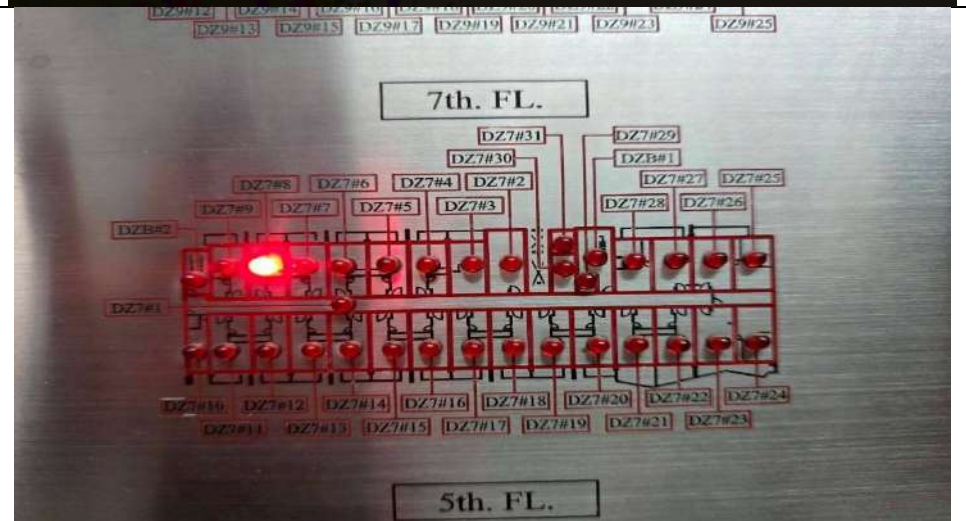

Room 706


Location / Dectector
activated



Fire Control Panel



Annunciator

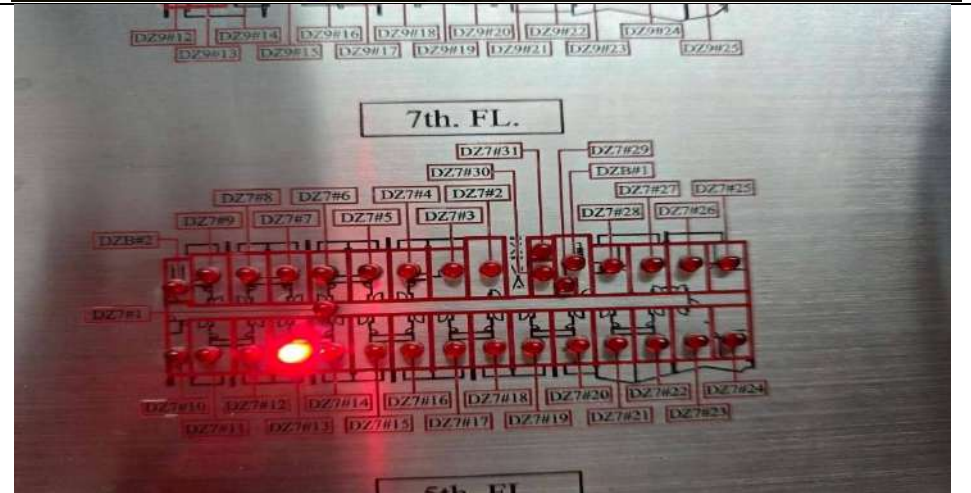



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
4	room 402	-	YES	-	-	
5	room 505	-	YES	-	-	
5	Room 507	-	YES	-	-	
7	Room 703	-	YES	-	-	
7	Room 706	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ4#10	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ5#6	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ5#5	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#8	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#13	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Pratchayarat Thongdee (Security Officer)

Mr. Adipong Pareesen (Security Supervisor)

(14 September 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(14 September 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 14 September 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#4/5/7)
 - room 402 - room 505 - room 507
 - room 703 - room 706
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

room 402


Location / Dectector
activated



Fire Control Panel



Annunciator

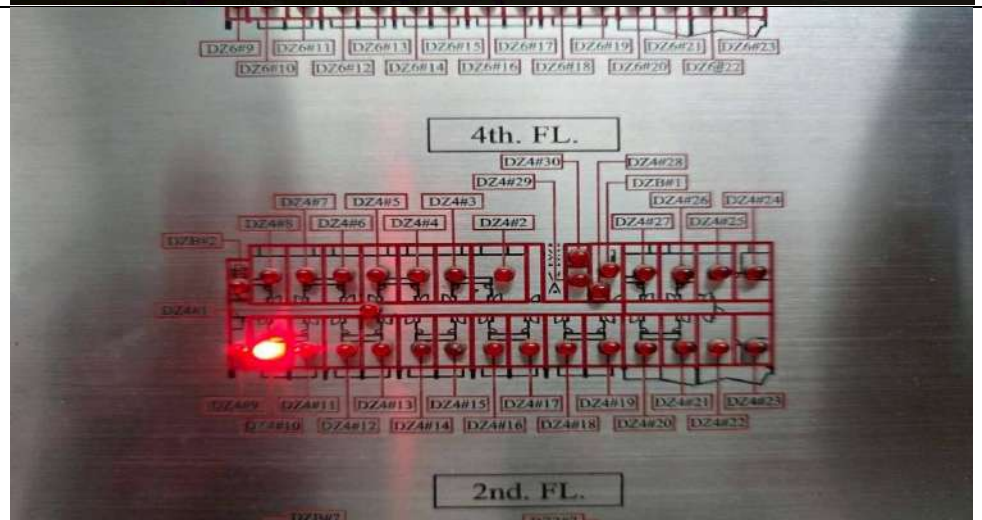

room 505


**Location / Dectector
activated**



Fire Control Panel




Annunciator

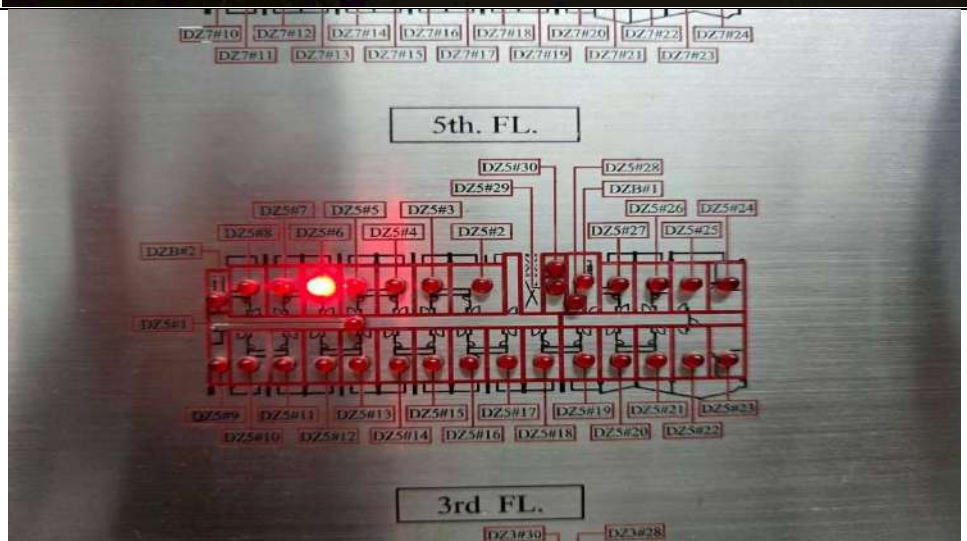

Room 507


Location / Detector activated

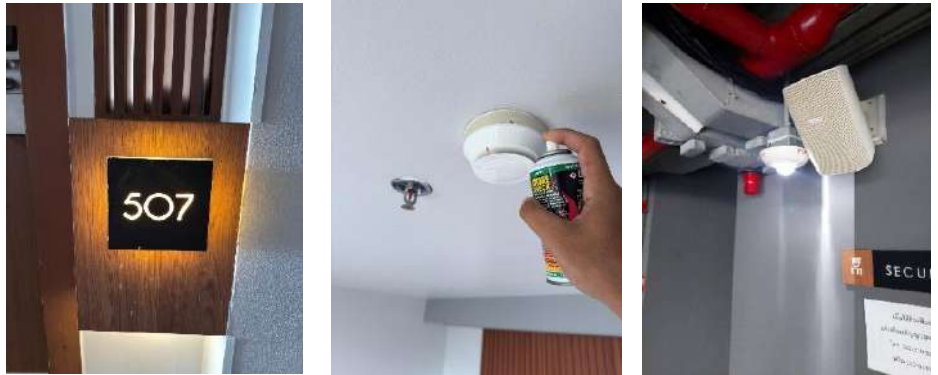

Fire Control Panel



Annunciator

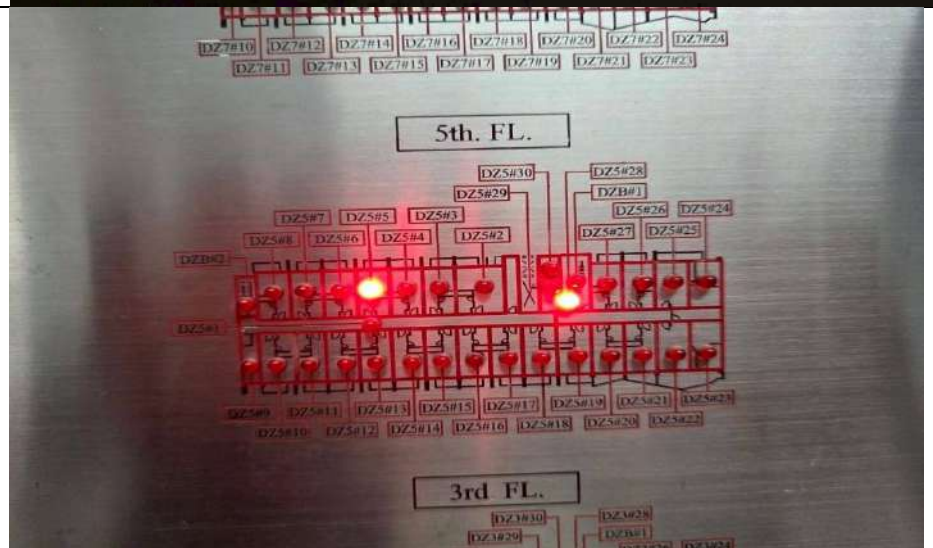

Room 703


**Location / Dectector
activated**



Fire Control Panel



Annunciator

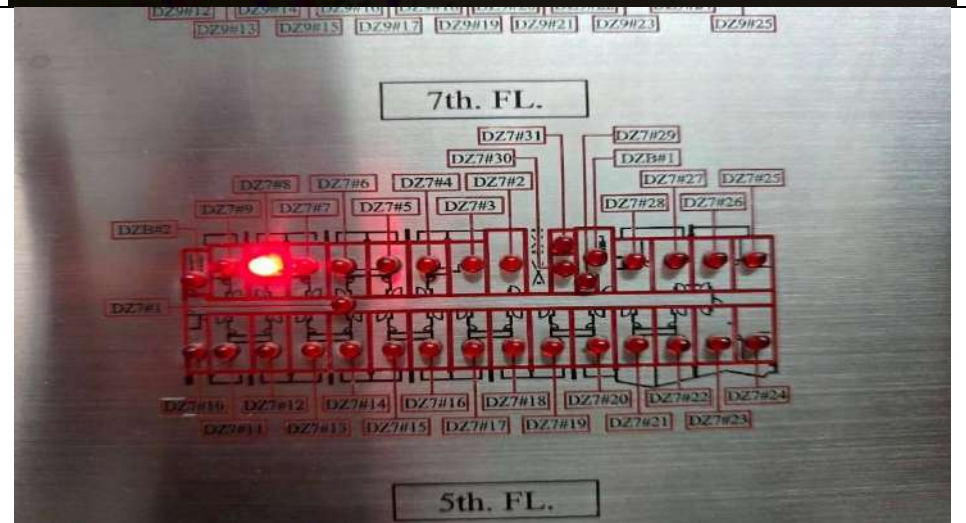

Room 706


Location / Detector activated



Fire Control Panel



Annunciator

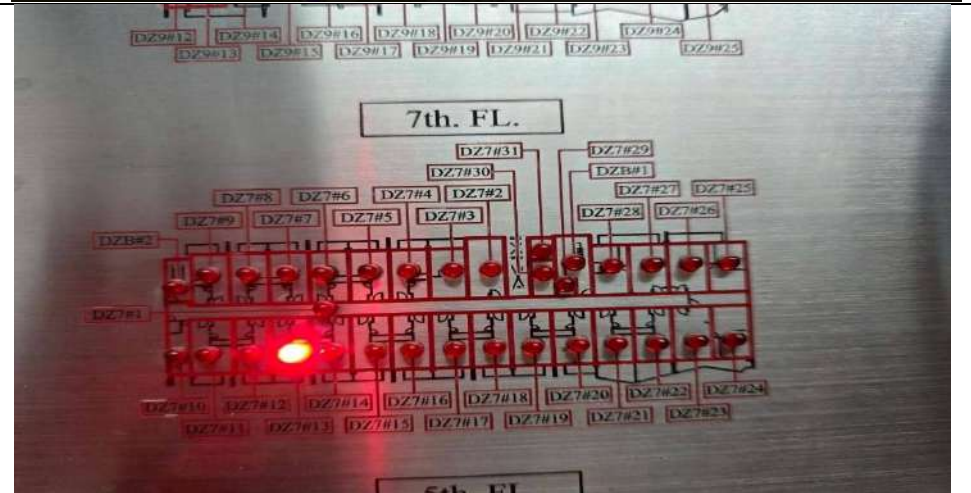



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
4	room 402	-	YES	-	-	
5	room 505	-	YES	-	-	
5	Room 507	-	YES	-	-	
7	Room 703	-	YES	-	-	
7	Room 706	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ4#10	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ5#6	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ5#5	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#8	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#13	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Pratchayarat Thongdee (Security Officer)

Mr. Adipong Pareesen (Security Supervisor)

(14 September 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(14 September 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 21 September 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor #1)
 - Lift Service #1 - Lift Staff #1 - HM office #1
 - RSVN office #1
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Lift Service FL.1


Location / Dectector
activated



Fire Control Panel




Annunciator

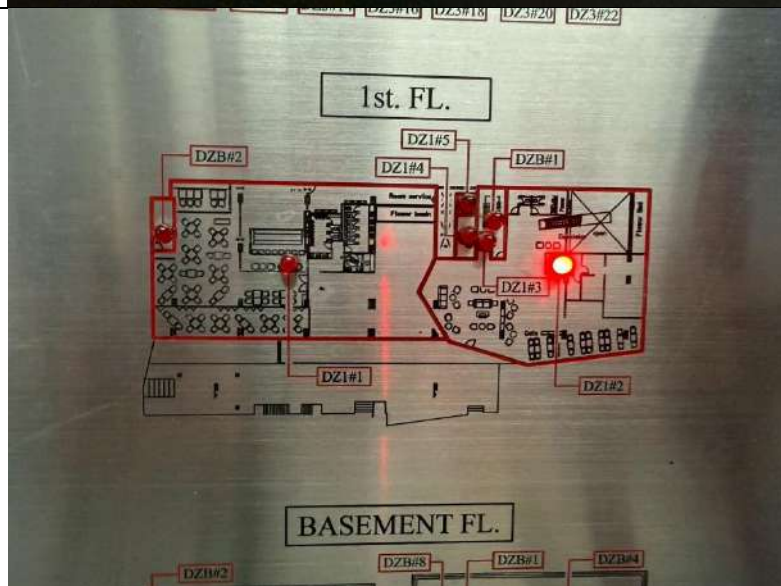

Lift Staff FL.1


Location / Dectector
activated

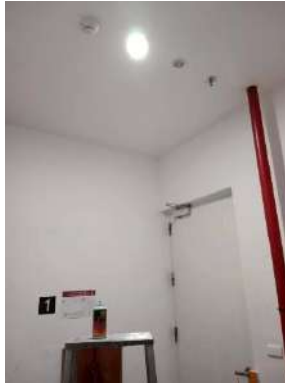


Fire Control Panel



Annunciator

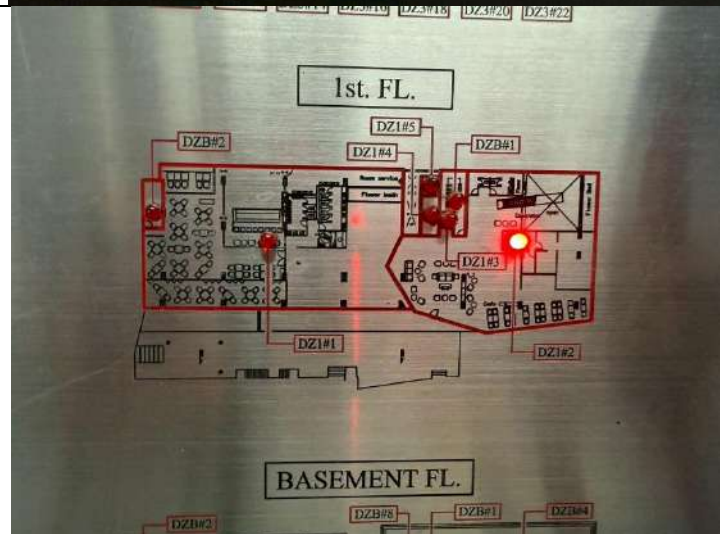

HM office FL.1

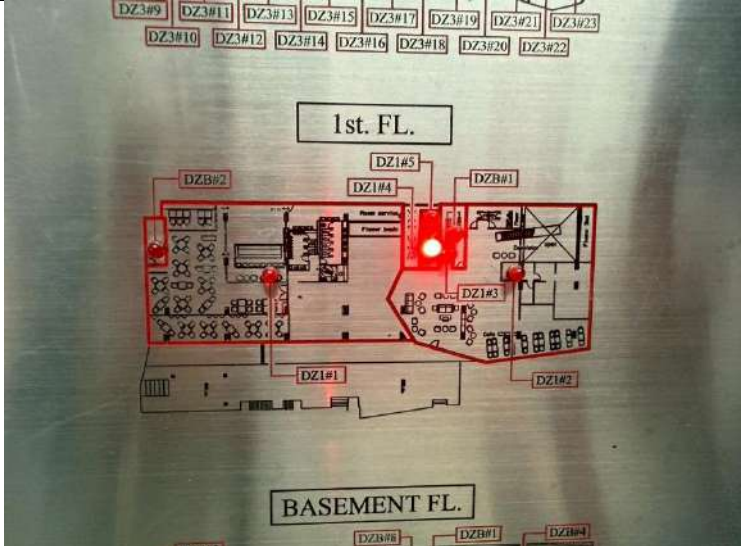Location / Dectector activated	
Fire Control Panel	
Annunciator	

RSVN office FL.1


**Location / Dectector
activated**



Fire Control Panel



Annunciator

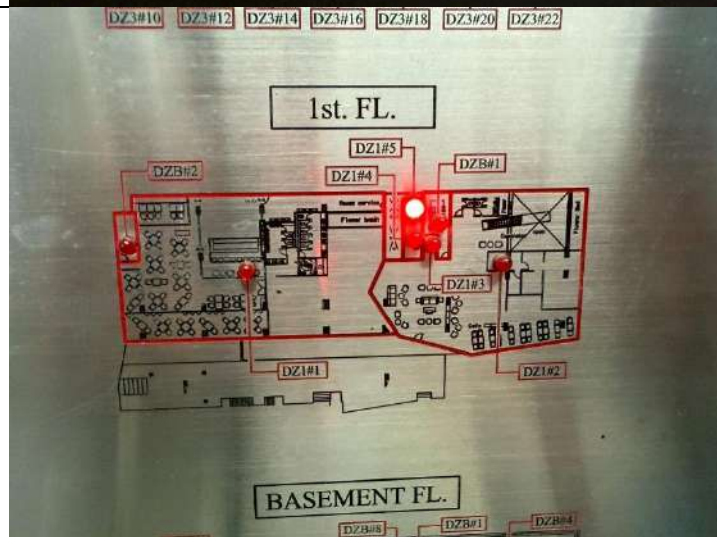



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
1	Lift Service FL.1	-	YES	-	-	
1	Lift Staff FL.1	-	YES	-	-	
1	HM office FL.1	-	YES	-	-	
1	RSVN office FL.1	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ1#2	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ1#2	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ1#4	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ1#5	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Supanut Sikanta (Security Officer)

Mr . Prasit Inta (Security Supervisor)

(21 September 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(21 September 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 05 October 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#6 Floor#7 Floor#8)
 - Room 608
 - Store Room FL.6
 - Store Room FL.7
 - Store Room FL.8
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room 608


Location / Dectector
activated



Fire Control Panel



Annunciator

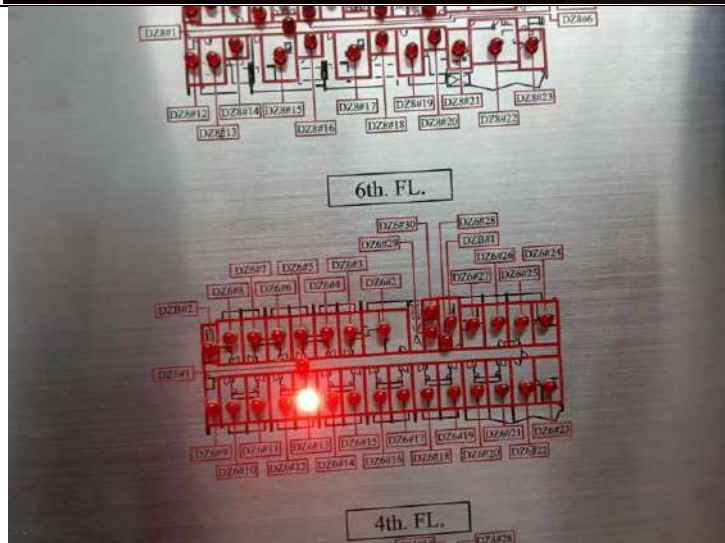

Store Room FL.6


Location / Dectector
activated



Fire Control Panel



Annunciator

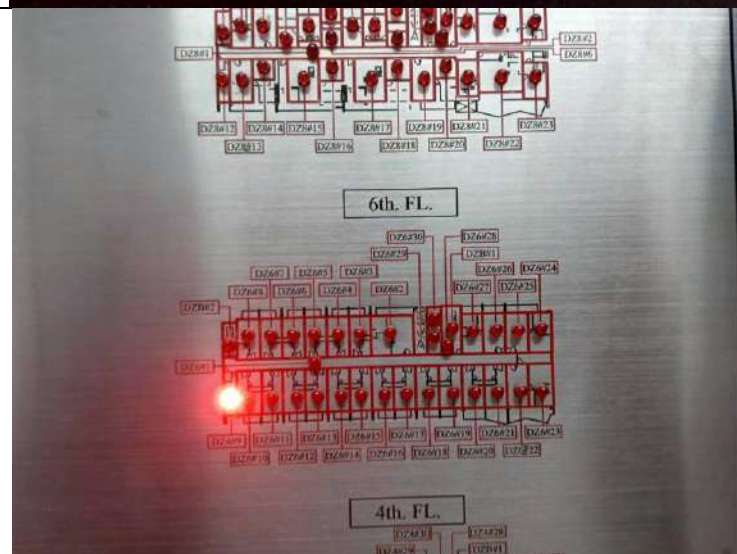

Store Room FL.7


Location / Dectector
activated



Fire Control Panel




Annunciator

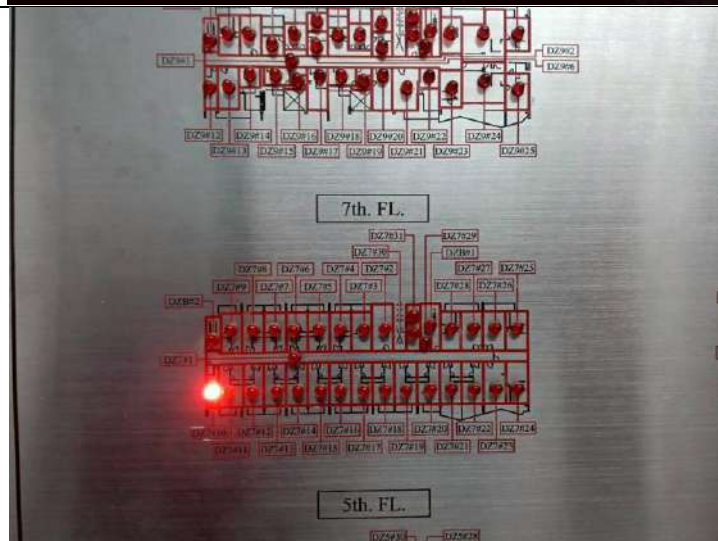


Store Room FL.8


Location / Dectector
activated

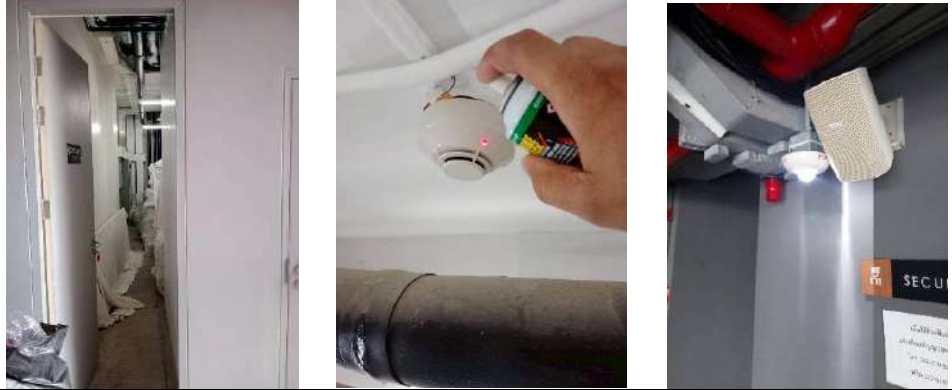

Fire Control Panel

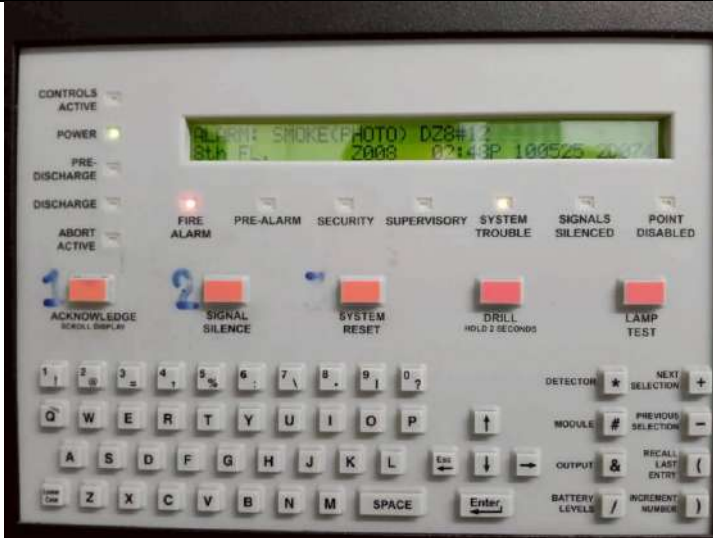

Annunciator

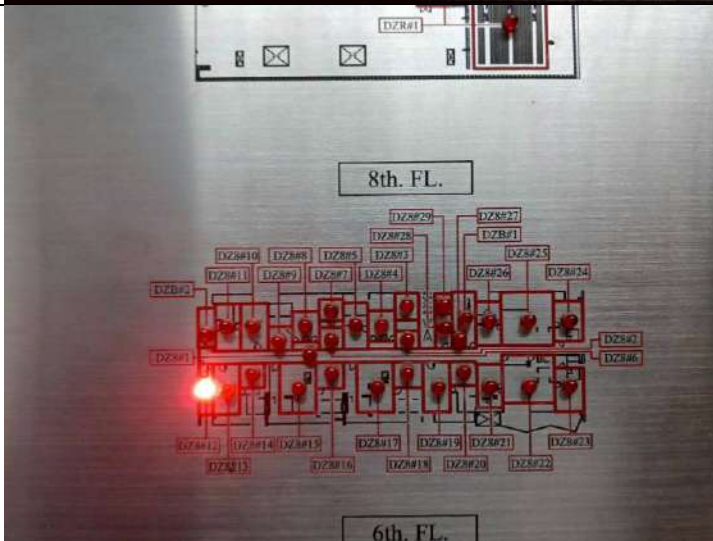



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
6	Room 608	-	YES	-	-	
6	Store Room FL.6	-	YES	-	-	
6	Store Room FL.7	-	YES	-	-	
6	Store Room FL.8	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ6#13 (608)	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ6#9 (Store Room)	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#10 (Store Room)	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ8#12 (Store Room)	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Suvaroj Lorkeawnunthakul (Security Officer)

Mr . Prasit Inta

(Security Supervisor))

(05 October 2025)

Report by: Mr. Prasit Inta

(Security Supervisor)

(05 October 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ / Automatic System ☐ Manual System

Date: 19 October 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor # 5 / 6)
 - Room 519
 - Room 620
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room 519


Location / Dectector
activated



Fire Control Panel



Annunciator

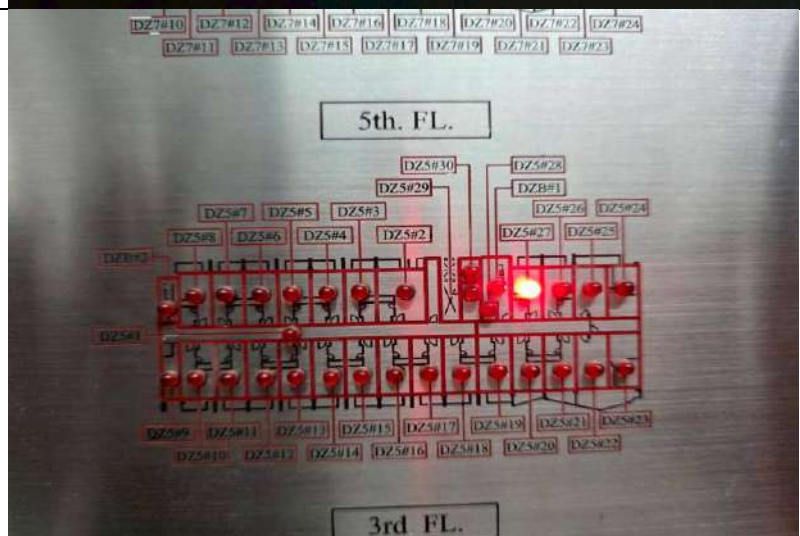

Room 620


Location / Dectector
activated



Fire Control Panel



Annunciator

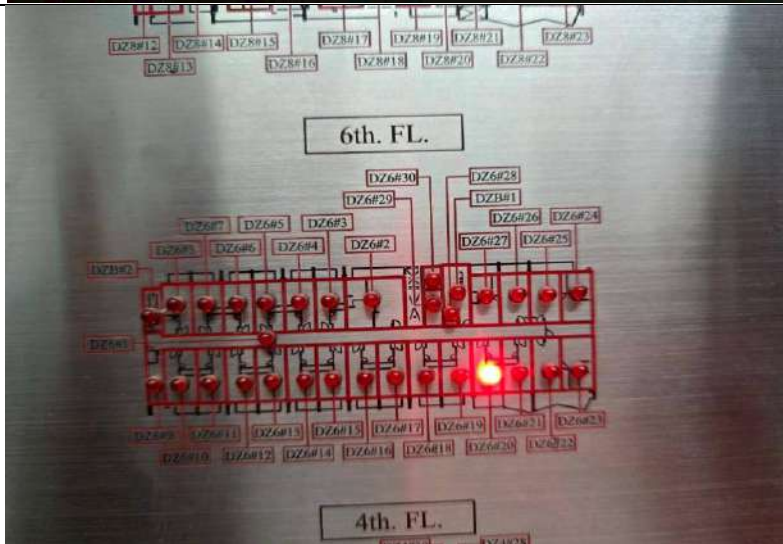

Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
5	Room 519	-	YES	-	-	
6	Room 620	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ5#27	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ6#20	YES	YES	/	-	/	-	/	-	/	-	-	/



Tested by: Mr. Banbhot Sunyaphap (Security Officer)

Mr . Adipong Pareesen (Security Supervisor)

(19 October 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(19 October 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ / Automatic System ☐ Manual System

Date: 20 October 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor # 3 / 4)
 - Pantry Floor-3
 - Pantry Floor-4
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Pantry Floor-3


Location / Dectector
activated



Fire Control Panel



Annunciator

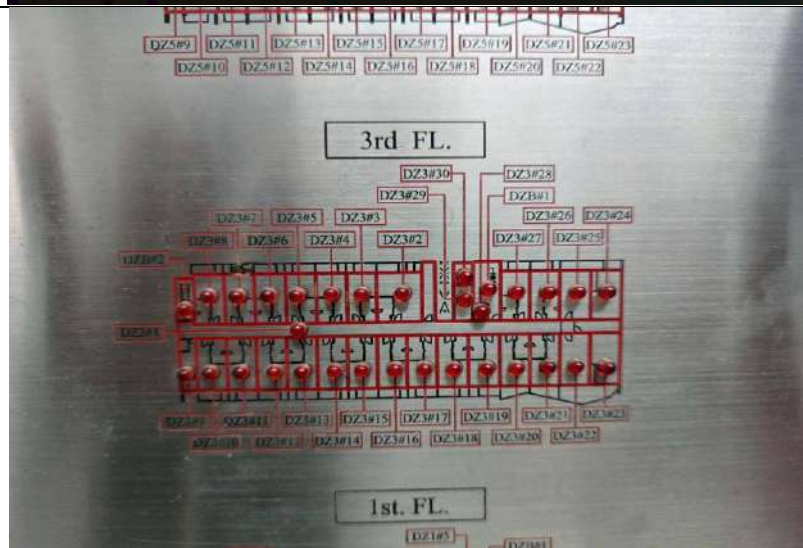

Pantry Floor-3


Location / Dectector
activated



Fire Control Panel



Annunciator

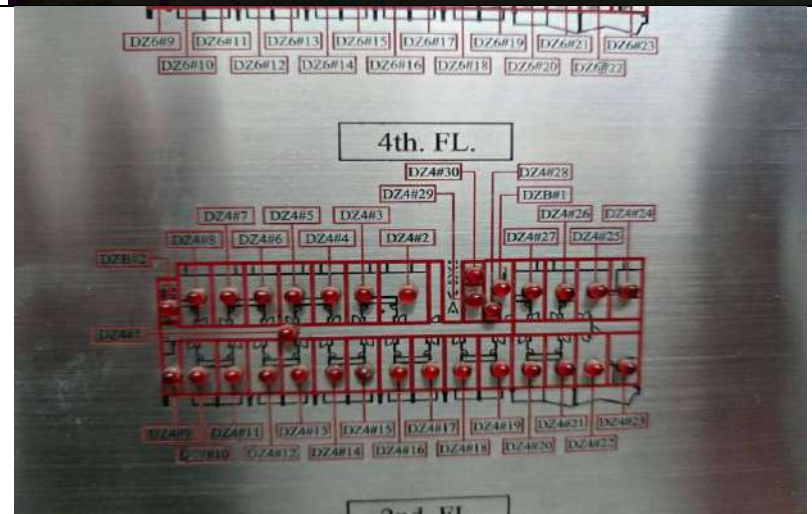

Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
3	Pantry Floor-3	-	No	-	-	
4	Pantry Floor-4	-	No	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
Pantry Floor-3	No	No	/	-	/	-	/	-	/	-	-	/
Pantry Floor-4	No	No	/	-	/	-	/	-	/	-	-	/



Tested by: Mr. Banbhot Sunyaphap (Security Officer)

Mr . Adipong Pareesen (Security Supervisor)

(20 October 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(20 October 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 28 October 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#B)
 - Accounting Officer - Engineer Officer
 - Housekeeping Officer
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Accounting Officer FL.B


Location / Dectector
activated



Fire Control Panel




Annunciator

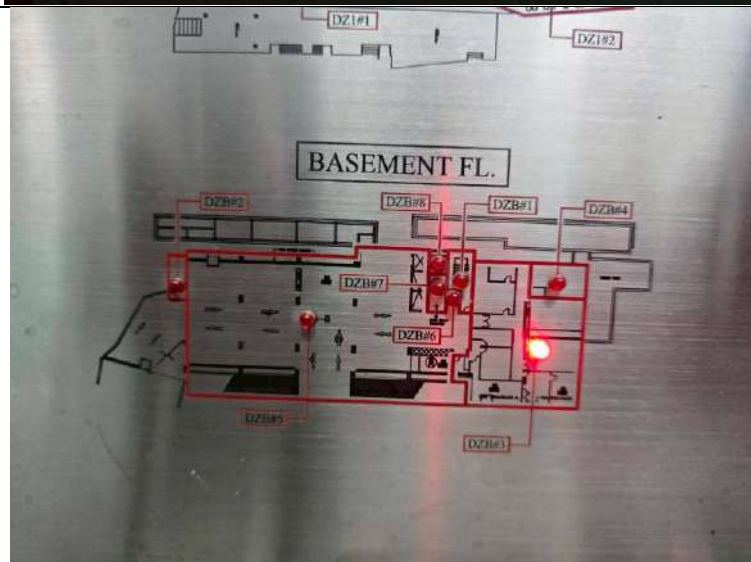

Engineer Officer FL.B


**Location / Dectector
activated**

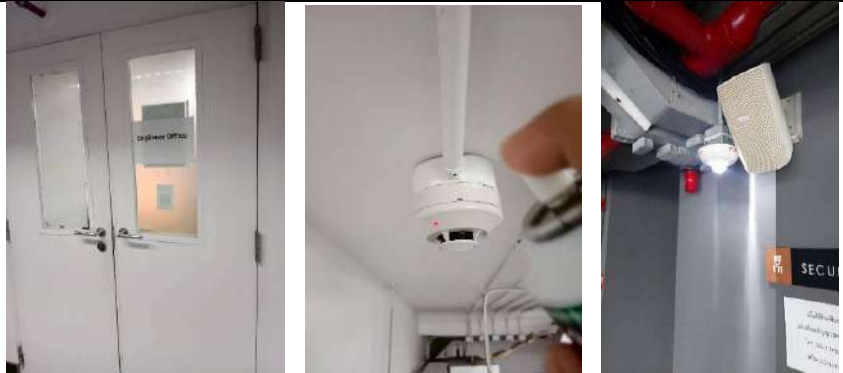

Fire Control Panel



Annunciator

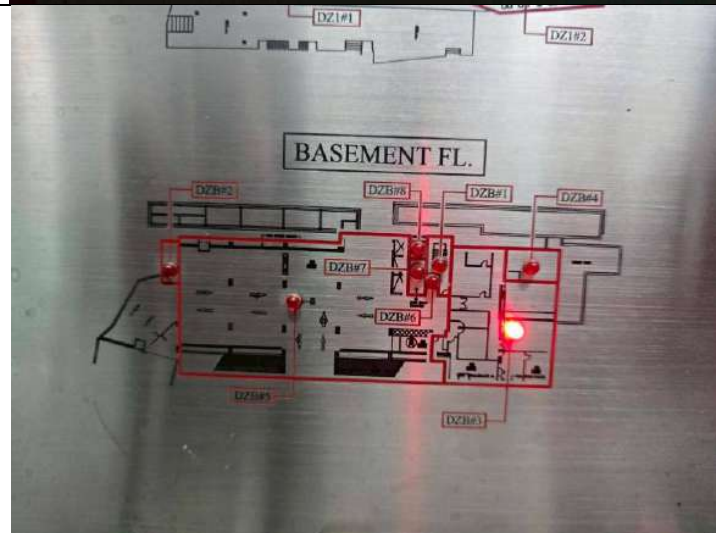

Housekeeping Officer FL.B 1


**Location / Dectector
activated**



Fire Control Panel



Annunciator

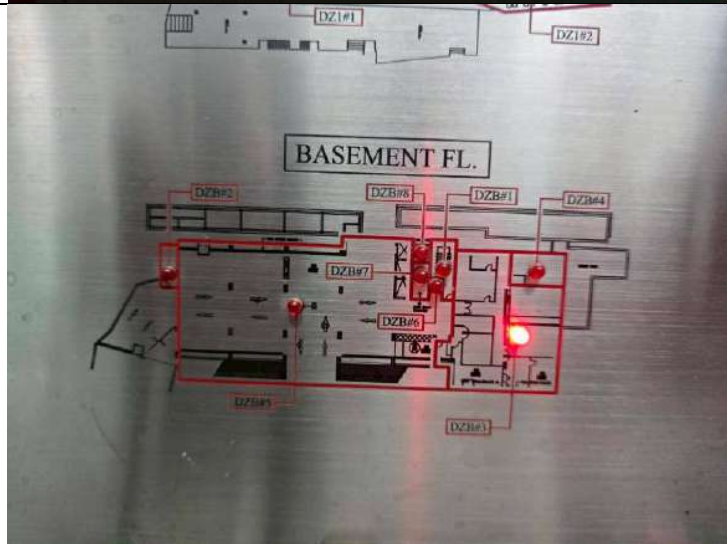

Housekeeping Officer FL.B 2


**Location / Dectector
activated**



Fire Control Panel



Annunciator

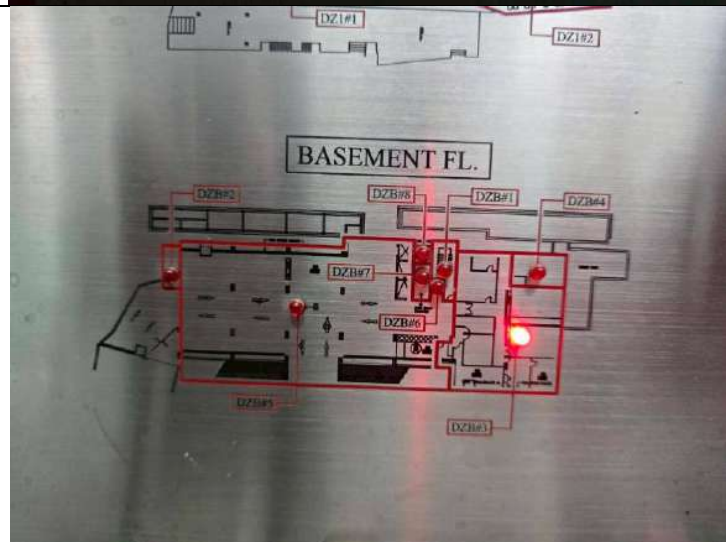



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
B	Accounting Officer	-	YES	-	-	
B	Engineer Officer	-	YES	-	-	
B	Housekeeping Officer 1	-	YES	-	-	
B	Housekeeping Officer 2	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Prasit Inta

(Security Supervisor)

Mr.Adipong Pareesen

(Security Supervisor)

(28 October 2025)

Report by: Mr. Prasit Inta

(Security Supervisor)

(28 October 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 04 November 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#5#B)
 - Room 518
 - T-Canteen 1/1
 - T-Canteen1/2
 - Hunan Resources Officer
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room 518


Location / Dectector
activated



Fire Control Panel



Annunciator

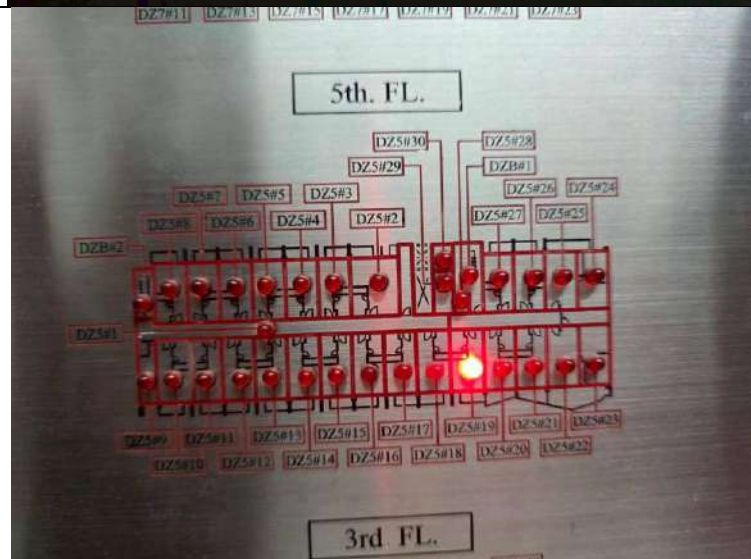

T-Canteen FL.B 1/1


**Location / Dectector
activated**



Fire Control Panel



Annunciator

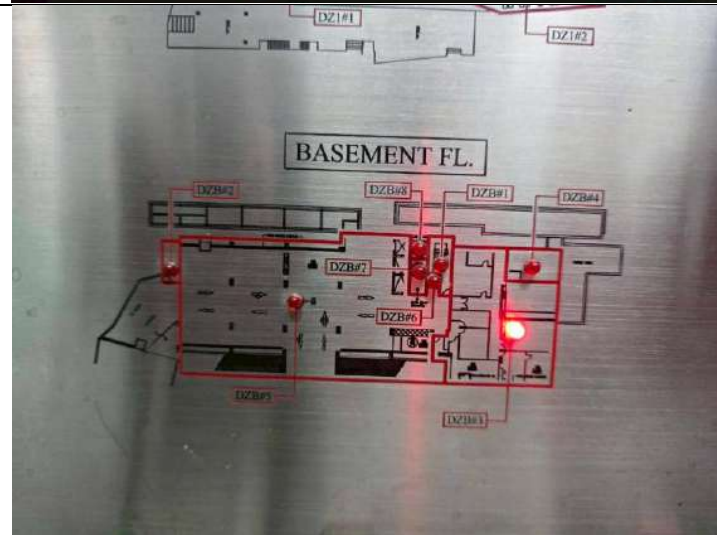

T-Canteen FL.B 1/2


Location / Dectector
activated



Fire Control Panel



Annunciator

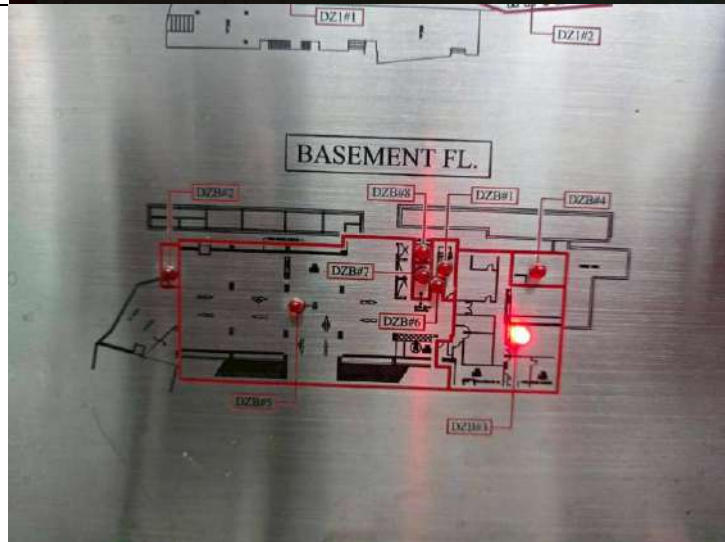

Hunan Resources Officer FL.B


**Location / Dectector
activated**



Fire Control Panel



Annunciator

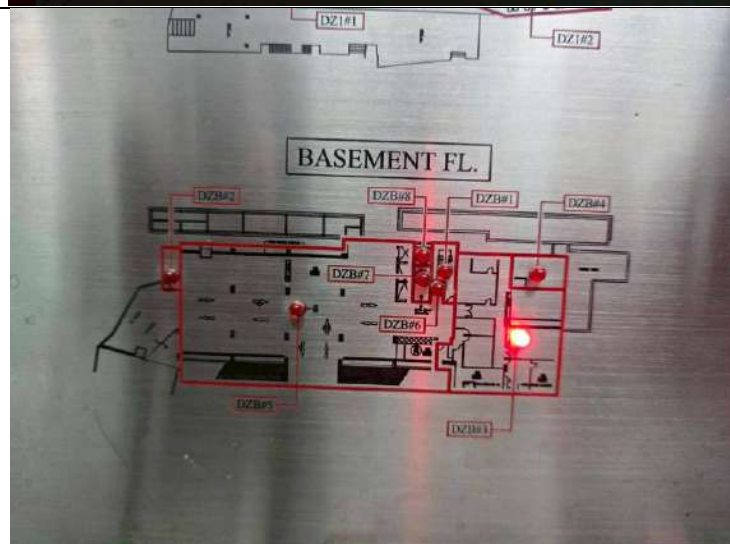



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
5	Room 518	-	YES	-	-	
B	T-Canteen 1/1	-	YES	-	-	
B	T-Canteen 1/2	-	YES	-	-	
B	Hunan Resources	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ5#19	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Prasit Inta

(Security Supervisor)

Mr.Adipong Pareesen

(Security Supervisor)

(04 November 2025)

Report by: Mr. Prasit Inta

(Security Supervisor)

(04 November 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 09 November 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#6/7/8/9)
 - Room control FL.6
 - Room control FL.7
 - Room control FL.8
 - Room control FL.9
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room control FL.6


Location / Dectector
activated



Fire Control Panel



Annunciator

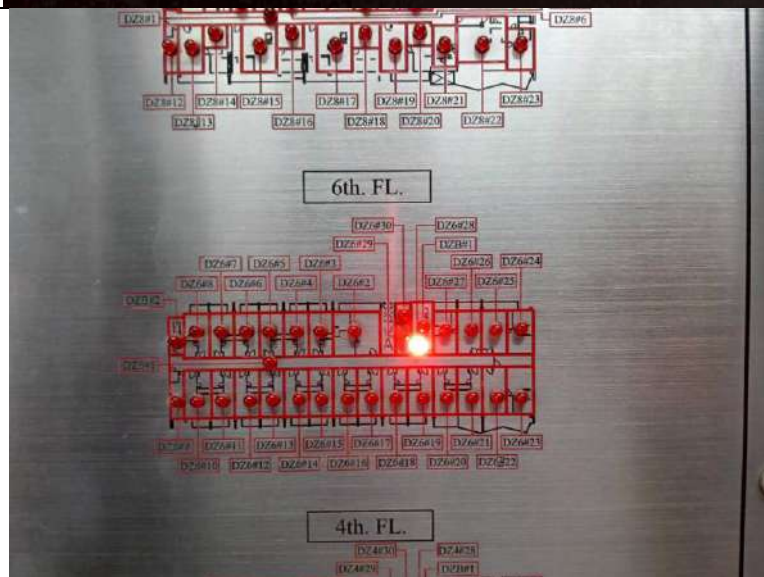

Room control FL.7


Location / Dectector
activated



Fire Control Panel



Annunciator

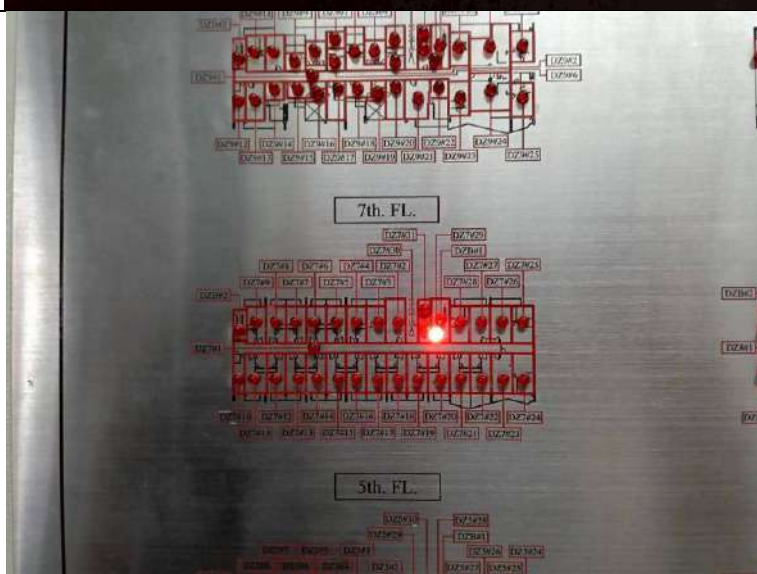


Room control FL.8


Location / Dectector
activated



Fire Control Panel

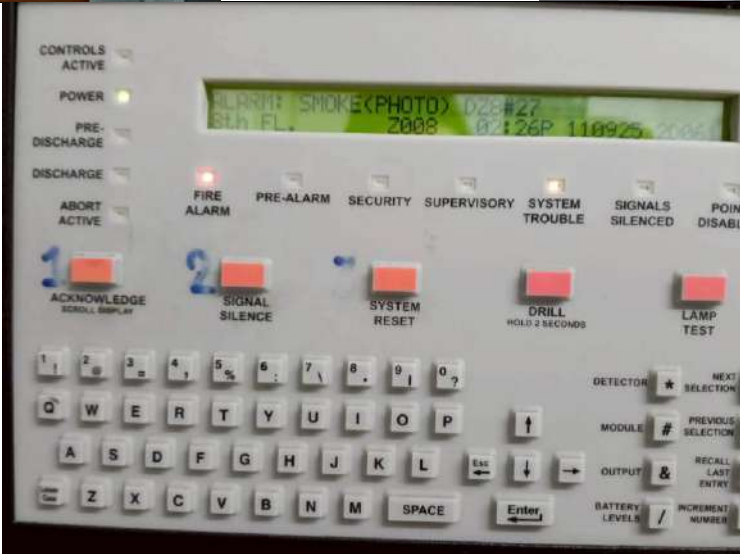

Annunciator

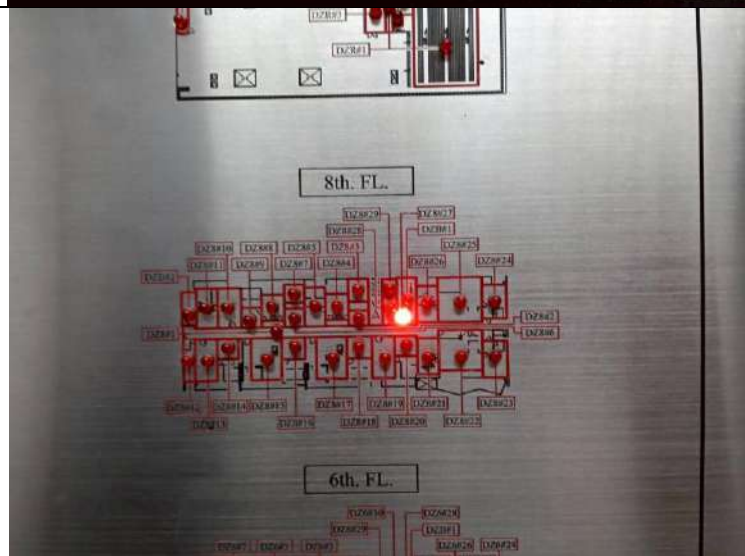

Room control FL.9


**Location / Dectector
activated**



Fire Control Panel



Annunciator

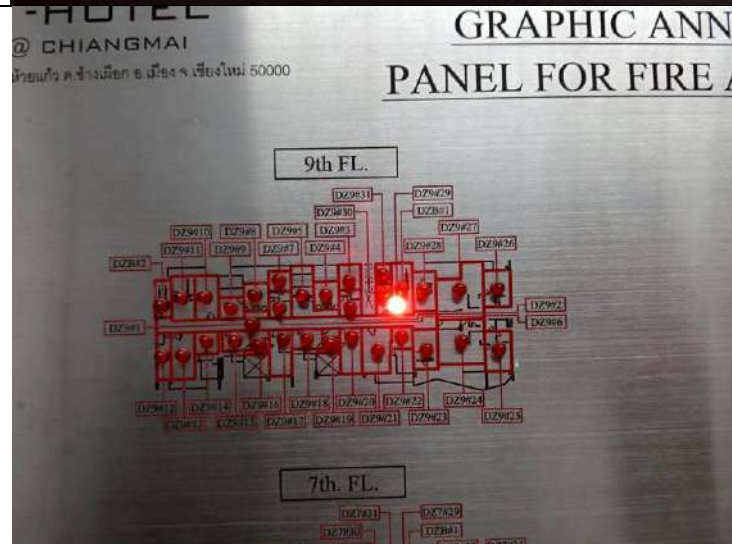



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
6	Room control 6	-	YES	-	-	
7	Room control 7	-	YES	-	-	
8	Room control 8	-	YES	-	-	
9	Room control 9	-	YES	-	-	



FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ6#28	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ7#29	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ8#27	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ9#29	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Suvaroj Lorkeawnunthakul (Security Officer)

Mr. Prasit Inta (Security Supervisor)

(09 November 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(09 November 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☐ / Automatic System ☐ Manual System

Date: 16 November 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor # B / G)
 - Control Room B
 - Control Room G
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Control Room B

Location / Dectector
activated



Fire Control Panel



Annunciator



Control Room G


Location / Dectector
activated



Fire Control Panel



Annunciator

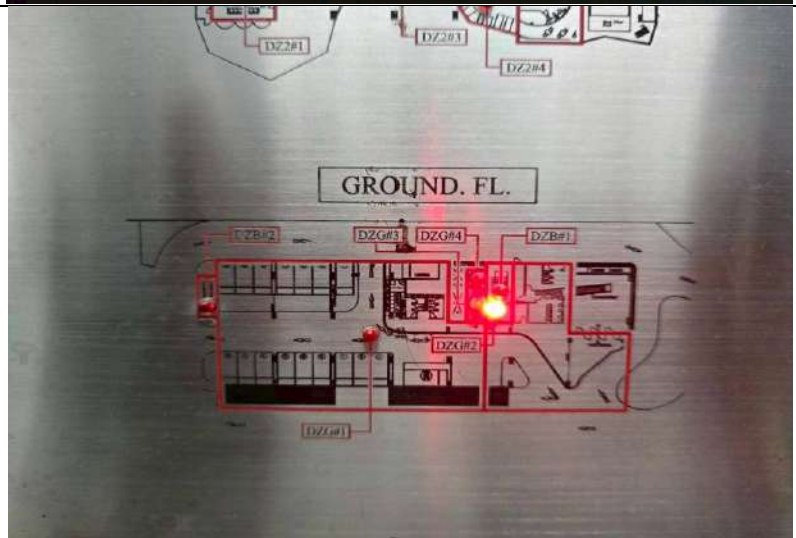



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
5	Control Room B	-	YES	-	-	
6	Control Room G	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZB#6	YES	YES	/	-	/	-	/	-	/	-	-	/
DZG#2	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Banbhot Sunyaphap (Security Officer)

Mr . Adipong Pareesen (Security Supervisor)

(16 Novemberr 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(16 November 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System


Date: 22 November 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#3)
- Room 305 - Room control FL.3
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Room 305


Location / Dectector
activated

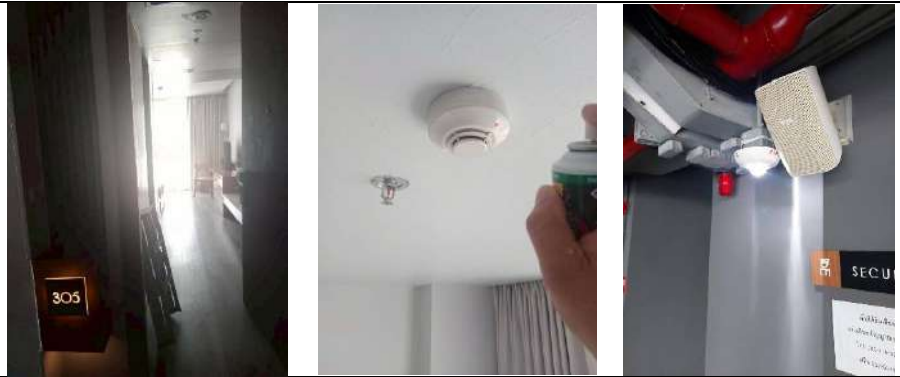

Fire Control Panel



Annunciator

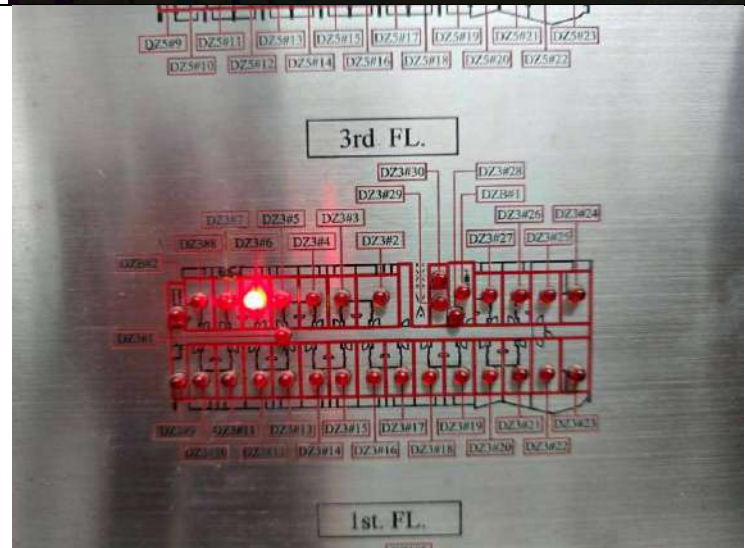

Room control FL.3


Location / Dectector activated



Fire Control Panel



Annunciator

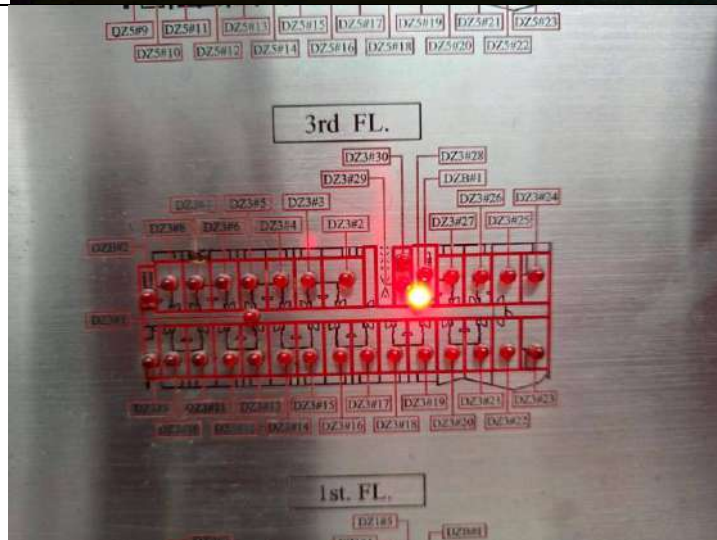



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
3	Room 305	-	YES	-	-	
3	Room control FL.3	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ3#6	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ3#28	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Prasit Inta

(Security Supervisor)

Mr.Adipong Pareesen

(Security Supervisor)

(22 November 2025)

Report by: Mr. Prasit Inta

(Security Supervisor)

(22 November 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 07 December 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#5)
 - Control room FL.5
 - Pantry FL.5
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Control Room FL.5

Location / Dectector
activated



Fire Control Panel



Annunciator



Pantry FL.5


Location / Dectector activated



Fire Control Panel



Annunciator

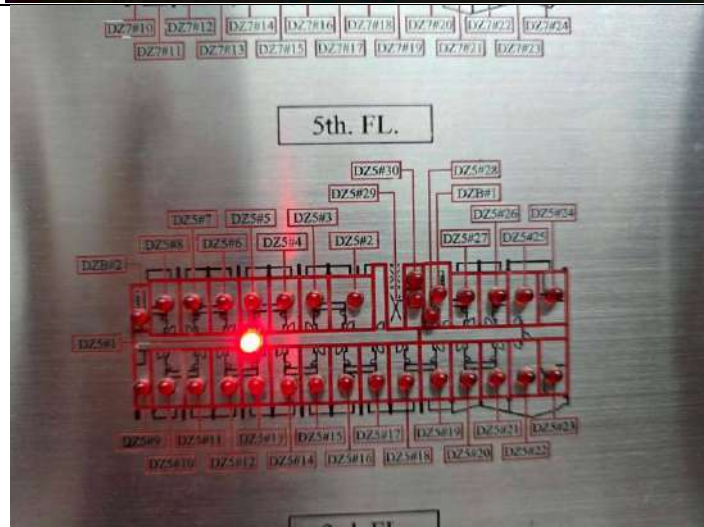



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
5	Control Room 5	-	YES	-	-	ดูอนันท์ไม่แสดงผล
5	Pantry FL.5	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ5#28	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ5#1	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Prasit Inta

(Security Supervisor)

Mr.Adipong Pareesen

(Security Supervisor)

(07 December 2025)

Report by: Mr. Prasit Inta

(Security Supervisor)

(07 December 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ / Automatic System ☐ Manual System

Date: 14 December 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#5)
- Store Floor 4 - Store Floor 5
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Store Floor 4


Location / Dectector
activated



Fire Control Panel



Annunciator

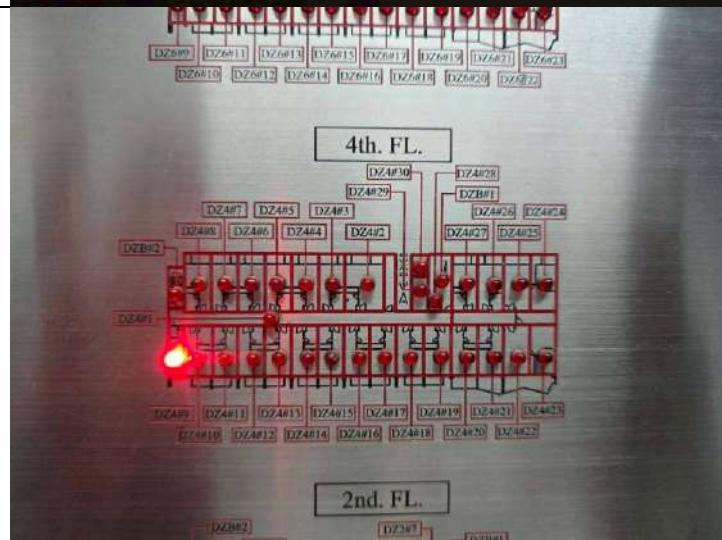



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 26 December 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#4)
- Control Room Floor 4
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Control Room Floor 4


Location / Dectector
activated



Fire Control Panel



Annunciator

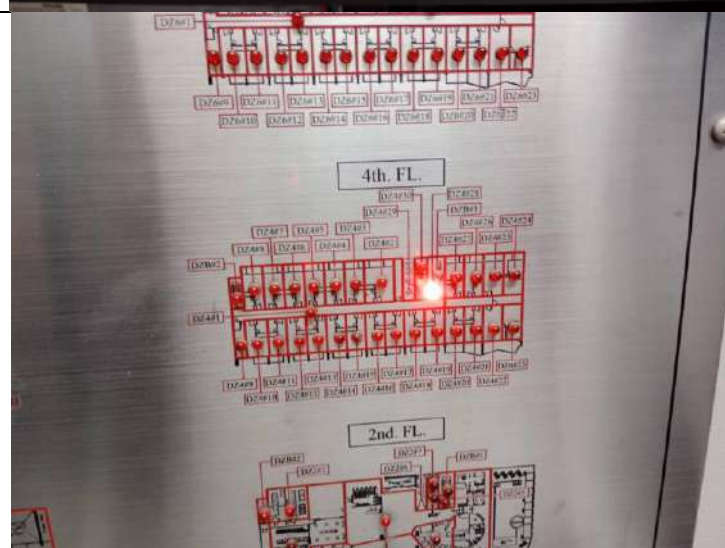



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
4	Control Room Floor 4	-	YES	-	-	ตู้บันทึกที่ไม่แสดงผล

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ4#28	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Prasit Inta (Security Supervisor)

Mr.Banphot Sunyaphap (Security Officer)

(26 December 2025)

Report by: Mr. Prasit Inta (Security Supervisor)

(26 December 2025)

Store Floor 5


**Location / Dectector
activated**



Fire Control Panel



Annunciator

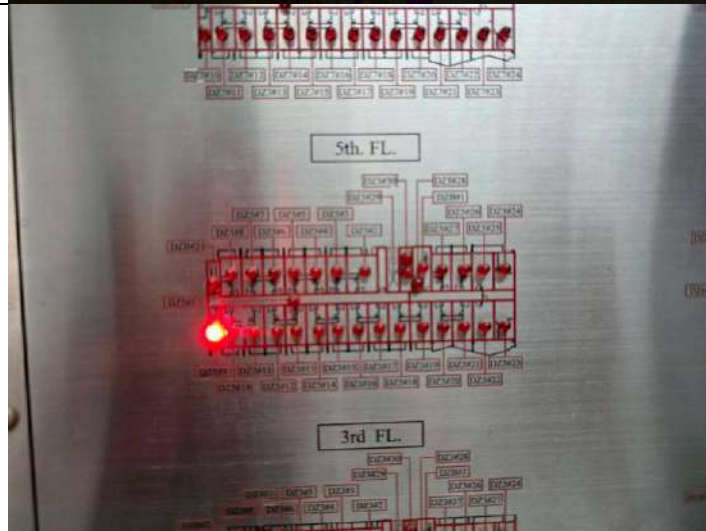



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
4	Store Floor 4	-	YES	-	-	ตู้ฉนวนที่ไม่แสดงผล
5	Store Floor 5	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ4#9	YES	YES	/	-	/	-	/	-	/	-	-	/
DZ5#9	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Prasit Inta

(Security Supervisor)

Mr.Adipong Pareesen

(Security Supervisor)

(14 December 2025)

Report by: Mr. Prasit Inta

(Security Supervisor)

(14 December 2025)



FIRE ALARM TESTING CHECKLIST

Activated by: ☒ Automatic System ☐ Manual System

Date: 23 December 2025 Time: 14.00 hrs.

STEP Testing

1. Select location as required (Floor#5)
- Store Floor 3 - AC.Store Floor B
 2. Using smoke detector tester spray, direct spraying to smoke detector.
 3. Waiting smoke detector activate, light blinking green to be red.
 4. Fire alarm control panel (FCP) at Control room is status checking.
 5. Graphic annunciator status checking.
 6. Let other devices responding, strobe light, buzzer, evacuation announcement 2 languages. (Chose silence mode to all sound active)
 7. Log record by Staff prepared in area.
 8. Reset alarm back to normal operation.
-

Store Floor 3


**Location / Dectector
activated**



Fire Control Panel



Annunciator

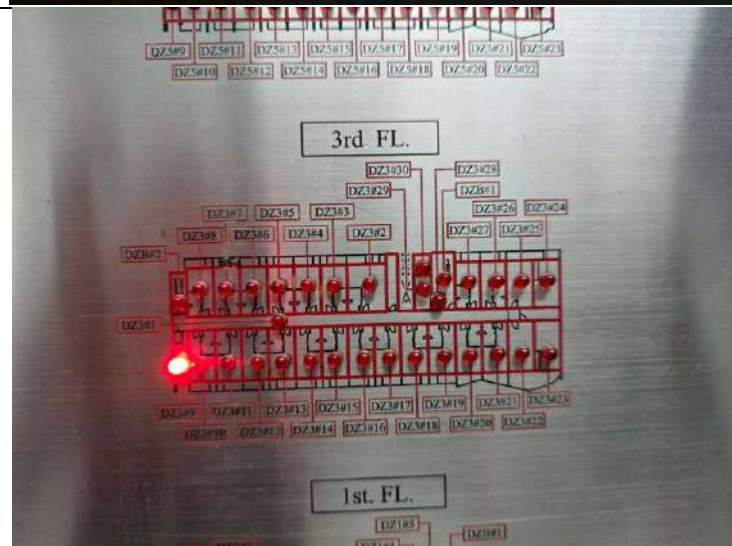

AC.Store Floor B


Location / Dectector activated



Fire Control Panel



Annunciator

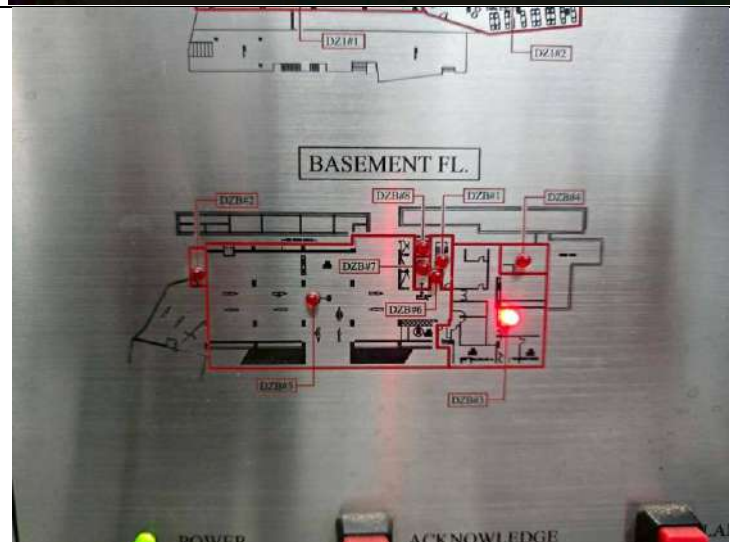



Floor	Location	Public Area	Strobe light	Bell	Pull Alarm	Remark
3	Store Floor 3	-	YES	-	-	ตู้บันทึกไม่แสดงผล
B	AC.Store Floor B	-	YES	-	-	

FCP	LED	Buzzer	Power		AC		Trouble		Alarm		Disable	
			On	Off	On	Off	On	Off	On	Off	On	Off
DZ3#9	YES	YES	/	-	/	-	/	-	/	-	-	/
DZB#3	YES	YES	/	-	/	-	/	-	/	-	-	/

Tested by: Mr. Prasit Inta

(Security Supervisor)

Mr.Adipong Pareesen

(Security Supervisor)

(23 December 2025)

Report by: Mr. Prasit Inta

(Security Supervisor)

(23 December 2025)
