

เอกสารแนบ 1

สำเนาหนังสือแจ้งผลการพิจารณารายงานการประเมินผลกระทบสิ่งแวดล้อม

สำนักงานนโยบายและแผนทรัพยากรธรรมชาติและสิ่งแวดล้อมได้พิจารณารายงานฯ และนำเสนอต่อคณะกรรมการผู้ชำนาญการพิจารณาการวิเคราะห์ผลกระทบสิ่งแวดล้อมด้านโครงการบริการชุมชน ในการประชุมครั้งที่ 10/2551 เมื่อวันที่ 22 เมษายน 2551 ซึ่งคณะกรรมการผู้ชำนาญการฯ มีมติเห็นชอบรายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อมโครงการโรงแรงแม่เหล็กไฟฟ้า โดยให้โครงการปฏิบัติตามมาตรฐานการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อมและมาตรการติดตามตรวจสอบคุณภาพสิ่งแวดล้อมที่โครงการโรงแรงแม่เหล็กไฟฟ้า ต้องยึดถือปฏิบัติอย่างเคร่งครัด ดังรายละเอียดตามสิ่งแวดล้อมสิ่งส่งมาด้วย 2 และการรายงานผลการปฏิบัติตามมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อมและมาตรการติดตามตรวจสอบคุณภาพสิ่งแวดล้อม ซึ่งรายละเอียดตามสิ่งแวดล้อมสิ่งส่งมาด้วย 3 อนึ่ง ตามมาตรา 50 วรรคท้าย ของพระราชบัญญัติส่งเสริมและรักษาคุณภาพสิ่งแวดล้อมแห่งชาติ พ.ศ.2535 เมื่อคณะกรรมการผู้ชำนาญการฯ ได้ให้ความเห็นชอบในรายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อมตามมาตรา 49 แล้ว ให้เจ้าหน้าที่รัฐมีอำนาจตามกฎหมายในการพิจารณาสิ่งส่งมาด้วย 3 สิ่งแวดล้อมตามมาตรา 49 แล้ว เพื่อให้เจ้าหน้าที่รัฐมีอำนาจตามกฎหมายในการพิจารณาสิ่งส่งมาด้วย 3 สิ่งแวดล้อมตามมาตรา 49 เพื่อให้หน่วยงานการวิเคราะห์ผลกระทบสิ่งแวดล้อมไปกำหนดเป็นเงื่อนไขในการส่งมอบใบอนุญาตนำเครื่องที่เสนอให้มาใช้งานการวิเคราะห์ผลกระทบสิ่งแวดล้อมไปกำหนดตามกฎหมายในเรื่องนี้ โดย การส่งมอบหรือต่ออายุใบอนุญาตไปอนุญาต โดยให้ถือว่าเป็นเงื่อนไขที่กำหนดตามกฎหมายในเรื่องนี้ด้วย ทั้งนี้ สำนักงานฯ ได้มีหนังสือแจ้งบริษัท ยัดกรีก จำกัด และสำนักงานสิ่งแวดล้อมแห่งชาติ อีกรีกด้วยแล้ว เพื่อดำเนินการต่อไปด้วยแล้ว

จึงเรียนมาเพื่อโปรดพิจารณาดำเนินการในส่วนที่เกี่ยวข้องต่อไป

ขอแสดงความนับถือ

คณะกรรมการกฤษฎีกาและคณะมนตรีความมั่นคงแห่งรัฐ

10. 10.10.2020

สำนักวิเคราะห์ผลกระทบสิ่งแวดล้อม
โทรศัพท์ 0-2265-6500 ต่อ 6814
โทรสาร 0-2265-6616



๒๖ มี.ค. ๑๐๙.๕๕๑๖

สำนักงานนโยบายและแผน
ทรัพยากรธรรมชาติและสิ่งแวดล้อม
60/1 ซอยพิบูลย์วัฒนา 7 ถนนพระรามที่ 6
กรุงเทพฯ 10400

18 มิถุนายน 2551

เรียง

เรียน
ผู้ว่าราชการกรุงเทพมหานคร

ข้าวงี้ พลเรือโท มาจากเมโยบายและแผนกทรัพยากรธรรมชาติและสิ่งแวดล้อม ที่ พท 1009.5/2801
จนถึงที่ 10 เมษายน 2551

สิ่งที่ส่งมาด้วย 1.สำเนาหนังสือบริษัท อีอาร์เอ็ม-สยาม จำกัด ลงวันที่ 11 เมษายน 2551

2.มาตรการป้องกันและแก้ไขปัญหาละเมิดสิ่งแวดล้อม และมาตรการติดตามตรวจสอบคุณภาพสิ่งแวดล้อมด้านโครงการในมหาวิทยาลัย เชียงใหม่ จำกัด ต้องยึดถือปฏิบัติอย่างเคร่งครัด

3. แนวทางการส่งเสริมการปฏิบัติตามมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อมและมาตรการติดตามตรวจสอบคุณภาพสิ่งแวดล้อม

ตามหนังสือที่อ้างถึง สำนักงานนโยบายและแผนทรัพยากรธรรมชาติและสิ่งแวดล้อม
ได้แจ้งผลการพิจารณารายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อมโครงการโรงไฟฟ้า ของบริษัท
โออิทรี จำกัด ตั้งอยู่ที่ถนนสหราษฎร์ แขวงสี่มืง เขตบางรัก กรุงเทพมหานคร จัดทำรายงาน โดยบริษัท
อิวอร์เอ็ม-สยาม จำกัด ซึ่งคณะกรรมการผู้ชำนาญการพิจารณารายงานการวิเคราะห์ผลกระทบ
สิ่งแวดล้อมด้านโครงการอิเล็กทรอนิกส์ที่ 6/2551 เมื่อวันที่ 4 มีนาคม 2551 มีมติไม่
เห็นชอบรายงานฯ ต่อมาบริษัท โออิทรีเอ็ม-สยาม จำกัด ได้เสนอรายงานฯ ที่แจ้งเพิ่มเติมให้สำนักงาน
ดำเนินการตามขั้นตอนการพิจารณา รายงานฯ ดังรายละเอียดตามสิ่งที่ส่งมาด้วย 1

2/ล้งน้ำกงาน...

เอกสารแบบ 2
สำเนาใบรับหนังสือแจ้งความประสงค์จะก่อสร้างอาคาร ตัดแปลง
หรือรื้อถอนอาคาร (กทม.6)

ความมาก

โดยไม่ยื่นคำขอรับใบอนุญาตตามมาตรา 39 ทวิ

แบบ กทม.6

ตามแบบ กทม.1 เลขที่ 328

ลงวันที่ 19 มิถุนายน 2551

ใบรับหนังสือแจ้งความประสงค์จะก่อสร้าง ดัดแปลง รื้อถอนหรือเคลื่อนย้ายอาคาร
หรือเปลี่ยนแปลงการใช้อาคาร โดยไม่ยื่นคำขอรับใบอนุญาต ตามมาตรา 39 ทวิ

เลขที่ 328 / 2551

ได้รับแจ้งจาก บริษัท โอ๊คทรี จำกัด โดย

เจ้าของอาคารหรือตัวแทนเจ้าของอาคาร/ผู้ครอบครองอาคาร อยู่บ้านเลขที่ 178/7 หมู่ที่
ตรอก/ซอย..... ถนน รัชดาภิเษก ตำบล/แขวง จันทระเกษม
อำเภอ/เขต จตุจักร จังหวัด กรุงเทพมหานคร ดังข้อความต่อไปนี้

ข้อ 1 ขอแจ้งความประสงค์จะทำการ ก่อสร้างอาคาร

ที่บ้านเลขที่..... หมู่ที่..... ตรอก/ซอย..... ถนน.....
ตำบล/แขวง สีลม อำเภอ/เขต บางรัก กรุงเทพมหานคร
ในที่ดินโฉนดที่ดินเลขที่/น.ส.3 เลขที่/ส.ค.1 เลขที่ 3078, 5021, 5022
เป็นที่ดินของ.....

โดยไม่ยื่นคำขอรับใบอนุญาตจากเจ้าพนักงานท้องถิ่น

จจรดยบด

ข้อ 2 เป็นอาคาร ชั้นใต้ดิน 2 ชั้น

พาณิชย์-สำนักงาน-ห้องประชุม

2.1 ชนิด ดึก 28 ชั้น จำนวน 1 หลัง เพื่อใช้เป็น โรงแรม (267 ห้อง)-ภัตตาคาร

พื้นที่ 38,061.00 ม.² ที่จอดรถ ที่กับริด และทางเข้า-ออกของรถ จำนวน 243 คัน

พื้นที่ 1,200.00 ม.²

2.2 ชนิด..... จำนวน..... หลัง เพื่อใช้เป็น.....

พื้นที่..... ม.² ที่จอดรถ ที่กับริด และทางเข้า-ออกของรถ จำนวน..... คัน

พื้นที่..... ม.²

2.3 ชนิด..... จำนวน..... หลัง เพื่อใช้เป็น.....

พื้นที่..... ม.² ที่จอดรถ ที่กับริด และทางเข้า-ออกของรถ จำนวน..... คัน

พื้นที่..... ม.²

ผู้อำนวยการกอง.....

หัวหน้ากลุ่มงาน.....

เจ้าหน้าที่ธุรการ.....

เจ้าหน้าที่พิมพ์/ทาง.....

วันที่ 19 มิ.ย. 2551

วันที่ 19 มิ.ย. 2551

วันที่ 19 มิ.ย. 2551

วันที่ 19 มิ.ย. 2551

ตามแผนผังบริเวณ แบบแปลน รายการประกอบแบบแปลนและรายการคำนวณที่แนบมาพร้อมนี้

ข้อ 3 โดยมี

- (1).....เป็นสถาปนิกผู้ออกแบบ
- (2).....เป็นสถาปนิกผู้ควบคุมงาน
- (3).....เป็นวิศวกรผู้ออกแบบโครงสร้าง
- (4).....เป็นวิศวกรผู้ควบคุมงาน โครงสร้าง
- (5).....เป็นวิศวกรผู้ออกแบบระบบปรับอากาศ
อากาศและระบบระบายอากาศและระบบ
ป้องกันเพลิงไหม้
- (6).....เป็นวิศวกรผู้ควบคุมงานระบบปรับอากาศ
อากาศและระบบระบายอากาศและระบบ
ป้องกันเพลิงไหม้
- (7).....เป็นวิศวกรผู้ออกแบบระบบบำบัด
น้ำเสียและการระบายน้ำทิ้ง
- (8).....เป็นวิศวกรผู้ควบคุมงานระบบบำบัด
น้ำเสียและการระบายน้ำทิ้ง
- (9).....เป็นวิศวกรผู้ออกแบบระบบลิฟต์/ไฟฟ้า
- (10).....เป็นวิศวกรผู้ควบคุมงานระบบลิฟต์/ไฟฟ้า

ข้อ 4 กำหนดแล้วเสร็จงาน 730 วัน โดยจะเริ่มขึ้นก่อสร้างอาคาร/ดัดแปลงอาคาร/รื้อถอนอาคาร/
เคลื่อนย้ายอาคาร/เปลี่ยนการใช้อาคาร เมื่อ 19 มิถุนายน 2551 และจะแล้วเสร็จเมื่อ 19 มิถุนายน 2553

ข้อ 5 ค่าธรรมเนียมในการตรวจแบบ.....	152,244.00	บาท
ค่าธรรมเนียมต่อระบายน้ำ รื้อ เชื้อน กำแพงหรืออื่นๆ.....	216.00	บาท
ค่าธรรมเนียมหรือที่จอดรถยนต์ภายนอกอาคาร.....	600.00	บาท
ค่าธรรมเนียมใบอนุญาต.....	20.00	บาท
รวมทั้งสิ้น.....	153,080.00	บาท

จำนวนการลง..... วันที่ 19 มิ.ย. 2551
..... วันที่ 19 มิ.ย. 2551
..... วันที่ 19 มิ.ย. 2551
..... วันที่ 19 มิ.ย. 2551

ข้อ 6 ผู้แจ้งต้องปฏิบัติตามเงื่อนไขดังต่อไปนี้

6.1 ผู้แจ้งต้องปฏิบัติตามหลักเกณฑ์ วิธีการ และเงื่อนไขตามที่กำหนดในกฎกระทรวงและหรือข้อบัญญัติท้องถิ่น ซึ่งออกตามความในมาตรา 8 (1) มาตรา 9 หรือมาตรา 10 แห่งพระราชบัญญัติควบคุมอาคาร พ.ศ.2522 แก้ไขเพิ่มเติม โดยพระราชบัญญัติควบคุมอาคาร (ฉบับที่ 2) พ.ศ.2535

6.2 จะต้องใช้ผ้าใบหรือวัสดุอื่นหรือเทียบเท่าหรือดีกว่า เพื่อป้องกันวัสดุก่อสร้างร่วงหล่นและฝุ่นละอองที่กระจายอันเนื่องมาจากการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร กันตัวอาคารสูงตลอดตั้งแต่ระดับดิน โดยยึดติดกับนั่งร้าน รอบนอกอาคาร ให้มีความสูงกว่าความสูงของอาคารขณะก่อสร้างไม่น้อยกว่า 2.00 เมตร ตลอดแนวอาคารด้านที่มีระยะราววัดจากแนวอาคารด้านนอกถึงที่สาธารณะหรือที่ดินข้างเจ้าของหรือผู้ครอบครองน้อยกว่าความสูงอาคารที่ได้รับอนุญาตและจะต้องรักษาให้อยู่ในสภาพดีตลอดเวลาการก่อสร้าง

6.3 จะต้องจัดให้มีปดองชั่วคราวสำหรับทั้งของและต้องจัดให้มีมาตรการป้องกันฝุ่นละออง มลพิษและเสียงดังอันเกิดจากการก่อสร้าง รวมทั้งวัสดุและอุปกรณ์ที่ใช้ในการก่อสร้างร่วงหล่น อันเป็นเหตุให้เกิดความเดือดร้อนรำคาญและเป็นภัยอันตรายแก่สุขภาพ ชีวิตและทรัพย์สิน ของประชาชนที่อยู่ในบริเวณใกล้เคียง

ข้อ 7 ภายในหนึ่งร้อยยี่สิบวันนับแต่วันที่ได้ออกใบรับแจ้ง ตามมาตรา 39 ทวิ หรือนับแต่วันที่เริ่มการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือเริ่มใช้อาคารที่ได้แจ้งไว้แล้วแต่กรณี ถ้าเจ้าพนักงานท้องถิ่นได้ตรวจพบว่าการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือเปลี่ยนการใช้อาคารที่ได้แจ้งไว้ ผิดแบบแปลน แบบแปลน รายการประกอบแบบแปลน หรือรายการคำนวณของอาคารที่ได้ยื่นไว้ ตามมาตรา 39 ทวิ ไม่ถูกต้องตามบทบัญญัติแห่งพระราชบัญญัติควบคุมอาคารฯ กฎกระทรวงหรือข้อบัญญัติท้องถิ่นที่ออกตามพระราชบัญญัติดังกล่าว หรือกฎหมายอื่นที่เกี่ยวข้อง เจ้าพนักงานท้องถิ่นยังคงมีอำนาจสั่งให้ผู้แจ้งดำเนินการแก้ไขให้ถูกต้อง หรือครบถ้วนภายในเจ็ดวันนับแต่วันที่ได้รับแจ้งคำสั่งดังกล่าว

ข้อ 8 ห้ามทำการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือเปลี่ยนการใช้อาคาร ดังนี้

8.1 การกระทำดังกล่าวเป็นการรुकล้ำที่สาธารณะ

8.2 การกระทำดังกล่าวเกี่ยวกับระยะหรือระดับระหว่างอาคารกับถนน ตรอก ซอย ทางเท้า หรือที่สาธารณะ เป็นการฝ่าฝืนกฎกระทรวง ประกาศหรือข้อบัญญัติท้องถิ่นที่ออกตามพระราชบัญญัติควบคุมอาคาร หรือ

ผู้อำนวยการกอง.....

นาย.....

วันที่ 19 มิ.ย. 2551

วันที่ 19 มิ.ย. 2551

วันที่ 19 มิ.ย. 2551

วันที่ 19 มิ.ย. 2551

8.3 การกระทำดังกล่าวที่เกี่ยวกับบริเวณห้ามก่อสร้าง คัดแปลง รื้อถอน เคลื่อนย้าย และใช้หรือ
เปลี่ยนการใช้อาคารชนิดหรือประเภทใดเป็นการฝ่าฝืนกฎกระทรวง ประกาศ หรือข้อบัญญัติท้องถิ่นที่ออกตาม
พระราชบัญญัติควบคุมอาคาร หรือกฎหมายอื่นที่เกี่ยวข้อง

ข้อ 9 ผู้แจ้งฯ ยังคงมีหน้าที่ต้องขออนุญาตเกี่ยวกับอาคารนั้น ตามกฎหมายอื่นในส่วนที่เกี่ยวข้อง
ต่อไปด้วย

ข้อ 10 ห้ามทำการก่อสร้าง คัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือใช้อาคารให้ผิดไปจาก
ที่ได้แจ้งไว้

ข้อ 11 ก่อนเริ่มลงมือก่อสร้างอาคาร ผู้ดำเนินการต้องสำรวจรายละเอียด ตำแหน่งความลึก และ
ขนาดของโครงสร้างใต้ดิน ฐานรากอาคารข้างเคียง หรือสิ่งก่อสร้างอื่นๆ เช่น ท่อ ประปา สายเคเบิล เป็นต้น
และวางมาตรการอย่างหนึ่งอย่างใดเพื่อป้องกันมิให้เกิดอันตรายต่อสุขภาพ ชีวิต ร่างกาย หรือทรัพย์สิน

ข้อ 12 เมื่อมีการขุดดินในบริเวณที่ใกล้หรือชิดอาคาร ถนนหรือกำแพง ลึกจนอาจเป็นอันตรายแก่อาคาร
ถนน หรือกำแพงนั้น ผู้ดำเนินการต้องจัดให้มีค้ำยัน เข็มพิค หรือฐานรากเสริมตามความจำเป็น เพื่อความปลอดภัย
และต้องตรวจสอบแก้ไขค้ำยัน เข็มพิค และฐานรากดังกล่าวให้มีสภาพมั่นคงและปลอดภัยอยู่เสมอ

ข้อ 13 ผู้แจ้งฯ ต้องปฏิบัติตามมาตรการป้องกันแก้ไขผลกระทบสิ่งแวดล้อมและแผนการติดตาม
ตรวจสอบคุณภาพสิ่งแวดล้อม ตามรายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ที่ได้รับความเห็นชอบจาก
สำนักงานนโยบายและแผนทรัพยากรธรรมชาติและสิ่งแวดล้อม ตามหนังสือที่ พส. 1009.5/4515 ลงวันที่ 18
มิถุนายน 2551 อย่างเคร่งครัด

ออกให้ ณ วันที่

รองผู้ว่าราชการจังหวัดนนทบุรี
โดยนายการแทนผู้อำนวยการสำนักงาน
ผู้ว่าราชการจังหวัดนนทบุรี
เจ้าพนักงานท้องถิ่น

ตามหนังสือแจ้งความประสงค์ฯ ตามแบบ กทม.1 เลขรับที่ 328
ลงวันที่ 19 เดือน มิถุนายน พ.ศ. 2551
ราย บริษัท โอ๊คทรี จำกัด

ผู้ว่าราชการจังหวัดนนทบุรี วันที่ 19, มิ.ย. 2551
หัวหน้าสำนักงาน วันที่ 19, มิ.ย. 2551
วันที่ 19, มิ.ย. 2551

คำเตือน

1. ถ้าผู้แจ้งฯจะบอกเลิกตัวผู้ควบคุมงานที่ระบุชื่อไว้ในใบแจ้ง หรือผู้ควบคุมงานจะบอกเลิกการเป็นผู้ควบคุมงาน ให้มีหนังสือแจ้งให้เจ้าพนักงานท้องถิ่นทราบ ทั้งนี้ ไม่เป็นการกระทบถึงสิทธิและหน้าที่ทางแพ่งระหว่างผู้แจ้งฯกับผู้ควบคุมงานนั้น ในการบอกเลิกตัวผู้ควบคุมงานนี้ ผู้แจ้งฯ จะต้องระงับการดำเนินการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคารไว้ก่อนจนกว่าจะมีผู้ควบคุมงานคนใหม่ และมีหนังสือแจ้งพร้อมกับส่งมอบหนังสือแสดงความยินยอมของผู้ควบคุมงานคนใหม่ ให้แก่เจ้าพนักงานท้องถิ่นแล้ว

2. ผู้แจ้งฯ ที่ต้องจัดให้มีพื้นที่ หรือสิ่งที่สร้างขึ้นเพื่อใช้เป็นที่จอดรถยนต์ ที่กักเก็บรถ และทางเข้าออกของรถตามที่กำหนดไว้ในใบแจ้งฯ ฉบับนี้ ต้องแสดงที่จอดรถยนต์ ที่กักเก็บรถ และทางเข้าออกของรถไว้ให้ปรากฏตามแผนผังบริเวณที่ได้แจ้งให้ กรุงเทพมหานคร ทราบ การดัดแปลงหรือใช้ที่จอดรถ ที่กักเก็บรถ และทางเข้าออกของรถเพื่อการอื่นนั้นต้องได้รับอนุญาตจากเจ้าพนักงานท้องถิ่น

3. เมื่อผู้แจ้งความประสงค์จะก่อสร้าง ดัดแปลง หรือเคลื่อนย้ายอาคารประเภทควบคุมการใช้ได้กระทำการตามที่ได้แจ้งเสร็จแล้ว ต้องแจ้งเป็นหนังสือให้เจ้าพนักงานท้องถิ่นทราบ ตามแบบที่เจ้าพนักงานท้องถิ่นกำหนด เพื่อทำการตรวจสอบการก่อสร้าง ดัดแปลง หรือเคลื่อนย้ายอาคาร นั้น และห้ามมิให้ใช้อาคารนั้นเพื่อกิจการดังที่ได้แจ้งไว้ ภายในกำหนด 30 วัน นับตั้งแต่วันที่เจ้าพนักงานท้องถิ่นได้รับแจ้ง

ผู้อำนวยการกอง.....

นายกเทศมนตรี.....

วันที่ 19 มิ.ย. 2551

วันที่ 19 มิ.ย. 2551

วันที่ 19 มิ.ย. 2551

วันที่ 19 มิ.ย. 2551

ด่วนมาก

โดยไม่ยื่นคำขอรับใบอนุญาตตาม มาตรา 39 ทวิ

แบบ กทม.6 เดิมเลขที่ 328/2551

ลงวันที่ 19 มิถุนายน 2551

ตามแบบ กทม.1 เลขที่ 274

ลงวันที่ 7 กรกฎาคม 2553

แบบ กทม.6

ใบรับหนังสือแจ้งความประสงค์จะก่อสร้าง คัดแปลง รื้อถอนหรือเคลื่อนย้ายอาคาร
หรือเปลี่ยนแปลงการใช้อาคาร โดยไม่ยื่นคำขอรับใบอนุญาต ตามมาตรา 39 ทวิ

เลขที่ 274 / 2553

ได้รับแจ้งจาก บริษัท โอ๊คทรี จำกัด โดย

เจ้าของอาคารหรือตัวแทนเจ้าของอาคาร/ผู้ครอบครองอาคาร อยู่บ้านเลขที่ 178/7 หมู่ที่
ตรอก/ซอย ถนน รัชดาภิเษก ตำบล/แขวง จันทน์เกษม

อำเภอ/เขต จตุจักร จังหวัด กรุงเทพมหานคร ดังข้อความต่อไปนี้

ข้อ 1 ขอแจ้งความประสงค์จะทำการ ก่อสร้างอาคาร (แก้ไขแบบแปลน)

ที่บ้านเลขที่ หมู่ที่ ตรอก/ซอย ถนน สาทร

ตำบล/แขวง สีลม อำเภอ/เขต บางรัก กรุงเทพมหานคร

ในที่ดินโฉนดที่ดินเลขที่/น.ส.3 เลขที่/ส.ด.1 เลขที่ 3078, 5021, 5022

เป็นที่ดินของ

โดยไม่ยื่นคำขอรับใบอนุญาตจากเจ้าพนักงานท้องถิ่น

จตุรตถยนต์

พาณิชย์-สำนักงาน-ห้องประชุม

ข้อ 2 เป็นอาคาร ชั้นใต้ดิน 2 ชั้น

2.1 ชนิด ตึก 28 ชั้น จำนวน 1 หลัง เพื่อใช้เป็น โรงแรม (237 ห้อง)-ภัตตาคาร

พื้นที่ 37,446.00 ม.² ที่จอดรถ ที่กั๊ปรด และทางเข้า-ออกของรถ จำนวน 243 คัน

พื้นที่ 1,200.00 ม.²

2.2 ชนิด จำนวน หลัง เพื่อใช้เป็น

พื้นที่ ม.² ที่จอดรถ ที่กั๊ปรด และทางเข้า-ออกของรถ จำนวน คัน

พื้นที่ ม.²

2.3 ชนิด จำนวน หลัง เพื่อใช้เป็น

พื้นที่ ม.² ที่จอดรถ ที่กั๊ปรด และทางเข้า-ออกของรถ จำนวน คัน

พื้นที่ ม.²

ผู้อำนวยการกอง
หัวหน้ากลุ่มงาน

วันที่ 7 ก.ค. 2553
วันที่ 7 ก.ค. 2553
วันที่ 7 ก.ค. 2553

ตามแผนผังบริเวณ แบบแปลน รายการประกอบแบบแปลนและรายการคำนวณที่แนบมา
พร้อมนี้

ข้อ 3 โดยมี

- (1).....เป็นสถาปนิกผู้ออกแบบ
- (2).....เป็นสถาปนิกผู้ควบคุมงาน
- (3).....เป็นวิศวกรผู้ออกแบบโครงสร้าง
- (4).....เป็นวิศวกรผู้ควบคุมงานโครงสร้าง
- (5).....เป็นวิศวกรผู้ออกแบบระบบปรับอากาศและระบบระบายอากาศและระบบป้องกันเพลิงไหม้
- (6).....เป็นวิศวกรผู้ควบคุมงานระบบปรับอากาศและระบบระบายอากาศ
- (7).....เป็นวิศวกรผู้ควบคุมงานระบบป้องกันเพลิงไหม้
- (8).....เป็นวิศวกรผู้ออกแบบระบบบำบัดน้ำเสียและการระบายน้ำทิ้ง
- (9).....เป็นวิศวกรผู้ควบคุมงานระบบบำบัดน้ำเสียและการระบายน้ำทิ้ง
- (10).....เป็นวิศวกรผู้ออกแบบระบบลิฟท์/ไฟฟ้า
- (11).....เป็นวิศวกรผู้ควบคุมงานระบบลิฟท์
- (12).....เป็นวิศวกรผู้ควบคุมงานระบบไฟฟ้า
- (13).....เป็นวิศวกรผู้ตรวจสอบงานออกแบบและคำนวณส่วนต่างๆ ของ โครงสร้างอาคาร

ผู้อำนวยการกอง.....

.....

วันที่ 7 ก.ค. 2553
วันที่ 7 ก.ค. 2553
วันที่ 7 ก.ค. 2553
วันที่ 7 ก.ค. 2553

ข้อ 4 กำหนดแล้วเสร็จงาน... 730... วัน โดยจะเริ่มต้นก่อสร้างอาคาร/คัดแปลงอาคาร/รื้อถอนอาคาร/
เคลื่อนย้ายอาคาร/เปลี่ยนการใช้อาคาร เมื่อ 7 กรกฎาคม 2553 และแล้วเสร็จเมื่อ 7 กรกฎาคม 2555

ข้อ 5 ค่าธรรมเนียมในการตรวจแบบ.....	149,784.00	บาท
ค่าธรรมเนียมทอระบายน้ำ รั้ว เขื่อน กำแพงหรืออื่น ๆ	216.00	บาท
ค่าธรรมเนียมทางวิ่งหรือที่จอดรถยนต์ภายนอกอาคาร.....	600.00	บาท
ค่าธรรมเนียมใบอนุญาต.....	20.00	บาท
รวมทั้งสิ้น.....	150,620.00	บาท

ข้อ 6 ผู้แจ้งต้องปฏิบัติตามเงื่อนไขดังต่อไปนี้

6.1 ผู้แจ้งต้องปฏิบัติตามหลักเกณฑ์ วิธีการ และเงื่อนไขตามที่กำหนดในกฎกระทรวงและหรือ
ข้อบัญญัติท้องถิ่น ซึ่งออกตามความในมาตรา 8 (11) มาตรา 9 หรือมาตรา 10 แห่งพระราชบัญญัติควบคุม
อาคาร พ.ศ.2522 แก้ไขเพิ่มเติม โดยพระราชบัญญัติควบคุมอาคาร (ฉบับที่ 2) พ.ศ.2535

6.2 จะต้องใช้ผ้าใบหรือวัสดุอื่นหรือเทียบเท่าหรือดีกว่า เพื่อป้องกันวัสดุก่อสร้างร่วงหล่นและ
ฝุ่นละอองฟุ้งกระจายอันเนื่องมาจากการก่อสร้าง คัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร กันตัวอาคารสูง
ตลอดตั้งแต่ระดับดิน โดยยึดติดกับนั่งร้าน รอบนอกอาคาร ให้มีความสูงกว่าความสูงของอาคารขณะก่อสร้าง
ไม่น้อยกว่า 2.00 เมตร ตลอดแนวอาคารด้านที่มีระยะราววัดจากแนวอาคารด้านนอกถึงที่สาธารณะหรือที่ดิน
ข้างเจ้าของหรือผู้ครอบครองน้อยกว่าความสูงอาคารที่ได้รับอนุญาตและจะต้องรักษาให้อยู่ในสภาพดี
ตลอดเวลาการก่อสร้าง

6.3 จะต้องจัดให้มีปล่องชั่วคราวสำหรับทิ้งของและต้องจัดให้มีมาตรการป้องกันฝุ่นละออง
มลพิษและเสียงดังอันเกิดจากการก่อสร้าง รวมทั้งวัสดุและอุปกรณ์ที่ใช้ในการก่อสร้างร่วงหล่น อันเป็นเหตุ
ให้เกิดความเดือดร้อนรำคาญและเป็นอันตรายแก่สุขภาพ ชีวิตและทรัพย์สิน ของประชาชนที่อยู่ในบริเวณ
ใกล้เคียง

ข้อ 7 ภายในหนึ่งร้อยยี่สิบวันนับแต่วันที่ได้ออกใบรับแจ้ง ตามมาตรา 39 ทวิ หรือนับแต่วันที่เริ่ม
การก่อสร้าง คัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือเริ่มใช้อาคารที่ได้แจ้งไว้แล้วแต่กรณี [ถ้า]
เจ้าพนักงานท้องถิ่นได้ตรวจพบว่าการก่อสร้าง คัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือเปลี่ยนการใช้
อาคารที่ได้แจ้งไว้ ผิดทั้งบริเวณ แบบแปลน รายการประกอบแบบแปลน หรือรายการคำนวณของอาคารที่
ได้ยื่นไว้ ตามมาตรา 39 ทวิ ไม่ถูกต้องตามบทบัญญัติแห่งพระราชบัญญัติควบคุมอาคารฯ กฎกระทรวงหรือ
ข้อบัญญัติท้องถิ่นที่ออกตามพระราชบัญญัติดังกล่าว หรือกฎหมายอื่นที่เกี่ยวข้อง เจ้าพนักงานท้องถิ่นยังคง
มีอำนาจสั่งให้ผู้แจ้งดำเนินการแก้ไขให้ถูกต้อง หรือรื้อถอนภายในเจ็ดวันนับแต่วันที่ได้รับแจ้งคำสั่งดังกล่าว

ผู้อำนวยการกอง..... วันที่ 7 ก.ค. 2553
หัวหน้ากอง..... วันที่ 7 ก.ค. 2553
..... วันที่ 7 ก.ค. 2553
..... วันที่ 7 ก.ค. 2553

ข้อ 8 ห้ามทำการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือเปลี่ยนการใช้อาคาร ดังนี้

8.1 การกระทำความผิดเป็นการรื้อถอนหรือเคลื่อนย้ายอาคาร

8.2 การกระทำความผิดเกี่ยวกับระยะหรือระดับระหว่างอาคารกับถนน ตรอก ซอย ทางเท้า หรือที่สาธารณะ เป็นการฝ่าฝืนกฎกระทรวง ประกาศหรือข้อบัญญัติท้องถิ่นที่ออกตามพระราชบัญญัติควบคุมอาคาร หรือ

8.3 การกระทำความผิดเกี่ยวกับบริเวณห้ามก่อสร้าง ดัดแปลง รื้อถอน เคลื่อนย้าย และใช้หรือเปลี่ยนการใช้อาคารชนิดหรือประเภทใดเป็นการฝ่าฝืนกฎกระทรวง ประกาศ หรือข้อบัญญัติท้องถิ่นที่ออกตามพระราชบัญญัติควบคุมอาคาร หรือกฎหมายอื่นที่เกี่ยวข้อง

ข้อ 9 ผู้แจ้งฯ ยังคงมีหน้าที่ต้องขออนุญาตเกี่ยวกับอาคารนั้น ตามกฎหมายอื่นในส่วนที่เกี่ยวข้องต่อไปด้วย

ข้อ 10 ห้ามทำการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือใช้อาคารให้ผิดไปจากที่ได้แจ้งไว้

ข้อ 11 ก่อนเริ่มลงมือก่อสร้างอาคาร ผู้ดำเนินการต้องสำรวจรายละเอียด ตำแหน่งความลึก และขนาดของโครงสร้างใต้ดิน ฐานรากอาคารข้างเคียง หรือสิ่งก่อสร้างอื่นๆ เช่น ท่อ ประปา สายเคเบิล เป็นต้น และวางมาตรการอย่างหนึ่งอย่างใดเพื่อป้องกันมิให้เกิดอันตรายต่อสุขภาพ ชีวิต ร่างกาย หรือทรัพย์สิน

ข้อ 12 เมื่อมีการขุดดินในบริเวณที่ใกล้หรือชิดอาคาร ถนนหรือกำแพง ลึกจนอาจเป็นอันตรายแก่อาคาร ถนน หรือกำแพงนั้น ผู้ดำเนินการต้องจัดให้มีลำยัน เข็มพืด หรือฐานรากเสริมตามความจำเป็น เพื่อความปลอดภัยและต้องตรวจสอบแก้ไขลำยัน เข็มพืด และฐานรากดังกล่าวให้มีสภาพมั่นคงและปลอดภัยอยู่เสมอ

ข้อ 13 ผู้แจ้งฯ ต้องปฏิบัติตามมาตรการป้องกันแก้ไขผลกระทบสิ่งแวดล้อมและแผนการติดตามตรวจสอบคุณภาพสิ่งแวดล้อม ตามรายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ที่ได้รับความเห็นชอบจากสำนักนโยบายและแผนทรัพยากรธรรมชาติและสิ่งแวดล้อม ตามหนังสือที่ ทส. 1009.5/4515 ลงวันที่ 18 มิถุนายน 2551 อย่างเคร่งครัด

ออกให้ ณ วันที่

7 8 2553

ผู้อำนวยการสำนักงานนโยบาย
และแผนทรัพยากรธรรมชาติและสิ่งแวดล้อม
เจ้าพนักงานท้องถิ่น

ตามหนังสือแจ้งความประสงค์ฯ ตามแบบ กทม.1 เลขรับที่ 274...

ลงวันที่ 7 เดือน กรกฎาคม พ.ศ. 2553

ราช บริษัท โออิที จำกัด

ผู้อำนวยการกอง

วันที่ 7 ก.ค. 2553

วันที่ 7 ก.ค. 2553

วันที่ 7 ก.ค. 2553

คำเตือน

1. ถ้าผู้แจ้งจะบอกเลิกตัวผู้ควบคุมงานที่ระบุชื่อไว้ในใบแจ้ง หรือผู้ควบคุมงานจะบอกเลิกการเป็นผู้ควบคุมงาน ให้มีหนังสือแจ้งให้เจ้าพนักงานท้องถิ่นทราบ ทั้งนี้ ไม่เป็นการกระทบถึงสิทธิและหน้าที่ทางแพ่งระหว่างผู้แจ้งกับผู้ควบคุมงานนั้น ในการบอกเลิกตัวผู้ควบคุมงานนี้ ผู้แจ้งฯ จะต้องระงับการดำเนินการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคารไว้ก่อนจนกว่าจะมีผู้ควบคุมงานคนใหม่ และมีหนังสือแจ้งพร้อมกับส่งมอบหนังสือแสดงความยินยอมของผู้ควบคุมงานคนใหม่ ให้แก่เจ้าพนักงานท้องถิ่นแล้ว
2. ผู้แจ้งฯ ที่ต้องจัดให้มีพื้นที่ หรือสิ่งก่อสร้างขึ้นเพื่อใช้เป็นที่ยจอดรถยนต์ ที่กั๊บลรด์ และทางเข้า ออกของรุดตามที่กำหนดไว้ให้ใบแจ้งฯ ฉบับนี้ ต้องแสดงที่ยจอดรถยนต์ ที่กั๊บลรด์ และทางเข้าออกของรุดไว้ให้ปรากฏตามแผนผังบริเวณที่ได้แจ้งให้ กรุงเทพมหานคร ทราบ การดัดแปลงหรือใช้ที่ยจอดรถ ที่กั๊บลรด์ และทางเข้าออกของรุดเพื่อการอื่นนั้นต้องได้รับอนุญาตจากเจ้าพนักงานท้องถิ่น
3. เมื่อผู้แจ้งความประสงค์จะก่อสร้าง ดัดแปลง หรือเคลื่อนย้ายอาคารประเภทควบคุมการใช้ได้กระทำการตามที่ได้แจ้งเสร็จแล้ว ต้องแจ้งเป็นหนังสือให้เจ้าพนักงานท้องถิ่นทราบ ตามแบบที่เจ้าพนักงานท้องถิ่นกำหนด เพื่อทำการตรวจสอบการก่อสร้าง ดัดแปลง หรือเคลื่อนย้ายอาคาร นั้น และห้ามมิให้ใช้อาคารนั้นเพื่อกิจการดังที่ได้แจ้งไว้ ภายในกำหนด 30 วัน นับตั้งแต่วันที่เจ้าพนักงานท้องถิ่นได้รับแจ้ง

ผู้อำนวยการกอง.....

หัวหน้า.....

1. เจ้าพนักงาน.....

วันที่ - 7 / 0 8 / 2553

วันที่ - 7 / 0 8 / 2553

วันที่ - 7 / 0 8 / 2553

วันที่ - 7 / 0 8 / 2553

ด่วนมาก

ขอเป็นคำขอรับใบอนุญาตตาม มาตรา ๘๖ ขว

แบบ กทม.๖ เดิมเลขที่ ๒๗๔/๒๕๕๓

ลงวันที่ ๗ กรกฎาคม ๒๕๕๓

ตามแบบ กทม.๑ เลขรับที่ ๒๕๘

ลงวันที่ ๒๐ พฤษภาคม ๒๕๕๔

แบบ กทม.๖

ใบรับหนังสือแจ้งความประสงค์จะก่อสร้าง ดัดแปลง รื้อถอนหรือเคลื่อนย้ายอาคาร
หรือเปลี่ยนการใช้อาคาร โดยไม่ยื่นคำขอรับใบอนุญาต ตามมาตรา ๓๔ ทวิ

เลขที่ ๒๕๔/๒๕๕๔

ได้รับแจ้งจาก..... บริษัท โอ๊คทรี จำกัด โดย.....
เจ้าของอาคารหรือตัวแทนเจ้าของอาคาร/ผู้ครอบครองอาคาร อยู่บ้านเลขที่..... ๑๗๘/๗
หมู่ที่..... ตรอก/ซอย..... ถนน..... รัชดาภิเษก..... ตำบล/แขวง..... จันทระเกษม
อำเภอ/เขต..... จตุจักร..... จังหวัด..... กรุงเทพมหานคร..... ดังข้อความต่อไปนี้
ข้อ ๑ ขอแจ้งความประสงค์จะทำการ..... ก่อสร้างและดัดแปลงอาคาร
ที่บ้านเลขที่..... หมู่ที่..... ตรอก/ซอย..... ถนน..... สาทร
ตำบล/แขวง..... สีสุม..... อำเภอ/เขต..... บางรัก..... กรุงเทพมหานคร
ในที่ดินโฉนดที่ดินเลขที่/น.ส.๓ เลขที่/ส.ค.๑ เลขที่..... ๓๐๗๘, ๕๐๒๑, ๕๐๒๒
เป็นที่ดินของ.....
โดยไม่ยื่นคำขอรับใบอนุญาตจากเจ้าพนักงานท้องถิ่น

ข้อ ๒ เป็นอาคาร..... จอทรถยนต์
พลาซีย - สำนักงาน - ห้องประชุม -
๒.๑ ชนิด..... ตึก ๒๕ ชั้น ชั้นใต้ดิน ๒ ชั้น จำนวน..... ๑..... หลัง เพื่อใช้เป็น..... โรงแรม (๒๓๗ ห้อง) - กิตติาคาร -
พื้นที่..... ๓๔,๑๕๕.๐๐ ตารางเมตร ที่จอดรถ ที่กัณฑ์รถ และทางเข้า-ออกของรถ จำนวน..... ๒๓๐..... คัน
พื้นที่..... ๑,๒๐๐.๐๐ ตารางเมตร (พื้นที่ส่วนดัดแปลง ๓,๑๐๐.๐๐ ตารางเมตร)
๒.๒ ชนิด..... จำนวน..... หลัง เพื่อใช้เป็น.....
พื้นที่..... ตารางเมตร ที่จอดรถ ที่กัณฑ์รถ และทางเข้า-ออกของรถ จำนวน..... คัน
พื้นที่..... ตารางเมตร
๒.๓ ชนิด..... จำนวน..... หลัง เพื่อใช้เป็น.....
พื้นที่..... ตารางเมตร ที่จอดรถ ที่กัณฑ์รถ และทางเข้า-ออกของรถ จำนวน..... คัน
พื้นที่..... ตารางเมตร
๒.๔ ชนิด..... จำนวน..... หลัง เพื่อใช้เป็น.....
พื้นที่..... ตารางเมตร ที่จอดรถ ที่กัณฑ์รถ และทางเข้า-ออกของรถ จำนวน..... คัน
พื้นที่..... ตารางเมตร
๒.๕ ชนิด..... จำนวน..... หลัง เพื่อใช้เป็น.....
พื้นที่..... ตารางเมตร ที่จอดรถ ที่กัณฑ์รถ และทางเข้า-ออกของรถ จำนวน..... คัน
พื้นที่..... ตารางเมตร

ผู้รับราชการ.....

.....

๒๐ กรกฎาคม ๒๕๕๔
๒๐ กรกฎาคม ๒๕๕๔
๒๐ กรกฎาคม ๒๕๕๔

ตามแผนผังบริเวณ แบบแปลน รายการประกอบแบบแปลน และรายการคำนวณที่แนบมาพร้อมนี้

ข้อ ๓ โดยมี

- | | | |
|---------|------------|---|
| (๑)... | [REDACTED] | เป็นสถาปนิกผู้ออกแบบ |
| (๒)... | [REDACTED] | เป็นสถาปนิกผู้ควบคุมงาน |
| (๓)... | [REDACTED] | เป็นวิศวกรผู้ออกแบบโครงสร้าง |
| (๔)... | [REDACTED] | เป็นวิศวกรผู้ควบคุมงานโครงสร้าง |
| (๕)... | [REDACTED] | เป็นวิศวกรผู้ออกแบบระบบปรับอากาศ
อากาศและระบบระบายอากาศและ
ระบบป้องกันเพลิงไหม้ |
| (๖)... | [REDACTED] | เป็นวิศวกรผู้ควบคุมงานระบบปรับอากาศ
อากาศและระบบระบายอากาศ |
| (๗)... | [REDACTED] | เป็นวิศวกรผู้ควบคุมงานระบบป้องกันเพลิงไหม้ |
| (๘)... | [REDACTED] | เป็นวิศวกรผู้ออกแบบระบบบำบัด
น้ำเสียและการระบายน้ำทิ้ง |
| (๙)... | [REDACTED] | เป็นวิศวกรผู้ควบคุมงานระบบบำบัด
น้ำเสียและการระบายน้ำทิ้ง |
| (๑๐)... | [REDACTED] | เป็นวิศวกรผู้ออกแบบระบบลิฟต์ |
| (๑๑)... | [REDACTED] | เป็นวิศวกรผู้ควบคุมงานระบบลิฟต์ |
| (๑๒)... | [REDACTED] | เป็นวิศวกรผู้ออกแบบระบบไฟฟ้า |
| (๑๓)... | [REDACTED] | เป็นวิศวกรผู้ควบคุมงานระบบไฟฟ้า |
| (๑๔)... | [REDACTED] | เป็นวิศวกรผู้ตรวจสอบงานออกแบบและ
คำนวณส่วนต่างๆ ของโครงสร้างอาคาร |

ข้อ ๔ กำหนดแล้วเสร็จงาน.....๗๓๐.....วัน โดยจะเริ่มต้นก่อสร้างอาคาร/ดัดแปลงอาคาร/รื้อถอนอาคาร/
เคลื่อนย้ายอาคาร/เปลี่ยนการใช้อาคารเมื่อ ๒๐ พฤษภาคม ๒๕๕๕ และจะแล้วเสร็จเมื่อ ๒๐ พฤษภาคม ๒๕๕๖

ข้อ ๕ ค่าธรรมเนียมในการตรวจแบบ.....	๑๒,๕๐๐.๐๐	บาท
ค่าธรรมเนียมใบอนุญาต.....	๑๐.๐๐	บาท
รวมทั้งสิ้น.....	๑๒,๕๑๐.๐๐	บาท

ข้อ ๖ ผู้แจ้งต้องปฏิบัติตามเงื่อนไขดังต่อไปนี้

๖.๑ ผู้แจ้งต้องปฏิบัติตามหลักเกณฑ์ วิธีการ และเงื่อนไขตามที่กำหนดในกฎกระทรวงและ หรือ
ข้อบัญญัติท้องถิ่น ซึ่งออกตามความในมาตรา ๘ (๑๑) มาตรา ๙ หรือมาตรา ๑๐ แห่งพระราชบัญญัติควบคุมอาคาร
พ.ศ.๒๕๒๒ แก้ไขเพิ่มเติม โดยพระราชบัญญัติควบคุมอาคาร (ฉบับที่ ๒) พ.ศ. ๒๕๓๕

ผู้อำนวยการกอง.....	[REDACTED]	วันที่ ๒๐ พ.ค. ๒๕๕๕
หัวหน้ากลุ่มงาน.....	[REDACTED]	วันที่ ๒๐ พ.ค. ๒๕๕๕
..... / หัวหน้าที่ปรึกษา.....	[REDACTED]	วันที่ ๒๐ พ.ค. ๒๕๕๕

๒.๒ จะต้องใช้ผ้าใบหรือวัสดุอื่นหรือเทียบเท่าหรือดีกว่า เพื่อป้องกันวัสดุก่อสร้างร่วงหล่น และฝุ่นละอองฟุ้งกระจายอันเนื่องมาจากการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร กันตัวอาคารสูงตลอดตั้งแต่ระดับดิน โดยยึดติดกับนั่งร้านรอบนอกอาคาร ให้มีความสูงกว่าความสูงของอาคารขณะก่อสร้างไม่น้อยกว่า ๒.๐๐ เมตร ตลอดแนวอาคารด้านที่มีระยะราบวัดจากแนวอาคารด้านนอกถึงที่สาธารณะหรือที่ดินต่างเจ้าของหรือผู้ครอบครองน้อยกว่าความสูงอาคารที่ได้รับอนุญาตและจะต้องรักษาให้อยู่ในสภาพดีตลอดเวลาการก่อสร้าง

๒.๓ จะต้องจัดให้มีปล่องชั่วคราวสำหรับทั้งของและต้องจัดให้มีมาตรการป้องกันฝุ่นละอองมลพิษและเสียงดังอันเกิดจากการก่อสร้าง รวมทั้งวัสดุและอุปกรณ์ที่ใช้ในการก่อสร้างร่วงหล่น อันเป็นเหตุให้เกิดความเดือดร้อนรำคาญและเป็นอันตรายแก่สุขภาพ ชีวิต และทรัพย์สินของประชาชนที่อยู่ในบริเวณใกล้เคียง

ข้อ ๗ ภายในหนึ่งร้อยยี่สิบวันนับแต่วันที่ได้ออกใบรับแจ้ง ตามมาตรา ๓๙ ทวิ หรือนับแต่วันที่เริ่มการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือเริ่มใช้อาคารที่ได้แจ้งไว้แล้วแต่กรณี ถ้าเจ้าพนักงานท้องถิ่นได้ตรวจพบว่าการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือเปลี่ยนการใช้อาคารที่ได้แจ้งไว้ แผนผังบริเวณแบบแปลน รายการประกอบแบบแปลน หรือรายการคำนวณของอาคาร ที่ได้ยื่นไว้ ตามมาตรา ๓๙ ทวิ ไม่ถูกต้องตามบทบัญญัติแห่งพระราชบัญญัติควบคุมอาคารฯ กฎกระทรวงหรือข้อบัญญัติท้องถิ่นที่ออกตามพระราชบัญญัติดังกล่าวหรือกฎหมายอื่นที่เกี่ยวข้องเจ้าพนักงานท้องถิ่นยังคงมีอำนาจสั่งให้ผู้แจ้งดำเนินการแก้ไขให้ถูกต้อง หรือครบถ้วนภายในเจ็ดวันนับแต่วันที่ได้รับแจ้งคำสั่งดังกล่าว

ข้อ ๘ ห้ามทำการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือเปลี่ยนการใช้อาคาร ดังนี้

๘.๑ การกระทำดังกล่าวเป็นการรบกวนที่สาธารณะ

๘.๒ การกระทำดังกล่าวที่เกี่ยวกับระยะหรือระดับระหว่างอาคารกับถนน ตรอก ซอย ทางเท้าหรือที่สาธารณะ เป็นการฝ่าฝืนกฎกระทรวง ประกาศหรือข้อบัญญัติท้องถิ่นที่ออกตามพระราชบัญญัติควบคุมอาคารหรือ

๘.๓ การกระทำดังกล่าวที่เกี่ยวกับบริเวณห้ามก่อสร้าง ดัดแปลง รื้อถอน เคลื่อนย้าย และใช้หรือเปลี่ยนการใช้อาคารชนิดหรือประเภทใดเป็นการฝ่าฝืนกฎกระทรวง ประกาศ หรือข้อบัญญัติท้องถิ่นที่ออกตามพระราชบัญญัติควบคุมอาคาร หรือกฎหมายอื่นที่เกี่ยวข้อง

ข้อ ๙ ผู้แจ้งฯ ยังคงมีหน้าที่ต้องขออนุญาตเกี่ยวกับอาคารนั้น ตามกฎหมายอื่นในส่วนที่เกี่ยวข้อง ต่อไปด้วย

ข้อ ๑๐ ห้ามทำการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคาร หรือใช้อาคารให้ผิดไปจากที่ได้แจ้งไว้จากที่ได้แจ้งไว้

ข้อ ๑๑ ก่อนเริ่มลงมือก่อสร้างอาคาร ผู้ดำเนินการต้องสำรวจรายละเอียด ตำแหน่ง ความลึก และขนาดของโครงสร้างใต้ดิน ฐานรากอาคารข้างเคียง หรือสิ่งก่อสร้างอื่นๆ เช่น ท่อประปา สายเคเบิล เป็นต้น และวางมาตรการอย่างหนึ่งอย่างใดเพื่อป้องกันมิให้เกิดอันตรายต่อสุขภาพ ชีวิต ร่างกาย หรือทรัพย์สิน

ข้อ ๑๒ เมื่อมีการขุดดินในบริเวณที่ใกล้หรือชิดอาคาร ถนนหรือกำแพง ลีกร่นอาจเป็นอันตรายแก่อาคาร ถนนหรือกำแพงนั้น ผู้ดำเนินการต้องจัดให้มีค้ำยัน เข็มพิค หรือฐานรากเสริมตามความจำเป็น เพื่อความปลอดภัย และต้องตรวจสอบแก้ไขค้ำยัน เข็มพิคและฐานรากดังกล่าวให้มีสภาพมั่นคงและปลอดภัยอยู่เสมอ

ผู้อำนวยการของ.....

วันที่ ๒๐, ๓๓๐, ๒๕๕๕
วันที่ ๒๐, ๒๕๕๕
วันที่ ๒๐, ๓๓๐, ๒๕๕๕
วันที่ ๒๐, ๒๕๕๕

ข้อ ๑๓ ผู้แจ้งฯ ต้องปฏิบัติตามมาตรการป้องกันแก้ไขผลกระทบสิ่งแวดล้อม และแผนการติดตามตรวจสอบ
คุณภาพสิ่งแวดล้อม ตามรายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ที่ได้รับความเห็นชอบจากสำนักงานนโยบาย
และแผนทรัพยากรธรรมชาติและสิ่งแวดล้อม ตามหนังสือที่ ทส ๑๐๐๙.๕/๔๕๑๕ ลงวันที่ ๑๘ มิถุนายน ๒๕๕๑
อย่างเคร่งครัด

ออกให้ ณ วันที่ ๒๐ พ.ค. ๒๕๕๕


ผู้อำนวยการส่วนยุทธศาสตร์
ปฏิบัติราชการแทนผู้ว่าราชการกรุงเทพมหานคร

ตามหนังสือแจ้งความประสงค์ฯ ตามแบบ กทม.๑ เลขรับที่ ๒๕๘
ลงวันที่ ๒๐ เดือน พฤษภาคม พ.ศ. ๒๕๕๕
ราย บริษัท โอ๊คทรี จำกัด

ผู้อำนวยการกอง


วันที่ ๒๐ พ.ค. ๒๕๕๕
วันที่ ๒๐ พ.ค. ๒๕๕๕
วันที่ ๒๐ พ.ค. ๒๕๕๕
วันที่ ๒๐ พ.ค. ๒๕๕๕

คำเตือน

๑. ถ้าผู้แจ้งฯจะบอกเลิกตัวผู้ควบคุมงานที่ระบุชื่อไว้ในใบแจ้ง หรือผู้ควบคุมงานจะบอกเลิกการเป็นผู้ควบคุมงาน ให้มีหนังสือแจ้งให้เจ้าพนักงานท้องถิ่นทราบ ทั้งนี้ ไม่เป็นการกระทบถึงสิทธิและหน้าที่ทางแพ่งระหว่างผู้แจ้งฯ กับผู้ควบคุมงานนั้น ในการบอกเลิกตัวผู้ควบคุมงานนี้ ผู้แจ้งฯ จะต้องระงับการดำเนินการก่อสร้าง ดัดแปลง รื้อถอน หรือเคลื่อนย้ายอาคารไว้ก่อนจนกว่าจะมีผู้ควบคุมงานคนใหม่ และ มีหนังสือแจ้งพร้อมกับส่งมอบหนังสือแสดงความยินยอมของผู้ควบคุมงานคนใหม่ ให้แก่เจ้าพนักงานท้องถิ่นแล้ว

๒. ผู้แจ้งฯ ที่ต้องจัดให้มีพื้นที่ หรือสิ่งทีสร้างขึ้นเพื่อใช้เป็นที่จอดรถยนต์ ที่กัลับริถ และทางเข้า ออกของรถตามที่กำหนดไว้ในใบแจ้งฯ ฉบับนี้ ต้องแสดงที่จอดรถยนต์ ที่กัลับริถ และทางเข้าออกของรถไว้ ให้ปรากฏตามแผนผังบริเวณที่ได้แจ้งให้ กรุงเทพมหานคร ทราบ การดัดแปลงหรือใช้ที่จอดรถ ที่กัลับริถ และทางเข้าออกของรถเพื่อการอื่นนั้นต้องได้รับอนุญาตจากเจ้าพนักงานท้องถิ่น

๓. เมื่อผู้แจ้งความประสงค์จะก่อสร้าง ดัดแปลง หรือเคลื่อนย้ายอาคารประเภทควบคุม การใช้ได้กระทำการตามที่ได้แจ้งเสร็จแล้ว ต้องแจ้งเป็นหนังสือให้เจ้าพนักงานท้องถิ่นทราบ ตามแบบที่เจ้าพนักงานท้องถิ่นกำหนด เพื่อทำการตรวจสอบการก่อสร้าง ดัดแปลง หรือเคลื่อนย้ายอาคาร นั้น และห้ามมิให้ใช้อาคารนั้นเพื่อกิจการดังที่ได้แจ้งไว้ ภายในกำหนด ๓๐ วัน นับตั้งแต่วันที่เจ้าพนักงานท้องถิ่นได้รับแจ้ง

เอกสารแบบ 3
สำเนาใบรับรองการก่อสร้างอาคาร ตัดแปลงอาคาร
หรือเคลื่อนย้ายอาคาร (จ.6)

อาคารโรงแรม
อาคารพาณิชย์
อาคารหอประชุม

อาคารประเภทควบคุมการใช้ ตามมาตรา 32
อาคารสำนักงานหรือที่ทำการ
การตัดแปลงอาคาร

แบบ อ. ๒

000131



ค่าเดือน

ให้จัดส่งรายงานผลการตรวจสอบใหญ่ของอาคาร ตามกฎกระทรวง
ว่าด้วยหลักเกณฑ์การตรวจสอบอาคาร พ.ศ. 2548 ภายใน 30
ก่อนใบรับรองการก่อสร้างอาคารจะมีระยะเวลาครบ 1 ปี

ใบรับรองการก่อสร้างอาคาร ตัดแปลงอาคาร หรือเคลื่อนย้ายอาคาร

เลขที่ ๑๙ / ๒๕๕๕

โดย

บริษัท โอ๊คทรี จำกัด

เจ้าของอาคาร/ผู้ครอบครองอาคาร

ใบรับรองฉบับนี้แสดงว่า

อยู่บ้านเลขที่ ๑๙๘/๗ ตรอก/ซอย ถนน รัชดาภิเษก หมู่ที่

ตำบล/แขวง จันทเกษม อำเภอ เขต จตุจักร จังหวัด กรุงเทพมหานคร

ได้ทำการ ก่อสร้างและตัดแปลง อาคาร เป็นไปโดยถูกต้องตามที่ได้รับอนุญาตในใบอนุญาต

เลขที่ ๒๕๘ / ๒๕๕๕ ลงวันที่ ๒๐ เดือน พฤษภาคม พ.ศ. ๒๕๕๕

ซึ่งอาคารดังกล่าวเป็นอาคารประเภทควบคุมการใช้ เจ้าพนักงานท้องถิ่นจึงออกใบรับรองให้ดังต่อไปนี้

ข้อ ๑ เป็นอาคาร ชั้นใต้ดิน ๒ ชั้น

(๑) ชนิด ดัก ๒๙ ชั้น จำนวน ๑ หลัง เพื่อใช้เป็น โรงแรม (๒๓๗ ห้อง)-ภัตตาคาร-

โดยมีที่จอดรถ ที่กั๊บลรด และทางเข้าออกของรด จำนวน ๒๓๐ คัน พาณิขย์-สำนักงาน-ห้องประชุม-จอรดลยนร

(๒) ชนิด จำนวน เพื่อใช้เป็น

โดยมีที่จอดรถ ที่กั๊บลรด และทางเข้าออกของรด จำนวน คัน

(๓) ชนิด จำนวน เพื่อใช้เป็น

โดยมีที่จอดรถ ที่กั๊บลรด และทางเข้าออกของรด จำนวน คัน

ที่บ้านเลขที่ ๘๙๙/๙๐๙ ถนน สาทร

หมู่ที่ ๘ ตำบล/แขวง สลิม อำเภอ/เขต บางรัก จังหวัด กรุงเทพมหานคร

โดย บริษัท โอ๊คทรี จำกัด เป็นเจ้าของอาคาร และ บริษัท โอ๊คทรี จำกัด

เป็นผู้ครอบครองอาคาร อยู่ในที่ดิน โฉนดที่ดิน เลขที่/น.ส.๓/๓๐/๓๐/๓๐/๓๐ เลขที่ ๓๐๗๘, ๕๐๒๑, ๕๐๒๒

เป็นที่ดินของ นาย... ตันจันทรพงศ์ และ นายดาที ตันจันทรพงศ์

ค่าธรรมเนียมใบรับรองการก่อสร้างและตัดแปลงอาคาร ฉบับละ ๑๐,๐๐๐ บาท

ข้อ ๒ ผู้ได้รับใบรับรองต้องปฏิบัติตามเงื่อนไข ดังต่อไปนี้

(๑) ผู้ได้รับใบรับรองต้องปฏิบัติตามหลักเกณฑ์ วิธีการ และเงื่อนไขตามที่กำหนดในกฎกระทรวง
และหรือข้อบัญญัติท้องถิ่น ซึ่งออกตามความในมาตรา ๘ (๑๑) มาตรา ๙ หรือมาตรา ๑๐ แห่งพระราชบัญญัติ
ควบคุมอาคาร พ.ศ. ๒๕๒๒ แก้ไขเพิ่มเติมตามพระราชบัญญัติควบคุมอาคาร (ฉบับที่ ๒) พ.ศ. ๒๕๓๕ และ (ฉบับที่ ๓) พ.ศ. ๒๕๔๓

(๒) ต้องปฏิบัติตามเงื่อนไขแนบท้ายใบรับรองฉบับนี้

เงื่อนไขท้ายใบรับรองการก่อสร้างและตัดแปลงอาคารเลขที่ ๑๙ / ๒๕๕๕
ราย บริษัท ไอศกรี จำกัด

ผู้ได้รับใบรับรองต้องปฏิบัติตามมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อมและ
มาตรการติดตามตรวจสอบคุณภาพสิ่งแวดล้อมตามรายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อมที่ได้รับความ
เห็นชอบจากสำนักงานนโยบายและแผนทรัพยากรธรรมชาติและสิ่งแวดล้อมตามหนังสือที่ พส ๑๐๐๙.๕/๔๕๑๕
ลงวันที่ ๑๘ มิถุนายน ๒๕๕๑



๕๕. ศาลากลาง จังหวัดขอนแก่น
ศาลากลางจังหวัดขอนแก่น
ศาลากลางจังหวัดขอนแก่น

ศาลากลางจังหวัดขอนแก่น
ศาลากลางจังหวัดขอนแก่น
ศาลากลางจังหวัดขอนแก่น

แสดงแจ้ง

คำเตือน

ศาลากลางจังหวัดขอนแก่นเป็นอาคารสาธารณะและสถานที่สำคัญ

๕๕. ศาลากลาง จังหวัดขอนแก่น ห้ามเจ้าของหรือผู้ครอบครองอาคารใช้หรือยินยอมให้บุคคลใดใช้อาคารเพื่อกิจการอื่น นอกจาก
กิจการของราชการหรือราชการส่วนท้องถิ่น
หรือในบริเวณบริเวณ

๒. ห้ามเจ้าของหรือผู้ครอบครองอาคาร เปลี่ยนการใช้อาคารบางประเภท ควบคุมการใช้สำหรับ
กิจการหนึ่งไปใช้เป็นอาคารประเภทควบคุมการใช้สำหรับอีกกิจการหนึ่ง เว้นแต่จะได้รับอนุญาตจากเจ้าพนักงาน
ท้องถิ่น

๓. ห้ามเจ้าของหรือผู้ครอบครองอาคารที่ต้องมีพื้นที่หรือสิ่งก่อสร้างขึ้นเพื่อใช้เป็นที่จอดรถ ที่กลับรถ
และทางเข้าออกของรถตามที่กำหนดไว้ในกฎกระทรวง ดัดแปลง หรือใช้ที่จอดรถ ที่กลับรถ และทางเข้าออกของ
รถนั้นเพื่อการอื่นไม่ว่าทั้งหมดหรือบางส่วน เว้นแต่จะได้รับใบอนุญาตจากเจ้าพนักงานท้องถิ่น

๔. ผู้ได้รับใบรับรองต้องแสดงใบรับรองฉบับนี้ไว้ในที่เปิดเผยและเห็นได้ง่าย ณ อาคารนั้น

เอกสารแนบ 4
สำเนาใบอนุญาตประกอบธุรกิจโรงแรม (ร.ร.2)
และบันทึกการแจ้งเปลี่ยนชื่อโรงแรม



ทะเบียนเลขที่..... ๓๘๐

ใบอนุญาตเลขที่..... ๔/๒๕๖๖

กระทรวงมหาดไทย

ใบอนุญาตประกอบธุรกิจโรงแรม

ใบอนุญาตฉบับนี้ให้ไว้เพื่อแสดงว่า บริษัท โอ๊คทรี จำกัด

โดย

ได้รับอนุญาตให้ประกอบธุรกิจโรงแรมตามมาตรา ๑๕ แห่งพระราชบัญญัติ
โรงแรม พ.ศ. ๒๕๕๗ โดยใช้ชื่อภาษาไทยว่า โซ แบงคอก

ชื่อภาษาต่างประเทศ (ถ้ามี) SO BANGKOK

โรงแรมประเภท ๓ จำนวนห้องพัก ๒๓๗ ห้อง

สถานที่ตั้ง เลขที่ ๒ ถนนสาทรเหนือ แขวงสีลม

เขตบางรัก กรุงเทพมหานคร

ตั้งแต่วันที่ ๓๑ เดือน มกราคม พ.ศ. ๒๕๖๖ ถึง วันที่ ๓๐ เดือน มกราคม พ.ศ. ๒๕๗๑

ออกให้ ณ วันที่ ๒ เดือน ธันวาคม พ.ศ. ๒๕๖๕

รองอธิบดีกรมการปกครอง ปฏิบัติราชการแทน

อธิบดีกรมการปกครอง

นายทะเบียนโรงแรมกรุงเทพมหานคร
ประทับตราประจำตำแหน่งเป็นสำคัญ

ที่ มท ๐๓๐๗.๖/ ๓๐๓๖



กรมการปกครอง

ถนนอังสฤงค์ กทม. ๑๐๒๐๐

๒ ธันวาคม ๒๕๖๕

เรื่อง ขอต้ออายุใบอนุญาตประกอบธุรกิจโรงแรม “โซ แบงคอก”

เรียน ผู้ประกอบธุรกิจโรงแรม “โซ แบงคอก”

อ้างถึง แบบคำขอต้ออายุใบอนุญาตประกอบธุรกิจโรงแรม (แบบ ร.ร. ๑/๑) เลขที่รับ ๑๔๑/๒๕๖๕
ลงวันที่ ๑๑ พฤศจิกายน ๒๕๖๕

สิ่งที่ส่งมาด้วย แบบบันทึกช่วยจำในการประกอบธุรกิจโรงแรม

จำนวน ๑ ชุด

ตามที่ บริษัท โอ๊คทรี จำกัด โดย [REDACTED] กรรมการ
ผู้มีอำนาจลงนามผูกพันบริษัท ผู้ประกอบธุรกิจโรงแรม “โซ แบงคอก” ได้ยื่นคำขอต้ออายุใบอนุญาตประกอบธุรกิจ
โรงแรมดังกล่าว ต่อนายทะเบียนโรงแรมกรุงเทพมหานคร ความละเอียดตามอ้างถึง นั้น

กรมการปกครองขอเรียนว่า นายทะเบียนโรงแรมกรุงเทพมหานครได้พิจารณาอนุญาตให้ท่าน
ต้ออายุใบอนุญาตประกอบธุรกิจโรงแรมดังกล่าวแล้ว ดังนั้น จึงขอให้ท่านไปรับใบอนุญาตประกอบธุรกิจโรงแรมข้างต้น
พร้อมกับชำระค่าธรรมเนียมการต้ออายุใบอนุญาต ณ ส่วนการรักษาสงบเรียบร้อย ๓ สำนักการสอบสวน
และนิติการ กรมการปกครอง (วังไชยา) ถนนนครสวรรค์ แขวงสี่แยกมหานาค เขตดุสิต กรุงเทพมหานคร ทั้งนี้
ขอความร่วมมือในการใช้บันทึกช่วยจำฯ เพื่อเป็นประโยชน์ในการบริหารจัดการโรงแรมต่อไป รายละเอียดปรากฏ
ตามสิ่งที่ส่งมาด้วย อนึ่ง เนื่องจากโรงแรมดังกล่าวเป็นโครงการหรือกิจการที่มีการจัดทำรายงานการประเมินผล
กระทบสิ่งแวดล้อม ดังนั้น ขอให้จัดทำรายงานผลการปฏิบัติตามมาตรการที่กำหนดไว้ในรายงานการประเมินผล
กระทบสิ่งแวดล้อมเสนอต่อนายทะเบียนโรงแรมกรุงเทพมหานคร ในฐานะเจ้าหน้าที่ซึ่งมีอำนาจอนุญาตด้วย รวมทั้ง
ขอให้ถือปฏิบัติตามเงื่อนไขที่คณะกรรมการผู้ชำนาญการพิจารณารายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม
ด้านโครงการบริการชุมชน ได้มีมติเห็นชอบรายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อมดังกล่าว ซึ่งสำนักงาน
นโยบายและแผนทรัพยากรธรรมชาติและสิ่งแวดล้อมได้แจ้งให้ทราบแล้วด้วย

จึงเรียนมาเพื่อทราบและดำเนินการ

ขอแสดงความนับถือ



ผู้อำนวยการสำนักการสอบสวนและนิติการ ปฏิบัติราชการแทน

อธิบดีกรมการปกครอง


นายทะเบียนโรงแรมกรุงเทพมหานคร

สำนักการสอบสวนและนิติการ

ส่วนการรักษาสงบเรียบร้อย ๓

โทร./โทรสาร ๐ ๒๓๕๖ ๕๕๑๘

MR-05



น.4/2

ที่ มท ๐๓๐๗.๖/๖๐๖๖๔



กรมการปกครอง
ถนนรัชฎาภิเศก กทม. ๑๐๒๐๐

๒๖ กันยายน ๒๕๕๙

เรื่อง บริษัท โอ๊คทรี จำกัด ขอเปลี่ยนชื่อโรงแรม

เรียน ผู้ประกอบธุรกิจโรงแรม โซฟิเทล โซ แบงคอก

ตามที่ บริษัท โอ๊คทรี จำกัด โดย น. [REDACTED] สำนักงานใหญ่ ตั้งอยู่เลขที่ ๒ ถนนสาทรเหนือ แขวงสีลม เขตบางรัก กรุงเทพมหานคร ผู้ประกอบธุรกิจโรงแรม โซฟิเทล โซ แบงคอก ตั้งอยู่เลขที่ ๒ ถนนสาทรเหนือ แขวงสีลม เขตบางรัก กรุงเทพมหานคร เป็นโรงแรมประเภท ๓ มีจำนวนห้องพัก ๒๓๗ ห้อง ออกให้ ณ วันที่ ๓๑ มกราคม ๒๕๕๖ ได้รับอนุญาตให้ประกอบธุรกิจโรงแรมตั้งแต่วันที่ ๓๑ มกราคม ๒๕๕๖ จนถึงวันที่ ๓๐ มกราคม ๒๕๖๑ ได้ยื่นคำขอเปลี่ยนชื่อโรงแรมจาก “โซฟิเทล โซ แบงคอก” เป็น “โซ โซฟิเทล แบงคอก” และเปลี่ยนชื่อจากภาษาอังกฤษ “SOFTEL SO BANGKOK” เป็น “SO SOFTEL BANGKOK” นั้น

นายทะเบียนโรงแรมกรุงเทพมหานครพิจารณาอนุญาตให้เปลี่ยนชื่อโรงแรมของผู้ประกอบธุรกิจ โรงแรมได้ตามคำขอ จึงขอให้ท่านไปรับใบอนุญาตประกอบธุรกิจโรงแรม ณ ส่วนรักษาความสงบเรียบร้อย ๓ สำนักการสอบสวนและนิติการ กรมการปกครอง (วังไชยา) ถนนนครสวรรค์ เขตดุสิต กรุงเทพมหานคร

จึงเรียนมาเพื่อทราบ

ขอแสดงความนับถือ



ผู้อำนวยการส่วนรักษาความสงบเรียบร้อย ๓ ปฏิบัติราชการแทน

ผู้อำนวยการสำนักการสอบสวนและนิติการ ปฏิบัติราชการแทน

อธิบดีกรมการปกครอง

นายทะเบียนโรงแรมกรุงเทพมหานคร

สำนักการสอบสวนและนิติการ
ส่วนรักษาความสงบเรียบร้อย ๓
โทร./โทรสาร ๐-๒๓๕๖-๙๕๕๙

เอกสารแบบ 5
สำหรับหนังสือรับรองจดทะเบียนบริษัท

ที่ 10031220049630



สำนักงานทะเบียนหุ้นส่วนบริษัทกลาง
กรมพัฒนาธุรกิจการค้า กระทรวงพาณิชย์

หนังสือรับรอง

ขอรับรองว่าบริษัทนี้ ได้จดทะเบียนเป็นนิติบุคคล ตามประมวลกฎหมายแพ่งและพาณิชย์
เมื่อวันที่ 31 มีนาคม 2548 ทะเบียนนิติบุคคลเลขที่ 0105548045937

ปรากฏข้อความในรายการตามเอกสารทะเบียนนิติบุคคล ณ วันออกหนังสือนี้ ดังนี้

1. ชื่อบริษัท บริษัท โอ๊คทรี จำกัด

2. กรรมการของบริษัทมี 6 คน ตามรายชื่อต่อไปนี้

1.

3.

5.

2. นายวีรวัฒน์ องค์กรวิญญู

4. นางทศพร อังสุรังษี

6. นายวรต ตันติพิภพ/

3. จำนวนหรือชื่อกรรมการซึ่งลงชื่อผูกพันบริษัทได้คือ

กรรมการสองในห้าคนนี้ลงลายมือชื่อร่วมกันและประทับตราสำคัญ

ของบริษัท/

4.ทุนจดทะเบียน 850,000,000.00 บาท / แปดร้อยห้าสิบล้านบาทถ้วน/

5. สำนักงานใหญ่ ตั้งอยู่เลขที่ 2 ถนนสาทรเหนือ แขวงสีลม เขตบางรัก กรุงเทพมหานคร/

6. วัตถุที่ประสงค์ของบริษัทมี 29 ข้อ ดังปรากฏในสำเนาเอกสารแนบท้ายหนังสือรับรองนี้ จำนวน 2 แผ่น โดยมีลายมือชื่อ

นายทะเบียนซึ่งรับรองเอกสารเป็นสำคัญ

ออกให้ ณ วันที่ 15 เดือน ธันวาคม พ.ศ. 2565



นายทะเบียน

คำเตือน : ผู้ใดควรตรวจสอบข้อความทราบท้ายหนังสือรับรองฉบับนี้ทุกครั้ง



กรมพัฒนาธุรกิจการค้า กระทรวงพาณิชย์
Department of Business Development
Ministry of Commerce

ก้าวสู่ปารุภกิจ
สู่ยุคดิจิทัล

Leading Business
Towards Digital
Transformation



จัดพิมพ์ เมื่อเวลา 10:38 น.

Ref:6510031220049630

1/4

ที่ 10031220049630



สำนักงานทะเบียนหุ้นส่วนบริษัทกลาง
กรมพัฒนาธุรกิจการค้า กระทรวงพาณิชย์

หนังสือรับรอง

ขอคารทราบ ประกอบหนังสือรับรอง ฉบับที่ 10031220049630

- นิติบุคคลนี้ได้ส่งงบการเงินปี 2564
- หนังสือรับรองเฉพาะข้อความที่ห้าง/บริษัทได้นำมาจดทะเบียนไว้เพื่อผลทางกฎหมายเท่านั้น ข้อเท็จจริงเป็นสิ่งที่ควรหาไว้พิจารณาฐานะ
- นายทะเบียนอาจเพิกถอนการจดทะเบียน ถ้าปรากฏว่าข้อความอันเป็นสาระสำคัญที่จดทะเบียน ไม่ถูกต้อง หรือเป็นเท็จ



กรมพัฒนาธุรกิจการค้า กระทรวงพาณิชย์
Department of Business Development
Ministry of Commerce

ก้าวสู่อนาคต
สู่ยุคดิจิทัล

Leading Business
Towards Digital
Transformation



วัตถุประสงค์ของ ห้างหุ้นส่วน/บริษัท นี้ มี.....29.....ข้อ ดังนี้

- (1) ประกอบกิจการผลิตภัณฑฺ์โลหะไฟฟ้าและอุปกรณ์ไฟฟ้า รวมทั้งอะไหล่เครื่องใช้และอิเล็กทรอนิกส์ทุกชนิด.....
- (2) ประกอบกิจการอุตสาหกรรมผลิต ประกอบและซ่อมเครื่องรับโทรทัศน์ เครื่องรับวิทยุ เครื่องขยายเสียง.....
เครื่องบันทึกเสียง เครื่องมือแพทย์ เครื่องเล่นจานเสียง เครื่องคอมพิวเตอร์ไฟฟ้า
- (3) ประกอบกิจการอุตสาหกรรมบรรจุอาหารกระป๋องทุกชนิด
- (4) กู้ยืมเงิน เบิกเงินกู้ยืมธนาคารนิติบุคคลหรือสถาบันการเงินอื่น และให้กู้ยืมเงินหรือให้เครดิตด้วยวิธีการอื่น โดยจะมีหลักประกันหรือไม่ก็ตาม รวมทั้งการรับออก โฉน และสละหลังตัวเงิน หรือตราสารที่เปลี่ยนมือได้อย่างอื่น
- (5) ทำการประกอบกิจการโรงงานอุตสาหกรรมร่วมผลิต ประกอบและซ่อมเครื่องรับวิทยุ เครื่องรับโทรทัศน์ ชิ้นส่วน-อะไหล่ของเครื่องรับวิทยุโทรทัศน์ เครื่องคิดเลข โทรทัศน์วงจรปิด กล้องโทรทัศน์ เครื่องบันทึกเสียง
- (6) ทำการประกอบกิจการโรงงานอุตสาหกรรมผลิตเครื่องอุปโภค บริโภค ตั้งโรงงาน ทำเครื่องกระป๋อง โรงงานทอผ้า
- (7) ทำการส่งสินค้าจากต่างประเทศ และส่งสินค้าไปยังต่างประเทศตามวัตถุประสงค์ของบริษัท
- (8) ทำการซื้อ-ขายสินค้า เครื่องไฟฟ้าทุกชนิด และเคมีภัณฑ์ทุกชนิด
- (9) ทำการเป็นนายหน้า ตัวแทน ตัวแทนค้าต่างในการซื้อขายสินค้าทุกชนิด(ยกเว้นกิจการประกันภัย กิจการหาสมาชิกให้สังคม และกิจการซื้อขายหลักทรัพย์)
- (10) ทำการรับเหมาก่อสร้าง และรับจ้างทำของตามวัตถุประสงค์ทั้งหมด ทำการโดยตนเอง เป็นตัวแทนในการขนส่งสินค้า และคนโดยสาร ทั้งทางบก เรือ อากาศ
- (11) กู้หรือให้กู้ยืมเงินโดยมี หรือไม่เป็นหลักประกันตลอดทั้งการประกันหนี้สินทุกประเภท ทั้งในและนอกประเทศ และทำความตกลงใดๆ กับรัฐบาล เทศบาล หรือบุคคลอื่นใด เพื่อให้ได้มาซึ่งสิทธิสัมปทาน ประทานบัตร และเอกสิทธิ์ใดๆ บรรดาที่บริษัท เห็นว่าจะทำให้สำเร็จตามวัตถุประสงค์ของบริษัท
- (12) เข้าเป็นคู่ถือหุ้นในบริษัทจำกัด หรือเป็นหุ้นส่วนจากัดความรับผิดชอบในหุ้นส่วน เพื่อประโยชน์ของบริษัท
- (13) ประกอบธุรกิจบริการรับเป็นผู้จัดการและดูแลผลประโยชน์ เป็นผลประโยชน์ และจัดการทรัพย์สินให้แก่ผู้อื่น
- (14) ทำกิน ซื้อเช่า เช่าซื้อ ขายฝากสิ่งของทรัพย์สินต่างๆ ที่เป็นเครื่องใช้ในบ้านสำนักงาน เครื่องใช้ในบ้าน เครื่องครัว เครื่องตกแต่งบ้านพาหนะ
- (15) ทำการส่งเข้ามา และส่งออกเพื่อการจัดซื้อและจำหน่ายหากำไร ซึ่งสินค้าและอุปกรณ์ทุกชนิด ได้แก่ สินค้าเกี่ยวกับเครื่องมือกล เครื่องมือวิทยาศาสตร์ เครื่องเลเซอร์และอุปกรณ์ เครื่องคำนวณ เครื่องวัดระยะทาง เครื่องเรดาร์ กล้องส่องในทางมืด เครื่องพิมพ์อิเล็กทรอนิกส์ เครื่องอิเล็กทรอนิกส์ ที่ใช้ในการทหาร เครื่องตรวจคลื่นสมอง เครื่องใช้สำหรับอิเล็กทรอนิกส์ เครื่องวิเคราะห์สารเคมี และอุปกรณ์ทุกชนิด เครื่องฉายรังสีทุกชนิด เครื่องตรวจหัวใจด้วยไฟฟ้า และเบตเตอร์ เครื่องเทเลกซ์ เครื่องมือทุนแรงทุกอย่างทุกชนิด รถยนต์ รถจักรยานยนต์ รถลากเข็นทุกชนิด เครื่องจักรกลและเครื่องยนต์และอุปกรณ์ทุกชนิด สินค้าอิเล็กทรอนิกส์ และเครื่องไฟฟ้าและอุปกรณ์ทุกชนิด



วัตถุประสงค์ของ ห้างหุ้นส่วน/บริษัท นี้ มี.....29.....ข้อ ดังนี้

(16) ประกอบกิจการพัฒนา ที่อยู่อาศัย แลกเปลี่ยน เช่า ให้เช่า ยืม ให้ยืม จำนำส่วนของผู้ถือหุ้นเงินใด ๆ ทั้ง

สินทรัพย์และอสังหาริมทรัพย์ เพื่อดำเนินการตามวัตถุประสงค์ของบริษัทดังกล่าวข้างต้นตลอดจนเพื่อเป็นการชำระหนี้ของ
ลูกหนี้ต่อบริษัท ทั้งภายในขอบเขตแห่งวัตถุประสงค์ของบริษัท และมีไว้เป็นการค้ำประกันค่าเช่าค่าตอบแทนหรือกิจการเครดิตฟองซิเอร์
นอกจากนี้เจ้าผู้ค้ำประกันบุคคลหรือนิติบุคคลในการปฏิบัติการชำระหนี้ใดๆ หรือการปฏิบัติงานของบริษัท ตามกฎหมายว่าด้วย
คนเช่าเมือง

(17) บริษัทมีอำนาจออกหุ้นโดยราคาสูงกว่ามูลค่าหุ้นที่ตราไว้

(18) ทำการจัดตั้งสำนักงานสาขาหรือแต่งตั้งตัวแทน ทั้งภายในและภายนอกประเทศ

(19) เข้าเป็นหุ้นส่วนจำกัดความรับผิดชอบในห้างหุ้นส่วน และเป็นผู้ถือหุ้นในบริษัทจำกัดอื่น

(20) ประกอบกิจการค้ายารักษาและป้องกันโรคสำหรับคนและสัตว์ เครื่องเวชภัณฑ์ เคมีภัณฑ์ เครื่องมือแพทย์ และ
เภสัชกรรม ปุ๋ย ยาปราบศัตรูพืช ยาปรุงรสและสัตว์ทุกชนิด เครื่องมือเครื่องใช้ทางวิทยาศาสตร์

(21) ประกอบกิจการค้ากระดาษ เครื่องเขียน แบบเรียน แบบพิมพ์ หนังสือ อุปกรณ์การเรียน เครื่องคำนวณ เครื่องพิมพ์
อุปกรณ์การพิมพ์ สิ่งพิมพ์ หนังสือพิมพ์ ตู้เก็บเอกสาร และเครื่องใช้ในสำนักงานทุกชนิด

(22) ประกอบกิจการโรงแรม กภัตตาคาร บาร์ ไนท์คลับ อพาร์ตเมนต์ โรงภาพยนตร์ และโรงมหรสพอื่น สถานพัก
ตากอากาศ สนามกีฬา สระว่ายน้ำ

(23) ประกอบกิจการสั่งเข้ามาจำหน่ายในประเทศ และส่งออกไปจำหน่ายยังต่างประเทศ ซึ่งสินค้าตามที่กำหนดไว้
ในวัตถุประสงค์

(24) ประกอบกิจการบริการทางด้านกฎหมาย ทางบัญชี ทางวิศวกรรม ทางสถาปัตยกรรม รวมทั้งกิจการโฆษณา

(25) ประกอบธุรกิจบริการรับค้าประกันหนี้สิน ความรับผิด และการปฏิบัติตามสัญญาของบุคคลอื่นรวมทั้งรับบริการ
ค้ำประกันบุคคลซึ่งเดินทางเข้ามาในประเทศไทยหรือเดินทางออกไปต่างประเทศตามกฎหมายว่าด้วยคนเข้าเมือง กฎหมายว่าด้วย
ภาษีอากร และกฎหมายอื่น

(26) ประกอบธุรกิจบริการรับเป็นที่ปรึกษาให้คำแนะนำปัญหาเกี่ยวกับด้านบริหารงาน พาณิชยกรรม อุตสาหกรรม
รวมทั้งปัญญการผลัด การตลาดและจัดจำหน่าย

(27) ประกอบกิจการประมูล เพื่อขายสินค้าและรับสร้างหาของ ตามวัตถุประสงค์ทั้งหมดให้แก่บุคคล คณะบุคคล
นิติบุคคล ส่วนราชการ และองค์กรของรัฐ

(28) ประกอบกิจการให้บริการในสถานประกอบการเพื่อสุขภาพ ประเภทสปาและกิจการนวดเพื่อสุขภาพ
หรือเพื่อเสริมความงาม

(29) ประกอบกิจการให้บริการเช่าที่พักรถทางอิเล็กทรอนิกส์



เอกสารแนบ 6
สำเนาเอกสารขออนุมัติการเชื่อมท่อน้ำเสียลงสู่บ่อรวบรวมน้ำเสีย
ของกรุงเทพมหานคร



ที่ กท ๑๐๐๓/ ๗๙๘

สำนักงานจัดการคุณภาพน้ำ สำนักการระบายน้ำ
๑๒๓ ถนนมิตรไมตรี เขตดินแดง กทม. ๑๐๔๐๐

๓๑ มีนาคม ๒๕๕๔

เรื่อง ขออนุมัติการเชื่อมต่อน้ำเสียลงสู่บ่อรวบรวมน้ำเสียของกรุงเทพมหานคร
โครงการ โรงแรม โซฟีเทล วิลล์ดา

เรียน กรรมการผู้จัดการบริษัท ไอศกรี จำกัด

อ้างถึง ๑.หนังสือเลขที่ SFV-LET-PLE No.๐๐๓/๕๓ ลงวันที่ ๑๑ พฤศจิกายน ๒๕๕๓
๒.หนังสือเลขที่ SFV-LET-PLE No.๐๐๔/๕๔ ลงวันที่ ๑๒ กุมภาพันธ์ ๒๕๕๔

ตามหนังสือที่อ้างถึง ๑.บริษัทฯ ขออนุมัติ Shop Drawing การเชื่อมต่อน้ำเสียลงสู่บ่อรวบรวมน้ำเสียของกรุงเทพมหานคร โครงการ โรงแรม โซฟีเทล วิลล์ดา และตามหนังสือที่อ้างถึง ๒. บริษัทฯ ได้ส่งรายละเอียดเพิ่มเติมขั้นตอนการเชื่อมต่อน้ำเสียลงสู่บ่อรวบรวมน้ำเสียของกรุงเทพมหานคร มาเพื่อพิจารณาอนุมัติรูปแบบการเชื่อมต่อน้ำเสียลงสู่บ่อรวบรวมน้ำเสียของกรุงเทพมหานคร โครงการ โรงแรม โซฟีเทล วิลล์ดา นั้น

สำนักงานจัดการคุณภาพน้ำ สำนักการระบายน้ำ ได้พิจารณาแล้วและอนุมัติการเชื่อมต่อน้ำเสียลงสู่บ่อรวบรวมน้ำเสียของกรุงเทพมหานคร ของโครงการ โรงแรม โซฟีเทล วิลล์ดา

จึงเรียนมาเพื่อทราบ

ขอแสดงความนับถือ



ผู้อำนวยการสำนักงานจัดการคุณภาพน้ำ
สำนักการระบายน้ำ

กลุ่มงานพัฒนาระบบบำบัดน้ำเสีย

โทร. ๐ ๒๒๔๖ ๐๒๗๔

โทรสาร ๐ ๒๒๔๖ ๐๒๗๔



ที่ กท 4303/2818

สำนักงานเขตบางรัก

5 ถนนนเรศ กทม. 10500

๕ ๑ ส. ก. 2550

เรื่อง ขออนุญาตรับรองการอนุญาตเชื่อมทางสาธารณะ และระบายน้ำลงสู่ที่ระบายน้ำสาธารณะประโยชน์

เรียน [REDACTED] กรรมการผู้จัดการบริษัท โอ๊คทรี จำกัด

อ้างถึง หนังสือบริษัทฯ ลงวันที่ 25 มิถุนายน 2550

ตามหนังสือที่อ้างถึง บริษัทฯ มีความประสงค์จะขออนุญาตให้เชื่อมทางสาธารณะ และระบายน้ำลงสู่ที่ระบายน้ำสาธารณะประโยชน์ ของที่ดิน โฉนดที่ดินเลขที่ 3078, 5021 และ 5022 เลขที่ดิน 97, 96 และ 95 ตำบลลิ้ม (บางรัก) อำเภอบางรัก กรุงเทพมหานคร ซึ่งตั้งอยู่บริเวณถนนสาทรเหนือและถนนพระรามที่ 4 เขตบางรัก กรุงเทพมหานคร เพื่อนำหนังสือรับรองฯ ไปใช้เป็นเอกสารประกอบการขออนุญาตก่อสร้างโครงการ โรงแรม ขนาด 281 ห้อง จำนวน 1 อาคาร นั้น

สำนักงานเขตบางรักได้พิจารณาแล้ว อนุญาตให้ [REDACTED] ดำเนินการตามประสงค์ได้ ทั้งนี้ จะต้องปฏิบัติให้เป็นไปตามเงื่อนไข ดังต่อไปนี้

1. จะต้องปฏิบัติตามข้อบัญญัติกรุงเทพมหานคร เรื่อง การควบคุมอาคาร พ.ศ. 2544 ออกโดยอาศัยอำนาจตามความในมาตรา 9 และมาตรา 10 แห่งพระราชบัญญัติควบคุมอาคาร พ.ศ. 2522 แก้ไขเพิ่มเติมโดยพระราชบัญญัติควบคุมอาคาร (ฉบับที่ 2) พ.ศ. 2535
2. จะต้องปฏิบัติตามกฎกระทรวง ฉบับที่ 51 (พ.ศ. 2541) ออกตามความในพระราชบัญญัติควบคุมอาคาร พ.ศ. 2522

อนึ่ง เมื่อทางบริษัทฯ ได้รับใบอนุญาตให้ทำการก่อสร้างตามโครงการดังกล่าวแล้ว ก่อนที่จะทำการเชื่อมทางและระบายน้ำลงสู่ที่ระบายน้ำสาธารณะประโยชน์ จะต้องแจ้งขออนุญาตจากสำนักงานเขตบางรัก อีกครั้งหนึ่ง เมื่อสำนักงานเขตบางรักตรวจสอบและอนุญาตแล้ว จึงจะทำการตามที่ขออนุญาตได้

จึงเรียนมาเพื่อโปรดทราบ

ขอแสดงความนับถือ

ฝ่ายโยธา

โทร 0 2236 1398 ต่อ 6242

โทรสาร 0 2235 6445

[REDACTED]
ผู้ช่วยผู้อำนวยการเขต รักษาการแทน

ผู้อำนวยการเขตบางรัก

ปลัดบริหารการแทนผู้ว่าราชการกรุงเทพมหานคร

เอกสารแนบ 7
สำเนานำส่งรายงานการปฏิบัติตามมาตรการฯ

SO/ BANGKOK

วันที่ 1 มกราคม 2569

เรื่อง นำส่งรายงานผลการปฏิบัติตามมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อม และมาตรการติดตามตรวจสอบผลกระทบสิ่งแวดล้อม โครงการโรงแรม โซ แบงคอก (โรงแรมวีรันทา) ของบริษัท โอ๊คทรี จำกัด (ระยะดำเนินการ) ฉบับประจำเดือนกรกฎาคม-ธันวาคม พ.ศ.2568

เรียน อธิบดีกรมการปกครอง

สิ่งที่ส่งมาด้วย อุปกรณ์จัดเก็บข้อมูลรายงานในรูปแบบไฟล์อิเล็กทรอนิกส์ โครงการโรงแรม โซ แบงคอก (โรงแรมวีรันทา) ของบริษัท โอ๊คทรี จำกัด (ระยะดำเนินการ) ฉบับประจำเดือนกรกฎาคม-ธันวาคม พ.ศ.2568 จำนวน 3 อัน

ข้าพเจ้า บริษัท โอ๊คทรี จำกัด ในฐานะเจ้าของโครงการโรงแรม โซ แบงคอก (โรงแรมวีรันทา) ของบริษัท โอ๊คทรี จำกัด (ระยะดำเนินการ) ตั้งอยู่ที่ ถนนสาทรเหนือ แขวงสีลม เขตบางรัก กรุงเทพมหานคร โดยได้มอบหมายให้บริษัท เอ บี อี เอ็น เอ็นจิเนียริง คอนซัลแตนท์ จำกัด เป็นผู้จัดทำรายงานผลการปฏิบัติตามมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อม และมาตรการติดตามตรวจสอบผลกระทบสิ่งแวดล้อมของโครงการนั้น

บัดนี้ บริษัทฯ ได้จัดทำรายงานผลการปฏิบัติตามมาตรการฯ เสร็จเรียบร้อยแล้ว ดังสิ่งที่ส่งมาด้วย จึงใคร่ขอส่งรายงานดังกล่าวมาพร้อมหนังสือฉบับนี้เพื่อให้กรมการปกครองดำเนินการตามอำนาจหน้าที่ต่อไป

จึงเรียนมาเพื่อโปรดพิจารณา

ขอแสดงความนับถือ



กรรมการผู้จัดการ

วังทองช้าง

วศ.อ. ๖๙

SO/ BANGKOK

วันที่ 1 มกราคม 2569

เรื่อง นำส่งรายงานผลการปฏิบัติตามมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อม และมาตรการติดตามตรวจสอบผลกระทบสิ่งแวดล้อม โครงการโรงแรม โซ แบงคอก (โรงแรมวีรันทา) ของบริษัท โอ๊คทรี จำกัด (ระยะดำเนินการ) ฉบับประจำเดือนกรกฎาคม-ธันวาคม พ.ศ.2568

เรียน ผู้อำนวยการเขตบางรัก

สิ่งที่ส่งมาด้วย อุปกรณ์จัดเก็บข้อมูลรายงานในรูปแบบไฟล์อิเล็กทรอนิกส์ โครงการโรงแรม โซ แบงคอก (โรงแรมวีรันทา) ของบริษัท โอ๊คทรี จำกัด (ระยะดำเนินการ) ฉบับประจำเดือนกรกฎาคม-ธันวาคม พ.ศ.2568 จำนวน 1 อัน

ข้าพเจ้า บริษัท โอ๊คทรี จำกัด ในฐานะเจ้าของโครงการโรงแรม โซ แบงคอก (โรงแรมวีรันทา) ของบริษัท โอ๊คทรี จำกัด (ระยะดำเนินการ) ตั้งอยู่ที่ ถนนสาทรเหนือ แขวงสีลม เขตบางรัก กรุงเทพมหานคร โดยได้มอบหมายให้บริษัท เอ บี อี เอ็น เอ็นจิเนียริง คอนซัลแตนท์ จำกัด เป็นผู้จัดทำรายงานผลการปฏิบัติตามมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อม และมาตรการติดตามตรวจสอบผลกระทบสิ่งแวดล้อมของโครงการนั้น

บัดนี้บริษัทฯ ได้จัดทำรายงานผลการปฏิบัติตามมาตรการฯ เสร็จเรียบร้อยแล้วดังสิ่งที่ส่งมาด้วย และพร้อมกันนี้ได้จัดส่งรายงานดังกล่าวไปยังกรมการปกครองเรียบร้อยแล้ว

จึงเรียนมาเพื่อโปรดพิจารณา

ขอแสดงความนับถือ



กรรมการผู้จัดการ

14/1/69
15.23 น.

เอกสารแนบ 8
เอกสารบันทึกสถิติการใช้ไฟฟ้าและน้ำประปา ในปี 2569

Utility Consumption Cost for January 2026												
Date	Reading Meter	Total consum /day (Kwh)	On Peak Reading	Total consum /day (Kwh)	Off Peak Reading	Total consum /day (Kwh)	On Peak Demand (Kw)	Diff / day (Kw)	Off Peak Demand (Kw)	Diff / day (Kw)	Water Meter Reading (m³)	Consum / Day (m³)
1	33298.83	19952	13892.563	0	19406.270	19952	1.045	0	1.053	0	323,160.0	278.364
2	33318.782	19739	13892.563	12137	19426.222	7601	1.045	0	1.053	0	323438.395	236.295
3	33338.5	19268	13904.7	0	19433.8	19268	1.045	0	1.053	0	323674.69	219.653
4	33357.8	20266	13904.7	0	19453.1	20265	1.045	0	1.053	0	323894.343	236.694
5	33378.1	18911	13904.7	11766	19473.4	7146	1.045	0	1.053	0	324131.037	227.455
6	33397	18400	13916.5	11952	19480.5	6447	1.045	0	1.053	0	324358.492	231.567
7	33415.4	19451	13928.4	12088	19486.9	7337	1.045	0	1.053	0	324590.059	194.989
8	33434.8	19194	13940.5	12262	19494.3	6959	1.045	15	1.053	0	324785.048	231.389
9	33454	16622	13952.8	11054	19501.2	5568	1.06	0	1.053	0	325016.437	222.334
10	33470.6	16562	13963.8	0	19506.8	16562	1.06	0	1.053	0	325238.771	202.402
11	33487.2	17607	13963.8	0	19523.4	17607	1.06	0	1.053	0	325441.173	254.227
12	33504.8	17018	13963.8	10864	19541	6153	1.06	0	1.053	0	325695.400	220.886
13	33521.8	17882	13974.7	11513	19547.1	6370	1.06	0	1.053	0	325916.286	234.322
14	33539.7	18049	13986.2	11474	19553.5	6574	1.06	0	1.053	0	326150.608	224.372
15	33557.8	18247	13997.7	11476	19560.1	6771	1.06	0	1.053	0	326374.980	233.576
16	33576	18666	14009.1	12812	19566.9	5855	1.06	35	1.053	0	326608.556	229.532
17	33594.7	20538	14022	0	19572.7	20539	1.095	0	1.053	0.024	326838.088	243.772
18	33615.2	20112	14022	0	19593.2	20111	1.095	0	1.077	0	327081.86	255.578
19	33635.3	21358	14022	12696	19613.4	8662	1.095	0	1.077	0	327337.438	281.729
20	33656.7	20953	14034.7	13252	19622	7701	1.095	22	1.077	0	327619.167	242.497
21	33677.6	20642	14047.9	12902	19629.7	7741	1.117	0	1.077	0	327861.664	248.644
22	33698.3	20674	14060.8	12812	19637.5	7860	1.117	0	1.077	0	328110.308	238.074
23	33718.9	19580	14073.6	12993	19645.3	6589	1.117	0	1.077	0	328348.382	240.336
24	33738.5	20032	14086.6	0	19651.9	20031	1.117	0	1.077	0	328588.718	251.352
25	33758.6	20111	14086.6	0	19671.9	20110	1.117	0	1.077	0	328840.07	263.219
26	33778.7	19835	14086.6	12315	19692	7521	1.117	0	1.077	0	329103.289	245.404
27	33798.5	19435	14098.9	12468	19699.6	6967	1.117	0	1.077	0	329348.693	224.582
28	33817.9	19642	14111.4	12727	19706.5	6915	1.117	0	1.077	0	329573.275	267.935
29	33837.6	20173	14124.1	13130	19713.5	7042	1.117	0	1.077	0	329841.21	263.788
30	33857.7	21462	14137.3	13576	19720.5	7888	1.117	51	1.077	0	330104.998	282.451
31	33879.2	20636	14150.8	0	19728.4	20637	1.168	0	1.077	0.067	330387.449	233.403
1	33899.8		14150.8		19749		1.168		1.144		330620.852	
		601017		258269		342749		123		0.091		7460.821

Utility Consumption Cost for January 2026							
	Unit price	Unit	Cost	City water used unit	7,461	Unit	
Kwh On	4.1839	258269	1,080,571.67	cost		117,607.98	Bht
Kwh OFF	2.6037	342749	892,415.57	Operation cost(Bht/unit)	0.15	1,119.12	Bht
Kw peak	132.93	1168	155,262.24	service charge		-	Bht
ft	(0.0972)	601018	(58,418.95)	cost		118,727.10	Bht
service charge	312.24		312.24	Vat	0.07	8,310.90	Bht
Sum			2,070,142.77	Total cost		127,038.00	Bht
VAT	0.07		144,909.99				
Grand total			2,215,052.76				

Utility Consumption Cost for February 2026												
Date	Reading Meter	Total consum /day (Kwh)	On Peak Reading	Total consum /day (Kwh)	Off Peak Reading	Total consum /day (Kwh)	On Peak Demand (Kw)	Diff / day (Kw)	Off Peak Demand (Kw)	Diff / day (Kw)	Water Meter Reading (m³)	Consum / Day (m³)
1	33921.330	19649	14150.832	12407	19771	7241	0	1046	1.089	0	330888.036	235.69
2	33941	19741	14163	12711	19778	7031	1.046	46	1.089	0	331123.727	247.3
3	33961	20019	14176	12839	19785	7180	1.092	17	1.089	0	331371.03	255.62
4	33981	20282	14189	13176	19792	7106	1.109	27	1.089	0	331626.647	249.31
5	34001	20863	14202	13953	19799	6911	1.136	51	1.089	0	331875.955	262.78
6	34022	21556	14216	0	19806	21555	1.187	0	1.089	0.061	332138.738	269.5
7	34043	22388	14216	0	19828	22388	1.187	0	1.150	0	332408.234	252.25
8	34066	20677	14216	12901	19850	7776	1.187	0	1.15	0	332660.485	245.73
9	34087	20275	14229	12798	19858	7477	1.187	0	1.15	0	332906.22	235.77
10	34107	20377	14242	12810	19865	7567	1.187	0	1.15	0	333141.991	231.35
11	34127	21912	14254	13826	19873	8086	1.187	0	1.15	0	333373.343	251.93
12	34149	20567	14268	13602	19881	6965	1.187	0	1.15	0	333625.278	265.41
13	34170	21295	14282	0	19888	21295	1.187	0	1.15	0	333890.686	265.8
14	34191	22241	14282	0	19909	22241	1.187	0	1.15	0	334156.486	273.83
15	34213	21449	14282	13430	19931	8020	1.187	0	1.15	0	334430.317	280.13
16	34235	21433	14295	13512	19939	7920	1.187	0	1.15	0	334710.442	268.33
17	34256	21920	14309	13283	19947	8637	1.187	0	1.15	0	334978.772	276.42
18	34278	21180	14322	13380	19956	7800	1.187	0	1.15	0	335255.188	282.03
19	34299	21074	14335	13934	19964	7141	1.187	0	1.15	0	335537.218	256.85
20	34320	21144	14349	0	19971	21144	1.187	0	1.15	0.032	335794.065	305.1
21	34341	23353	14349	0	19992	23352	1.187	0	1.182	0	336099.167	285.74
22	34365	21917	14349	13710	20015	8207	1.187	0	1.182	0	336384.905	262.35
23	34387	22037	14363	13752	20024	8285	1.187	0	1.182	0	336647.257	244.58
24	34409	21825	14377	13588	20032	8237	1.187	0	1.182	0	336891.835	266.89
25	34431	21589	14390	13378	20040	8211	1.187	0	1.182	0	337158.7	247.98
26	34452	20175	14404	13264	20048	6912	1.187	0	1.182	0	337406.703	234.15
27	34472	21875	14417	0	20055	21874	1.187	0	1.182	0	337640.85	265.92
28	34494	20464	14417	0	20077	20465	1.187	0	1.182	0	337906.769	252.59
1	34514.607		14417.086		20098		1.187		1.182		338159.354	
		593277		266254		327024		1187		0.093		7271.318

Utility Consumption Cost for February 2026							
Unit price	Unit	Cost	City water used unit	7,271	Unit		
Kwh On	4.1839	266254	1,113,980.11	cost		114,611.94	Bht
Kwh OFF	2.6037	327024	851,472.39	Operation cost(Bht/unit)	0.15	1,090.70	Bht
Kw peak	132.93	1187	157,787.91	service charge		-	Bht
ft	(0.0972)	593278	(57,666.62)	cost		115,702.64	Bht
service charge	312.24		312.24	Vat	0.07	8,099.18	Bht
Sum			2,065,886.03	Total cost		123,801.82	Bht
VAT	0.07		144,612.02				
Grand total			2,210,498.05				

Utility Consumption Cost for March 2026												
Date	Reading Meter	Total consum /day (Kwh)	On Peak Reading	Total consum /day (Kwh)	Off Peak Reading	Total consum /day (Kwh)	On Peak Demand (Kw)	Diff / day (Kw)	Off Peak Demand (Kw)	Diff / day (Kw)	Water Meter Reading (m³)	Consum / Day (m3)
1	34494.143	20464	14417.086	0	20077.059	20465	1.187	0	1.080	0.000	337,906.8	252.59
2	34514.607	21886	14417.086	12716	20097.524	9169	1.067	0	1.080	0	338159.354	268.39
3	34536.493	20361	14429.802	0	20106.693	20362	1.067	0	1.080	0	338427.739	238.26
4	34556.854	20690	14429.802	12422	20127.055	8267	1.067	9	1.080	0	338666	252.32
5	34577.544	20903	14442.224	12771	20135.322	8132	1.076	0	1.080	0	338918.316	253.75
6	34598.447	21344	14454.995	13843	20143.454	7501	1.076	119	1.080	0	339172.07	250.41
7	34619.791	21039	14468.838	0	20150.955	21038	1.195	0	1.080	0	339422.476	284.24
8	34640.83	21738	14468.838	0	20171.993	21739	1.195	0	1.080	0.047	339706.719	241.41
9	34662.568	21437	14468.838	12979	20193.732	8459	1.195	0	1.127	0	339948.125	257.44
10	34684.005	21360	14481.817	13420	20202.191	7939	1.195	0	1.127	0	340205.567	299.1
11	34705.365	21221	14495.237	13143	20210.13	8077	1.195	0	1.127	0	340504.664	244.36
12	34726.586	21079	14508.38	12952	20218.207	8128	1.195	0	1.127	0	340749.025	216.97
13	34747.665	20210	14521.332	13259	20226.335	6952	1.195	0	1.127	0	340965.994	225.09
14	34767.875	21811	14534.591	0	20233.287	21811	1.195	0	1.127	0	341191.087	269.88
15	34789.686	21279	14534.591	0	20255.098	21278	1.195	0	1.127	0	341460.966	268.19
16	34810.965	21291	14534.591	13058	20276.376	8234	1.195	0	1.127	0	341729.152	249.96
17	34832.256	20968	14547.649	13473	20284.61	7494	1.195	0	1.127	0	341979.115	284.29
18	34853.224	22422	14561.122	13419	20292.104	9003	1.195	0	1.127	0	342263.406	251.86
19	34875.646	21795	14574.541	13556	20301.107	8239	1.195	0	1.127	0	342515.265	242.02
20	34897.441	21614	14588.097	13732	20309.346	7882	1.195	0	1.127	0	342757.28	253.08
21	34919.055	21932	14601.829	0	20317.228	21933	1.195	0	1.127	0.034	343010.358	249.8
22	34940.987	21829	14601.829	0	20339.161	21829	1.195	0	1.161	0	343260.163	295.9
23	34962.816	21256	14601.829	13451	20360.99	7804	1.195	0	1.161	0	343556.067	254.96
24	34984.072	21751	14615.28	13239	20368.794	8512	1.195	0	1.161	0	343811.027	259.43
25	35005.823	22728	14628.519	13781	20377.306	8947	1.195	0	1.161	0	344,070.5	268.96
26	35028.551	21839	14642.3	13458	20386.253	8381	1.195	0	1.161	0	344339.421	277.21
27	35050.390	21412	14655.758	13524	20394.634	7888	1.195	0	1.161	0	344616.629	260.75
28	35071.802	21901	14669.282	0	20402.522	21901	1.195	0	1.161	0	344877.382	254.6
29	35093.703	21541	14669.282	0	20424.423	21512	1.195	0	1.161	0	345131.977	247.22
30	35115.244	21511	14669.282	13353	20445.935	8187	1.195	0	1.161	0	345379.196	246.87
31	35136.755	22369	14682.635	13947	20454.122	8423	1.195	0	1.161	0	345626.066	262.93
1	35159.124		14696.582		20482.545		1.195		1.161		345,889.0	
		664981		279496		385486		128		0.081		7982.23

Utility Consumption Cost for March 2026						
Unit price	Unit	Cost	City water used unit	7,982	Unit	
Kwh On	4.1839	279496	1,169,383.31	cost	125,851.47	Bht
Kwh OFF	2.6037	385486	1,003,689.90	Operation cost(Bht/unit)	0.15	1,197.33 Bht
Kw peak	132.93	1195	158,851.35	service charge	-	Bht
ft	(0.0972)	664982	(64,636.25)	cost	127,048.81	Bht
service charge	312.24		312.24	Vat	0.07	8,893.42 Bht
Sum			2,267,600.55	Total cost	135,942.22	Bht
VAT	0.07		158,732.04			
Grand total			2,426,332.59			

Utility Consumption Cost for April 2026												
Date	Reading Meter	Total consum /day (Kwh)	On Peak Reading	Total consum /day (Kwh)	Off Peak Reading	Total consum /day (Kwh)	On Peak Demand (Kw)	Diff / day (Kw)	Off Peak Demand (Kw)	Diff / day (Kw)	Water Meter Reading (m ³)	Consum / Day (m3)
1	35159.124	23130	14696.582	14700	20462.55	8430	0	1262	0	1.088	345,889.0	264.26
2	35182.254	22305	14711.28	13565	20470.975	8740	1.262	0	1.088	0	346153.26	249.917
3	35204.559	22164	14724.847	14181	20479.715	7983	1.262	0	1.088	0	346403.177	253.629
4	35226.723	22603	14739.028	0	20487.698	22602	1.262	0	1.088	0.045	346656.806	285.89
5	35249.326	21056	14739.028	0	20510.300	21056	1.262	0	1.133	0	346942.696	261.49
6	35270.382	20848	14739.028	0	20531.356	20849	1.262	0	1.133	0	347204.186	230.536
7	35291.230	22448	14739.028	13645	20552.205	8803	1.262	0	1.133	0	347434.722	241.455
8	35313.678	22143	14752.673	13443	20561.008	8700	1.262	0	1.133	0	347676.177	240.232
9	35335.821	21783	14766.116	13451	20569.708	8331	1.262	0	1.133	0	347916.409	242.504
10	35357.604	22364	14779.567	13690	20578.039	8674	1.262	0	1.133	0	348158.913	247.555
11	35379.968	22367	14793.257	0	20586.713	22329	1.262	0	1.133	0.063	348406.468	281.005
12	35402.335	22565	14793.257	0	20609.042	22603	1.262	0	1.196	0	348687.473	286.862
13	35424.900	21717	14793.257	0	20631.645	21717	1.262	0	1.196	0	348974.335	262.462
14	35446.617	21764	14793.257	0	20653.362	21764	1.262	0	1.196	0	349236.797	245.271
15	35468.381	22255	14793.257	0	20675.126	22255	1.262	0	1.196	0	349482.068	243.338
16	35490.636	22056	14793.257	13540	20697.381	8517	1.262	0	1.196	0	349725.406	263.389
17	35512.692	21768	14806.797	13581	20705.898	8186	1.262	0	1.196	0	349988.795	358.969
18	35534.460	22617	14820.378	0	20714.084	22618	1.262	0	1.196	0	350347.764	262.36
19	35557.077	22448	14820.378	0	20736.702	22446	1.262	0	1.196	0	350610.124	269.587
20	35579.525	21935	14820.378	13606	20759.148	8330	1.262	0	1.196	0	350879.711	296.28
21	35601.460	22448	14833.984	13461	20767.478	7988	1.262	0	1.196	0	351175.991	238.924
22	35623.908	22378	14847.445	14083	20775.466	9295	1.262	0	1.196	0	351414.915	330.4
23	35646.286	22198	14861.528	13601	20784.761	8596	1.262	0	1.196	0	351745.315	255.568
24	35668.484	21856	14875.129	13544	20793.357	8312	1.262	0	1.196	0	352000.883	247.711
25	35690.340	22156	14888.673	0	20801.669	22156	1.262	0	1.196	0	352,248.6	269.544
26	35712.496	20880	14888.673	0	20823.825	20881	1.262	0	1.196	0	352518.138	234.118
27	35733.376	22228	14888.673	13509	20844.706	8719	1.262	0	1.196	0	352752.256	261.943
28	35755.604	22550	14902.182	13863	20853.425	8686	1.262	0	1.196	0	353014.199	269.632
29	35778.154	21199	14916.045	13451	20862.111	7748	1.262	0	1.196	0	353283.831	262.23
30	35799.353	23341	14929.496	14001	20869.859	9340	1.262	0	1.196	0	353546.061	306.339
1	35822.694		14943.497		20879.199		1.262		1.196		353852.4	
		663570		246915		416654		0		1.196		7963.4


Utility Consumption Cost for April 2026							
	Unit price	Unit	Cost	City water used unit		7,963	Unit
Kwh On	4.1839	246915	1,033,067.67	cost		125,553.75	Bht
Kwh OFF	2.6037	416654	1,084,842.02	Operation cost(Bht/unit)	0.15	1,194.51	Bht
Kw peak	132.93	1262	167,757.66	service charge		-	Bht
ft	(0.0972)	663569	(64,498.91)	cost		126,748.26	Bht
service charge	312.24		312.24	Vat	0.07	8,872.38	Bht
Sum			2,221,480.68	Total cost		135,620.64	Bht
VAT	0.07		155,503.65				
Grand total			2,376,984.33				

Utility Consumption Cost for May 2026												
Date	Reading Meter	Total consum /day (Kwh)	On Peak Reading	Total consum /day (Kwh)	Off Peak Reading	Total consum /day (Kwh)	On Peak Demand (Kw)	Diff / day (Kw)	Off Peak Demand (Kw)	Diff / day (Kw)	Water Meter Reading (m ³)	Consum / Day (m ³)
1	35822.694	22792	14943.497	0	20879.199	22792	0	0	1.196	-0.05	353852.4	264.225
2	35845.486	22730	14943.497	0	20901.99	22731	0	0	1.146	0.006	354,116.6	272.297
3	35868.216	23769	14943.50	0	20924.722	23768	0	0	1.152	0.048	354388.92	307.03
4	35891.985	23352	14943.497	0	20948.490	23352	0	0	1.200	0	354695.952	306.385
5	35915.337	23133	14943.497	13584	20971.842	9550	0	1160	1.200	0	355002.337	267.481
6	35938.470	23322	14957.081	13851	20981.392	9471	1.160	3	1.200	0	355269.818	257.3
7	35961.792	23684	14970.932	14089	20990.863	9595	1.163	15	1.200	0	355527.118	284.039
8	35985.476	22502	14985.021	13683	21000.458	8818	1.178	0	1.200	0	355811.157	281.759
9	36007.978	21299	14998.704	0	21009.276	21299	1.178	0	1.200	0	356092.916	247.137
10	36029.277	22229	14998.704	0	21030.575	22230	1.178	0	1.2	0	356340.053	255.539
11	36051.506	22709	14998.704	13427	21052.805	9282	1.178	0	1.200	0	356595.592	281.738
12	36074.215	22197	15012.131	13029	21062.087	9167	1.178	0	1.200	0	356877.330	234.052
13	36096.412	23001	15025.160	13713	21071.254	9289	1.178	0	1.200	0	357111.382	300.121
14	36119.413	22372	15038.873	13990	21080.543	8382	1.178	0	1.2	0	357411.503	289.541
15	36141.785	23866	15052.863	13571	21088.925	10294	1.178	0	1.2	0	357701.044	283.293
16	36165.651	22192	15066.434	0	21099.219	22193	1.178	0	1.2	0	357984.337	264.509
17	36187.843	21619	15066.434	0	21121.412	21618	1.178	0	1.2	0	358248.846	247.601
18	36209.462	23201	15066.434	13522	21143.030	9679	1.178	0	1.2	0	358496.447	280.115
19	36232.663	22113	15079.956	13172	21152.709	8940	1.178	0	1.2	0	358776.562	282.283
20	36254.776	22502	15093.128	13557	21161.649	8946	1.178	0	1.2	0	359058.845	260.305
21	36277.278	22727	15106.685	13582	21170.595	9145	1.178	0	1.2	0	359319.15	240.386
22	36300.005	22078	15120.267	14101	21179.74	7978	1.178	43	1.2	0	359559.536	265.158
23	36322.083	23766	15134.368	0	21187.718	23766	1.221	0	1.2	0.008	359824.694	317.721
24	36345.849	23447	15134.368	0	21211.484	23447	1.221	0	1.208	0	360142.415	290.017
25	36369.296	23643	15134.368	14056	21234.931	9587	1.221	0	1.208	0	360432.432	279.498
26	36392.939	24765	15148.424	14549	21244.518	10215	1.221	0	1.208	0	360,711.9	307.48
27	36417.704	22437	15162.973	14356	21254.733	8082	1.221	0	1.208	0	361019.41	316.603
28	36440.141	24243	15177.329	14710	21262.815	9532	1.221	0	1.208	0	361336.013	314.539
29	36464.384	23608	15192.039	14769	21272.347	8839	1.221	0	1.208	0	361650.552	294.75
30	36487.992	23723	15206.808	0	21281.186	3814	1.221	0	1.208	0.01	361945.302	279.199
31	36511.715	22901	15206.808	0	21285	42777	1.221		1.218		362224.501	241.751
1	36534.616		15206.808		21327.777		0		0		362466.252	
		711922		263311		448578		1221		0.022		8613.852

Utility Consumption Cost for May 2026										
	Unit price		Unit	Cost	City water used unit		8,614		Unit	
Kwh On	4.1839	263311	1,101,666.89	cost		135,837.40		Bht		
Kwh OFF	2.6037	448578	1,167,962.54	Operation cost(Bht/unit)	0.15	1,292.08		Bht		
Kw peak	132.93	0	-	service charge		-		Bht		
ft	(0.1623)	711889	(115,539.58)	cost		137,129.48		Bht		
service charge	312.24		312.24	Vat	0.07	9,599.06		Bht		
Sum			2,154,402.09	Total cost		146,728.54		Bht		
VAT	0.07		150,808.15							
Grand total			2,305,210.23							

Utility Consumption Cost for June 2026												
Date	Reading Meter	Total consum /day (Kwh)	On Peak Reading	Total consum /day (Kwh)	Off Peak Reading	Total consum /day (Kwh)	On Peak Demand (Kw)	Diff / day (Kw)	Off Peak Demand (Kw)	Diff / day (Kw)	Water Meter Reading (m³)	Consum / Day (m3)
1	36534.616	21583	15206.808	12950	21327.777	8667	0	1108	0	1	362466.252	232.188
2	36556.199	21849	15219.76	13311	21336.444	8537	1.108	5	1.000	0.018	362698.44	219.4
3	36578.048	21392	15233.069	0	21344.981	21392	1.113	0	1.018	0.076	362917.840	215.672
4	36599.440	20243	15233.069	13215	21366.373	7029	1.113	5	1.094	0	363133.512	218.36
5	36619.683	21919	15246.284	13513	21373.402	8406	1.118	35	1.094	0	363351.872	243.473
6	36641.602	22260	15259.797	0	21381.808	22260	1.153	0	1.094	0.006	363595.345	268.102
7	36663.862	21193	15259.797	0	21404.068	21158	1.153	0	1.100	0.005	363863.447	222.568
8	36685.055	21912	15259.797	13253	21425.226	8693	1.153	0	1.105	0	364086.015	242.42
9	36706.967	21204	15273.05	13218	21433.919	7986	1.153	0	1.105	0	364328.435	223.636
10	36728.171	21491	15286.268	13148	21441.905	8344	1.153	0	1.105	0	364552.071	244.436
11	36749.662	21941	15299.416	12959	21450.249	8982	1.153	0	1.105	0	364796.507	266.843
12	36771.603	21590	15312.375	13511	21459.231	8078	1.153	0	1.105	0	365063.350	264.008
13	36793.193	21746	15325.886	0	21467.309	21714	1.153	0	1.105	0	365327.358	225.118
14	36814.939	19247	15325.886	0	21489.023	19280	1.153	0	1.105	0	365552.476	240.356
15	36834.186	21087	15325.886	13183	21508.303	7903	1.153	0	1.105	0	365792.832	230.369
16	36855.273	22753	15339.069	13541	21516.206	9212	1.153	44	1.105	0.045	366023.201	277.855
17	36878.026	21771	15352.610	13447	21525.418	8325	1.197	0	1.15	0	366301.056	239.7
18	36899.797	20675	15366.057	13633	21533.743	7040	1.197	0	1.15	-0.045	366540.756	245.294
19	36920.472	22908	15379.690	13550	21540.783	9360	1.197	0	1.105	0	366786.05	268.812
20	36943.380	21007	15393.24	0	21550.143	20970	1.197	0	1.105	0.029	367054.862	255.188
21	36964.387	20834	15393.24	0	21571.113	20871	1.197	0	1.134	0.008	367310.05	269.472
22	36985.221	22302	15393.24	13500	21591.984	8792	1.197	0	1.142	0	367579.522	278.348
23	37007.523	22003	15406.74	13355	21600.776	8658	1.197	0	1.142	0	367857.870	275.978
24	37029.526		15420.095		21609.434		1.197		1.142		368133.848	
25												
26												
27												
28												
29												
30												
1												
		494910		213287		281657		1197		1.142		5667.60

Utility Consumption Cost for June 2026							
	Unit price	Unit	Cost	City water used unit		5,668	Unit
Kwh On	4.1839	213287	892,371.48	cost		89,257.09	Bht
Kwh OFF	2.6037	281657	733,350.33	Operation cost(Bht/unit)	0.15	850.14	Bht
Kw peak	132.93	0	-	service charge		-	Bht
ft	(0.1623)	494944	(80,329.41)	cost		90,107.23	Bht
service charge	312.24		312.24	Vat	0.07	6,307.51	Bht
Sum			1,545,704.64	Total cost		96,414.74	Bht
VAT	0.07		108,199.32				
Grand total			1,653,903.96				

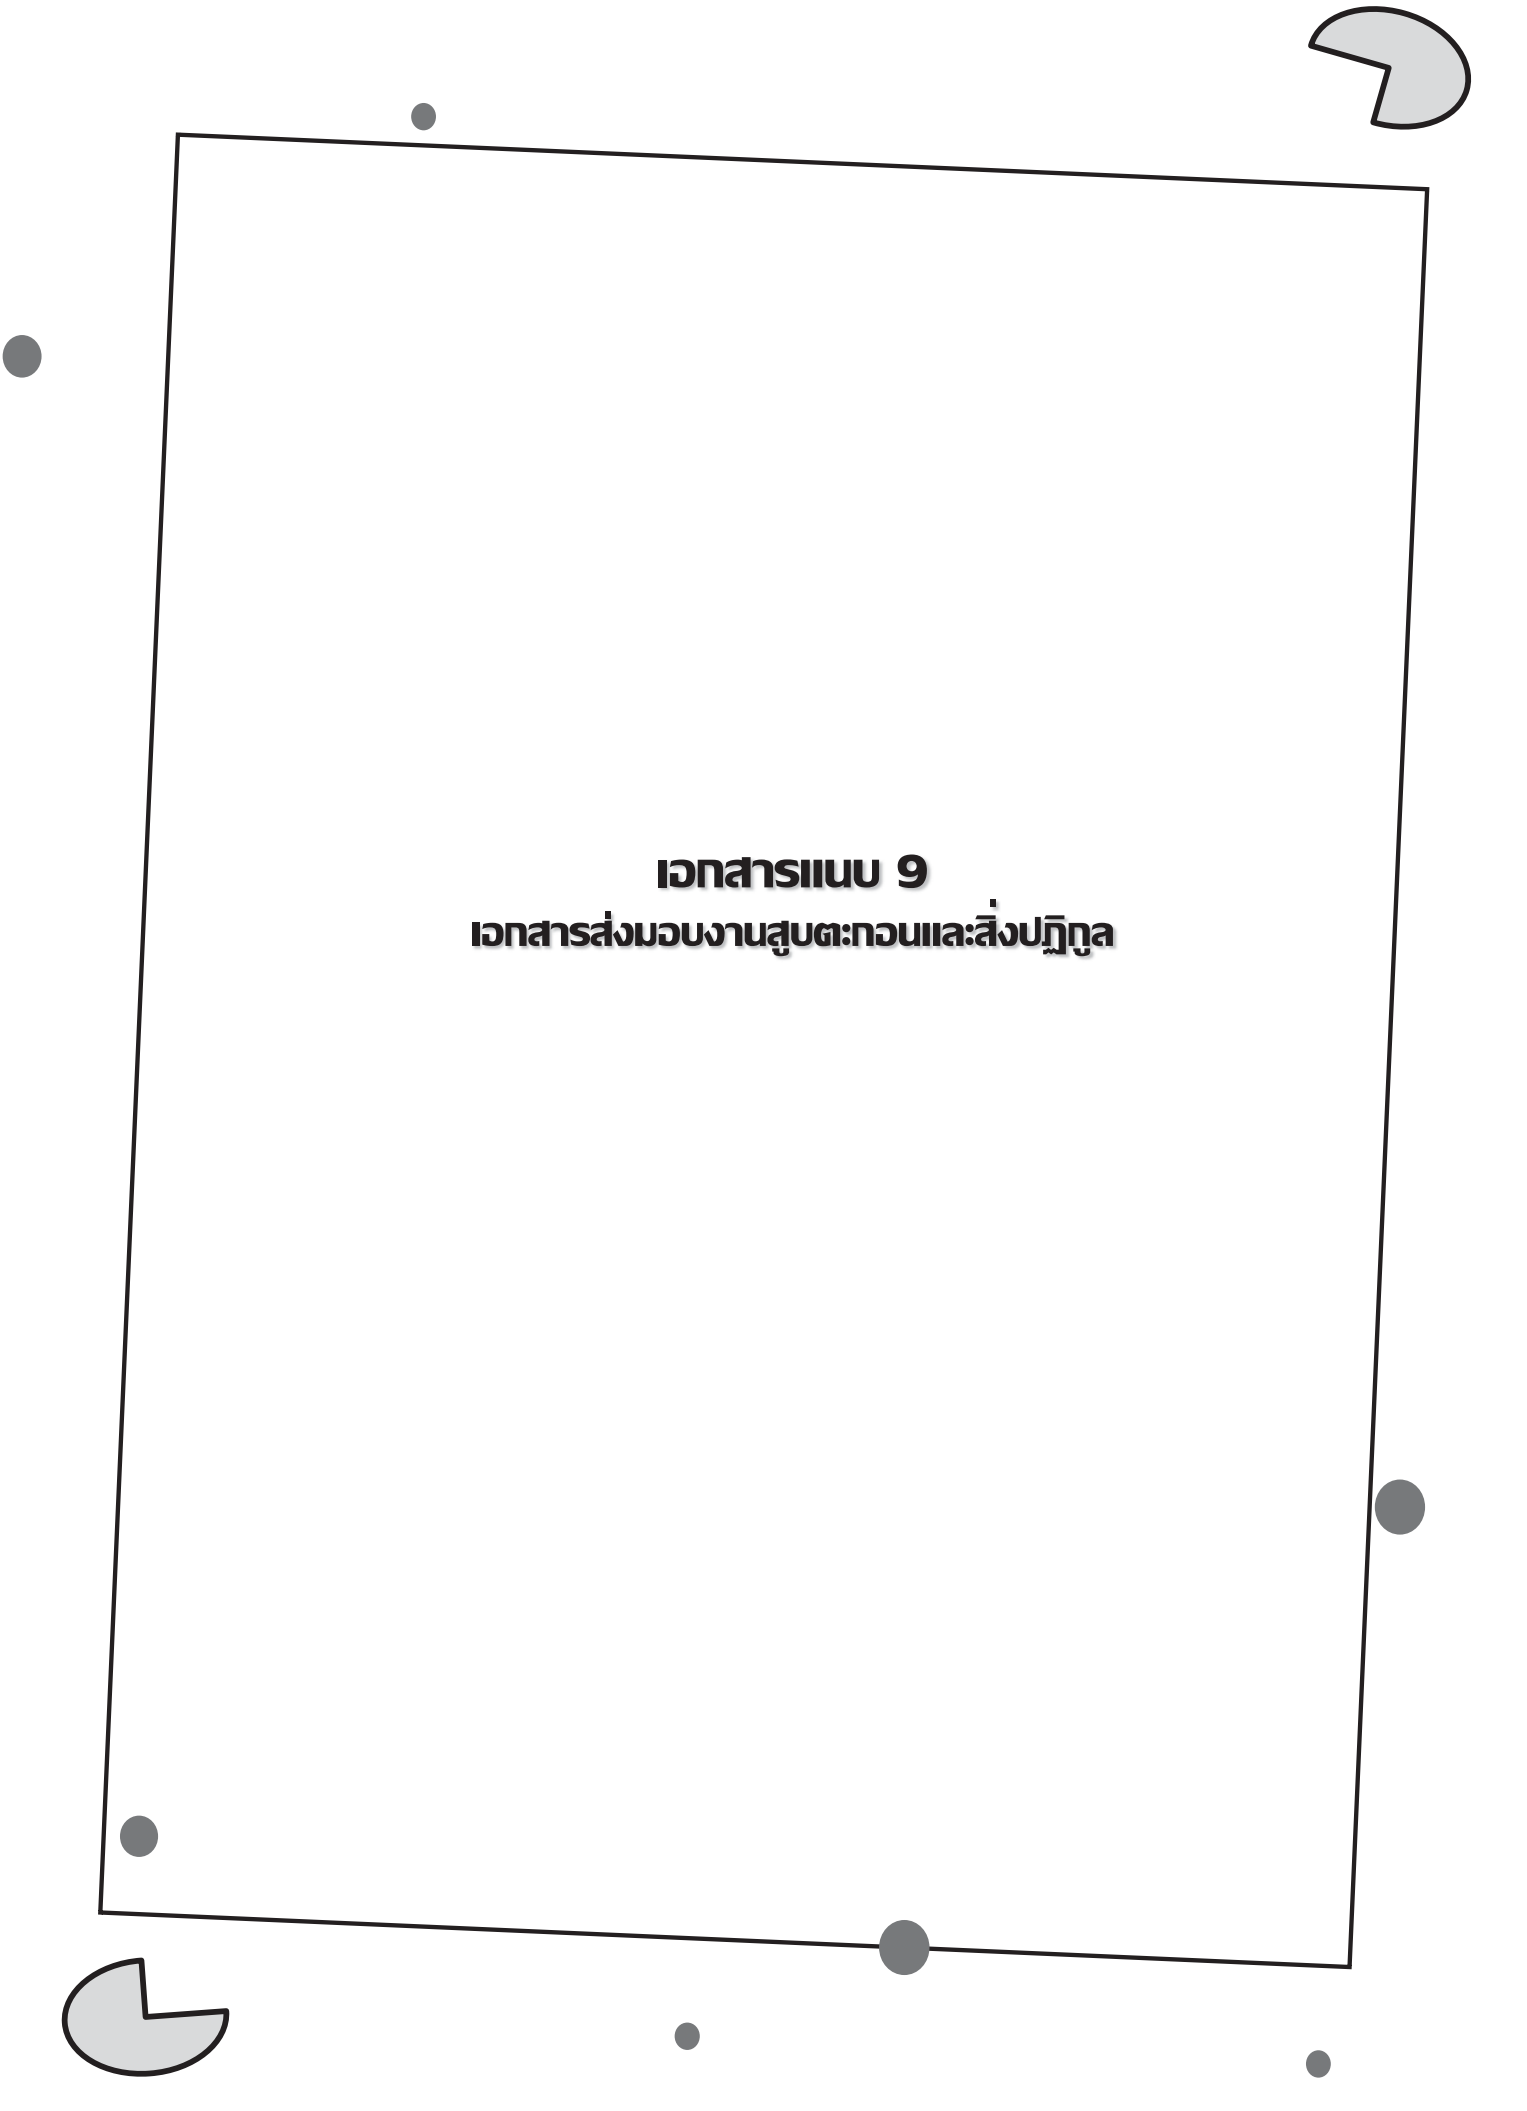

ເອກສານແບບ 9

ເອກສານສົ່ງມວນງານສູ່ບະຫວັນແລະສິ່ງປຶກສາ

ภาพประกอบการส่งมอบงาน สุบสิ่งปฏิกูล SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้าบริการ เมื่อวันที่ 2 เมษายน 2569

บ่อไขมัน sump
(หน้า Canteen)
ก่อนเข้าบริการ



บ่อไขมัน sump
(หน้า Canteen)
ขณะเข้าบริการ




บ่อไขมัน sump
(หน้า Canteen)
ขณะเข้าบริการ



ภาพประกอบการส่งมอบงาน สุบสิ่งปฏิกูล SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้าบริการ เมื่อวันที่ 2 เมษายน 2569

บ่อไขมัน sump
(หน้า Canteen)
หลังทำเสร็จ

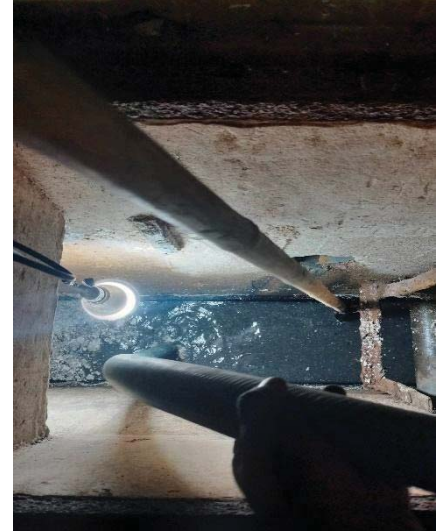

บ่อไขมัน sump
(หน้า Canteen)
หลังทำเสร็จ



ภาพประกอบการส่งมอบงาน สุบสิ่งปฏิกูล SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้าบริการ เมื่อวันที่ 2 เมษายน 2569

บ่อเกรอะ
 (ชั้น B2)
 ก่อนเข้าบริการ



บ่อเกรอะ
 (ชั้น B2)
 ขณะเข้าบริการ



บ่อเกรอะ
 (ชั้น B2)
 ขณะเข้าบริการ

บ่อเกรอะ
 (ชั้น B2)
 หลังบริการเสร็จ




ภาพประกอบการส่งมอบงาน สุบสิ่งปฏิกูล SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้าบริการ เมื่อวันที่ 2 เมษายน 2569


บ่อดักไขมัน
(ชั้น B1)
ก่อนเข้าบริการ



บ่อดักไขมัน
(ชั้น B1)
ขณะเข้าบริการ

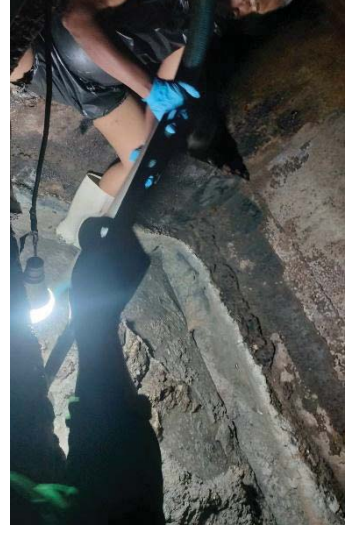


บ่อดักไขมัน
(ชั้น B1)
ขณะเข้าบริการ

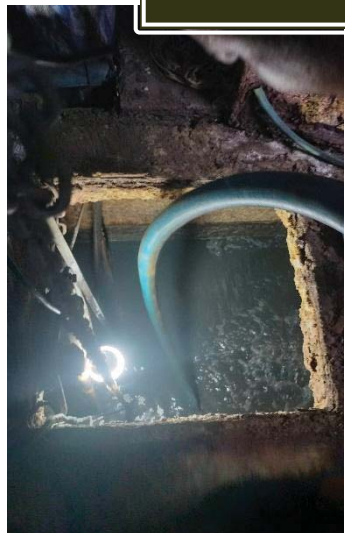

ภาพประกอบการส่งมอบงาน สุบสิ่งปลูก SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้าบริการ เมื่อวันที่ 2 เมษายน 2569

บ่อดักไขมัน
(ชั้น B1)
หลังบริการเสร็จ

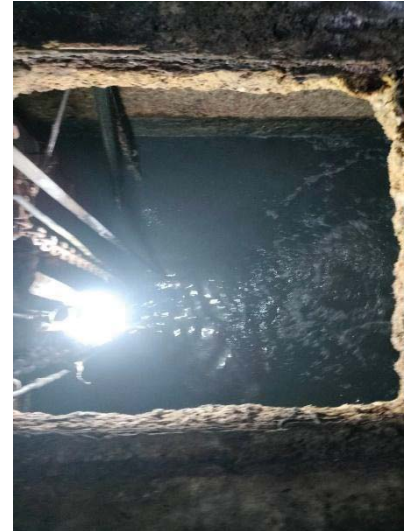


บ่อดักไขมัน
(ชั้น B1)
หลังบริการเสร็จ




ภาพประกอบการส่งมอบงาน สุบสิ่งปฏิกูล SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้าบริการ เมื่อวันที่ 2 เมษายน 2569

บ่อเติมอากาศ
(Aeration Tank)
ก่อนเข้าบริการ

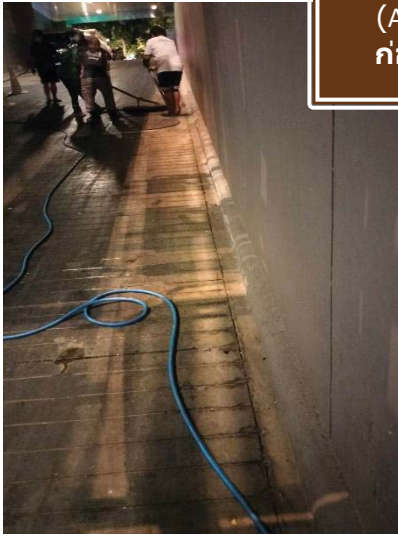

บ่อเติมอากาศ
(Aeration Tank)
ขณะบริการ


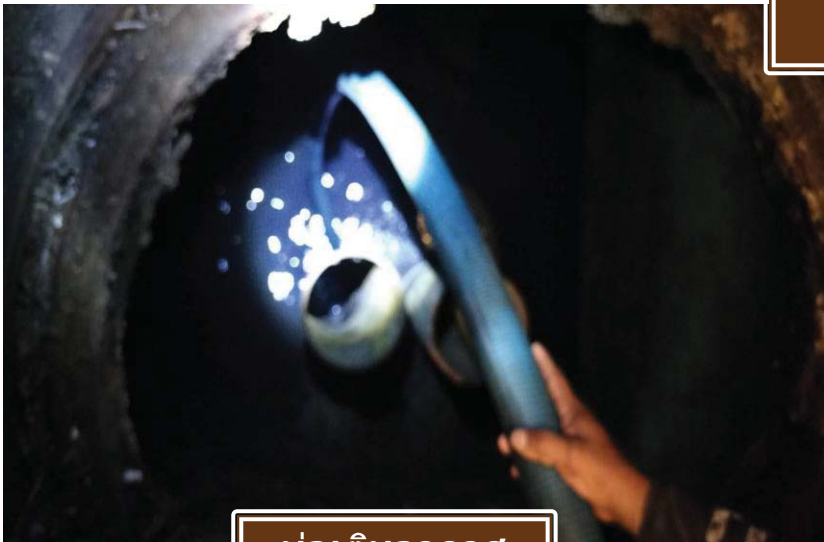


บ่อเติมอากาศ
(Aeration Tank)
หลังบริการเสร็จ





ภาพประกอบการส่งมอบงาน สุบสิ่งปฏิกูล SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้านบริการ เมื่อวันที่ 2 เมษายน 2569


บ่อปรับสภาพ
 (Equalization Tank)
 ก่อนเข้านบริการ

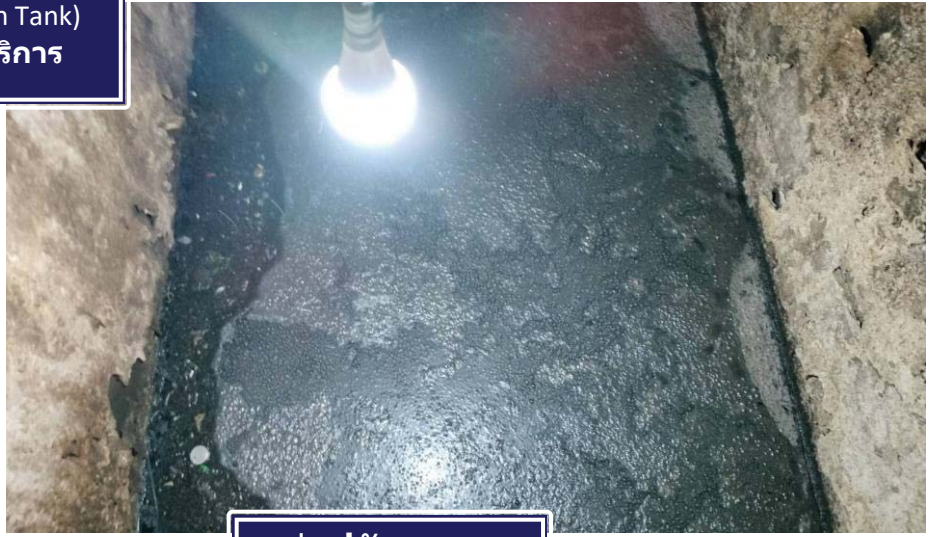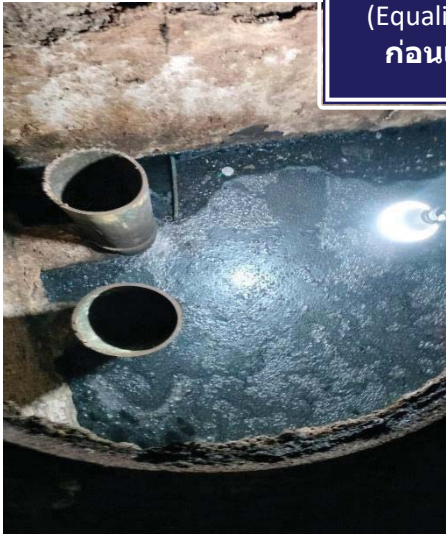

บ่อปรับสภาพ
 (Equalization Tank)
 ขณะเข้านบริการ

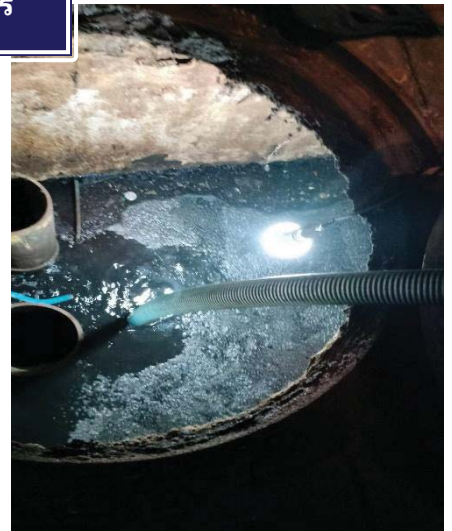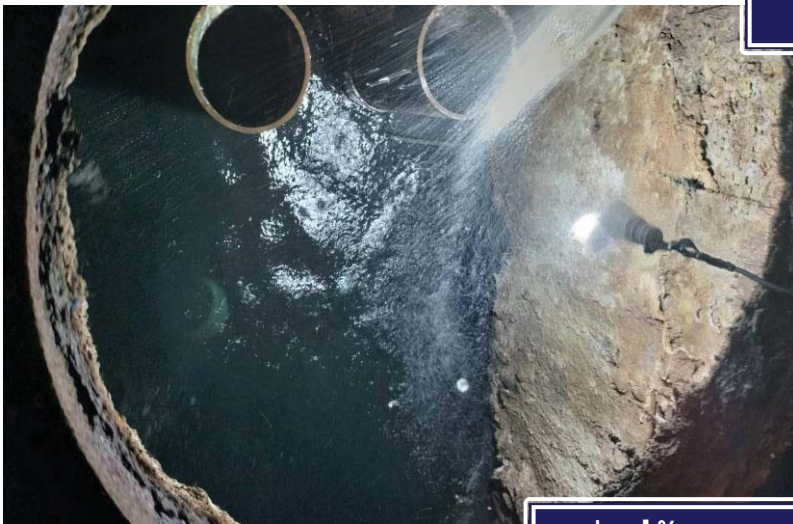


บ่อปรับสภาพ
 (Equalization Tank)
 หลังบริการเสร็จ


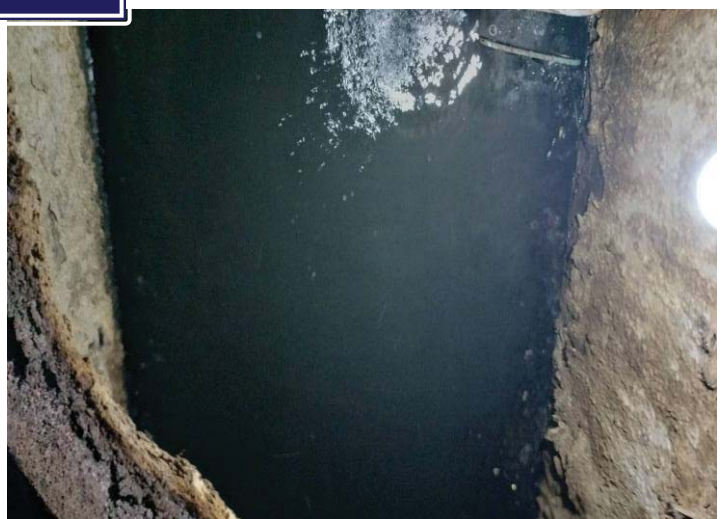


ภาพประกอบการส่งมอบงาน สุบสิ่งปฏิกูล SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้าบริการ เมื่อวันที่ 2 เมษายน 2569


บ่อเกรอะ
 (แลมปีทางลง)
 ก่อนเข้าบริการ

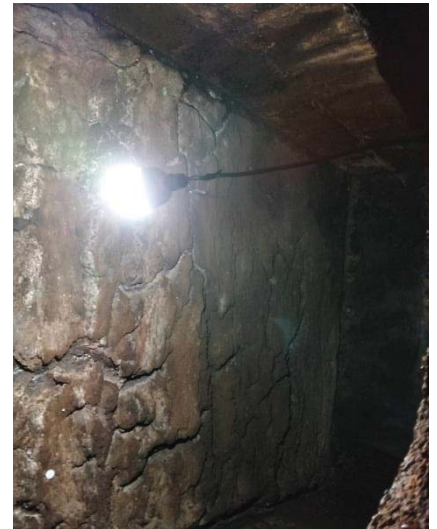

บ่อเกรอะ
 (แลมปีทางลง)
 ขณะเข้าบริการ

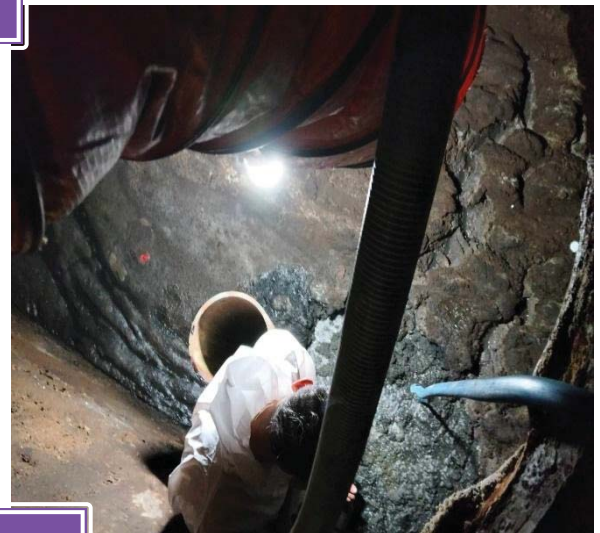
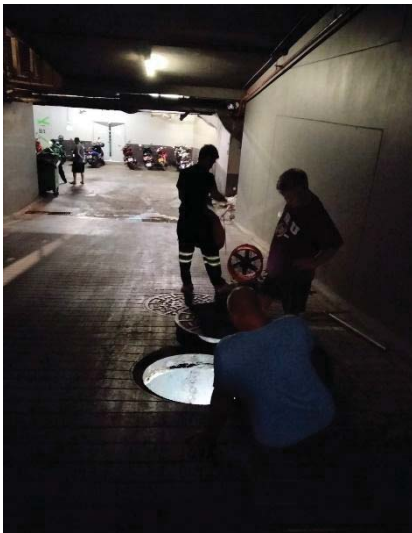


บ่อเกรอะ
 (แลมปีทางลง)
 ขณะเข้าบริการ

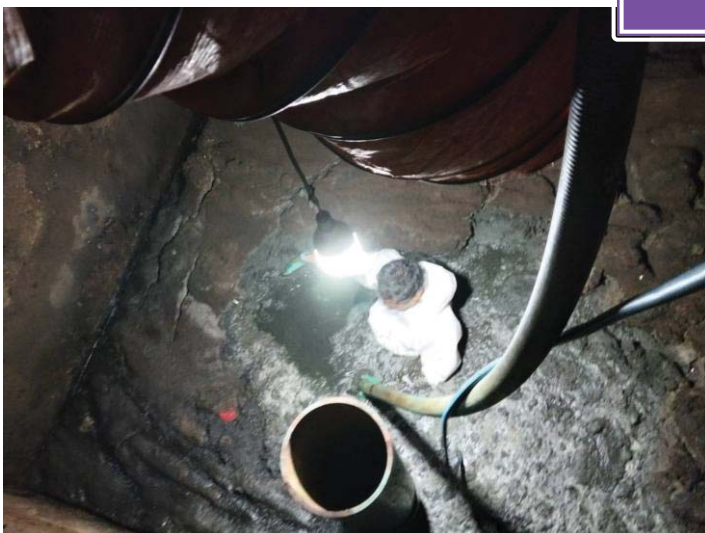


ภาพประกอบการส่งมอบงาน สุบสิ่งปฏิกูล SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้าบริการ เมื่อวันที่ 2 เมษายน 2569



บ่อเกรอะ
(แลมปีทางลง)
ขณะเข้าบริการ

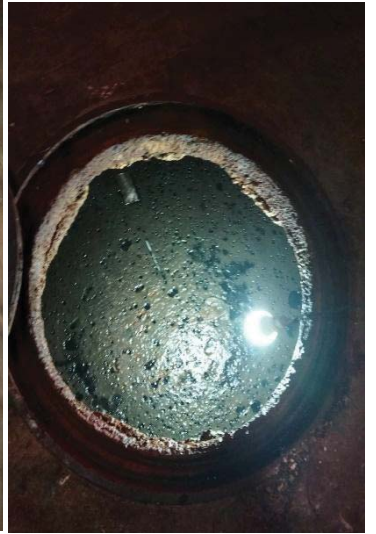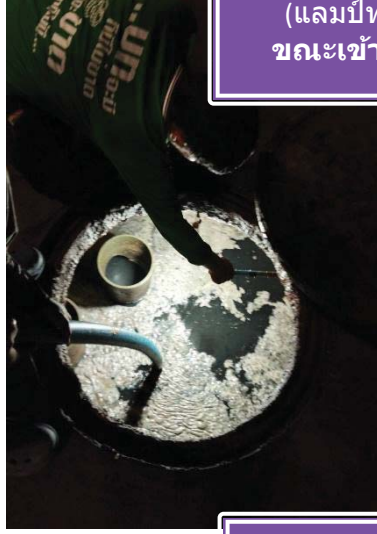

บ่อเกรอะ
(แลมปีทางลง)
ขณะเข้าบริการ

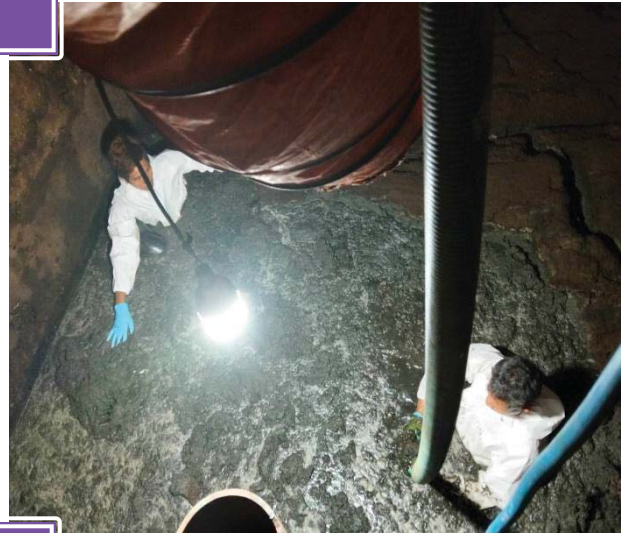

บ่อเกรอะ
(แลมปีทางลง)
ขณะเข้าบริการ

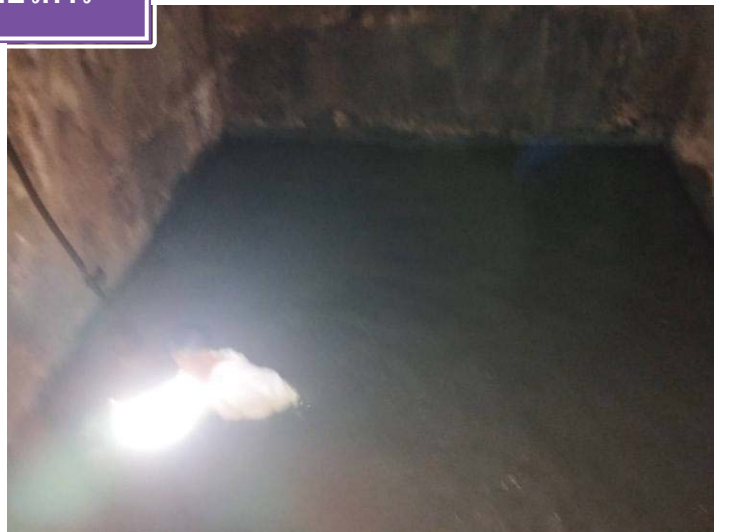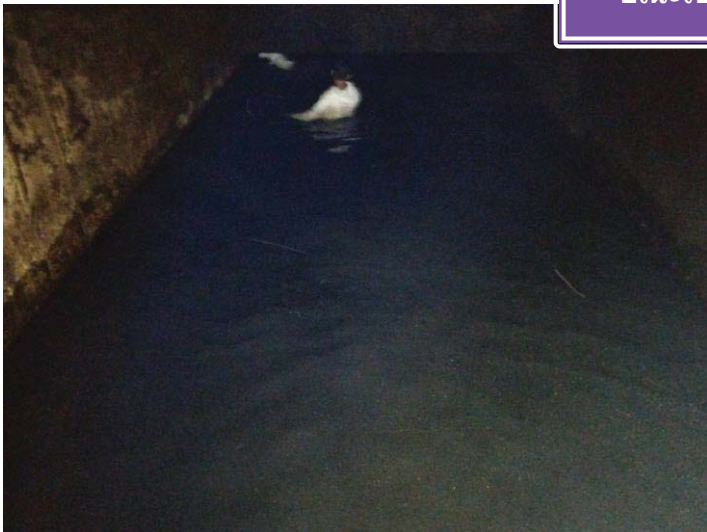

ภาพประกอบการส่งมอบงาน สุบสิ่งปฏิกูล SO/ BANGKOK
(บ่อบำบัดน้ำเสีย - ก่อนการบริการ ขณะบริการ และหลังบริการเสร็จ)
เข้าบริการ เมื่อวันที่ 2 เมษายน 2569

บ่อเกรอะ
(แลมปีทางลง)
หลังบริการเสร็จ



บ่อเกรอะ
(แลมปีทางลง)
หลังบริการเสร็จ



เอกสารแนบ 10
ตัวอย่างภาพการบุตลอกทางระบายน้ำของโครงการ ในปี 2569

SO/ BANGKOK

Gutter Drainage Cleaning 1/2026

Date: 15-April-2026

Located: G Floor



Technician:



Duty Engineer/Leader:



เอกสารแนบ 11
เอกสารการทำดัชนี:มูลพวย ในปี 2569



ใบเสร็จรับเงิน(สำเนา 1) วันที่ 6 มีนาคม 2568

เลขที่ 6800002481

สำนักงานเขต บางรัก โทร 0 2236 1395
ที่อยู่สำนักงานเขต 5 ถ.นเศศ แขวงสีพระยา เขตบางรัก กรุงเทพมหานคร 10500

ชื่อผู้ชำระค่าธรรมเนียม บริษัท โอ๊คทรี จำกัด (โรงแรม โซแบงคอก)
ที่อยู่ เลขที่ 2 ถนนสาทรเหนือ แขวงสีลม เขตบางรัก กรุงเทพมหานคร 10500

ปริมาณมูลฝอยทั่วไป 1,220.00 ลิตร/วัน
มีค่าธรรมเนียมจัดการมูลฝอยประจำเดือน ส.ค. 68

รายละเอียดดังนี้

ลำดับ	รายการ	จำนวนเงิน (บาท)
1	ค่าดับและขนมูลฝอย	4,000
2	ค่ากำจัดมูลฝอย	0
3		
รวมทั้งสิ้น (บาท)		4,000

เป็นจำนวนเงิน 4,000 บาท

ประวัติการชำระค่าธรรมเนียม ปีงบประมาณ 2568

เดือน	บาท	เดือน	บาท
ค.ค.	-	ม.ย.	-
พ.ย.	-	พ.ค.	-
ธ.ค.	-	มิ.ย.	-
ม.ค.	-	ก.ค.	-
ก.พ.	-	ส.ค.	4,000
มี.ค.	-	ก.ย.	-

จำนวนเงินทั้งสิ้น สี่พันบาทถ้วน

ช่องทางการชำระเงิน (Payment) เช็ค ลงวันที่ 28 กุมภาพันธ์ 2568
เลขที่เช็ค (Cheque No.) 80032545

ธนาคาร (Bank) ธ. กสิกรไทย - สาขาถนนสาทร

วันที่เมื่อ 06 มีนาคม 2568 เวลา 13:35 น.

ใบเสร็จรับเงินนี้จะสมบูรณ์เมื่อกรุงเทพมหานครเรียกเก็บเงินได้ครบถ้วนแล้ว

กรุณาเก็บใบเสร็จไว้เพื่อเป็นหลักฐานการชำระเงินของท่าน



ใบเสร็จรับเงิน(สำเนา 1) วันที่ 6 มีนาคม 2568

เลขที่ 6800002482

สำนักงานเขต บางรัก โทร 0 2236 1395
ที่อยู่สำนักงานเขต 5 ถ.นเศศ แขวงสีพระยา เขตบางรัก กรุงเทพมหานคร 10500

ชื่อผู้ชำระค่าธรรมเนียม บริษัท โอ๊คทรี จำกัด (โรงแรม โซแบงคอก)
ที่อยู่ เลขที่ 2 ถนนสาทรเหนือ แขวงสีลม เขตบางรัก กรุงเทพมหานคร 10500

ปริมาณมูลฝอยทั่วไป 1,220.00 ลิตร/วัน
มีค่าธรรมเนียมจัดการมูลฝอยประจำเดือน ก.ย. 68

รายละเอียดดังนี้

ลำดับ	รายการ	จำนวนเงิน (บาท)
1	ค่าดับและขนมูลฝอย	4,000
2	ค่ากำจัดมูลฝอย	0
3		
รวมทั้งสิ้น (บาท)		4,000

เป็นจำนวนเงิน 4,000 บาท

ประวัติการชำระค่าธรรมเนียม ปีงบประมาณ 2568

เดือน	บาท	เดือน	บาท
ค.ค.	-	ม.ย.	-
พ.ย.	-	พ.ค.	-
ธ.ค.	-	มิ.ย.	-
ม.ค.	-	ก.ค.	-
ก.พ.	-	ส.ค.	-
มี.ค.	-	ก.ย.	4,000

จำนวนเงินทั้งสิ้น สี่พันบาทถ้วน

ช่องทางการชำระเงิน (Payment) เช็ค ลงวันที่ 28 กุมภาพันธ์ 2568
เลขที่เช็ค (Cheque No.) 80032545

ธนาคาร (Bank) ธ. กสิกรไทย - สาขาถนนสาทร

วันที่เมื่อ 06 มีนาคม 2568 เวลา 13:36 น.

ใบเสร็จรับเงินนี้จะสมบูรณ์เมื่อกรุงเทพมหานครเรียกเก็บเงินได้ครบถ้วนแล้ว

กรุณาเก็บใบเสร็จไว้เพื่อเป็นหลักฐานการชำระเงินของท่าน

เอกสารแนบ 12
เอกสารตรวจสอบระบบรักษาความปลอดภัย ในปี 2569

VENTILATION FAN (Belt Driven 3P)

ชื่อเครื่อง: 6A-01 Brand/ ยี่ห้อ: Kruger Model/ รุ่น: Bsb900tm
 ขนาดเครื่อง: 3460/15 CFM. ขนาดมอเตอร์: 4 KW. Serial No.: Bkno800510 วันที่ตรวจเช็ค: 1 Jan 26
 สถานที่ติดตั้ง: Substation Room ชั้น 6

ความถี่	Item	รายการตรวจเช็ค / ดำเนินการ	ผลการตรวจเช็ค		ผลการแก้ไข		บันทึกเพิ่มเติม	
			ปกติ	ผิดปกติ	เสร็จ	ไม่เสร็จ		
ประจำ 1 เดือน		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง						
	1	ตรวจสอบสภาพภายนอกและภายในตู้ควบคุม	/					
	2	ตรวจเช็คจุดต่อทางไฟฟ้า และความแน่นของขั้วไฟจุดต่างๆ	/					
	3	ทำความสะอาดและเป่าฝุ่นทั้งภายในและภายนอกตู้ควบคุม	☒	ดำเนินการ	☐	ไม่ได้ดำเนินการ เนื่องจาก		
	4	ตรวจเช็ค Pilot Lamp และอุปกรณ์ต่างๆ เช่น Fuse, Meter ฯลฯ	/					
	5	ตรวจสอบสภาพทั่วไปของพัดลม	/					
	6	ทำความสะอาดและเป่าฝุ่นหน้ากรังจ่ายลม	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก
	7	ถอดล้าง Filler กรองอากาศ (ถ้ามี)	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก
	8	ถอดล้างตะแกรงกันแมลงหรือกันนก (ถ้ามี)	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก
	9	หล่อลื่นลูกปืนมอเตอร์และลูกปืน Blower	☒	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก		
	10	ตรวจเช็คและปรับตั้งสายพาน (เปลี่ยนทุก 3000 ชั่วโมง หรือ 1 ปี)			☒	ดำเนินการปรับตั้ง	☐	ชำรุดมาก ควรเปลี่ยนใหม่
		ON CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง แล้วเดินเครื่อง						
	11	วัดแรงดันไฟฟ้าเข้าเครื่อง	R-N <u>220</u> V. S-N <u>220</u> V. T-N <u>220</u> V.					
			R-S <u>380</u> V. S-T <u>380</u> V. T-R <u>380</u> V.					
	12	วัดกระแสไฟฟ้าของมอเตอร์พัดลม	R <u>6.2</u> A. S <u>6.2</u> A. T <u>6.1</u> A.					Name Plate FLA - <u>6.4</u> A.
13	ตรวจเช็คสภาพการทำงานทั่วไปและเสียงที่อาจดังผิดปกติ	/						
14	ตรวจความสั่นสะเทือน (Alignment) ของตัวเครื่อง	/						
15	ตรวจสอบอุณหภูมิของเบรคและมอเตอร์เบื้องต้น (โดยการสัมผัส)	/						
ประจำ 1 ปี		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง						
	16	ทำความสะอาด Blower และตัวถังเครื่อง	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก		
	17	ตรวจเช็คสภาพของลูกปืน หรือเปลี่ยน(เมื่อจำเป็น)					เปลี่ยนทุกๆ 10000 ชั่วโมง หรือไม่เกิน 5 ปี	
	18	ตรวจเช็คขั้วไฟฟ้า และฉนวนยึดสายที่หลวมหรือไม่แน่น	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก		
19	ตรวจเช็คความมั่นคงของ Support เครื่อง							

รายละเอียดกรณีผิดปกติ และการแก้ไข หรือแก้ไขไม่แล้วเสร็จ:

รายการอะไหล่ที่ใช้ไป:

ไม่มี

Technician

Duty Engineer

Chief Engineer

VENTILATION FAN (Belt Driven 3P)

☒ Monthly ☐ Yearly

ชื่อเครื่อง 6A-01

Brand/ ยี่ห้อ : Kruger

Model/ รุ่น : Bsb900 fm

ขนาดเครื่อง 540 l/s CFM.

ขนาดมอเตอร์ 4 KW.

Serial No. : BKMO600510

วันที่ตรวจเช็ค 3 Feb 25

สถานที่ติดตั้ง Substation room ชั้น 6

ความถี่	Item	รายการตรวจเช็ค / ดำเนินการ	ผลการตรวจเช็ค		ผลการแก้ไข		บันทึกเพิ่มเติม
			ปกติ	ผิดปกติ	เสร็จ	ไม่เสร็จ	
ประจำ 1 เดือน		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง					
	1	ตรวจสอบสภาพภายนอกและภายในตู้ควบคุม					
	2	ตรวจเช็คจุดต่อทางไฟฟ้า และความแน่นของขั้วไฟจุดต่างๆ					
	3	ทำความสะอาดและเป่าฝุ่นทั้งภายในและภายนอกตู้ควบคุม	☒	ดำเนินการ	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	4	ตรวจเช็ค Pilot Lamp และอุปกรณ์ต่างๆ เช่น Fuse, Meter ฯลฯ					
	5	ตรวจสอบสภาพทั่วไปของพัดลม					
	6	ทำความสะอาดและเป่าฝุ่นหน้ากรังจ่ายลม	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	☐ ไม่ได้ดำเนินการ เนื่องจาก
	7	ถอดล้าง Filter กรองอากาศ (ถ้ามี)	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	☐ ไม่ได้ดำเนินการ เนื่องจาก
	8	ถอดล้างตะแกรงกันแมลงหรือกันนก (ถ้ามี)	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	☐ ไม่ได้ดำเนินการ เนื่องจาก
	9	หล่อลื่นลูกปืนมอเตอร์และลูกปืน Blower			☐	ดำเนินการเรียบร้อยแล้ว	☐ ไม่ได้ดำเนินการ เนื่องจาก
	10	ตรวจเช็คและปรับตั้งสายพาน (เปลี่ยนทุก 3000 ชั่วโมง หรือ 1 ปี)			☒	ดำเนินการปรับตั้ง	☐ ชำรุดมาก ควรเปลี่ยนใหม่
		ON CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง แล้วเดินเครื่อง					
	11	วัดแรงดันไฟฟ้าเข้าเครื่อง	R-N <u>220</u> V. S-N <u>220</u> V. T-N <u>220</u> V.				
			R-S <u>380</u> V. S-T <u>380</u> V. T-R <u>380</u> V.				
	12	วัดกระแสไฟฟ้าของมอเตอร์พัดลม	R <u>6.2</u> A. S <u>6.2</u> A. T <u>6.1</u> A.				Name Plate FLA = <u>6.4</u> A.
ประจำ 1 ปี		ตรวจสอบสภาพการทำงานทั่วไปและเสียงที่อาจดังผิดปกติ					
	13	ตรวจความสั่นสะเทือน (Alignment) ของตัวเครื่อง					
	14	ตรวจสอบอุณหภูมิของเบร็กและมอเตอร์เบืองตัน (โดยการสัมผัส)					
	15	OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง					
	16	ทำความสะอาด Blower และตัวถังเครื่อง	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	17	ตรวจเช็คสภาพของลูกปืน หรือเปลี่ยน(เมื่อจำเป็น)					เปลี่ยนทุก 10000 ชั่วโมง หรือไม่เกิน 5 ปี
	18	ตรวจเช็คขั้วไฟฟ้า และฉนวนลวดสายที่หุ้มฉนวนไม่แน่น	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	19	ตรวจเช็คความมั่นคงของ Support เครื่อง					

รายละเอียดกรณีผิดปกติ และการแก้ไข หรือแก้ไขไม่แล้วเสร็จ :

รายการอะไหล่ที่ใช้ไป :

ไม่มี

Technician _____
(_____)

Duty Engineer _____
(_____)

Chief Engineer _____
(_____)

VENTILATION FAN (Belt Driven 3P)

ชื่อเครื่อง 6A-01 Brand/ ยี่ห้อ: Kruger Model/ รุ่น: Bsbaoom
 ขนาดเครื่อง 5460 Ws CFM. ขนาดมอเตอร์ A KW. Serial No.: Bkmo60510 วันที่ตรวจเช็ค 3 Mar 26
 สถานที่ติดตั้ง Substation room ชั้น 6

ความถี่	Item	รายการตรวจเช็ค / ดำเนินการ	ผลการตรวจเช็ค		ผลการแก้ไข		บันทึกเพิ่มเติม		
			ปกติ	ผิดปกติ	เสร็จ	ไม่เสร็จ			
ประจำ 1 เดือน		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง							
	1	ตรวจสอบสภาพภายนอกและภายในตู้ควบคุม	✓						
	2	ตรวจเช็คจุดต่อทางไฟฟ้า และความแน่นของขั้วไฟจุดต่างๆ	✓						
	3	ทำความสะอาดและเป่าฝุ่นทั้งภายในและภายนอกตู้ควบคุม	✓	ดำเนินการ	✓	ไม่ได้ดำเนินการ เนื่องจาก			
	4	ตรวจเช็ค Pilot Lamp และอุปกรณ์ต่างๆ เช่น Fuse, Meter ฯลฯ	✓						
	5	ตรวจสอบสภาพทั่วไปของพัดลม	✓						
	6	ทำความสะอาดและเป่าฝุ่นหน้ากรังจ่ายลม	✓	ไม่มี	✓	ดำเนินการเรียบร้อยแล้ว	✓	ไม่ได้ดำเนินการ เนื่องจาก	
	7	ถอดล้าง Filler ทรงอากาศ (ถ้ามี)	✓	ไม่มี	✓	ดำเนินการเรียบร้อยแล้ว	✓	ไม่ได้ดำเนินการ เนื่องจาก	
	8	ถอดล้างตะแกรงกันแมลงหรือกันนก (ถ้ามี)	✓	ไม่มี	✓	ดำเนินการเรียบร้อยแล้ว	✓	ไม่ได้ดำเนินการ เนื่องจาก	
	9	หล่อลื่นลูกปืนมอเตอร์และลูกปืน Blower	✓		✓	ดำเนินการเรียบร้อยแล้ว	✓	ไม่ได้ดำเนินการ เนื่องจาก	
	10	ตรวจเช็คและปรับตั้งสายพาน (เปลี่ยนทุก 3000 ชั่วโมง หรือ 1 ปี)				✓	ดำเนินการปรับตั้ง	✓	ทำตาม ควรเปลี่ยนใหม่
		ON CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง แล้วเดินเครื่อง							
	11	วัดแรงดันไฟฟ้าเข้าเครื่อง	R-N <u>220</u> V. S-N <u>220</u> V. T-N <u>220</u> V.						
			R-S <u>380</u> V. S-T <u>380</u> V. T-R <u>380</u> V.						
	12	วัดกระแสไฟฟ้าของมอเตอร์พัดลม	R <u>6.2</u> A. S <u>6.2</u> A. T <u>6.2</u> A.					Name Plate FLA - <u>6.3</u> A.	
13	ตรวจเช็คสภาพการทำงานทั่วไปและเสียงที่อาจดังผิดปกติ								
14	ตรวจความสั่นสะเทือน (Alignment) ของตัวเครื่อง								
15	ตรวจสอบอุณหภูมิของเบร้งและมอเตอร์เบื้องต้น (โดยการสัมผัส)								
ประจำ 1 ปี		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง							
	16	ทำความสะอาด Blower และตัวถังเครื่อง	✓	ดำเนินการเรียบร้อยแล้ว	✓	ไม่ได้ดำเนินการ เนื่องจาก			
	17	ตรวจเช็คสภาพของลูกปืน หรือเปลี่ยน(เมื่อจำเป็น)					เปลี่ยนทุก 10000 ชั่วโมง หรือไม่เกิน 5 ปี		
	18	ตรวจเช็คขั้วไฟฟ้า และฉนวนหุ้มสายที่หุ้มความถี่แน่น	✓	ดำเนินการเรียบร้อยแล้ว	✓	ไม่ได้ดำเนินการ เนื่องจาก			
	19	ตรวจเช็คความมั่นคงของ Support เครื่อง							

รายละเอียดกรณีผิดปกติ และการแก้ไข หรือแก้ไขไปแล้วเสร็จ :

รายการอะไหล่ที่ใช้ไป :

Technician

Duty Engineer

Chief Engineer

VENTILATION FAN (Belt Driven 3P)

☐ Monthly ☐ Yearly

ชื่อเครื่อง 6A-01

Brand/ ยี่ห้อ: Kruger

Model/ รุ่น: Bsb 300tn

ขนาดเครื่อง 540x615 CFM.

ขนาดมอเตอร์ 4 KW.

Serial No.: Bkmo600510

วันที่ตรวจเช็ค 3 Apr 26

สถานที่ติดตั้ง Substation room ชั้น 6

ความถี่	Item	รายการตรวจเช็ค / ดำเนินการ	ผลการตรวจเช็ค		ผลการแก้ไข		บันทึกเพิ่มเติม
			ปกติ	ผิดปกติ	เสร็จ	ไม่เสร็จ	
ประจำ 1 เดือน		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง					
	1	ตรวจสอบสภาพภายนอกและภายในตู้ควบคุม					
	2	ตรวจเช็คจุดต่อทางไฟฟ้า และความแน่นของขั้วไฟจุดต่างๆ					
	3	ทำความสะอาดและเป่าฝุ่นทั้งภายในและภายนอกตู้ควบคุม	☒	ดำเนินการ	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	4	ตรวจเช็ค Pilot Lamp และอุปกรณ์ต่างๆ เช่น Fuse, Meter ฯลฯ					
	5	ตรวจสอบสภาพทั่วไปของพัดลม					
	6	ทำความสะอาดและเป่าฝุ่นหน้ากระจายลม	☒ ไม่มี	☐ ดำเนินการเรียบร้อยแล้ว	☐ ไม่ได้ดำเนินการ เนื่องจาก		
	7	ถอดล้าง Filler กรองอากาศ (ถ้ามี)	☒ ไม่มี	☐ ดำเนินการเรียบร้อยแล้ว	☐ ไม่ได้ดำเนินการ เนื่องจาก		
	8	ถอดล้างตะแกรงกันแมลงหรือกันนก (ถ้ามี)	☒ ไม่มี	☐ ดำเนินการเรียบร้อยแล้ว	☐ ไม่ได้ดำเนินการ เนื่องจาก		
	9	หล่อลื่นลูกปืนมอเตอร์และลูกปืน Blower	☒	ดำเนินการเรียบร้อยแล้ว	☐ ไม่ได้ดำเนินการ เนื่องจาก		
	10	ตรวจเช็คและปรับตั้งสายพาน (เปลี่ยนทุก 3000 ชั่วโมง หรือ 1 ปี)			☒ ดำเนินการปรับตั้ง	☐ จารุดมาก ควรเปลี่ยนใหม่	
		ON CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง แล้วเดินเครื่อง					
	11	วัดแรงดันไฟฟ้าเข้าเครื่อง	R-N 220 V. S-N 220 V. T-N 220 V.				
			R-S 380 V. S-T 380 V. T-R 380 V.				
	12	วัดกระแสไฟฟ้าของมอเตอร์พัดลม	R 6.2 A. S 6.1 A. T 6.2 A.				Name Plate FLA - 6.4 A.
13	ตรวจสอบสภาพการทำงานทั่วไปและเสียงที่อาจดังผิดปกติ						
14	ตรวจสอบความสั่นสะเทือน (Alignment) ของตัวเครื่อง						
15	ตรวจสอบอุณหภูมิของเบรจและมอเตอร์เบืองตัน (โดยการสัมผัส)						
ประจำ 1 ปี		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง					
	16	ทำความสะอาด Blower และตัวถังเครื่อง	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	17	ตรวจสอบสภาพของลูกปืน หรือเปลี่ยน(เมื่อจำเป็น)				เปลี่ยนทุกๆ 10000 ชั่วโมง หรือไม่เกิน 5 ปี	
	18	ตรวจเช็คขั้วไฟฟ้า และขันน็อตหัวสายที่หลวมไม่แน่น	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	19	ตรวจเช็คความมั่นคงของ Support เครื่อง					

รายละเอียดกรณีผิดปกติ และการแก้ไข หรือแก้ไขไม่แล้วเสร็จ :

รายการอะไหล่ที่ใช้ไป :

Technician _____
(_____)

Duty Engineer _____
(_____)

Chief Engineer _____
(_____)

VENTILATION FAN (Belt Driven 3P)

☒ Monthly☐ Yearly

ชื่อเครื่อง 6A-01

Brand/ ป้าย : Kruger

Model/ રૂન: bsb 90072m

ขนาดเครื่อง 540 LB CFM.

ขนาดมอเตอร์ 4 KW.

Serial No. : DKM06002510

วันที่ตรวจเช็ค 5 May 25

สถานที่ติดตั้ง Substation room ชั้น 6

ความถี่	Item	รายการตรวจเช็ค / ดำเนินการ	ผลการตรวจเช็ค		ผลการแก้ไข		บันทึกเพิ่มเติม		
			ปกติ	ผิดปกติ	เสร็จ	ไม่เสร็จ			
ประจำ 1 เดือน		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง							
	1	ตรวจสอบสภาพภายนอกและภายในตู้ควบคุม		/					
	2	ตรวจเช็คจุดต่อทางไฟฟ้า และความแน่นของขั้วไฟจุดต่างๆ		/					
	3	ทำความสะอาดและเป่าฝุ่นทั้งภายในและภายนอกตู้ควบคุม	☒	ดำเนินการ	☐	ไม่ได้ดำเนินการ เนื่องจาก			
	4	ตรวจเช็ค Pilot Lamp และอุปกรณ์ต่างๆ เช่น Fuse, Meter ฯลฯ		/					
	5	ตรวจสอบสภาพทั่วไปของพัดลม		/					
	6	ทำความสะอาดและเป่าฝุ่นหน้ากริ่งจ่ายลม	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	7	ถอดล้าง Filter กรองอากาศ (ถ้ามี)	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	8	ถอดล้างตะแกรงกั้นแมลงหรือก้นกบ (ถ้ามี)	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	9	หล่อลื่นลูกปืนมอเตอร์และลูกปืน Blower	☒	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก			
	10	ตรวจเช็คและปรับตั้งสายพาน (เปลี่ยนทุก 3000 ชั่วโมง หรือ 1 ปี)				☒	ดำเนินการปรับตั้ง	☐	ว่าดูมาก ควรเปลี่ยนใหม่
		ON CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง แล้วเดินเครื่อง							
	11	วัดแรงดันไฟฟ้าเข้าเครื่อง	R-N 220 V.	S-N 220 V.	T-N 220 V.				
			R-S 380 V.	S-T 380 V.	T-R 380 V.				
	12	วัดกระแสไฟฟ้าของมอเตอร์พัดลม	R 6.1 A.	S 6.1 A.	T 6.2 A.			Name Plate FLA = A.	
13	ตรวจเช็คสภาพการทำงานทั่วไปและเสียงที่อาจดังผิดปกติ		/						
14	ตรวจความสั่นสะเทือน (Alignment) ของตัวเครื่อง		/						
15	ตรวจสอบอุณหภูมิของเบร้งและมอเตอร์เบื้องต้น (โดยการสัมผัส)		/						
ประจำ 1 ปี		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง							
	16	ทำความสะอาด Blower และตัวถังเครื่อง	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก			
	17	ตรวจเช็คสภาพของลูกปืน หรือเปลี่ยน(เมื่อจำเป็น)					เปลี่ยนทุก 10000 ชั่วโมง หรือไม่เกิน 5 ปี		
	18	ตรวจเช็คขั้วไฟฟ้า และขันน็อตสายที่หุ้มฉนวนให้แน่น	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก			
	19	ตรวจเช็คความมั่นคงของ Support เครื่อง							

รายละเอียดกรณีผิดปกติ และการแก้ไข หรือแก้ไขไม่แล้วเสร็จ :

รายการอะไหล่ที่ใช้ไป :

Skf $\frac{24}{24}$ 19200

Technician_____

Duty Engineer: _____

Chief Engineer _____

(_____)

(_____

(_____)

VENTILATION FAN (Belt Driven 3P)

ชื่อเครื่อง: 4A-01 Brand/ ยี่ห้อ: Kruger Model/ รุ่น: Bsbroom
 ขนาดเครื่อง: 540L/s CFM. ขนาดมอเตอร์: 4 KW. Serial No.: Bkno600910 วันที่ตรวจเช็ค: 3/6/26
 สถานที่ติดตั้ง: Substation room ชั้น 6

ความถี่	Item	รายการตรวจเช็ค / ดำเนินการ	ผลการตรวจเช็ค		ผลการแก้ไข		บันทึกเพิ่มเติม
			ปกติ	ผิดปกติ	เสร็จ	ไม่เสร็จ	
ประจำ 1 เดือน		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง	/				
	1	ตรวจสอบสภาพภายนอกและภายในตู้ควบคุม	/				
	2	ตรวจเช็คจุดต่อทางไฟฟ้า และความแน่นของขั้วไฟจุดต่างๆ	/				
	3	ทำความสะอาดและปาดฝุ่นทั้งภายในและภายนอกตู้ควบคุม	☒	ดำเนินการ	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	4	ตรวจเช็ค Pilot Lamp และอุปกรณ์ต่างๆ เช่น Fuse, Meter ฯลฯ	/				
	5	ตรวจสอบสภาพทั่วไปของพัดลม	/				
	6	ทำความสะอาดและปาดฝุ่นหน้ากริดจ่ายลม	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	ไม่ได้ดำเนินการ เนื่องจาก
	7	ถอดล้าง Filter กรองอากาศ (ถ้ามี)	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	ไม่ได้ดำเนินการ เนื่องจาก
	8	ถอดล้างตะแกรงกันแมลงหรือก้นก (ถ้ามี)	☒	ไม่มี	☐	ดำเนินการเรียบร้อยแล้ว	ไม่ได้ดำเนินการ เนื่องจาก
	9	หล่อลื่นลูกปืนมอเตอร์และลูกปืน Blower	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	10	ตรวจเช็คและปรับตั้งสายพาน (เปลี่ยนทุก 3000 ชั่วโมง หรือ 1 ปี)			☒	ดำเนินการปรับตั้ง	☐ วัสดุมาก ควรเปลี่ยนใหม่
		ON CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง แล้วเดินเครื่อง					
	11	วัดแรงดันไฟฟ้าเข้าเครื่อง	R-N <u>220</u> V. S-N <u>220</u> V. T-N <u>220</u> V.				
			R-S <u>380</u> V. S-T <u>380</u> V. T-R <u>380</u> V.				
	12	วัดกระแสไฟฟ้าของมอเตอร์พัดลม	R <u>6.1</u> A. S <u>6.2</u> A. T <u>6.1</u> A.				Name Plate FLA = <u>6.4</u> A.
ประจำ 1 ปี	13	ตรวจเช็คสภาพการทำงานทั่วไปและเสียงที่อาจดังผิดปกติ	/				
	14	ตรวจความสั่นสะเทือน (Alignment) ของตัวเครื่อง	/				
	15	ตรวจสอบอุณหภูมิของเบร็กและมอเตอร์เบร็ก (โดยการสัมผัส)	/				
		OFF CB ที่จ่ายกระแสไฟฟ้าเข้าเครื่อง					
	16	ทำความสะอาด Blower และตัวถังเครื่อง	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	17	ตรวจเช็คสภาพของลูกปืน หรือเปลี่ยน (เมื่อจำเป็น)					เปลี่ยนทุกๆ 10000 ชั่วโมง หรือไม่เกิน 5 ปี
	18	ตรวจเช็คขั้วไฟฟ้า และฉนวนที่สายที่หุ้มฉนวนไฟฟ้าน	☐	ดำเนินการเรียบร้อยแล้ว	☐	ไม่ได้ดำเนินการ เนื่องจาก	
	19	ตรวจเช็คความมั่นคงของ Support เครื่อง					

รายละเอียดกรณีผิดปกติ และการแก้ไข หรือแก้ไขไปแล้วเสร็จ :

รายการอะไหล่ที่ใช้ไป :

WD 40 & SKF 111000

Technician _____
 (_____)

Duty Engineer _____
 (_____)

Chief Engineer _____
 (_____)

เอกสารแนบ 13
สำเนาเอกสารการไฟฟ้าช้อนดับเพลิง และซ่อมอพยพหนีไฟ



วุฒิบัตรเลขที่:สปภ.(กปภ.๒).๑๖๑๑ /๒๕๖๔

กรุงเทพมหานคร

ได้รับใบอนุญาตจากกรมสวัสดิการและคุ้มครองแรงงาน ใบอนุญาตเลขที่ ๐๑๐๒-๐๒-๒๕๖๗-๐๑๕๑
ขอรับรองว่า

.....
โรงแรม โซ แบนคอก

ตั้งอยู่เลขที่ ๒ ถนนสาทรเหนือ แขวงสีลม เขตบางรัก กรุงเทพมหานคร ๑๐๕๐๐

ได้ดำเนินการฝึกซ้อมดับเพลิงและฝึกซ้อมอพยพหนีไฟ

ตามกฎหมายกระทรวงกำหนดมาตรฐานในการบริหาร จัดการ และดำเนินการด้านความปลอดภัย อาชีวอนามัย
และสภาพแวดล้อมในการทำงานเกี่ยวกับการป้องกันและระงับอัคคีภัย พ.ศ. ๒๕๕๕ ลงวันที่ ๗ ธันวาคม พ.ศ. ๒๕๕๕

มีผู้เข้ารับการฝึกอบรม จำนวน ๙๒ คน

เมื่อวันที่ ๗ ตุลาคม ๒๕๖๘

ให้ไว้ ณ วันที่ ๑๖ ต.ค. ๒๕๖๘



ผู้อำนวยการสำนักป้องกันและบรรเทาสาธารณภัย
ปฏิบัติราชการแทนผู้อำนวยการกรุงเทพมหานคร

เอกสารแบบ 14
สำเนาเอกสารการตรวจสอบระบบป้องกันอัคคีภัย

เอกสารตรวจสอบระบบดับเพลิง



บริษัท ยูไนเต็ด เพาเวอร์ เอ็นจิเนียริง จำกัด

UNITED POWER ENGINEERING CO., LTD.

4 Soi Sukhumvit 81 (Sriplot), Sukhumvit Rd, Bangkok, Phrakhanong, Bangkok 10260, THAILAND Tel: (662) 7425366 (12 Lines) Fax: (662) 7425378, 7425379

4 ซอยสุขุมวิท 81 (ศรีพลท) ถนนสุขุมวิท แขวงบางจาก เขตพระโขนง กรุงเทพฯ 10260 โทร. (662) 7425366 (12 Lines) โทรสาร. (662) 7425378, 7425379

<http://www.unitedpower.co.th> / e-mail : upe@unitedpower.co.th

MAINTENANCE SCHEDULES & RECORDS

Customer Name and Address	Tech	Sales	Time	Date	Job No.
OAKTREE COMPANY LIMITED.	W.P.S.K./P.S.E	KP	11.00	14/4/19	110-9026/10
	Project Name				Times No.
	SO BANGKOK (VERANDA)				FP-01 (LOW ZONE)

Other	ครั้งที่ 2/2			
29	ตรวจสอบและปรับข้อต่อทั้งหมดในระบบท่อที่มากับเครื่องสูบน้ำ (ในกรณีของเครื่องสูบน้ำดับเพลิง) อาทิ รีลฟวาล์ว (Relief Valve) , สวิตช์แรงดัน และอื่นๆ	☒	☐	*
30	ปรับแต่งโปรแกรมการตั้งเวลาของนาฬิกา (ในกรณีของเครื่องสูบน้ำดับเพลิง)	☒	☐	
31	ตรวจสอบระบบการติดเครื่องยนต์อัตโนมัติ (ในกรณีของเครื่องสูบน้ำดับเพลิงที่ได้มาตรฐาน NFPA 20)	☒	☐	
32	ตรวจสอบการทำงานของวงจรรีเลย์เบรกเกอร์ (ในกรณีของเครื่องสูบน้ำดับเพลิงชนิดเครื่องยนต์ดีเซล)	☒	☐	

B. Half Year Service Inspection

Item	Description	Yes	No	Remark
Driver		Brand: , Model: , S/N:		
[ENGINE]		A.C Power Supply : V/ DC Ph/ Hz , Speed rpm., Power (KW/HP), Full load - A.]		
	ในกรณีของเครื่องสูบน้ำที่ขับเคลื่อนด้วยมอเตอร์	☐	☐	
33	ตรวจสอบความต้านทานของ Motor Stator	☐	☐	
	ในกรณีของเครื่องสูบน้ำที่ขับเคลื่อนด้วยเครื่องยนต์	☐	☐	
34	ตรวจสอบระบบทางเข้าอากาศ	☒	☐	
35	ตรวจสอบการกรองอากาศ	☒	☐	

The Undersigned herewith declares that the job has been completed to entire satisfaction.

* B1 = 12.95 V
B2 = 12.63 V
- Auto Start - 130 Psi



Customer/Company Stamp



Technician

Inspector/Consultant



บริษัท ยูไนเต็ด เพาเวอร์ เอ็นจิเนียริง จำกัด

UNITED POWER ENGINEERING CO., LTD.

4 Soi Sukhumvit 81 (Supt), Sukhumvit Rd., Bangkok, Phrakhanong, Bangkok 10260, THAILAND Tel: (662) 7425366 (12 Lines) Fax: (662) 7425378, 7425379

4 ซอยสุขุมวิท 81 (ศิริพจน์) ถนนสุขุมวิท แขวงบางจาก เขตพระโขนง กรุงเทพฯ 10260 โทร. (662) 7425366 (12 Lines) โทรสาร. (662) 7425378, 7425379

<http://www.unitedpower.co.th> / e-mail : upe@unitedpower.co.th

MAINTENANCE & RECORDS

Customer Name and Address	Tech	Sales	Time	Date	Job No.
OAKTREE COMPANY LIMITED.	Service	KP	11:00	18/4/18	110-9026/10
	Project Name				Times No.
	SO BANGKOK (VERANDA)				FP-01 (LOW ZONE)

C. Annual Service Inspection

ครั้งที่ 2/2

Item	Description	Yes	No	Remark
Pump F/P	[Brand: AURORA , Model: 6-481-14HH , S/N: 10-1937360			
	Capacity : 1250 gpm. , TDH : 160 PSI ft, Speed : 3000 rpm.]			
36	ตรวจสอบการทำงานของเบรค	☒	☐	
37	ตรวจสอบและปรับแต่งการ Alignment ของเครื่องสูบน้ำและตัวจุดกำลัง	☒	☐	
ENGINE	[Brand: CLARKE , Model: JU6H-UF54 , S/N: RE6068T785546			
	A.C Power Supply : V/ DC Ph/ Hz , Speed 3000 rpm., Power 216 (KW/HP), Full load - A.]			
	ในกรณีของเครื่องสูบน้ำที่ขับเคลื่อนด้วยเครื่องยนต์			
38	เปลี่ยนถ่ายน้ำมันเครื่องและไส้กรอง	☒	☐	เปลี่ยนไส้กรอง
39	เปลี่ยนไส้กรองเชื้อเพลิง	☒	☐	OK
40	เปลี่ยนไส้กรองหล่อเย็นและตรวจสอบนํ้าหล่อเย็น	☒	☐	OK
41	เปลี่ยนไส้กรองอากาศ	☒	☐	OK
42	ตรวจสอบการตั้งค่าสวิตช์โอเวอร์สเปด	☒	☐	OK
43	ตรวจสอบระบบท่ออ่อนทั้งหมด	☒	☐	OK
44	ตรวจสอบอุปกรณ์ควบคุมในระบบไฟฟ้าทั้งหมด	☒	☐	OK

Pump	Driver
Brand : AURORA	Brand : MARATHON
Model : PVM8-110	Model :
S/N : 2545581-10	S/N : E2012

JOCKEY PUMP TEST RECORD

Driver	A.C. Power Supply	380	V/	3	Ph/	50	Hz	Vac L1-L2: 397.1 V
	RPM	2845	rpm					L2-L3: 397.1 V
	Size	3.70	Hp	KW				L3-L1: 399.0 V
	Full load	7.2	Amp.					
	Type of Mounting	☒ Vertical Mount		☐ Horizontal Mount				
	Starting Type	☒ D.O.L.		☐ Star-Delta				
	Inboard Ball Bearing	☒ O.K.		☐ Not O.K.				
	Outboard Ball Bearing	☒ O.K.		☐ Not O.K.				
	Current Consumption	L1	5.63	Amp.	L2	5.39	Amp.	L3
								6.01 Amp.

The Undersigned herewith declares that the job has been completed to entire satisfaction.

Customer/Company Stamp

Technician

Inspector/Consultant



บริษัท ยูไนเต็ด เพาเวอร์ เอ็นจิเนียริง จำกัด

UNITED POWER ENGINEERING CO., LTD.

4 Soi Sukhumvit 81 (Simpco), Sukhumvit Rd, Bangjok, Phrakong, Bangkok 10260, THAILAND Tel: (662) 7425366 (12 Lines) Fax: (662) 7425378, 7425379

4 ซอยสุขุมวิท 81 (สิริพจน์) ถนนสุขุมวิท แขวงบางจาก เขตพระโขนง กรุงเทพฯ 10260 โทร. (662) 7425366 (12 Lines) โทรสาร. (662) 7425378, 7425379

http://www.unitedpower.co.th / e-mail : upe@unitedpower.co.th

MAINTENANCE SCHEDULES & RECORDS

Customer Name and Address	Tech	Sales	Time	Date	Job No.
OAKTREE COMPANY LIMITED.	WS, RS, SK, PP, SR	KP	11:00	8/11/09	110-9026/10
	Project Name				Times No.
	SO BANGKOK (VERANDA)				FP-01 (LOW ZONE)

A. Normal Inspection

ครั้งที่ 2/2

Item	Description	Yes	No	Remark
Pump F/P				
[Brand: AURORA , Model: 6-481-14HH , S/N: 10-1937360 Capacity : 1250 gpm. , TDH : 160 PSI ft, Speed : 3000 rpm.]				
1	การตรวจสอบทางกายภาพ อาทิ การระบายอากาศในห้อง, ความผิดปกติด้านเสียง, อุณหภูมิ, ความลื่นสะเทือน และความถูกต้องของการติดตั้ง	☒	☐	ok 1/1
2	การรั่วของระบบท่อและข้อต่อที่เชื่อมต่อกับเครื่องสูบน้ำ	☒	☐	
3	ตรวจสอบการรั่วของแพ็คกิ้งซีล หรือแมคคาณิคัลซีล	☒	☐	
4	เงื่อนไขการสูบน้ำและการจ่ายรวมทั้งเกจที่เกี่ยวข้องทั้งหมด	☒	☐	Sue - 0.75'
5	ประสิทธิภาพของเครื่องสูบน้ำ ณ จุดทำงาน	☒	☐	Dis - 15.5'
6	ตรวจสอบ Shut-off head pressure	☒	☐	
7	ตรวจสอบอุณหภูมิและการสั่นที่เบี่ยงและระบบการหล่อลื่น	☒	☐	
ENGINE				
[Brand: CLARKE , Model: JU6H-UF54 , S/N: RE6068T785546 A.C Power Supply : V/ DC Ph/ Hz, Speed 3000 rpm., Power 216 (KW/HP), Full load - A.]				
กรณีของเครื่องสูบน้ำที่ขับเคลื่อนด้วยมอเตอร์ไฟฟ้า				
8	ตรวจสอบการระบายอากาศของมอเตอร์	☐	☐	
9	ตรวจสอบอุณหภูมิ, ความลื่นสะเทือนบนเฟรมมอเตอร์และที่เบี่ยง	☐	☐	
10	ตรวจสอบเงื่อนไข Coupling และการปรับระดับหาจุดศูนย์	☐	☐	
11	ตรวจสอบสายพานและความตึงสายพาน (ถ้าขับเคลื่อนด้วยระบบสายพาน)	☐	☐	
12	ตรวจสอบระบบหล่อลื่น, ทั้งประเภทที่หล่อลื่นด้วยจารบี หรือน้ำมันหล่อลื่น	☐	☐	
13	ตรวจสอบความสิ้นเปลืองพลังงาน	☐	☐	
กรณีของเครื่องสูบน้ำที่ขับเคลื่อนด้วยเครื่องยนต์				
14	ตรวจสอบ Coupling และการปรับหาศูนย์	☒	☐	
15	ตรวจสอบการระบายความร้อนเครื่องยนต์ Temp = 98 C	☒	☐	
16	ตรวจสอบระดับน้ำมันหล่อลื่น Oil Pressure = 75 Psi	☒	☐	
17	ตรวจสอบระดับน้ำยาหล่อเย็น Line Cooling = 40 Psi	☒	☐	
18	ตรวจสอบสายพานและแรงตึงสายพาน	☒	☐	
19	ถ่ายตะกอนออกจากถังเชื้อเพลิง	☒	☐	
20	ทำความสะอาด, ระบบหล่อเย็น และตรวจสอบไดรเวอร์น้ำดิบ	☒	☐	
21	ตรวจสอบคุณภาพของแบตเตอรี่	☒	☐	
22	ตรวจสอบเสียงรบกวนเครื่องจักรอื่นที่ไม่ปกติ	☒	☐	
Electric & Control				
[Brand: CUTLER HAMMER , Model: FD120 , S/N: 16BK349D Voltage Supply : V, Starter type , Cabinet type]				
23	ตรวจสอบคุณสมบัติของไฟฟ้าจากแหล่งจ่าย	☒	☐	120 V
24	ตรวจสอบการเชื่อมต่อของเทอร์มินัลต่างๆ	☒	☐	ok
25	ตรวจสอบการตั้งโอเวอร์โวลด์	☒	☐	
26	ตรวจสอบระบบการป้องกันทั้งหมดและรวมถึงอุปกรณ์ป้องกัน	☒	☐	ok 1/1
27	ตรวจสอบการทำงานของตัวจุดกำลัง	☒	☐	
28	ตรวจสอบการเชื่อมต่อสายภายใน	☒	☐	


The Undersigned certifies that the job has been completed to entire satisfaction.

Customer/Company Stamp



Technician

Inspector/Consultant


เอกสารตรวจสอบระบบแจ้งเตือนภัย



TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 1109

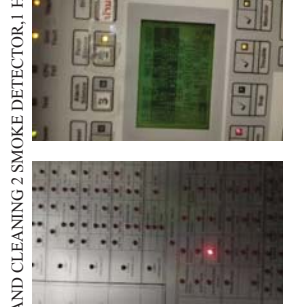


TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 1109



TEST AND CLEANING 3 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 1107

TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 1107

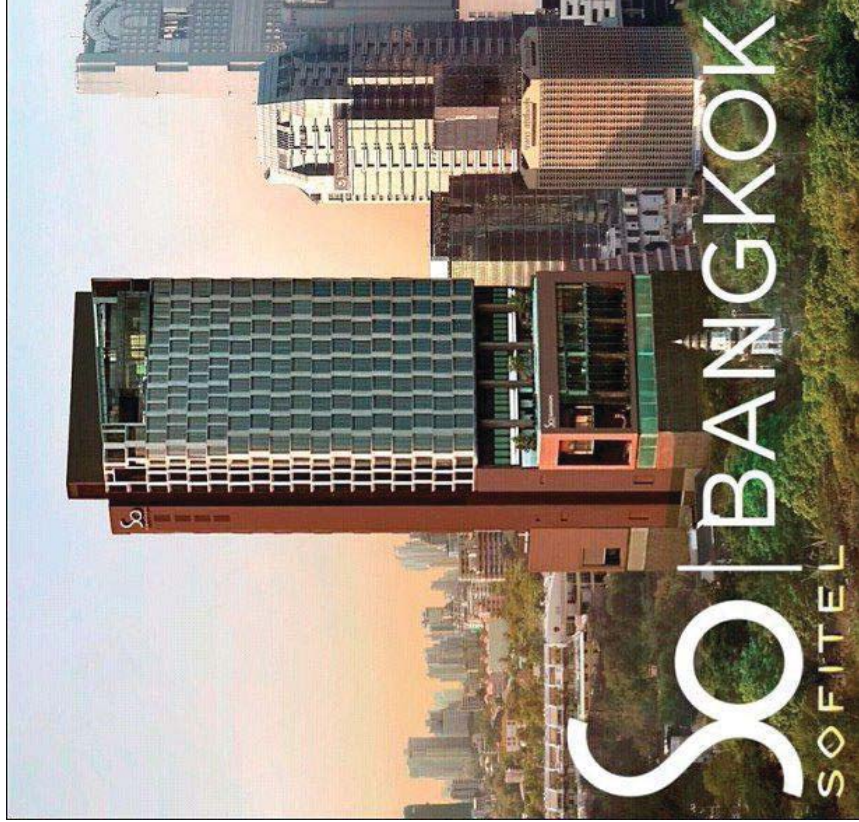






TEST AND CLEANING 1 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 1109





TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 2109



TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 2104



TEST AND CLEANING 1 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 1108





TEST AND CLEANING 1 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 1509




TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 2507



TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 2318



TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 2417



TEST AND CLEANING 1 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 2004




TEST AND CLEANING 1 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 2003




TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 2216



TEST AND CLEANING 2 SMOKE DETECTOR,1 HEAT DETECTOR ROOM 2318

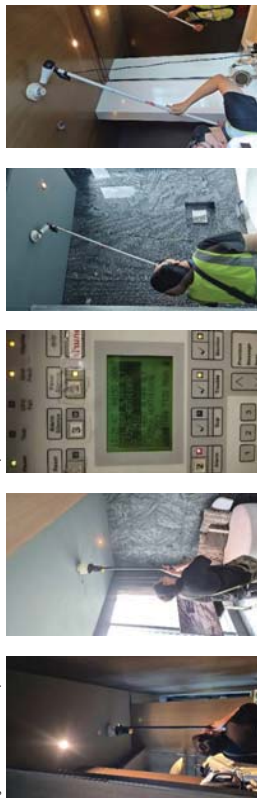


TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2512

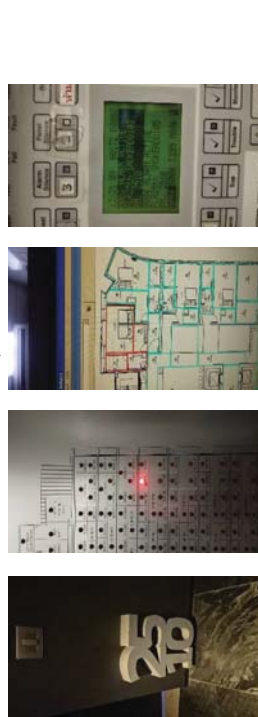

TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2510




TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2710



TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2507




TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2513

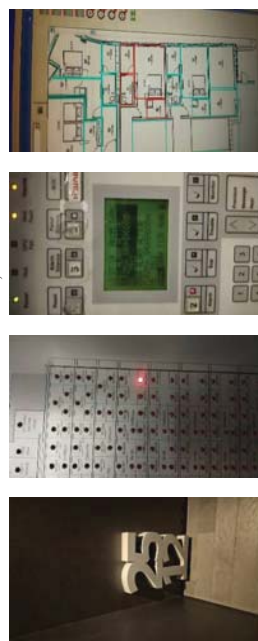




TEST AND CLEANING 6 SMOKE DETECTOR,4 HEAT DETECTOR ROOM 2816

TEST AND CLEANING 6 SMOKE DETECTOR,4 HEAT DETECTOR ROOM 2816

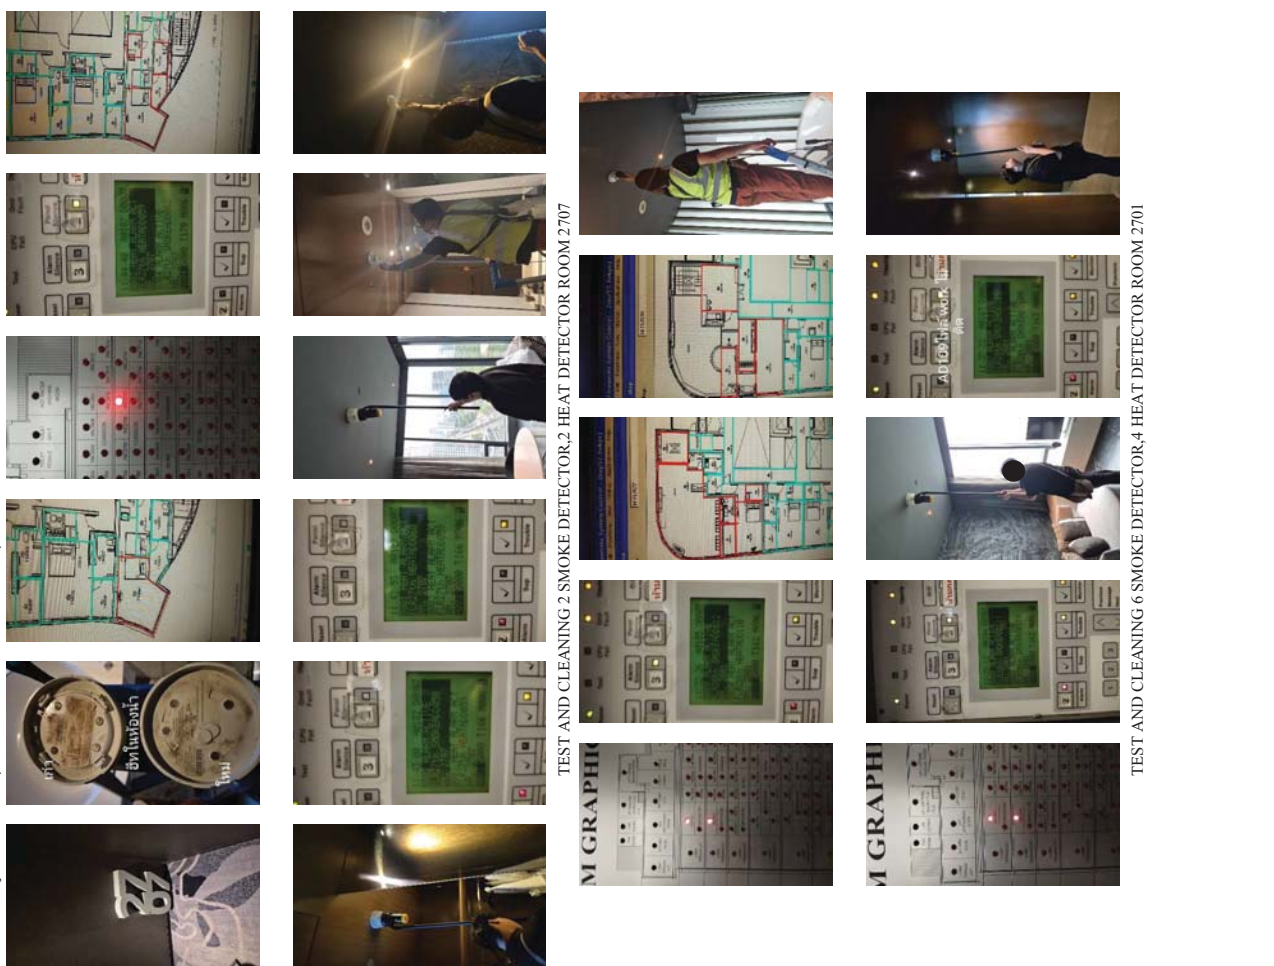


TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2701


TEST AND CLEANING 6 SMOKE DETECTOR,4 HEAT DETECTOR ROOM 2701

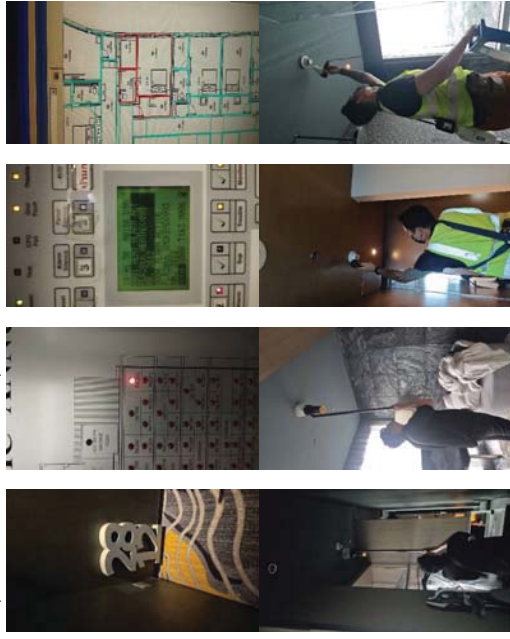


TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2812

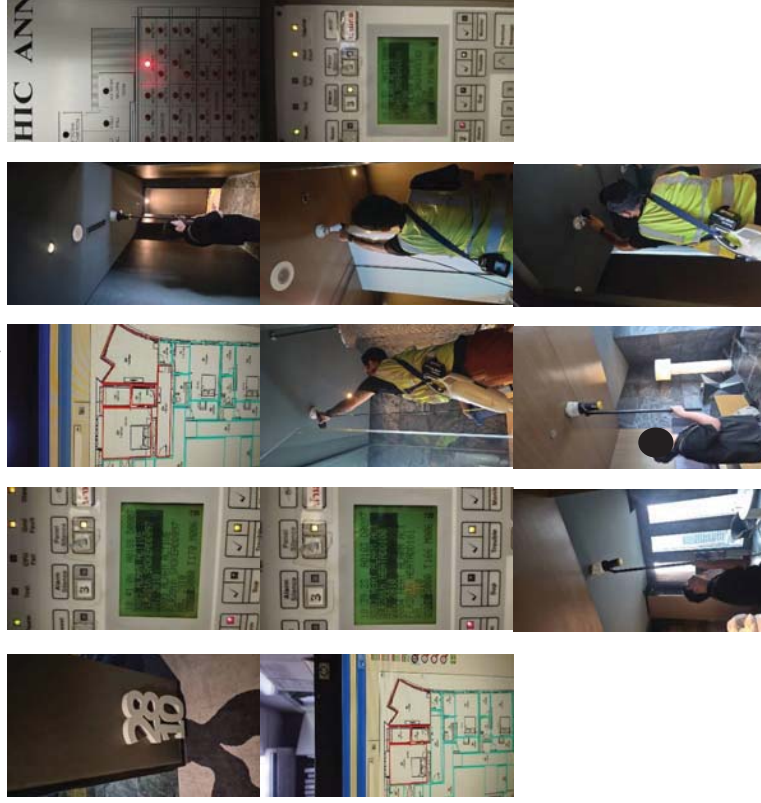


TEST AND CLEANING 3 SMOKE DETECTOR,3 HEAT DETECTOR ROOM 2810

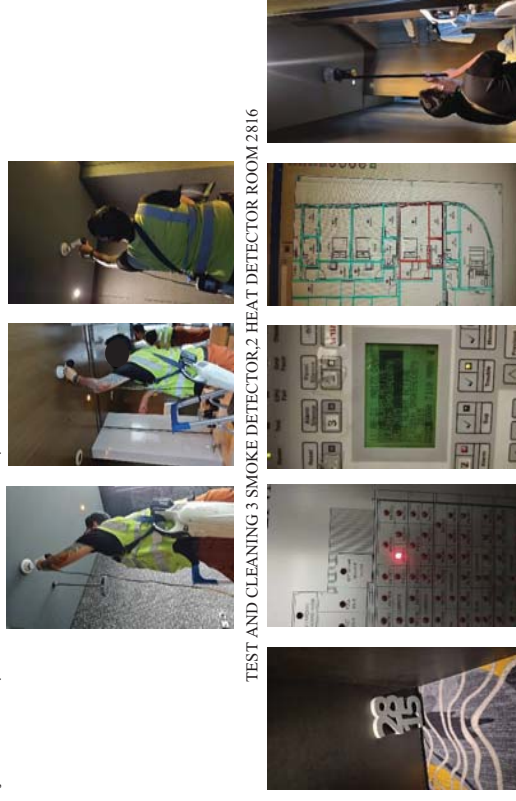

TEST AND CLEANING 3 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2816

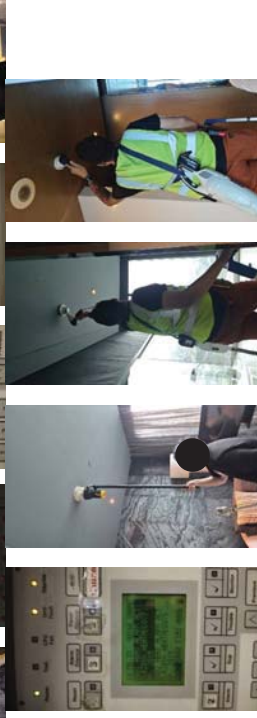

TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2815

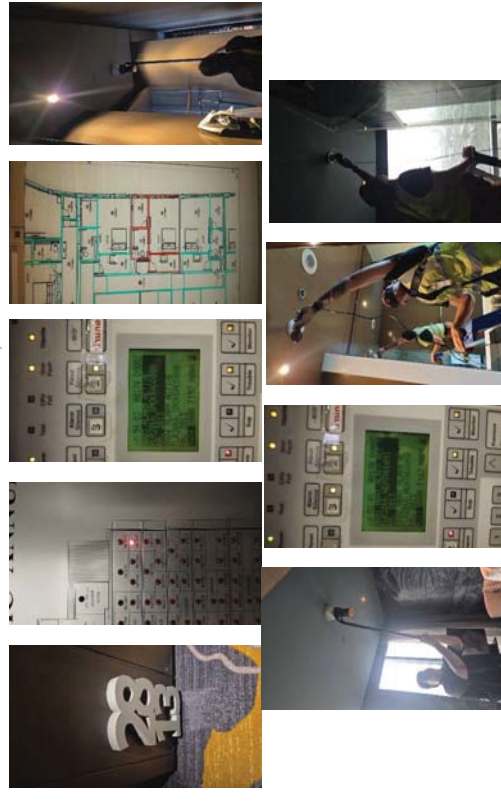


TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2813



TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 2807



TEST AND CLEANING 3 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2807




TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2804



TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 22



TEST AND CLEANING 3 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2806




TEST AND CLEANING 2 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2804




TEST AND CLEANING 3 SMOKE DETECTOR,2 HEAT DETECTOR ROOM 2806




TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 23

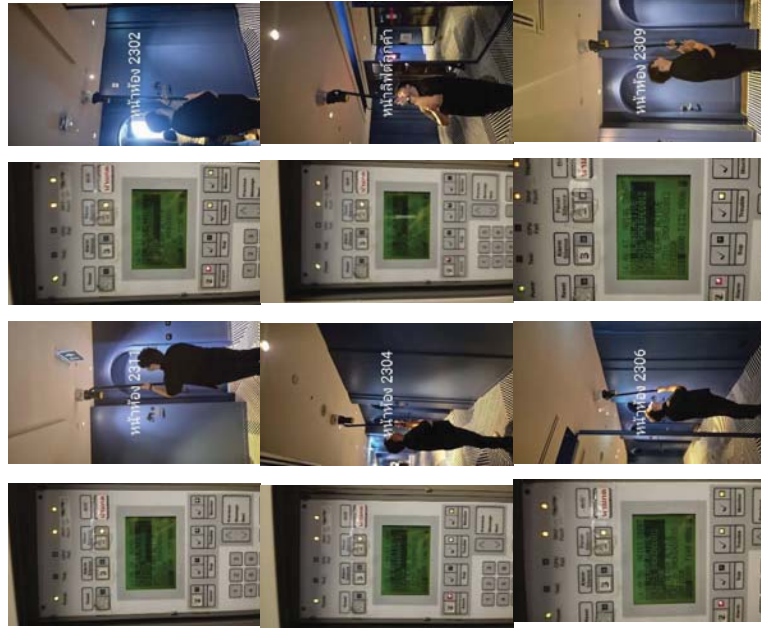


TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 23

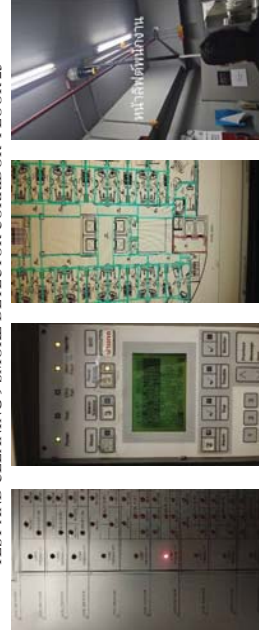

TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 23

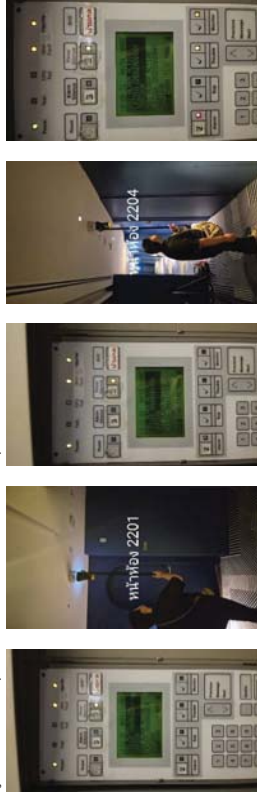

TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 22

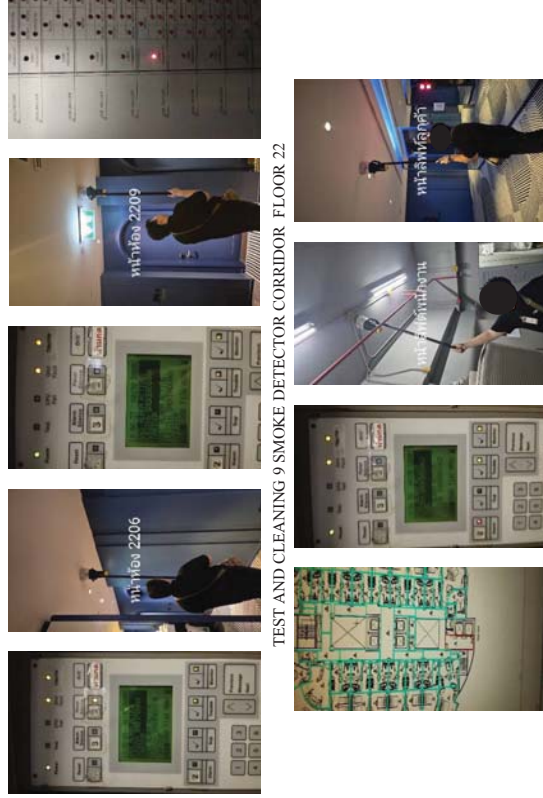

TEST AND CLEANING SMOKE DETECTOR IN FRONT OF LIFT STAFF & CUSTOMER FLOOR 22







TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 24




TEST AND CLEANING 1 SMOKE DETECTOR IN FRONT FLOOR 24



TEST AND CLEANING 10 SMOKE DETECTOR CORRIDOR FLOOR 26




TEST AND CLEANING SMOKE DETECTOR IN FRONT OF LIFT STAFF FLOOR 23




TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 24



TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1601

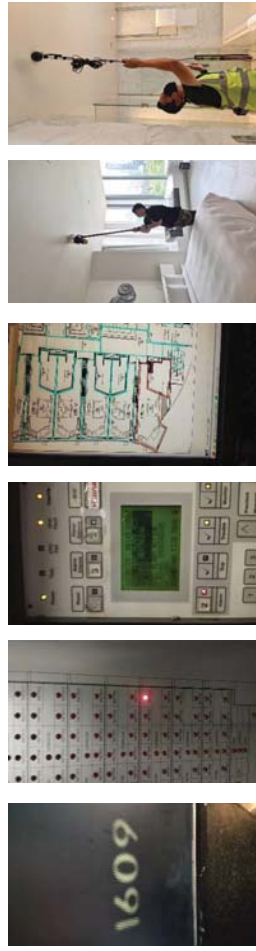


TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1601

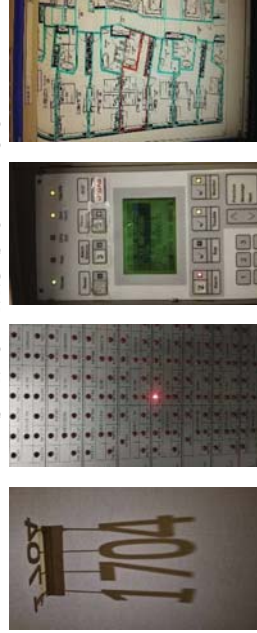

TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1704




TEST AND CLEANING 10 SMOKE DETECTOR CORRIDOR FLOOR 28


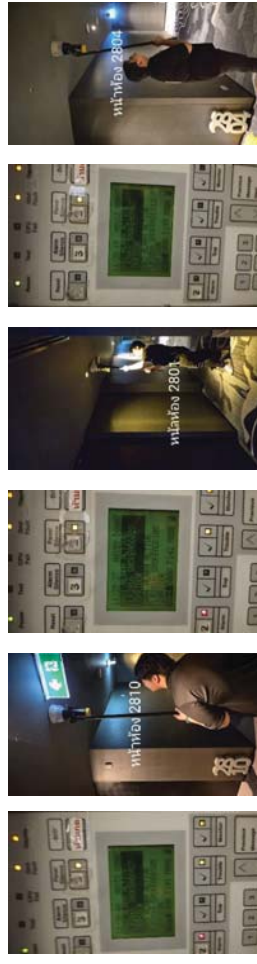


TEST AND CLEANING 10 SMOKE DETECTOR CORRIDOR FLOOR 28








TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1704



TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 2304



TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 2203




TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 2217






TEST AND CLEANING 10 SMOKE DETECTOR CORRIDOR FLOOR 19




TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 21



TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 21



TEST AND CLEANING 2 SMOKE DETECTOR, 2 HEAT DETECTOR ROOM 2604




TEST AND CLEANING 10 SMOKE DETECTOR CORRIDOR FLOOR 19




TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1508



TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1507

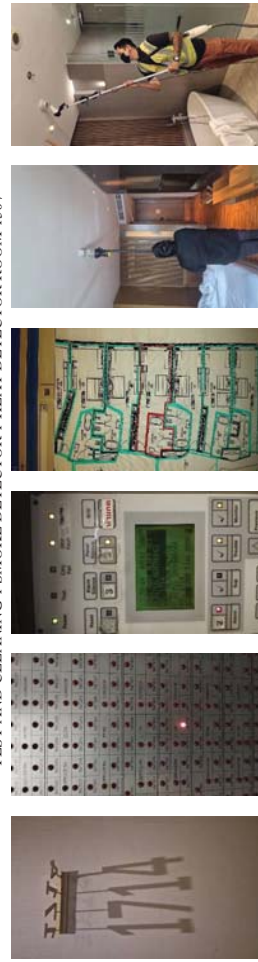


TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1714

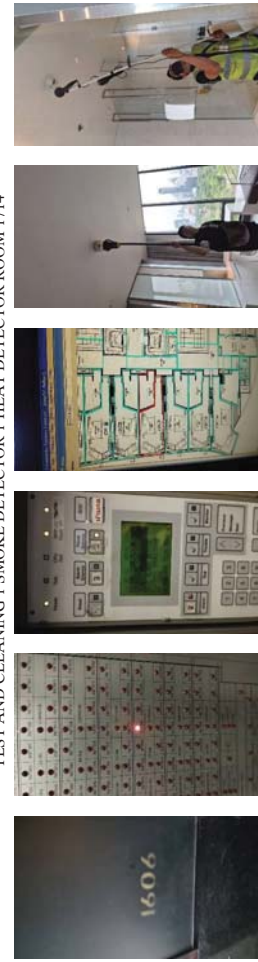


TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1606




TEST AND CLEANING 9 SMOKE DETECTOR CORRIDOR FLOOR 21

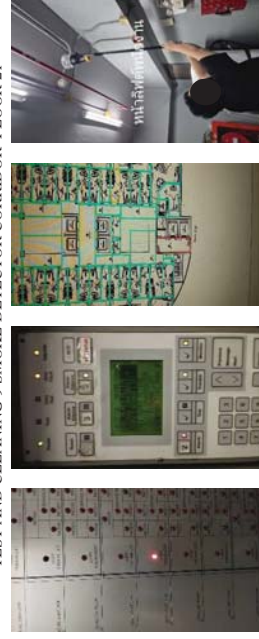


TEST AND CLEANING SMOKE DETECTOR IN FRONT OF LIFT STAFF FLOOR 21

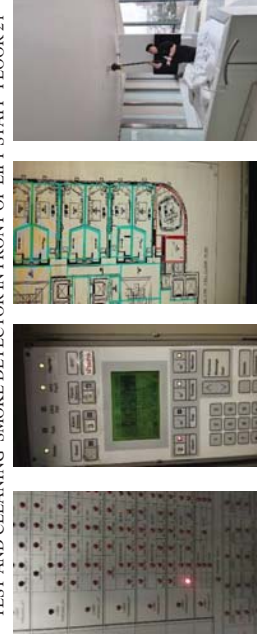

TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1418

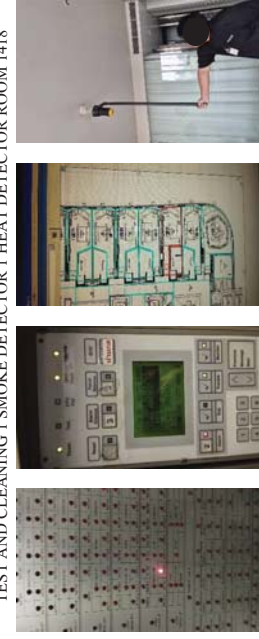

TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1416




TEST AND CLEANING 1 SMOKE DETECTOR, 1 HEAT DETECTOR ROOM 1806




TEST AND CLEANING 1 SMOKE DETECTOR ,1HEAT DETECTOR ROOM 1808



TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1809



TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1904




TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1608




TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1607



TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1709




TEST AND CLEANING 1 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1804




TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 2309



TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1704



TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 2001



TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 2108



TEST AND CLEANING 2 SMOKE DETECTOR 1 HEAT DETECTOR ROOM 1704



CLEAN THE CABINET AFTER COLLECTING THE TEST FIRE ALARM



งานเปลี่ยนอุปกรณ์ SGA HRS จำนวน 1 ตัว Purchase Order 51343399913667UCJE0G

EDWARD SERVICE TECHNOLOGY CO., LTD.
202/9 MOO 6, NONTHABURI 1 ROAD, BANGKASAW, MUANG, NONTHABURI 11000 THAILAND

เอกสารตรวจสอบถักดับเพลิง

SO/ BANGKOK

Month June 2026 -Fire Extinguisher Inspection Report

P20-03	Electric room			1			✓
Floor 19th							
P19-01	Inside fire hose cabinet FHC 19-01		1				✓
P19-02	Inside fire hose cabinet FHC 19-02		1				✓
P19-03	Electric room		1				✓
Floor 18th							
P18-01	Inside fire hose cabinet FHC 18-01		1				✓
P18-02	Inside fire hose cabinet FHC 18-02		1				✓
P18-03	Electric room		1				✓
Floor 17th							
P17-01	Inside fire hose cabinet FHC 17-01		1				✓
P17-02	Inside fire hose cabinet FHC 17-02		1				✓
P17-03	Electric room		1				✓
Floor 16th							
P16-01	Inside fire hose cabinet FHC 16-01		1				✓
P16-02	Inside fire hose cabinet FHC 16-02		1				✓
P16-03	Electric room		1				✓
Floor 15th							
P15-01	Inside fire hose cabinet FHC 15-01		1				✓
P15-02	Inside fire hose cabinet FHC 15-02		1				✓
P15-03	Electric room		1				✓
Floor 14th							
P14-01	Inside fire hose cabinet FHC 14-01		1				✓
P14-02	Inside fire hose cabinet FHC 14-02		1				✓
P14-03	Electric room		1				✓
Floor 13th (Spa)							
P13-01	Inside fire hose cabinet FHC11 M	1					✓
P13-02	Inside fire hose cabinet FHC 11-01		1				✓
P13-03	Inside fire hose cabinet FHC 11-02		1				✓
P13-04	In Front of Gains Mauntha room		1				✓
Floor 10th (Bo RT)							
P10-01	Inside fire hose cabinet FHC 10-01		1				✓
P10-02	Inside fire hose cabinet FHC 10-02		1				✓
P10-03	In Lift Control room Low zone		1				✓
P10-04	Electric room		1				✓
P10-05	In Front of Gains Pump room(Pool)		1				✓
P10-06	Water Club		1				✓
Floor 09th							
P09-01	Inside fire hose cabinet FHC 09-01		1				✓
P09-02	Inside fire hose cabinet FHC 09-02		1				✓
P09-03	In Front of behin the counter		1				✓
Floor 08th (Ballroom)							
P08-01	Inside fire hose cabinet FHC 08-01		1				✓
P08-02	Inside fire hose cabinet FHC 08-02		1				✓
P08-03	Inside fire hose cabinet FHC 08-03		1				✓
P08-04	In the Ballroom		2				✓
P08-05	In the Kitchen Bakery		1				✓
P08-06	BQ Kitchen		1	1			✓
Floor 07th (Redown/SOSHI)							
P07-01	Inside fire hose cabinet FHC 07-01		1				✓
P07-02	Inside fire hose cabinet FHC 07-02		1				✓
P07-03	Inside fire hose cabinet FHC 07-03		1				✓
P07-04	Redown reception		1				✓
P07-05	Main kitchen		1	1			✓
P07-06	Front of Social Room2		1				✓
P07-07	Japanese Kitchen		1	1			✓
P07-08	Ballroom terrace	1					✓
Floor 06th							
P06-01	Inside fire hose cabinet FHC 06-01		1				✓
P06-02	Inside fire hose cabinet FHC 06-02		1				✓
P06-03	Inside fire hose cabinet FHC 06-03		1				✓
P06-04	Laundry Room		1				✓

Code	Location	Type of Fire Extinguisher				Status	Remarks
		Dry Chemical	C-02	Wet Chemical	Fire Blanket		
Roof Top Floor							
P30-01	No Lift Control room U9 L10		1			✓	
P30-02	Inside fire hose cabinet FHC 30-01		1			✓	
P30-03	Inside fire hose cabinet FHC 30-02		1			✓	
P30-04	Fire Terrace		1			✓	
P30-05	No Lift Control room high zone		2			✓	
Floor 29th							
P29-01	Inside fire hose cabinet FHC 29-01		1			✓	
P29-02	Inside fire hose cabinet FHC 29-02		1			✓	
P29-03	Inside lift		1			✓	
P29-04	Inside lift kitchen			1	1	✓	
P29-05	Inside water pump room	1				✓	
Floor 28th							
P28-01	Inside fire hose cabinet FHC 28-01		1			✓	
P28-02	Inside fire hose cabinet FHC 28-02		1			✓	
P28-03	Electric room		1			✓	
Floor 27th							
P27-01	Inside fire hose cabinet FHC 27-01		1			✓	
P27-02	Inside fire hose cabinet FHC 27-02		1			✓	
P27-03	Electric room		1			✓	
Floor 26th							
P26-01	Inside fire hose cabinet FHC 26-01		1			✓	
P26-02	Inside fire hose cabinet FHC 26-02		1			✓	
P26-03	Electric room		1			✓	
Floor 25th(Club Signature)							
P25-01	Inside fire hose cabinet FHC 25-01		1			✓	
P25-02	Inside fire hose cabinet FHC 25-02		1			✓	
P25-03	Electric room		1			✓	
P25-04	Club Signature Kitchen		1			✓	
Floor 24th							
P24-01	Inside fire hose cabinet FHC 24-01		1			✓	
P24-02	Inside fire hose cabinet FHC 24-02		1			✓	
P24-03	Electric room		1			✓	
Floor 23rd							
P23-01	Inside fire hose cabinet FHC 23-01		1			✓	
P23-02	Inside fire hose cabinet FHC 23-02		1			✓	
P23-03	Electric room		1			✓	
Floor 22nd							
P22-01	Inside fire hose cabinet FHC 22-01		1			✓	
P22-02	Inside fire hose cabinet FHC 22-02		1			✓	
P22-03	Electric room		1			✓	
Floor 21st							
P21-01	Inside fire hose cabinet FHC 21-01		1			✓	
P21-02	Inside fire hose cabinet FHC 21-02		1			✓	
P21-03	Electric room		1			✓	
Floor 20th							
P20-01	Inside fire hose cabinet FHC 20-01		1			✓	
P20-02	Inside fire hose cabinet FHC 20-02		1			✓	

SO/ BANGKOK

Month May 2026 -Fire Extinguisher Inspection Report

Code	Location	Type of Fire Extinguisher				Status	Remarks
		Dry Chemical	Co2	Wet Chemical	Fire Blanket		
Roof Top Floor							
P30-01	In Lift Control room U9 L10		1			✓	
P30-02	Inside fire hose cabinet FHC 30-01		1			✓	
P30-03	Inside fire hose cabinet FHC 30-02		1			✓	
P30-04	1st Terrace		1			✓	
P30-05	In Lift Control room high zone		2			✓	
Floor 29th							
P29-01	Inside fire hose cabinet FHC 29-01		1			✓	
P29-02	Inside fire hose cabinet FHC 29-02		1			✓	
P29-03	Inside iris		1			✓	
P29-04	Inside iris kitchen			1	1	✓	
P29-05	Inside water pump room	1				✓	
Floor 28th							
P28-01	Inside fire hose cabinet FHC 28-01		1			✓	
P28-02	Inside fire hose cabinet FHC 28-02		1			✓	
P28-03	Electric room		1			✓	
Floor 27th							
P27-01	Inside fire hose cabinet FHC 27-01		1			✓	
P27-02	Inside fire hose cabinet FHC 27-02		1			✓	
P27-03	Electric room		1			✓	
Floor 26th							
P26-01	Inside fire hose cabinet FHC 26-01		1			✓	
P26-02	Inside fire hose cabinet FHC 26-02		1			✓	
P26-03	Electric room		1			✓	
Floor 25th(Club Signature)							
P25-01	Inside fire hose cabinet FHC 25-01		1			✓	
P25-02	Inside fire hose cabinet FHC 25-02		1			✓	
P25-03	Electric room		1			✓	
P25-04	Club Signature Kitchen		1			✓	
Floor 24th							
P24-01	Inside fire hose cabinet FHC 24-01		1			✓	
P24-02	Inside fire hose cabinet FHC 24-02		1			✓	
P24-03	Electric room		1			✓	
Floor 23rd							
P23-01	Inside fire hose cabinet FHC 23-01		1			✓	
P23-02	Inside fire hose cabinet FHC 23-02		1			✓	
P23-03	Electric room		1			✓	
Floor 22nd							
P22-01	Inside fire hose cabinet FHC 22-01		1			✓	
P22-02	Inside fire hose cabinet FHC 22-02		1			✓	
P22-03	Electric room		1			✓	
Floor 21st							
P21-01	Inside fire hose cabinet FHC 21-01		1			✓	
P21-02	Inside fire hose cabinet FHC 21-02		1			✓	
P21-03	Electric room		1			✓	
Floor 20th							
P20-01	Inside fire hose cabinet FHC 20-01		1			✓	
P20-02	Inside fire hose cabinet FHC 20-02		1			✓	

P06-05	In Front of Server room				1		✓
P06-06	Generator room				1		✓
P06-07	MOO room						✓
P06-08	Chiller room				1		✓
P06-09	Transformer room				1		✓
Floor 05th (Car park)							
P05-01	Inside fire hose cabinet FHC 05-01				1		✓
P05-02	Inside fire hose cabinet FHC 05-02				1		✓
P05-03	Inside fire hose cabinet FHC 05-03				1		✓
P05-04	Additional extinguishers			3			✓
Floor 04th (Car park)							
P04-01	Inside fire hose cabinet FHC 04-01				1		✓
P04-02	Inside fire hose cabinet FHC 04-02				1		✓
P04-03	Inside fire hose cabinet FHC 04-03				1		✓
P04-04	Additional extinguishers			3			✓
Floor 03rd (Car park)							
P03-01	Inside fire hose cabinet FHC 03-01				1		✓
P03-02	Inside fire hose cabinet FHC 03-02				1		✓
P03-03	Inside fire hose cabinet FHC 03-03				1		✓
P03-04	Additional extinguishers			3			✓
Floor 02nd (Car park)							
P02-01	Inside fire hose cabinet FHC 02-01				1		✓
P02-02	Inside fire hose cabinet FHC 02-02				1		✓
P02-03	Inside fire hose cabinet FHC 02-03				1		✓
P02-04	Additional extinguishers			2			✓
Floor 6							
G001-01	Inside fire hose cabinet FHC G-01				1		✓
G001-02	Inside fire hose cabinet FHC G-02				1		✓
G001-03	In Front of IOP				1		✓
G001-04	Beside Gonggong				1		✓
G001-05	In Front of store PA				1		✓
G001-06	GAS Room				1		✓
G001-07	In Fire cart				5	1	3
Basement 01							
B01-01	Inside fire hose cabinet FHC B1-01				1		✓
B01-02	Inside fire hose cabinet FHC B1-02				1		✓
B01-03	Inside fire hose cabinet FHC B1-03				1		✓
B01-04	Inside fire hose cabinet FHC B1-04				1		✓
B01-05	In Front of SO Safe room				1		✓
B01-06	Canteen kitchen					1	✓
Basement 02							
B02-01	Inside fire hose cabinet FHC B2-01				1		✓
Total					21	117	5
Grand Total					149		

Dry Chemical	Total = 21 kA
Co2	Total = 117 kA
Wet Chemical	Total = 5 kA
Fire Blanket	Total = 6 kA
Damage	0

Checked By:  Security Officer / Supervisor

Acknowledged By:  Security Manager / Asst. Security Manager

P06-05	In Front of Server room			1			✓
P06-06	Generator room			1			✓
P06-07	MOD room			1			✓
P06-08	Chiller room			1			✓
P06-09	Transformer room			1			✓
Floor 05th (Car park)							
P05-01	Inside fire hose cabinet FHC-05-01			1			✓
P05-02	Inside fire hose cabinet FHC-05-02			1			✓
P05-03	Inside fire hose cabinet FHC-05-03			1			✓
P05-04	Additional extinguishers		3				✓
Floor 04th (Car park)							
P04-01	Inside fire hose cabinet FHC-04-01			1			✓
P04-02	Inside fire hose cabinet FHC-04-02			1			✓
P04-03	Inside fire hose cabinet FHC-04-03			1			✓
P04-04	Additional extinguishers		3				✓
Floor 03rd (Car park)							
P03-01	Inside fire hose cabinet FHC-03-01			1			✓
P03-02	Inside fire hose cabinet FHC-03-02			1			✓
P03-03	Inside fire hose cabinet FHC-03-03			1			✓
P03-04	Additional extinguishers		3				✓
Floor 02nd (Car park)							
P02-01	Inside fire hose cabinet FHC-02-01			1			✓
P02-02	Inside fire hose cabinet FHC-02-02			1			✓
P02-03	Inside fire hose cabinet FHC-02-03			1			✓
P02-04	Additional extinguishers		2				✓
Floor 0							
G00-01	Inside fire hose cabinet FHC-G-01			1			✓
G00-02	Inside fire hose cabinet FHC-G-02			1			✓
G00-03	In Front of ROF			1			✓
G00-04	Beside Congeorge			1			✓
G00-05	In Front of Store PA		1				✓
G00-06	Gas Room			1			✓
G00-07	In Fire cart		5	1	3		✓
Basement 01							
B01-01	Inside fire hose cabinet FHC-B1-01			1			✓
B01-02	Inside fire hose cabinet FHC-B1-02			1			✓
B01-03	Inside fire hose cabinet FHC-B1-03			1			✓
B01-04	Inside fire hose cabinet FHC-B1-04			1			✓
B01-05	In Front of SO Safe room			1			✓
B01-06	Canteen Kitchen			1			✓
Basement 02							
B02-01	Inside fire hose cabinet FHC-B2-01		1				✓
Total				21	117	5	6
Grand Total				149			

Dry Chemical	Total = 2116
Co-2	Total = 117
Wet Chemical	Total = 5
Fire Blanket	Total = 6
Damage	0

Checked By:
Security Officer / Supervisor

Acknowledged By:
Security Manager / Asst. Security Manager

P20-03	Electric room			1			✓
Floor 19th							
P19-01	Inside fire hose cabinet FHC-19-01			1			✓
P19-02	Inside fire hose cabinet FHC-19-02			1			✓
P19-03	Electric room			1			✓
Floor 18th							
P18-01	Inside fire hose cabinet FHC-18-01			1			✓
P18-02	Inside fire hose cabinet FHC-18-02			1			✓
P18-03	Electric room			1			✓
Floor 17th							
P17-01	Inside fire hose cabinet FHC-17-01			1			✓
P17-02	Inside fire hose cabinet FHC-17-02			1			✓
P17-03	Electric room			1			✓
Floor 16th							
P16-01	Inside fire hose cabinet FHC-16-01			1			✓
P16-02	Inside fire hose cabinet FHC-16-02			1			✓
P16-03	Electric room			1			✓
Floor 15th							
P15-01	Inside fire hose cabinet FHC-15-01			1			✓
P15-02	Inside fire hose cabinet FHC-15-02			1			✓
P15-03	Electric room			1			✓
Floor 14th							
P14-01	Inside fire hose cabinet FHC-14-01			1			✓
P14-02	Inside fire hose cabinet FHC-14-02			1			✓
P14-03	Electric room			1			✓
Floor 11st (Spa)							
P11-01	Inside fire hose cabinet FHC11-M		1				✓
P11-02	Inside fire hose cabinet FHC-11-01			1			✓
P11-03	Inside fire hose cabinet FHC11-02			1			✓
P11-04	In Front of Gamm Muntha room			1			✓
Floor 10th (Go RT)							
P10-01	Inside fire hose cabinet FHC-10-01			1			✓
P10-02	Inside fire hose cabinet FHC-10-02			1			✓
P10-03	In Lift Control room Low zone			1			✓
P10-04	Electric room			1			✓
P10-05	In Front of Gamm Pump room(Pool)			1			✓
P10-06	Water Club			1			✓
Floor 09th							
P09-01	Inside fire hose cabinet FHC-09-01			1			✓
P09-02	Inside fire hose cabinet FHC-09-02			1			✓
P09-03	In Front of behind the counter			1			✓
Floor 08th (Ballroom)							
P08-01	Inside fire hose cabinet FHC-08-01			1			✓
P08-02	Inside fire hose cabinet FHC-08-02			1			✓
P08-03	Inside fire hose cabinet FHC-08-03			1			✓
P08-04	In the Ballroom			2			✓
P08-05	In the Kitchen Bakery			1			✓
P08-06	BQ Kitchen			1	1		✓
Floor 07th (Redoven/SOS-H)							
P07-01	Inside fire hose cabinet FHC-07-01			1			✓
P07-02	Inside fire hose cabinet FHC-07-02			1			✓
P07-03	Inside fire hose cabinet FHC-07-03			1			✓
P07-04	Redoven Reception			1			✓
P07-05	Main Kitchen			1	1		✓
P07-06	Front of Social Room2			1			✓
P07-07	Japanese Kitchen			1	1		✓
P07-08	Redoven terrace		1				✓
Floor 06th							
P06-01	Inside fire hose cabinet FHC-06-01			1			✓
P06-02	Inside fire hose cabinet FHC-06-02			1			✓
P06-03	Inside fire hose cabinet FHC-06-03			1			✓
P06-04	Laundry Room			1			✓

P20-03	Electric room			1				✓	
Floor 19th									
F19-01	Inside fire hose cabinet FHC 19-01			1				✓	
F19-02	Inside fire hose cabinet FHC 19-02			1				✓	
F19-03	Electric room			1				✓	
Floor 18th									
F18-01	Inside fire hose cabinet FHC 18-01			1				✓	
F18-02	Inside fire hose cabinet FHC 18-02			1				✓	
F18-03	Electric room			1				✓	
Floor 17th									
F17-01	Inside fire hose cabinet FHC 17-01			1				✓	
F17-02	Inside fire hose cabinet FHC 17-02			1				✓	
F17-03	Electric room			1				✓	
Floor 16th									
F16-01	Inside fire hose cabinet FHC 16-01			1				✓	
F16-02	Inside fire hose cabinet FHC 16-02			1				✓	
F16-03	Electric room			1				✓	
Floor 15th									
F15-01	Inside fire hose cabinet FHC 15-01			1				✓	
F15-02	Inside fire hose cabinet FHC 15-02			1				✓	
F15-03	Electric room			1				✓	
Floor 14th									
F14-01	Inside fire hose cabinet FHC 14-01			1				✓	
F14-02	Inside fire hose cabinet FHC 14-02			1				✓	
F14-03	Electric room			1				✓	
Floor 11st (Spa)									
F11-01	Inside fire hose cabinet FHC11-01	1						✓	
F11-02	Inside fire hose cabinet FHC 11-01			1				✓	
F11-03	Inside fire hose cabinet FHC 11-02			1				✓	
F11-04	In Front of Gam Muntha room			1				✓	
Floor 10th (5o RT)									
F10-01	Inside fire hose cabinet FHC 10-01			1				✓	
F10-02	Inside fire hose cabinet FHC 10-02			1				✓	
F10-03	In Lift Control room Low zone							✓	
F10-04	Electric room							✓	
F10-05	In Front of Gam Pump room(Pool)			1				✓	
F10-06	Water Club			1				✓	
Floor 09th									
F09-01	Inside fire hose cabinet FHC 09-01			1				✓	
F09-02	Inside fire hose cabinet FHC 09-02			1				✓	
F09-03	In Front of behin the counter			1				✓	
Floor 08th (Ballroom)									
F08-01	Inside fire hose cabinet FHC 08-01			1				✓	
F08-02	Inside fire hose cabinet FHC 08-02			1				✓	
F08-03	Inside fire hose cabinet FHC 08-03			1				✓	
F08-04	In the Ballroom			2				✓	
F08-05	In the Kitchen Bakery			1				✓	
F08-06	BQ Kitchen				1	1		✓	
Floor 07th (Redoven/505H)									
F07-01	Inside fire hose cabinet FHC 07-01			1				✓	
F07-02	Inside fire hose cabinet FHC 07-02			1				✓	
F07-03	Inside fire hose cabinet FHC 07-03			1				✓	
F07-04	Redoven Reception			1				✓	
F07-05	Main Kitchen			1				✓	
F07-06	Front of Social Room2			1				✓	
F07-07	Japanese Kitchen			1		1		✓	
F07-08	Redoven terrace				1			✓	
Floor 06th									
F06-01	Inside fire cabinet FHC 06-01			1				✓	
F06-02	Inside fire hose cabinet FHC 06-02			1				✓	
F06-03	Inside fire hose cabinet FHC 06-03			1				✓	
F06-04	Laundry Room			1				✓	

SO/ BANGKOK

Month April 2026 :Fire Extinguisher Inspection Report

Code	Location	Type of Fire Extinguisher				Status	Remarks
		Dry Chemical					
		CO2	Wet Chemical	Fire Blanket	Good		
Roof Top Floor							
F30-01	In Lift Control room L9-L10		1			✓	
F30-02	Inside fire hose cabinet FHC 30-01		1			✓	
F30-03	Inside fire hose cabinet FHC 30-02					✓	
F30-04	Infra Terrace		1			✓	
F30-05	In Lift Control room high zone		2			✓	
Floor 29th							
F29-01	Inside fire hose cabinet FHC 29-01		1			✓	
F29-02	Inside fire hose cabinet FHC 29-02		1			✓	
F29-03	Inside Iris		1			✓	
F29-04	Inside Iris Kitchen			1	1	✓	
F29-05	Inside water pump room	1				✓	
Floor 28th							
F28-01	Inside fire hose cabinet FHC 28-01		1			✓	
F28-02	Inside fire hose cabinet FHC 28-02		1			✓	
F28-03	Electric room		1			✓	
Floor 27th							
F27-01	Inside fire hose cabinet FHC 27-01		1			✓	
F27-02	Inside fire hose cabinet FHC 27-02		1			✓	
F27-03	Electric room		1			✓	
Floor 26th							
F26-01	Inside fire hose cabinet FHC 26-01		1			✓	
F26-02	Inside fire hose cabinet FHC 26-02		1			✓	
F26-03	Electric room		1			✓	
Floor 25th(Club Signature)							
F25-01	Inside fire hose cabinet FHC 25-01		1			✓	
F25-02	Inside fire hose cabinet FHC 25-02		1			✓	
F25-03	Electric room		1			✓	
F25-04	Club Signature Kitchen		1			✓	
Floor 24th							
F24-01	Inside fire hose cabinet FHC 24-01		1			✓	
F24-02	Inside fire hose cabinet FHC 24-02		1			✓	
F24-03	Electric room		1			✓	
Floor 23rd							
F23-01	Inside fire hose cabinet FHC 23-01		1			✓	
F23-02	Inside fire hose cabinet FHC 23-02		1			✓	
F23-03	Electric room		1			✓	
Floor 22nd							
F22-01	Inside fire hose cabinet FHC 22-01		1			✓	
F22-02	Inside fire hose cabinet FHC 22-02		1			✓	
F22-03	Electric room		1			✓	
Floor 21st							
F21-01	Inside fire hose cabinet FHC 21-01		1			✓	
F21-02	Inside fire hose cabinet FHC 21-02		1			✓	
F21-03	Electric room		1			✓	
Floor 20th							
F20-01	Inside fire hose cabinet FHC 20-01		1			✓	
F20-02	Inside fire hose cabinet FHC 20-02		1			✓	

SO/ BANGKOK

Month March 2026 :Fire Extinguisher Inspection Report

Code	Location	Type of Fire Extinguisher				Status	Remarks
		Dry Chemical	Co2	Wet Chemical	Fire Blanket		
Roof Top Floor							
F30-01	In Lift Control room U9 L10		1			✓	
F30-02	Inside fire hose cabinet FHC 30-01		1			✓	
F30-03	Inside fire hose cabinet FHC 30-02		1			✓	
F30-04	1st Terrace		1			✓	
F30-05	In Lift Control room high zone		2			✓	
Floor 29th							
F29-01	Inside fire hose cabinet FHC 29-01		1			✓	
F29-02	Inside fire hose cabinet FHC 29-02		1			✓	
F29-03	Inside iris		1			✓	
F29-04	Inside iris kitchen			1	1	✓	
F29-05	Inside water pump room	1				✓	
Floor 28th							
F28-01	Inside fire hose cabinet FHC 28-01		1			✓	
F28-02	Inside fire hose cabinet FHC 28-02		1			✓	
F28-03	Electric room		1			✓	
Floor 27th							
F27-01	Inside fire hose cabinet FHC 27-01		1			✓	
F27-02	Inside fire hose cabinet FHC 27-02		1			✓	
F27-03	Electric room		1			✓	
Floor 26th							
F26-01	Inside fire hose cabinet FHC 26-01		1			✓	
F26-02	Inside fire hose cabinet FHC 26-02		1			✓	
F26-03	Electric room		1			✓	
Floor 25th(Club Signature)							
F25-01	Inside fire hose cabinet FHC 25-01		1			✓	
F25-02	Inside fire hose cabinet FHC 25-02		1			✓	
F25-03	Electric room		1			✓	
F25-04	Club Signature Kitchen		1			✓	
Floor 24th							
F24-01	Inside fire hose cabinet FHC 24-01		1			✓	
F24-02	Inside fire hose cabinet FHC 24-02		1			✓	
F24-03	Electric room		1			✓	
Floor 23rd							
F23-01	Inside fire hose cabinet FHC 23-01		1			✓	
F23-02	Inside fire hose cabinet FHC 23-02		1			✓	
F23-03	Electric room		1			✓	
Floor 22nd							
F22-01	Inside fire hose cabinet FHC 22-01		1			✓	
F22-02	Inside fire hose cabinet FHC 22-02		1			✓	
F22-03	Electric room		1			✓	
Floor 21st							
F21-01	Inside fire hose cabinet FHC 21-01		1			✓	
F21-02	Inside fire hose cabinet FHC 21-02		1			✓	
F21-03	Electric room		1			✓	
Floor 20th							
F20-01	Inside fire hose cabinet FHC 20-01		1			✓	
F20-02	Inside fire hose cabinet FHC 20-02		1			✓	

F06-05	In Front of Server room			1			✓
F06-06	Generatr room			1			✓
F06-07	MOD room			1			✓
F06-08	Chiller room			1			✓
F06-09	Transformer room			1			✓
Floor 05th (Car park)							
F05-01	Inside fire hose cabinet FHC 05-01			1			✓
F05-02	Inside fire hose cabinet FHC 05-02			1			✓
F05-03	Inside fire hose cabinet FHC 05-03			1			✓
F05-04	Additional extinguishers			3			✓
Floor 04th (Car park)							
F04-01	Inside fire hose cabinet FHC 04-01			1			✓
F04-02	Inside fire hose cabinet FHC 04-02			1			✓
F04-03	Inside fire hose cabinet FHC 04-03			1			✓
F04-04	Additional extinguishers			3			✓
Floor 03rd (Car park)							
F03-01	Inside fire hose cabinet FHC 03-01			1			✓
F03-02	Inside fire hose cabinet FHC 03-02			1			✓
F03-03	Inside fire hose cabinet FHC 03-03			1			✓
F03-04	Additional extinguishers			3			✓
Floor 02nd (Car park)							
F02-01	Inside fire hose cabinet FHC 02-01			1			✓
F02-02	Inside fire hose cabinet FHC 02-02			1			✓
F02-03	Inside fire hose cabinet FHC 02-03			1			✓
F02-04	Additional extinguishers			2			✓
Floor 0							
G01-01	Inside fire hose cabinet FHC G-01			1			✓
G01-02	Inside fire hose cabinet FHC G-02			1			✓
G01-03	In Front of POF			1			✓
G01-04	Beside Congeorge			1			✓
G01-05	In Front of Store PA			1			✓
G01-06	Gas Room			1			✓
G01-07	In Fire cart			5	1	3	✓
Basement 01							
B01-01	Inside fire hose cabinet FHC B1-01			1			✓
B01-02	Inside fire hose cabinet FHC B1-02			1			✓
B01-03	Inside fire hose cabinet FHC B1-03			1			✓
B01-04	Inside fire hose cabinet FHC B1-04			1			✓
B01-05	In Front of SO Safe room			1			✓
B01-06	Canteen Kitchen			1			✓
Basement 02							
B02-01	Inside fire hose cabinet FHC B2-01			1			✓
Total				21	117	5	Grand Total 149
Total = 21 f/s							
Dry Chemical				Total = 117 f/s			
Co2				Total = 5 f/s			
Wet Chemical				Total = 6 f/s			
Fire Blanket				Total = 6 f/s			
Damage				0			

Checked By:.....

Security Officer / Supervisor

Acknowledged By:.....

Security Manager/Asst. Security Manager

P06-05	In Front of Server room			1			✓
P06-06	Generator room			1			✓
P06-07	MOU room			1			✓
P06-08	Chiller room			1			✓
P06-09	Transformer room			1			✓
Floor 05th (Car park)							
P05-01	Inside fire hose cabinet FHC-05-01		1				✓
P05-02	Inside fire hose cabinet FHC-05-02		1				✓
P05-03	Inside fire hose cabinet FHC-05-03		1				✓
P05-04	Additional extinguishers		3				✓
Floor 04th (Car park)							
P04-01	Inside fire hose cabinet FHC-04-01		1				✓
P04-02	Inside fire hose cabinet FHC-04-02		1				✓
P04-03	Inside fire hose cabinet FHC-04-03		1				✓
P04-04	Additional extinguishers		3				✓
Floor 03rd (Car park)							
P03-01	Inside fire hose cabinet FHC-03-01		1				✓
P03-02	Inside fire hose cabinet FHC-03-02		1				✓
P03-03	Inside fire hose cabinet FHC-03-03		1				✓
P03-04	Additional extinguishers		3				✓
Floor 02nd (Car park)							
P02-01	Inside fire hose cabinet FHC-02-01		1				✓
P02-02	Inside fire hose cabinet FHC-02-02		1				✓
P02-03	Inside fire hose cabinet FHC-02-03		1				✓
P02-04	Additional extinguishers		2				✓
Floor 0							
G00-01	Inside fire hose cabinet FHC-G-01		1				✓
G00-02	Inside fire hose cabinet FHC-G-02		1				✓
G00-03	In Front of ROF			1			✓
G00-04	Beside Congeorge			1			✓
G00-05	In Front of Store PA		1				✓
G00-06	Gas Room		1				✓
G00-07	In Fire cart		5	1	3		✓
Basement 01							
B01-01	Inside fire hose cabinet FHC-B1-01		1				✓
B01-02	Inside fire hose cabinet FHC-B1-02		1				✓
B01-03	Inside fire hose cabinet FHC-B1-03		1				✓
B01-04	Inside fire hose cabinet FHC-B1-04		1				✓
B01-05	In Front of SO Safe room			1			✓
B01-06	Canteen Kitchen				1		✓
Basement 02							
B02-01	Inside fire hose cabinet FHC-B2-01		1				✓
Total			43	104	5	6	Grand Total 158

Dry Chemical	Total = 43 f/s
Co-2	Total = 104 f/s
Wet Chemical	Total = 5 f/s
Fire Blanket	Total = 6 f/s
Damage	0

Checked By:
Security Officer / Supervisor

Acknowledged By:
Security Manager / Asst. Security Manager

P20-03	Electric room			1			✓
Floor 19th							
P19-01	Inside fire hose cabinet FHC-19-01		1				✓
P19-02	Inside fire hose cabinet FHC-19-02		1				✓
P19-03	Electric room		1				✓
Floor 18th							
P18-01	Inside fire hose cabinet FHC-18-01		1				✓
P18-02	Inside fire hose cabinet FHC-18-02		1				✓
P18-03	Electric room		1				✓
Floor 17th							
P17-01	Inside fire hose cabinet FHC-17-01		1				✓
P17-02	Inside fire hose cabinet FHC-17-02		1				✓
P17-03	Electric room		1				✓
Floor 16th							
P16-01	Inside fire hose cabinet FHC-16-01		1				✓
P16-02	Inside fire hose cabinet FHC-16-02		1				✓
P16-03	Electric room		1				✓
Floor 15th							
P15-01	Inside fire hose cabinet FHC-15-01		1				✓
P15-02	Inside fire hose cabinet FHC-15-02		1				✓
P15-03	Electric room		1				✓
Floor 14th							
P14-01	Inside fire hose cabinet FHC-14-01		1				✓
P14-02	Inside fire hose cabinet FHC-14-02		1				✓
P14-03	Electric room		1				✓
Floor 11st (Spa)							
P11-01	Inside fire hose cabinet FHC11-M	1					✓
P11-02	Inside fire hose cabinet FHC-11-01		1				✓
P11-03	Inside fire hose cabinet FHC11-02		1				✓
P11-04	In Front of Gamm Muntha room		1				✓
Floor 10th (6o RT)							
P10-01	Inside fire hose cabinet FHC-10-01		1				✓
P10-02	Inside fire hose cabinet FHC-10-02		1				✓
P10-03	In Lift Control room Low zone		1				✓
P10-04	Electric room		1				✓
P10-05	In Front of Gamm Pump room(Pool)		1				✓
P10-06	Water Club		1				✓
Floor 09th							
P09-01	Inside fire hose cabinet FHC-09-01		1				✓
P09-02	Inside fire hose cabinet FHC-09-02		1				✓
P09-03	In Front of behind the counter		1				✓
Floor 08th (Ballroom)							
P08-01	Inside fire hose cabinet FHC-08-01		1				✓
P08-02	Inside fire hose cabinet FHC-08-02		1				✓
P08-03	Inside fire hose cabinet FHC-08-03		1				✓
P08-04	In the Ballroom		2				✓
P08-05	In the Kitchen Bakery		1				✓
P08-06	BQ Kitchen			1	1		✓
Floor 07th (Redoven/SOS-H)							
P07-01	Inside fire hose cabinet FHC-07-01		1				✓
P07-02	Inside fire hose cabinet FHC-07-02		1				✓
P07-03	Inside fire hose cabinet FHC-07-03		1				✓
P07-04	Redoven Reception		1				✓
P07-05	Main Kitchen		1	1			✓
P07-06	Front of Social Room2		1				✓
P07-07	Japanese Kitchen		1	1	1		✓
P07-08	Redoven terrace	1					✓
Floor 06th							
P06-01	Inside fire hose cabinet FHC-06-01	1					✓
P06-02	Inside fire hose cabinet FHC-06-02	1					✓
P06-03	Inside fire hose cabinet FHC-06-03	1					✓
P06-04	Laundry Room	1	1				✓

P20-03	Electric room			1				✓	
Floor 19th									
F19-01	Inside fire hose cabinet FHC 19-01			1				✓	
F19-02	Inside fire hose cabinet FHC 19-02			1				✓	
F19-03	Electric room			1				✓	
Floor 18th									
F18-01	Inside fire hose cabinet FHC 18-01			1				✓	
F18-02	Inside fire hose cabinet FHC 18-02			1				✓	
F18-03	Electric room			1				✓	
Floor 17th									
F17-01	Inside fire hose cabinet FHC 17-01			1				✓	
F17-02	Inside fire hose cabinet FHC 17-02			1				✓	
F17-03	Electric room			1				✓	
Floor 16th									
F16-01	Inside fire hose cabinet FHC 16-01			1				✓	
F16-02	Inside fire hose cabinet FHC 16-02			1				✓	
F16-03	Electric room			1				✓	
Floor 15th									
F15-01	Inside fire hose cabinet FHC 15-01			1				✓	
F15-02	Inside fire hose cabinet FHC 15-02			1				✓	
F15-03	Electric room			1				✓	
Floor 14th									
F14-01	Inside fire hose cabinet FHC 14-01			1				✓	
F14-02	Inside fire hose cabinet FHC 14-02			1				✓	
F14-03	Electric room			1				✓	
Floor 11st (Spa)									
F11-01	Inside fire hose cabinet FHC11-01		1					✓	
F11-02	Inside fire hose cabinet FHC 11-01			1				✓	
F11-03	Inside fire hose cabinet FHC 11-02			1				✓	
F11-04	In Front of Gam Muntha room			1				✓	
Floor 10th (5o RT)									
F10-01	Inside fire hose cabinet FHC 10-01			1				✓	
F10-02	Inside fire hose cabinet FHC 10-02			1				✓	
F10-03	In Lift Control room Low zone			1				✓	
F10-04	Electric room							✓	
F10-05	In Front of Gam Pump room(Pool)			1				✓	
F10-06	Water Club			1				✓	
Floor 09th									
F09-01	Inside fire hose cabinet FHC 09-01			1				✓	
F09-02	Inside fire hose cabinet FHC 09-02			1				✓	
F09-03	In Front of behin the counter			1				✓	
Floor 08th (Ballroom)									
F08-01	Inside fire hose cabinet FHC 08-01			1				✓	
F08-02	Inside fire hose cabinet FHC 08-02			1				✓	
F08-03	Inside fire hose cabinet FHC 08-03			1				✓	
F08-04	In the Ballroom			2				✓	
F08-05	In the Kitchen Bakery			1				✓	
F08-06	BQ Kitchen				1	1		✓	
Floor 07th (Redoven/505H)									
F07-01	Inside fire hose cabinet FHC 07-01			1				✓	
F07-02	Inside fire hose cabinet FHC 07-02			1				✓	
F07-03	Inside fire hose cabinet FHC 07-03			1				✓	
F07-04	Redoven Reception			1				✓	
F07-05	Main Kitchen			1		1		✓	
F07-06	Front of Social Room2			1				✓	
F07-07	Japanese Kitchen			1		1	1	✓	
F07-08	Redoven terrace				1			✓	
Floor 06th									
F06-01	Inside fire cabinet FHC 06-01		1					✓	
F06-02	Inside fire hose cabinet FHC 06-02		1					✓	
F06-03	Inside fire hose cabinet FHC 06-03		1					✓	
F06-04	Laundry Room			1				✓	

SO/ BANGKOK

Month February 2026 :Fire Extinguisher Inspection Report

Code	Location	Type of Fire Extinguisher				Status	Remarks
		Dry Chemical		Wet Chemical			
		CO2	Fire Blanket				
Roof Top Floor							
F30-01	In Lift Control room L9-L10	1				✓	
F30-02	Inside fire hose cabinet FHC 30-01	1				✓	
F30-03	Inside fire hose cabinet FHC 30-02					✓	
F30-04	In1s Terrace	1				✓	
F30-05	In Lift Control room high zone	2				✓	
Floor 29th							
F29-01	Inside fire hose cabinet FHC 29-01	1				✓	
F29-02	Inside fire hose cabinet FHC 29-02	1				✓	
F29-03	Inside Iris	1				✓	
F29-04	Inside Iris Kitchen		1	1		✓	
F29-03	Inside water pump room	1				✓	
Floor 28th							
F28-01	Inside fire hose cabinet FHC 28-01	1				✓	
F28-02	Inside fire hose cabinet FHC 28-02	1				✓	
F28-03	Electric room	1				✓	
Floor 27th							
F27-01	Inside fire hose cabinet FHC 27-01	1				✓	
F27-02	Inside fire hose cabinet FHC 27-02	1				✓	
F27-03	Electric room	1				✓	
Floor 26th							
F26-01	Inside fire hose cabinet FHC 26-01	1				✓	
F26-02	Inside fire hose cabinet FHC 26-02	1				✓	
F26-03	Electric room	1				✓	
Floor 25th(Club Signature)							
F25-01	Inside fire hose cabinet FHC 25-01	1				✓	
F25-02	Inside fire hose cabinet FHC 25-02	1				✓	
F25-03	Electric room	1				✓	
F25-04	Club Signature Kitchen	1				✓	
Floor 24th							
F24-01	Inside fire hose cabinet FHC 24-01	1				✓	
F24-02	Inside fire hose cabinet FHC 24-02	1				✓	
F24-03	Electric room	1				✓	
Floor 23rd							
F23-01	Inside fire hose cabinet FHC 23-01	1				✓	
F23-02	Inside fire hose cabinet FHC 23-02	1				✓	
F23-03	Electric room	1				✓	
Floor 22nd							
F22-01	Inside fire hose cabinet FHC 22-01	1				✓	
F22-02	Inside fire hose cabinet FHC 22-02	1				✓	
F22-03	Electric room	1				✓	
Floor 21st							
F21-01	Inside fire hose cabinet FHC 21-01	1				✓	
F21-02	Inside fire hose cabinet FHC 21-02	1				✓	
F21-03	Electric room	1				✓	
Floor 20th							
F20-01	Inside fire hose cabinet FHC 20-01	1				✓	
F20-02	Inside fire hose cabinet FHC 20-02	1				✓	

SO/ BANGKOK

Month January 2026 :Fire Extinguisher Inspection Report

Code	Location	Type of Fire Extinguisher				Status	Remarks
		Dry Chemical	Co2	Wet Chemical	Fire Blanket		
Roof Top Floor							
F30-01	In Lift Control room U9 L10		1			✓	
F30-02	Inside fire hose cabinet FHC 30-01		1			✓	
F30-03	Inside fire hose cabinet FHC 30-02					✓	
F30-04	1st Terrace		1			✓	
F30-05	In Lift Control room high zone		2			✓	
Floor 29th							
F29-01	Inside fire hose cabinet FHC 29-01		1			✓	
F29-02	Inside fire hose cabinet FHC 29-02		1			✓	
F29-03	Inside Iris		1			✓	
F29-04	Inside Iris Kitchen			1	1	✓	
F29-05	Inside water pump room	1				✓	
Floor 28th							
F28-01	Inside fire hose cabinet FHC 28-01		1			✓	
F28-02	Inside fire hose cabinet FHC 28-02		1			✓	
F28-03	Electric room		1			✓	
Floor 27th							
F27-01	Inside fire hose cabinet FHC 27-01		1			✓	
F27-02	Inside fire hose cabinet FHC 27-02		1			✓	
F27-03	Electric room		1			✓	
Floor 26th							
F26-01	Inside fire hose cabinet FHC 26-01		1			✓	
F26-02	Inside fire hose cabinet FHC 26-02		1			✓	
F26-03	Electric room		1			✓	
Floor 25th(Club Signature)							
F25-01	Inside fire hose cabinet FHC 25-01		1			✓	
F25-02	Inside fire hose cabinet FHC 25-02		1			✓	
F25-03	Electric room		1			✓	
F25-04	Club Signature Kitchen		1			✓	
Floor 24th							
F24-01	Inside fire hose cabinet FHC 24-01		1			✓	
F24-02	Inside fire hose cabinet FHC 24-02		1			✓	
F24-03	Electric room		1			✓	
Floor 23rd							
F23-01	Inside fire hose cabinet FHC 23-01		1			✓	
F23-02	Inside fire hose cabinet FHC 23-02		1			✓	
F23-03	Electric room		1			✓	
Floor 22nd							
F22-01	Inside fire hose cabinet FHC 22-01		1			✓	
F22-02	Inside fire hose cabinet FHC 22-02		1			✓	
F22-03	Electric room		1			✓	
Floor 21st							
F21-01	Inside fire hose cabinet FHC 21-01		1			✓	
F21-02	Inside fire hose cabinet FHC 21-02		1			✓	
F21-03	Electric room		1			✓	
Floor 20th							
F20-01	Inside fire hose cabinet FHC 20-01		1			✓	
F20-02	Inside fire hose cabinet FHC 20-02		1			✓	

F06-05	In Front of Server room			1			✓
F06-06	Generatr room			1			✓
F06-07	MOD room			1			✓
F06-08	Chiller room			1			✓
F06-09	Transformer room			1			✓
Floor 05th (Car park)							
F05-01	Inside fire hose cabinet FHC 05-01		1				✓
F05-02	Inside fire hose cabinet FHC 05-02		1				✓
F05-03	Inside fire hose cabinet FHC 05-03		1				✓
F05-04	Additional extinguishers		3				✓
Floor 04th (Car park)							
F04-01	Inside fire hose cabinet FHC 04-01		1				✓
F04-02	Inside fire hose cabinet FHC 04-02		1				✓
F04-03	Inside fire hose cabinet FHC 04-03		1				✓
F04-04	Additional extinguishers		3				✓
Floor 03rd (Car park)							
F03-01	Inside fire hose cabinet FHC 03-01		1				✓
F03-02	Inside fire hose cabinet FHC 03-02		1				✓
F03-03	Inside fire hose cabinet FHC 03-03		1				✓
F03-04	Additional extinguishers		3				✓
Floor 02nd (Car park)							
F02-01	Inside fire hose cabinet FHC 02-01		1				✓
F02-02	Inside fire hose cabinet FHC 02-02		1				✓
F02-03	Inside fire hose cabinet FHC 02-03		1				✓
F02-04	Additional extinguishers		2				✓
Floor 0							
G01-01	Inside fire hose cabinet FHC G-01		1				✓
G01-02	Inside fire hose cabinet FHC G-02		1				✓
G01-03	In Front of POF		1				✓
G01-04	Beside Congeorge		1				✓
G01-05	In Front of Store PA		1				✓
G01-06	Gas Room		1				✓
G01-07	In Fire cart		5	1	3		✓
Basement 01							
B01-01	Inside fire hose cabinet FHC B1-01		1				✓
B01-02	Inside fire hose cabinet FHC B1-02		1				✓
B01-03	Inside fire hose cabinet FHC B1-03		1				✓
B01-04	Inside fire hose cabinet FHC B1-04		1				✓
B01-05	In Front of SO Safe room		1				✓
B01-06	Canteen Kitchen			1			✓
Basement 02							
B02-01	Inside fire hose cabinet FHC B2-01		1				✓
Total				43	104	5	Grand Total 158

Dry Chemical	Total = 43 f/s
Co2	Total = 104 f/s
Wet Chemical	Total = 5 f/s
Fire Blanket	Total = 6 f/s
Damage	0

Checked By:
Security Officer / Supervisor

Acknowledged By:
Security Manager/Asst. Security Manager

P06-05	In Front of Server room			1			✓
P06-06	Generator room			1			✓
P06-07	MOU room			1			✓
P06-08	Chiller room			1			✓
P06-09	Transformer room			1			✓
Floor 05th (Car park)							
P05-01	Inside fire hose cabinet FHC-05-01		1				✓
P05-02	Inside fire hose cabinet FHC-05-02		1				✓
P05-03	Inside fire hose cabinet FHC-05-03		1				✓
P05-04	Additional extinguishers		3				✓
Floor 04th (Car park)							
P04-01	Inside fire hose cabinet FHC-04-01		1				✓
P04-02	Inside fire hose cabinet FHC-04-02		1				✓
P04-03	Inside fire hose cabinet FHC-04-03		1				✓
P04-04	Additional extinguishers		3				✓
Floor 03rd (Car park)							
P03-01	Inside fire hose cabinet FHC-03-01		1				✓
P03-02	Inside fire hose cabinet FHC-03-02		1				✓
P03-03	Inside fire hose cabinet FHC-03-03		1				✓
P03-04	Additional extinguishers		3				✓
Floor 02nd (Car park)							
P02-01	Inside fire hose cabinet FHC-02-01		1				✓
P02-02	Inside fire hose cabinet FHC-02-02		1				✓
P02-03	Inside fire hose cabinet FHC-02-03		1				✓
P02-04	Additional extinguishers		2				✓
Floor 0							
G00-01	Inside fire hose cabinet FHC-G-01		1				✓
G00-02	Inside fire hose cabinet FHC-G-02		1				✓
G00-03	In Front of ROF			1			✓
G00-04	Beside Congeorge			1			✓
G00-05	In Front of Store PA		1				✓
G00-06	Gas Room		1				✓
G00-07	In Fire cart		5	1	3		✓
Basement 01							
B01-01	Inside fire hose cabinet FHC-B1-01		1				✓
B01-02	Inside fire hose cabinet FHC-B1-02		1				✓
B01-03	Inside fire hose cabinet FHC-B1-03		1				✓
B01-04	Inside fire hose cabinet FHC-B1-04		1				✓
B01-05	In Front of SO Safe room			1			✓
B01-06	Canteen Kitchen				1		✓
Basement 02							
B02-01	Inside fire hose cabinet FHC-B2-01		1				✓
Total			43	104	5	6	Grand Total 158


Dry Chemical	Total = 43 f6
G-2	Total = 104 f6
Wet Chemical	Total = 5 f6
Fire Blanket	Total = 6 f6u
Damage	0

Checked By:
Security Officer / Supervisor

Acknowledged By:
Security Manager / Asst. Security Manager

P20-03	Electric room			1			✓
Floor 19th							
P19-01	Inside fire hose cabinet FHC-19-01			1			✓
P19-02	Inside fire hose cabinet FHC-19-02			1			✓
P19-03	Electric room			1			✓
Floor 18th							
P18-01	Inside fire hose cabinet FHC-18-01			1			✓
P18-02	Inside fire hose cabinet FHC-18-02			1			✓
P18-03	Electric room			1			✓
Floor 17th							
P17-01	Inside fire hose cabinet FHC-17-01			1			✓
P17-02	Inside fire hose cabinet FHC-17-02			1			✓
P17-03	Electric room			1			✓
Floor 16th							
P16-01	Inside fire hose cabinet FHC-16-01			1			✓
P16-02	Inside fire hose cabinet FHC-16-02			1			✓
P16-03	Electric room			1			✓
Floor 15th							
P15-01	Inside fire hose cabinet FHC-15-01			1			✓
P15-02	Inside fire hose cabinet FHC-15-02			1			✓
P15-03	Electric room			1			✓
Floor 14th							
P14-01	Inside fire hose cabinet FHC-14-01			1			✓
P14-02	Inside fire hose cabinet FHC-14-02			1			✓
P14-03	Electric room			1			✓
Floor 11st (Spa)							
P11-01	Inside fire hose cabinet FHC11-M		1				✓
P11-02	Inside fire hose cabinet FHC-11-01			1			✓
P11-03	Inside fire hose cabinet FHC11-02			1			✓
P11-04	In Front of Gamm Muntha room			1			✓
Floor 10th (6o RT)							
P10-01	Inside fire hose cabinet FHC-10-01			1			✓
P10-02	Inside fire hose cabinet FHC-10-02			1			✓
P10-03	In Lift Control room Low zone			1			✓
P10-04	Electric room			1			✓
P10-05	In Front of Gamm Pump room(Pool)			1			✓
P10-06	Water Club			1			✓
Floor 09th							
P09-01	Inside fire hose cabinet FHC-09-01			1			✓
P09-02	Inside fire hose cabinet FHC-09-02			1			✓
P09-03	In Front of behind the counter			1			✓
Floor 08th (Ballroom)							
P08-01	Inside fire hose cabinet FHC-08-01			1			✓
P08-02	Inside fire hose cabinet FHC-08-02			1			✓
P08-03	Inside fire hose cabinet FHC-08-03			1			✓
P08-04	In the Ballroom			2			✓
P08-05	In the Kitchen Bakery			1			✓
P08-06	BQ Kitchen				1	1	✓
Floor 07th (Redoven/SOS-H)							
P07-01	Inside fire hose cabinet FHC-07-01			1			✓
P07-02	Inside fire hose cabinet FHC-07-02			1			✓
P07-03	Inside fire hose cabinet FHC-07-03			1			✓
P07-04	Redoven Reception			1			✓
P07-05	Main Kitchen			1		1	✓
P07-06	Front of Social Room2			1			✓
P07-07	Japanese Kitchen			1		1	✓
P07-08	Redoven terrace		1				✓
Floor 06th							
P06-01	Inside fire hose cabinet FHC-06-01		1				✓
P06-02	Inside fire hose cabinet FHC-06-02		1				✓
P06-03	Inside fire hose cabinet FHC-06-03		1				✓
P06-04	Laundry Room		1	1			✓

เอกสารแบบ 15
ใบรับรองการตรวจสอบอาคาร



เลขที่ ๒๑๕๘/๒๕๖๙

รายงานผลการตรวจสอบประจำปี ครั้งที่ ๒
ตามใบรับรองการตรวจสอบประจำปี ครั้งที่ ๑
เลขที่ ๒๓๙๔/๒๕๖๘ ลงวันที่ ๘ สิงหาคม ๒๕๖๘

แบบ ร.๑

ตามใบรับรองการตรวจสอบใหญ่เลขที่ ๒๒๔๐/๒๕๖๗
ลงวันที่ ๑๑ มิถุนายน ๒๕๖๗

ใบรับรองการตรวจสอบอาคาร

ใบรับรองฉบับนี้ออกให้เพื่อแสดงว่า

อาคาร โรงแรม โซ แบงคอก

โดย บริษัท โอ๊คทรี จำกัด

ตั้งอยู่เลขที่ ๒

ตรอก/ซอย - ถนน สหพรหม

อำเภอ/เขต บางรัก จังหวัด

กรุงเทพมหานคร

ได้ผ่านการตรวจสอบอาคาร ตามพระราชบัญญัติ ควบคุมอาคาร พ.ศ. ๒๕๒๒ แล้ว

เจ้าพนักงานท้องถิ่นได้พิจารณาผลการตรวจสอบอาคาร ซึ่งทำการตรวจสอบโดยผู้ตรวจสอบชื่อ พันตำรวจโท กองกาญจน์ ฉันทบริดา

เลขทะเบียน บ.๑๐๔๐/๒๕๕๐ ออกให้ ณ วันที่ ๑๒ ธันวาคม ๒๕๖๘ อาคารนี้มีสภาพปลอดภัยในการใช้งาน

คำเตือน

๑. ใบรับรองฉบับนี้เป็นการรับรองเฉพาะการตรวจสอบอาคาร

มิได้เป็นการรับรองความถูกต้องของการก่อสร้างอาคาร
ดัดแปลงอาคาร หรือเคลื่อนย้ายอาคารแต่อย่างใด

๒. ให้จัดส่งรายงานผลการตรวจสอบอาคารภายใน ๓๐ วัน

ก่อนใบรับรองการตรวจสอบอาคาร (แบบ ร.๑) จะมี

ระยะเวลาครบ ๑ ปี

BID 47151798066856

(อ้างอิงเลขเดิม 996AA814F1D0)

ตำแหน่ง ผู้อำนวยการสำนักงานการโยธา

ปฏิบัติราชการแทนผู้ว่าราชการกรุงเทพมหานคร

เจ้าพนักงานท้องถิ่น



เอกสารแบบ 16
เอกสารรับรองผลการตรวจวิเคราะห์คุณภาพน้ำทิ้ง



MR-05

Analysis / Test Report

TESTING
No.0009
Lot ID: 261054

Date Received : Jan 06, 2026
Date Reported : Jan 16, 2026
Report Number : 3489988-1

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O :
Project Name :
Project Location :

Page 1 of 2

Sample Number		261054-2					
Sampled Date		Jan 06, 2026 10:54 AM					
Sample Description		Wastewater					
Location		Storage Tank					
Date Analysis Commenced		Jan 07, 2026					
Condition of Sample		Contained in one amber glass bottle and four plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)					
Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Water Testing							
BOD (5 days at 20 degree C)	mg/L	-	2.0	182	≤20	Standard Methods for the Examination of Water and Wastewater: APHA, AWWA & WEF, 24th ed., 2023, part 5210 B, part 4500 - O G	Bangkok
Oil & Grease	mg/L	-	3	11	≤20	Standard Methods for the Examination of Water and Wastewater: APHA, AWWA & WEF, 24th ed., 2023, part 5520 B	Bangkok
pH at 25 degree C	-	-	-	7.3	5.5-9.0	Standard Methods for the Examination of Water and Wastewater: APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Settleable Solid *	mL/L/hr	-	0.1	<0.1	No Standard	Standard Methods for the Examination of Water and Wastewater: APHA, AWWA & WEF, 24th ed., 2023, part 2540 F	Bangkok
Sulfide *	mg/L	-	0.5	<0.5	≤1	Standard Methods for the Examination of Water and Wastewater: APHA, AWWA & WEF, 24th ed., 2023, part 4500-52 (C, F)	Bangkok
Total Dissolved solids Dried at 180 degree C	mg/L	-	5	344	≤1000	Standard Methods for the Examination of Water and Wastewater: APHA, AWWA & WEF, 24th ed., 2023, part 2540 C	Bangkok
Total Kjeldahl Nitrogen as N *	mg/L	0.15	1.0	34.0	≤35	Standard Methods for the Examination of Water and Wastewater: APHA, AWWA & WEF, 24th ed., 2023, part 4500-Norg (C)	Bangkok
Total Suspended Solids Dried at 103-105 degree C	mg/L	-	5	40	≤30	Standard Methods for the Examination of Water and Wastewater: APHA, AWWA & WEF, 24th ed., 2023, part 2540 D	Bangkok

Guideline : Notification of Ministry of Natural Resources and Environment B.E. 2567 on Effluent Control Standard from Types and Sized of Buildings, Type A.

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Scientist (3)



ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7891-101/ EMAIL

S:Report, AL_GLP (3.38PM)

Analysis / Test Report

TESTING
No.0009
Lot ID: 261054

Date Received : Jan 06, 2026
Date Reported : Jan 16, 2026
Report Number : 3489987-1

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O :
Project Name :
Project Location :

Page 1 of 1

Sample Number		261054-1					
Sampled Date		Jan 06, 2026 10:47 AM					
Sample Description		Consumption Water					
Location		Swimming Pool					
Date Analysis Commenced		Jan 07, 2026					
Condition of Sample		Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)					
Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok
Total Coliform	MPN/100mL	-	-	<1.1	<10	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 B	Bangkok
Water Testing							
pH at 25 degree C *	-	-	-	7.5	7.2-8.4	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Residual Free Chlorine *	mg/L	-	0.1	0.8	0.6-1.0	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-CI (F)	Bangkok

Guideline : ค่ามาตรฐานของกรมการสาธารณสุข ฉบับที่ 1/2550 เพื่อการควบคุมการปนเปื้อนจากสารชีวภาพ พืชรากาหรณ์ฯ ในน้ำประปา

Sampling By : Chuladit Warin

Remark :
- LOD : Limit of Detection
- < : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Scientist (3)



ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7891-101/ EMAIL

S:Report, AL_GLP (3.38PM)

u.16/1



MR-05

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : กรุงเทพมหานคร
Project Name :
Project Location :

Sample Number 261054-2
Sampled Date Jan 06, 2026 10:54 AM
Sample Description Wastewater
Location Storage Tank
Date Analysis Commenced Jan 07, 2026
Condition of Sample Contained in one amber glass bottle and four plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Page 1 of 2

Analyte	Unit	LOQ (LOR)	Result	Guideline (1)	Guideline (2)	Method	Testing Location
Water Testing							
BOD (5 days at 20 degree C)	mg/L	-	182	≤20	≤150	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 5210 B, part 4500 - O G	Bangkok
Oil & Grease	mg/L	-	11	≤20	≤20	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 5520 B	Bangkok
pH at 25 degree C		-	7.3	5.5-9.0	6-9	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Settleable Solid *	mL/L/hr	-	<0.1	No Standard	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 2540 F	Bangkok
Sulfide *	mg/L	-	<0.5	≤1	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-S2 (C, F)	Bangkok
Total Dissolved Solids Dried at 180 degree C	mg/L	-	344	≤1000	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 2540 C	Bangkok
Total Kjeldahl Nitrogen as N *	mg/L	0.15	34.0	≤35	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-Norg (C)	Bangkok
Total Suspended Solids Dried at 103-105 degree C	mg/L	-	40	≤30	≤150	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 2540 D	Bangkok

Guideline : Guideline 1 : Notification of Ministry of Natural Resources and Environment B.E. 2567 on Effluent Control Standard from Types and Sized of Buildings, Type A.
Guideline 2 : Bangkok Metropolitan Administration Regulation B.E. 2568 (2025)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any form without the written approval of the laboratory.

Approved by

Section Head

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any form without the written approval of the laboratory.

Approved by

SCIENTIST (C)

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O :
Project Name :
Project Location :

Sample Number 261054-2
Sampled Date Jan 06, 2026 10:54 AM
Sample Description Wastewater
Location Storage Tank
Date Analysis Commenced Jan 07, 2026
Condition of Sample Contained in one amber glass bottle and four plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Page 2 of 2

Sampling by : Chuladet Warin

Remark :

- LOD : Limit of Detection
- "<" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

TESTING

No.0009

Lot ID: 261054

Date Received : Jan 06, 2026

Date Reported : Jan 16, 2026

Report Number : 3489988-1



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 8099434
Project Name :
Project Location :

TESTING
No.0009
Lot ID: 269023

Date Received : Feb 02, 2026
Date Reported : Mar 04, 2026
Report Number : 3507413-1 Rev. No.1

Page 1 of 1

Sample Number 269023-1
Sampled Date Feb 02, 2026 1:10 PM
Sample Description Consumption Water
Location Swimming Pool
Date Analysis Commenced Feb 03, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok
Total Coliform	MPN/100mL	-	-	<1.1	<10	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 B	Bangkok
Water Testing							
pH at 25 degree C *	-	-	-	7.6	7.2-8.4	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Residual Free Chlorine *	mg/L	-	0.1	0.9	0.6-1.0	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-Cl (F)	Bangkok

Guideline : ตามมาตรฐานการตรวจวัดตาม 1/2550 เพื่อการควบคุมการปนเปื้อนของน้ำดื่ม

Note : This Analysis test Report is reissued to supersede Report No. 3507413-1, Date Reported : Feb 12, 2026 due to the revision of guideline from Mo guideline

Sampling By : Panupong Homewong

- Remark :**
- LOD : Limit of Detection
 - "c" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
 - Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
 - Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Section Head

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7941-101/ EMAIL

S:\Reports\AL GL.rpt (8:44AM)

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 8099434
Project Name :
Project Location :

TESTING
No.0009
Lot ID: 261094

Date Received : Jan 06, 2026
Date Reported : Feb 26, 2026
Report Number : 3505194-1 Rev. No.1

Page 2 of 2

Note : This Analysis test Report is reissued to supersede Report No. 3505194-1, Date Reported : Jan 16, 2026 due to the revision of guideline from Bangkok Metropolitan Administration Regulation B.E. 2568 (2025)

Sampling By : Chulaladet Warin

- Remark :**
- LOD : Limit of Detection
 - "c" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
 - Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
 - Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Section Head

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7941-101/ EMAIL

S:\Reports\AL 2GL.rpt (11:16AM)



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๘๖๖๖๖๖
Project Name :
Project Location :

TESTING
No.0009
Lot ID: 269023

Date Received : Feb 02, 2026
Date Reported : Feb 24, 2026
Report Number : 3507414-1 Rev. No.1

Page 2 of 2

Note : This Analysis test Report is reissued to supersede Report No. 3507414-1, Date Reported : Feb 12, 2026 due to the revision of guideline from No guideline

Sampling By : Panupong Homewong

Remark :

- LOD : Limit of Detection
- "L" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any manner without the written approval of the laboratory.

Approved by



Section Head

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7941-101/ EMAIL

S:\Reports_AU_2026\pt (9-164M)

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๘๖๖๖๖๖
Project Name :
Project Location :

TESTING
No.0009
Lot ID: 269023

Date Received : Feb 02, 2026
Date Reported : Feb 24, 2026
Report Number : 3507414-1 Rev. No.1

Page 1 of 2

Sample Number 269023-2
Sampled Date Feb 02, 2026 1:45 PM
Sample Description Wastewater
Location Storage Tank
Date Analysis Commenced Feb 03, 2026
Condition of Sample Contained in one amber glass bottle and four plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline (1)	Guideline (2)	Method	Testing Location
Water Testing								
BOD (5 days at 20 degree C)	mg/L	-	2.0	77.8	≤20	≤150	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 5210 B, part 4500 - O G	Bangkok
Oil & Grease	mg/L	-	3	14	≤20	≤20	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 5520 B	Bangkok
pH at 25 degree C		-	-	7.3	5.5-9.0	6-9	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Settleable Solid *	mL/L/hr	-	0.1	0.1	No Standard	No Standard	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 2540 F	Bangkok
Sulfide *	mg/L	-	0.5	0.6	≤1	No Standard	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 4500 - S2 (C, F)	Bangkok
Total Dissolved solids Dried at 180 degree C	mg/L	-	5	264	≤1000	No Standard	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 2540 C	Bangkok
Total Kjeldahl Nitrogen as N *	mg/L	0.15	1.0	48.0	≤35	No Standard	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 4500 - Norg (C)	Bangkok
Total Suspended Solids Dried at 103-105 degree C	mg/L	-	5	49	≤30	≤150	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 2540 D	Bangkok

Guideline : Guideline 1 : Notification of Ministry of Natural Resources and Environment B.E. 2567 on Effluent Control Standard from Types and Sized of Buildings, Type A.
Guideline 2 : Bangkok Metropolitan Administration Regulation B.E. 2568 (2025)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any manner without the written approval of the laboratory.

Approved by



Section Head

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7941-101/ EMAIL

S:\Reports_AU_2026\pt (9-164M)



Analysis / Test Report

TESTING
No.0009
Lot ID: 2618437

Client : mDree koN pany ON lted
20- orTL hatLorn RoadOhlon OSanBraO SanBoO TLailand b, S,,
P/O : สฎุภรจ้ง
Project Name :
Project Location :
Date Received : F ar b002, 26
Date Reported : F ar 2402, 26
Report - - N uer : 35373, , lb

9aBb b ar2

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline (1)	Guideline (2)	Method	Testing Location
Water Testing								
SmD W days at 2, deBree KU	NB/C	1	2),	b43	≤2,	≤b5,	handard F etLods for tLe HEaN nation q9 ar and 9 asteWater) AgwaOA9 A x 9 H&L 2fTL ed02, 230 part 52b, S0part f5,, 1 mG	SanBoO
ml x Grease	NB/C	1	3	b7	≤2,	≤2,	handard F etLods for tLe HEaN nation q9 ar and 9 asteWater) AgwaOA9 A x 9 H&L 2fTL ed02, 230part 552, S	SanBoO
pw at 25 deBree k		1	1	42	535B),	618	handard F etLods for tLe HEaN nation q9 ar and 9 asteWater) AgwaOA9 A x 9 H&L 2fTL ed02, 230 part f5,, 1w18U	SanBoO
hettleaule holid *	N/C/L/r	1	, b)	, b)	- o hstandard		handard F etLods for tLe HEaN nation q9 ar and 9 asteWater) AgwaOA9 A x 9 H&L 2fTL ed02, 230part 25f, &	SanBoO
h. lfde *	NB/C	1	, 5	, 7	sb	- o hstandard	handard F etLods for tLe HEaN nation q9 ar and 9 asteWater) AgwaOA9 A x 9 H&L 2fTL ed02, 230part f5,, 31c, W&L	SanBoO
Total Dissolved solids Dried at b7, deBree k	NB/C	1	5	37f	sb,, ,	- o hstandard	handard F etLods for tLe HEaN nation q9 ar and 9 asteWater) AgwaOA9 A x 9 H&L 2fTL ed02, 230part 25f, k	SanBoO
Total KjeldalI - itroBen as - *	NB/C	, b5	b),	3338	≤35	- o hstandard	handard F etLods for tLe HEaN nation q9 ar and 9 asteWater) AgwaOA9 A x 9 H&L 2fTL ed02, 230part f5,, 1- orb WU	SanBoO
Total h. spended holid Dried PoN b, 31b, 5 deBree k	NB/C	1	5	75	≤3,	≤b5,	handard F etLods for tLe HEaN nation q9 ar and 9 asteWater) AgwaOA9 A x 9 H&L 2fTL ed02, 230part 25f, D	SanBoO

Guideline : G. ideline b : - otification opF instry op- at. ral Reso. rces and HviromN ent S3H) 2564 on HR. ent control hstandard PoN Types and hized op
S. ilidinB0Type A)
G. ideline 2 : SanBoOOf etropolian AdN instration ReB. lation S3H) 2567 W, 25U

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced except in full without the written approval of the laboratory.

Approved by

Section head

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

48/ b5b, b/ #F AEC

h/ Reports/AL_2607a W 3, gF U

Analysis / Test Report

TESTING
No.0009
Lot ID: 2618437

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : สฎุภรจ้ง
Project Name :
Project Location :
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 3538299-1

Page 1 of 1

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Not Detected	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok
Total Coliform	MPN/100mL	-	-	<1.1	<10	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 9221 B	Bangkok
Water Testing							
pH at 25 degree C *		-	-	7.6	7.2-8.4	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Residual Free Chlorine *	mg/L	-	0.1	0.8	0.6-1.0	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 4500-Cl (F)	Bangkok

Guideline : ส่วนหน้าของผลการทดสอบ อยู่หน้า 1/2550 ซึ่งการควบคุมการปนเปื้อนจากการตรวจหาเชื้อจุลินทรีย์ในน้ำดื่ม

Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- < : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced except in full without the written approval of the laboratory.

Approved by

Scientist (S)

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7841-101/ EMAIL

S/Reports/AL_GL.rpt (3.44M)



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๙๐๖๖๓๖
Project Name :
Project Location :

Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 3538301-1

Page 1 of 1

Sample Number 2618437-3
Sample Date Mar 11, 2026 10:25 AM
Sample Description Consumption Water
Location Shower Water Sample : Guest room 2605
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Legionella spp.</i>	CFU/L	-	-	Not Detected**	Not Detected	ISO 11731 (2017)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower B.E. 2544

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- "L" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be responsible for any errors or omissions in the data or the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : maDree koN pany ON ited
20- orit. hatLorn RoadOhlon OsanBraO SanBoO TLailand b, S,,
P/O : ๙๐๖๖๓๖
Project Name :
Project Location :

Lot ID: 2618437
Date Received : Far bb02, 26
Date Reported : Far 2402, 26
Report - Nuer : 35373, , Ib

9aBb, 2 of 2

Sampling By : gicLai SoonyonB
ReNaO :
- CrD : GINit oPDetection
- "L" : Goller Luan CrQ VON it oP ReportinBU
- AnalyteINaOod * is/are not incl. ded in scope oP Accreditation Ihm/HK b4, 25)
- hAN pIIB is not incl. ded in scope oP accreditation Ihm/HK b4, 25

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be responsible for any errors or omissions in the data or the laboratory.

Approved by

Section Head

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๓๐๖๖๓๖
Project Name :
Project Location :

Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 3538303-1

Page 1 of 1

Sample Number 2618437-5
Sampled Date Mar 11, 2026 10:15 AM
Sample Description Consumption Water
Location Cooling Tower Water Sample
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards GAP (A, HSI, PAE)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Legionella spp.</i>	CFU/L	-	-	Not Detected	Not Detected	ISO 11731 (2017E)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower BJJ 2544

Note : FF Not Detected mean Bacteria not found in agar plate

Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- Q/Q : Lower than LO* Limit of ReportingE

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced except in full without the written approval of the laboratory.

Approved by

Scientist GIE

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๓๐๖๖๓๖
Project Name :
Project Location :

Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 3538302-1

Page 1 of 1

Sample Number 2618437-4
Sampled Date Mar 11, 2026 10:10 AM
Sample Description Consumption Water
Location Spa Water Sample Vao Chattan
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Legionella spp.</i>	CFU/L	-	-	Not Detected**	Not Detected	ISO 11731 (2017)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower B.E. 2544

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- %C : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced except in full without the written approval of the laboratory.

Approved by

Scientist (P)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๓๐๒๓๖๓
Project Name :
Project Location :
Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 3538305-1

Page 1 of 1

Sample Number 2618437-7
Sampled Date Mar 11, 2026 10:20 AM
Sample Description Consumption Water
Location Roof Tank
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards GAP (A, HSI, PAE)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing <i>Legionella spp</i>	CFU/L	-	-	Not Detected	FF	SO 11731 (2017E)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower BUN 2544

Note : FF Not Detected mean Bacteria not found in agar plate

Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- Q/Q : Lower than LO* Limit of * quantitationE / LOR Limit of ReportingE

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any way without the written approval of the laboratory.

Approved by

Scientist GE

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๓๐๒๓๖๓
Project Name :
Project Location :
Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 353830-1

Page 1 of 1

Sample Number 2618-3716
Sampled Date Mar 11, 2026 10:35 AM
Sample Description Consumption Water
Location undergroud Tank
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (AT HA, NSL, PAE)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing <i>Legionella spp</i>	CFU/L	U	U	Not Detected	FF	SO 11731 (2017E)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower BUN 25--

Note : FF Not Detected mean Bacteria not found in agar plate

Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- Q/Q : Lower than LO* Limit of * quantitationE / LOR Limit of ReportingE

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any way without the written approval of the laboratory.

Approved by

Scientist GE

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



MR-05

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๓๐๖๖๓๖
Project Name :
Project Location :

Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 3538307-1

Page 1 of 1

Sample Number 2618437-9
Sampled Date Mar 11, 2026 10:15 AM
Sample Description Consumption Water
Location Cooling Tower Water Sample
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in one plastic bottle, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing <i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok

Guideline :

Sampling By : Pichai Boonyong

Remark :

- LOD : Limit of Detection
- "c" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๓๐๖๖๓๖
Project Name :
Project Location :

Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 3538306-1

Page 1 of 1

Sample Number 2618437-8
Sampled Date Mar 11, 2026 10:30 AM
Sample Description Consumption Water
Location Kitchen
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing <i>Legionella spp.</i>	CFU/L	-	-	Not Detected**	Not Detected	ISO 11731 (2017)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower B.E. 2544

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Pichai Boonyong

Remark :

- LOD : Limit of Detection
- "c" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๓๐๒๓๖๓
Project Name :
Project Location :
Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 3538307-1

Page 1 of 1

Sample Number 2618439-11
Sample Date Mar 11, 2026 10:10 AM
Sample Description Consumption Water
Location Spa Water Sample
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in one plastic bottle, sample containers comply to pretreatment - preservation standards WPC(A), HSLPAE

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing <i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	No Standard	Standard Methods for the Examination of Water and Wastewater, AP(A), AWWA & WLF, 24th ed., 2023, part 7221 F	Bangkok

Guideline :
Sampling By : Pichai Boonyong
Remark :
- LOD : Limit of Detection
- "c" : Lower than LOQ Limit of Quantitation / LOR Limit of Reporting

Approved by

Scientist WE

Results apply to the sample as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any way without the written approval of the laboratory.

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๓๐๒๓๖๓
Project Name :
Project Location :
Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 3538307-1

Page 1 of 1

Sample Number 2618437-10
Sample Date Mar 11, 2026 10:25 AM
Sample Description Consumption Water
Location Shower 9 after Sample
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in one plastic bottle, sample containers comply to pretreatment - preservation standards WPC(A), HSLPAE

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing <i>Escherichia coli</i>	in 100 mL	7	7	Not Detected	No Standard	Standard Methods for the Examination of Water and Wastewater, AP(A), AWWA & WLF, 24th ed., 2023, part 7221 F	Bangkok

Guideline :
Sampling By : Pichai Boonyong
Remark :
- LOD : Limit of Detection
- "c" : Lower than LOQ Limit of Quantitation / LOR Limit of Reporting

Approved by

Scientist WE

Results apply to the sample as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any way without the written approval of the laboratory.

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

ISO/IEC 17025
Accreditation No. 1031147

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 0000000000
Project Name :
Project Location :

Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report Number : 35383111-1

Page 1 of 1

Sample Number 2618437-13
Sample Date Mar 11, 2026 10:30 AM
Sample Description Consumption Water
Location Kitchen
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in one plastic bottle, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Method	Testing Location
Microbiological Testing						
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok

Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- "c" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used for any other purpose without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7661-101 / ENAIL

S:\Reports\All\NGC\pt (3-47PM)



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 0000000000
Project Name :
Project Location :

Lot ID: 2618437
Date Received : Mar 11, 2026
Date Reported : Mar 28, 2026
Report N-muer : 353831071

Page 1 of 1

Sample Number 2618437-12
Sample Date Mar 11, 2026 10:00 AM
Sample Description Consumption 9 ater
Location bood
Date Analysis Commenced Mar 12, 2026
Condition of Sample Contained in one plastic uottle, sample containers comply to pretreatment 7 preservation standards Wbwa, (SHBAU

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Escherichia coli</i>	in 100 mL	7	7	Not Detected	No Standard	Standard Methods for the Examination of Water and Wastewater, 19th ed., 2018, part 9221 F	Bangkok

Guideline :

Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- "c" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used for any other purpose without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

461101 / ENAIL

S:\Reports\All\NGC\pt (3-47PM)



MR-05

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๙๐๒๖๖๖
Project Name :
Project Location :
Sample Number : 2628039-2
Sample Date : Apr 09, 2026 9:50 AM
Sample Description : Wastewater
Location : Storage Tank
Date Analysis Commenced : Apr 10, 2026
Condition of Sample : Contained in one amber glass bottle and four plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Page 2 of 3

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Water Testing							
BOD (5 days at 20 degree C)	mg/L	-	2.0	96.2	≤20	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 5210 B, part 4500 - O G	Bangkok
Oil & Grease	mg/L	-	3	<3	≤20	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 5520 B	Bangkok
pH at 25 degree C	-	-	-	7.3	5.5-9.0	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Settleable Solid *	mL/L/hr	-	0.1	0.4	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 2540 F	Bangkok
Sulfide *	mg/L	-	0.5	<0.5	≤1	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-52 (C, F)	Bangkok
Total Dissolved solids Dried at 180 degree C	mg/L	-	5	316	≤1000	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 2540 C	Bangkok
Total Kjeldahl Nitrogen as N *	mg/L	0.15	1.0	40.3	≤35	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-Norg (C)	Bangkok
Total Suspended Solids Dried from 103-105 degree C	mg/L	-	5	47	≤30	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 2540 D	Bangkok

Guideline : Guideline 1 : Notification of Ministry of Natural Resources and Environment B.E. 2567 on Effluent Control Standard from Types and Sized of Buildings, Type A.
Guideline 2 : Bangkok Metropolitan Administration Regulation B.E. 2568 (2025)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced except in full without the written approval of ALS.

Approved by

Section Head

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ๙๐๒๖๖๖
Project Name :
Project Location :
Sample Number : 2628039-1
Sample Date : Apr 09, 2026 9:30 AM
Sample Description : Consumption Water
Location : Swimming Pool
Date Analysis Commenced : Apr 09, 2026
Condition of Sample : Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Page 1 of 3

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok
Total Coliform	MPN/100mL	-	-	<1.1	<10	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 B	Bangkok
Water Testing							
pH at 25 degree C *	-	-	-	7.9	7.2-8.4	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Residual Free Chlorine *	mg/L	-	0.1	0.8	0.6-1.0	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-CI (F)	Bangkok

Guideline : ค่ามาตรฐานของกรมการสาธารณสุข ฉบับที่ 1/2550 เรื่อง การควบคุมการปนเปื้อนของน้ำดื่ม น้ำกินในชุมชน
Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- < : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced except in full without the written approval of ALS.

Approved by

Section Head

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 8099434
Project Name :
Project Location :
Sample Number : 2628039-1
Sampled Date : Apr 09, 2026 9:30 AM
Sample Description : Consumption Water
Location : Swimming Pool
Date Analysis Commenced : Apr 09, 2026
Condition of Sample : Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Page 1 of 1

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok
Total Coliform	MPN/100mL	-	-	<1.1	<10	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 B	Bangkok
Water Testing							
pH at 25 degree C *		-	-	7.9	7.2-8.4	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Residual Free Chlorine *	mg/L	-	0.1	0.8	0.6-1.0	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-CI (F)	Bangkok

Guideline : ตามมาตรฐานการตรวจวิเคราะห์ ณ วันที่ 1/2550 เพื่อการควบคุมการปนเปื้อนของน้ำดื่มที่จำหน่ายในกรุงเทพมหานคร
Note : This Analysis test Report is reissued to supersede Report No. 3540372-1, Date Reported : Apr 23, 2026 due to the additional of guideline.

Sampling By : Pichai Boonyong

Remark :
- LOD : Limit of Detection
- "<" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Section Head

Approved by

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences
www.alsglobal.com
RIGHT SOLUTIONS RIGHT PARTNER

7941-101/ EMAIL

S:\Reports\AL_GL.rpt (1003AM)

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 8099434
Project Name :
Project Location :
Sample Number : 2628039-1
Sampled Date : Apr 09, 2026 9:30 AM
Sample Description : Consumption Water
Location : Swimming Pool
Date Analysis Commenced : Apr 09, 2026
Condition of Sample : Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Page 3 of 3

Remark :
- LOD : Limit of Detection
- "<" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Section Head

Approved by

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences
www.alsglobal.com
RIGHT SOLUTIONS RIGHT PARTNER

7941-101/ EMAIL

S:\Reports\AL_GL.rpt (2156PM)



Analysis / Test Report

Client 6maDree koN pany ON itev
20- ortL hatLorn RoavOhlon OSanBrao SanBoo OTLailanv 1F3FF
P/O : 8uipn3n
Project Name 6
Project Location 6

TESTING
No.0009
Lot ID: 2628039
: ate ReBicev 6Apr Fb02F2,
: ate Reportev 6Apr 2d02F2,
Report - . N uer 6433d34571

Note : TLis Analysis test Report is reiss. ev to s. perseve Report - ox435F4d2710: ate Reportev 6Apr 2402F2, v. e to tLe avtional oPB. ivellinx
Sampling By : giDLai SoonynonB

ReLarO6
- Cnt 6ONit op: etedion
- < < 6OWer tlan Cnt* vONit op: antiation / ONR vONit opReportinBE
- AnaliveNE NarOv Kis/are not ind. vev in sDope opADeviation QmVQK 1dF23x
- han plnB is not ind. vev in sDope opADeviation QmVQK 1dF23

9aBx 2 dP2

Res. Its apply to tLe anhwedAs s. uhterO. nless tLe anhwed Vae Dnv. Dev. by
ADN tLe report suat ind. ue resp. nless tLe anhwed Vae Dnv. Dev. by
ADN tLe report suat ind. ue resp. nless tLe anhwed Vae Dnv. Dev. by
ADN tLe report suat ind. ue resp. nless tLe anhwed Vae Dnv. Dev. by

Approved by

heDion (eav

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

www.alsglobal.com

LIFE SCIENCES

RIGHT SOLUTIONS RIGHT PARTNER

d.513F11/19 AQZ

16 Reports JAN 28 Opt. v6B040 E

Analysis / Test Report

Client 6maDree koN pany ON itev
20- ortL hatLorn RoavOhlon OSanBrao SanBoo OTLailanv 1F3FF
P/O : 8uipn3n
Project Name 6
Project Location 6

TESTING
No.0009
Lot ID: 2628039
: ate ReBicev 6Apr Fb02F2,
: ate Reportev 6Apr 2d02F2,
Report - . N uer 6433d34571

Sample Number 2, 2F4bZ
Sample Date Apr Fb02F2, b6F A9
Sample Description MastWater
Location htorBe TanO
Date Analysis Commenced Apr 1F02F2,
Condition of Sample Kontainev in one an uer Blass uottle anv Rb. r plastDuoties0sanNple Bntainers DnNply to pretreatN ent. 7 preseration stanvarvs vAg(AOHlHgAE

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline (1)	Guideline (2)	Method	Testing Location
Water Testing								
Sm: v8 vays at 2F veBree kE	NB/C	7	2F	b, 2	≤2F	≤13F	hanvarv 9etLows Rbr tLe Ujanination oPM ater anv MastWaterxAg(AOAHMA & MUQ 25TL evw02F240 part 321F S9part 53FF 7 m 8	SanBoo
ml & 8 rease	NB/C	7	4	* 4	≤2F	≤2F	hanvarv 9etLows Rbr tLe Ujanination oPM ater anv MastWaterxAg(AOAHMA & MUQ 25TL evw02F240part 332F S	SanBoo
p(at 23 veBree k	7	7	7	d4	3x7dxF	, 7	hanvarv 9etLows Rbr tLe Ujanination oPM ater anv MastWaterxAg(AOAHMA & MUQ 25TL evw02F240 part 53FF 7(v6E	SanBoo
hettleaule holiv K	N/Q/Lr	7	Fx1	F65	- o htanvarv	- o htanvarv	hanvarv 9etLows Rbr tLe Ujanination oPM ater anv MastWaterxAg(AOAHMA & MUQ 25TL evw02F240part 235F G	SanBoo
h. lRve K	NB/C	7	F8	* F8	≤1	- o htanvarv	hanvarv 9etLows Rbr tLe Ujanination oPM ater anv MastWaterxAg(AOAHMA & MUQ 25TL evw02F240part 53FF712 k0	SanBoo
Total : issolcev solivs : riev at 1F veBree k	NB/C	7	3	41,	≤1FFF	- o htanvarv	hanvarv 9etLows Rbr tLe Ujanination oPM ater anv MastWaterxAg(AOAHMA & MUQ 23TL evw02F240part 235F k	SanBoo
Total J xelvalI - itroben as - K	NB/C	Fx3	1F	5F4	≤43	- o htanvarv	hanvarv 9etLows Rbr tLe Ujanination oPM ater anv MastWaterxAg(AOAHMA & MUQ 25TL evw02F240part 53FF7- oB	SanBoo
Total h. spanvev holivs : riev PoN 1F471F3 veBree k	NB/C	7	3	5d	≤4F	≤13F	hanvarv 9etLows Rbr tLe Ujanination oPM ater anv MastWaterxAg(AOAHMA & MUQ 25TL evw02F240part 235F :	SanBoo

Guideline : 8. iveline 1 6- otitidation op9 inistry op- at. ral Reso. rDes anv UncironN ent SxUX23, d on UR: ent kontrol htanvarv PoN Types anv hIev op
S. ilvinBs0Type Ax
8. iveline 2 6SanBoo9 etropolitan AvN inistration ReB. lation SxUX23, f v6F23E

Res. Its apply to tLe anhwedAs s. uhterO. nless tLe anhwed Vae Dnv. Dev. by
ADN tLe report suat ind. ue resp. nless tLe anhwed Vae Dnv. Dev. by
ADN tLe report suat ind. ue resp. nless tLe anhwed Vae Dnv. Dev. by
ADN tLe report suat ind. ue resp. nless tLe anhwed Vae Dnv. Dev. by

Approved by

heDion (eav

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

www.alsglobal.com

LIFE SCIENCES

RIGHT SOLUTIONS RIGHT PARTNER

d.513F11/19 AQZ

16 Reports JAN 28 Opt. v6B040 E



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangkok, Bangkok Thailand 10500
Lot ID : 2635721
Date Received : May 11, 2026
Date Reported : May 20, 2026
Report Number : 3575920-1

TESTING
No.0009
Client Ref

Page 1 of 2

Sample Number	Sample Date	Sample Description	Location	Date Analysis Commenced	Condition of Sample	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
2635721-2	May 11, 2026 9:40 AM	Wastewater Storage Tank	May 12, 2026	Contained in one amber glass bottle and four plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)		mg/L						
BOD (5 days at 20 degree C)	107	≤20	≤150	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed, 2023, part 5210 B, part 4500 - O G								Bangkok
Oil & Grease	9	≤20	≤20	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed, 2023, part 5520 B		mg/L						Bangkok
pH at 25 degree C	7.4	5.5-9.0	6-9	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed, 2023, part 4500 - H (B)								Bangkok
Settleable Solid *	<0.1	No Standard	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed, 2023, part 2540 F		mL/L						Bangkok
Sulfide *	<0.5	≤1	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed, 2023, part 4500-S2 (C)		mg/L						Bangkok
Total Dissolved Solids Dried at 180 degree C	292	≤1000	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed, 2023, part 2540 C		mg/L						Bangkok
Total Kjeldahl Nitrogen as N *	31.5	≤35	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed, 2023, part 4500-Norg (C)		mg/L						Bangkok
Total Suspended Solids Dried from 103-105 degree C	43	≤30	≤150	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed, 2023, part 2540 D		mg/L						Bangkok

Guideline : Notification of Ministry of Natural Resources and Environment B.E. 2567 on Effluent Control Standard from Types and Sized of Buildings, Type A.
Guideline 2 : Bangkok Metropolitan Administration Regulation B.E. 2568 (2025)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used for any other purpose without the written approval of the laboratory.

App2 Badbye

Scientist (3)

Read its apply to the sample(s) as of limited, unless the sampling is as confirmed by ALS. The report shall not be reproduced or used for any other purpose without the written approval of the laboratory.

Approved by

Section Head



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangkok, Bangkok Thailand 10500
Lot ID : 2635721
Date Received : 9 ay 11, 2026
Date Reported : 9 ay 27, 2026
Report Number : 35-5u1ubd RevNoP1

TESTING
No.0009
Lot ID

Page 1 of 1

Sample Number	Sample Date	Sample Description	Location	Date Analysis Commenced	Condition of Sample	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
2635-21bt	9 ay 11, 2026 u:30 A9	Cons mption water S (imming Noel	9 ay 12, 2026	Contained in (o plastic bottles, sample containers comply to pretreatment b preservation standards HAMJA, ES) Mx		in 100 mL	b	b	Not Detected	Not Detected	Standard 9 ethods Wt the waste(aterAMJA, AwWA & w) F, 24th edP 2023, part u221 F	Bangkok
Total Coliform	9 MW/100mL	b	b	<10		9 MW/100mL	b	b	<10	<10	Standard 9 ethods Wt the waste(aterAMJA, AwWA & w) F, 24th edP 2023, part u221 B	Bangkok
Water Testing	pU at 25 degree C *	b	b	-P		mg/L	b	0P1	1P	006b1P	Standard 9 ethods Wt the waste(aterAMJA, AwWA & w) F, 24th edP 2023, part 4500 BU Fx	Bangkok
Resid al Free Chlorine *		b	b	1P		mg/L	b	0P1	1P	006b1P	Standard 9 ethods Wt the waste(aterAMJA, AwWA & w) F, 24th edP 2023, part 4500 BU Fx	Bangkok

Guideline : ส่วนที่ ๑๖ ของกฎกระทรวงกำหนดมาตรฐานในการบริหารและการจัดการด้านความปลอดภัย อาชีวอนามัย และสภาพแวดล้อมในการทำงาน พ.ศ. ๒๕๖๑
Note : This Analysis test Report is relisf ed to sf persede Report NoP35-5u1ubd, Date Reported : 9 ay 21, 2026 dfe to the revision oLgT idelineTotal Coliform Worm Not Detected to <10
Sampling By : Mchal Boonyong

Remark :
- LOD : Limit of Detection
- "L" : Limit of Reporting
- "C" : Limit of Reporting
- Analyte marked * is/are not incl ded in scope of Accreditation ISO/IEC 17025
- Sampling is not incl ded in scope of Accreditation ISO/IEC 17025

Read its apply to the sample(s) as of limited, unless the sampling is as confirmed by ALS. The report shall not be reproduced or used for any other purpose without the written approval of the laboratory.

Approved by

Section Head



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : คุณกฤษณ์
Project Name :
Project Location :

TESTING
No.0009
Lot ID: 2646680
Date Received : Jun 01, 2026
Date Reported : Jun 20, 2026
Report Number : 3601851-1

Page 1 of 1

Sample Number		2646680-1						
Sampled Date		Jun 01, 2026 11:20 AM						
Sample Description		Consumption Water						
Location		Swimming Pool						
Date Analysis Commenced		Jun 01, 2026						
Condition of Sample		Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)						
Analyte		Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing								
<i>Escherichia coli</i>		in 100 mL	-	-	Not Detected	Not Detected	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok
<i>Legionella spp. *</i>		CFU/L	-	-	Not Detected**	No Standard	ISO 11731 (2017)	Bangkok
Total Coliform		MPN/100mL	-	-	<1.1	<10	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 9221 B	Bangkok
Water Testing								
pH at 25 degree C *			-	-	7.4	7.2-8.4	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Residual Free Chlorine *		mg/L	-	0.1	0.8	0.6-1.0	Standard Methods for the Examination of Water and Wastewater. APHA, AWWA & WEF, 24th ed., 2023, part 4500-CI (F)	Bangkok

Guideline : ค่าเกณฑ์มาตรฐานการทดสอบ อยู่ที่ 1/2550 ซึ่ง การควบคุมการปนเปื้อนจากการตรวจวัดค่าการปนเปื้อน ๑ ในล้านส่วน

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Atitipon Yaso

Remark :
- LOD : Limit of Detection
- "<" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. This report shall not be reproduced or used in any way without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7641-101/ EMAIL

S:\Reports\AL_GLP\ (5:11PM)

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
LI De : คุณกฤษณ์
LI De 671 a :
LI De 671 m :

TESTING
No.0009
Client ID: 0009
Date Received : May 11, 2026
Date Reported : May 20, 2026
Report Number : 3575920-1

S71 pH test yee@ichai Boonyong

Remark :
- LOD : Limit of Detection
- "<" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. This report shall not be reproduced or used in any way without the written approval of the laboratory.

App2 Badbye

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

Life Sciences

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7641-101/ EMAIL

S:\Reports\AL_GLP\ (5:28PM)



Analysis / Test Report

Client : Oaktree Company Limited

2, North Sathorn Road, Silom, Bangkok, Bangkok Thailand 10500

P/O : ศุภฤกษ์

Project Name :

Project Location :

TESTING

No.0009

Lot ID: 2646680

Date Received : Jun 01, 2026

Date Reported : Jun 20, 2026

Report Number : 3601852-1

Page 2 of 2

Sampling By : Attipon Yaso

Remark :

- LOD : Limit of Detection
- " < " : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025



Analysis / Test Report

Client : Oaktree Company Limited

2, North Sathorn Road, Silom, Bangkok, Bangkok Thailand 10500

P/O : ศุภฤกษ์

Project Name :

Project Location :

TESTING

No.0009

Lot ID: 2646680

Date Received : Jun 01, 2026

Date Reported : Jun 20, 2026

Report Number : 3601852-1

Page 1 of 2

Sample Number 2646680-2

Sampled Date Jun 01, 2026 11:55 AM

Sample Description Wastewater

Location Storage Tank

Date Analysis Commenced Jun 02, 2026

Condition of Sample Contained in one amber glass bottle and four plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline (1)	Guideline (2)	Method	Testing Location
Water Testing								
BOD (5 days at 20 degree C)	mg/L	-	2.0	123	≤20	≤150	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 5210 B, part 4500 - O G	Bangkok
Oil & Grease	mg/L	-	3	13	≤20	≤20	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 5520 B	Bangkok
pH at 25 degree C		-	-	7.4	5.5-9.0	6-9	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500 - H (B)	Bangkok
Settleable Solid *	mL/L/hr	-	0.1	0.4	No Standard	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 2540 F	Bangkok
Sulfide *	mg/L	-	0.5	1.2	≤1	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-S2 (C)	Bangkok
Total Dissolved solids Dried at 180 degree C	mg/L	-	5	264	≤1000	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 2540 C	Bangkok
Total Kjeldahl Nitrogen as N *	mg/L	0.15	1.0	29.4	≤35	No Standard	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 4500-Norg (C)	Bangkok
Total Suspended Solids Dried from 103-105 degree C	mg/L	-	5	39	≤30	≤150	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 2540 D	Bangkok

Guideline : Guideline 1 : Notification of Ministry of Natural Resources and Environment B.E. 2567 on Effluent Control Standard from Types and Sized of Buildings, Type A.
Guideline 2 : Bangkok Metropolitan Administration Regulation B.E. 2568 (2025)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any way without the written approval of the laboratory.

Approved by

Scientist (3)

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company

www.alsglobal.com

LIFE SCIENCES

RIGHT SOLUTIONS RIGHT PARTNER

7641-1017/EMAL

7641-1017/EMAL

LIFE SCIENCES

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

S:\Reports\AL_2646680 (5:11PM)



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 80997430
Project Name :
Project Location :

Lot ID: 2646680
Date Received : Jun 01, 2026
Date Reported : Jun 20, 2026
Report Number : 3601854-1

Page 1 of 1

Sample Number 2646680-4
Sampled Date Jun 01, 2026 11:45 AM
Sample Description Consumption Water
Location Spa Water Sample Srinhapapata
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Legionella spp.</i>	CFU/L	-	-	Not Detected**	Not Detected	ISO 11731 (2017)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower B.E. 2544

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Attipon Yaso

Remark :

- LOD : Limit of Detection
- "L" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be responsible for any error in the written approval of the laboratory.

Approved by

Scientist (3)

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 80997430
Project Name :
Project Location :

Lot ID: 2646680
Date Received : Jun 01, 2026
Date Reported : Jun 20, 2026
Report Number : 3601853-1

Page 1 of 1

Sample Number 2646680-3
Sampled Date Jun 01, 2026 11:40 AM
Sample Description Consumption Water
Location Shower Water Sample : Guest room 2810
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Legionella spp.</i>	CFU/L	-	-	Not Detected**	Not Detected	ISO 11731 (2017)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower B.E. 2544

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Attipon Yaso

Remark :

- LOD : Limit of Detection
- "L" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be responsible for any error in the written approval of the laboratory.

Approved by

Scientist (3)

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 8099434
Project Name :
Project Location :

Lot ID: 2646680
Date Received : Jun 01, 2026
Date Reported : Jun 20, 2026
Report Number : 3601856-1

Page 1 of 1

Sample Number 2646680-6
Sampled Date Jun 01, 2026 12:00 PM
Sample Description Consumption Water
Location Underground Tank
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Legionella spp.</i>	CFU/L	-	-	Not Detected**	Not Detected	ISO 11731 (2017)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower B.E. 2544

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Attipon Yaso

Remark :

- LOD : Limit of Detection
- "L" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 8099434
Project Name :
Project Location :

Lot ID: 2646680
Date Received : Jun 01, 2026
Date Reported : Jun 20, 2026
Report Number : 3601855-1

Page 1 of 1

Sample Number 2646680-5
Sampled Date Jun 01, 2026 11:30 AM
Sample Description Consumption Water
Location Cooling Tower Water Sample
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Legionella spp.</i>	CFU/L	-	-	Not Detected**	Not Detected	ISO 11731 (2017)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower B.E. 2544

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Attipon Yaso

Remark :

- LOD : Limit of Detection
- "L" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in full without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 8099434
Project Name :
Project Location :

Lot ID: 2646680
Date Received : Jun 01, 2026
Date Reported : Jun 20, 2026
Report Number : 3601858-1

Page 1 of 1

Sample Number 2646680-8
Sampled Date Jun 01, 2026 11:50 AM
Sample Description Consumption Water
Location Kitchen
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Legionella spp.</i>	CFU/L	-	-	Not Detected**	Not Detected	ISO 11731 (2017)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower B.E. 2544

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Attipon Yaso

Remark :
- LOD : Limit of Detection
- "L" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be responsible for any error in the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 8099434
Project Name :
Project Location :

Lot ID: 2646680
Date Received : Jun 01, 2026
Date Reported : Jun 20, 2026
Report Number : 3601857-1

Page 1 of 1

Sample Number 2646680-7
Sampled Date Jun 01, 2026 11:35 AM
Sample Description Consumption Water
Location Roof Tank
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Guideline / Specification	Method	Testing Location
Microbiological Testing							
<i>Legionella spp.</i>	CFU/L	-	-	Not Detected**	Not Detected	ISO 11731 (2017)	Bangkok

Guideline : Notification of Department of Health about Legionella Control in Cooling Tower B.E. 2544

Note : ** Not Detected mean Bacteria not found in agar plate.

Sampling By : Attipon Yaso

Remark :
- LOD : Limit of Detection
- "L" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be responsible for any error in the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS Limited Company



ISO/IEC 17025
Accreditation No. 1031/47

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ฅงุฒิวิจย
Project Name :
Project Location :

Lot ID: 2646680
Date Received :Jun 01, 2026
Date Reported :Jun 20, 2026
Report Number :3601860-1

Page 1 of 1

Sample Number 2646680-10
Sampled Date Jun 01, 2026 11:40 AM
Sample Description Consumption Water
Location Shower Water Sample Room 2810
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Method	Testing Location
Microbiological Testing						
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok

Sampling By : Altipon Yaso
Remark :

- LOD : Limit of Detection
- "u" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any manner without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS limited Company



ISO/IEC 17025
Accreditation No. 1031/47

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : ฅงุฒิวิจย
Project Name :
Project Location :

Lot ID: 2646680
Date Received :Jun 01, 2026
Date Reported :Jun 20, 2026
Report Number :3601859-1

Page 1 of 1

Sample Number 2646680-9
Sampled Date Jun 01, 2026 11:30 AM
Sample Description Consumption Water
Location Cooling Tower Water Sample
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Method	Testing Location
Microbiological Testing						
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok

Sampling By : Altipon Yaso
Remark :

- LOD : Limit of Detection
- "u" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any manner without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS limited Company



Analysis / Test Report

TESTING
No.0009

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 80997430
Project Name :
Project Location :
Lot ID: 2646680
Date Received :Jun 01, 2026
Date Reported :Jun 20, 2026
Report Number :3601862-1

Page 1 of 1

Sample Number 2646680-12
Sampled Date Jun 01, 2026 12:00 PM
Sample Description Consumption Water
Location Pool
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Method	Testing Location
Microbiological Testing						
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok

Sampling By : Attipon Yaso
Remark :
- LOD : Limit of Detection
- "u" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any way without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO.,LTD. An ALS limited Company



Analysis / Test Report

ISO/IEC 17025
Accreditation No. 10311/47

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : 80997430
Project Name :
Project Location :
Lot ID: 2646680
Date Received :Jun 01, 2026
Date Reported :Jun 20, 2026
Report Number :3601861-1

Page 1 of 1

Sample Number 2646680-11
Sampled Date Jun 01, 2026 11:45 AM
Sample Description Consumption Water
Location Spa Water Sample Srinapapata
Date Analysis Commenced Jun 01, 2026
Condition of Sample Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Method	Testing Location
Microbiological Testing						
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok

Sampling By : Attipon Yaso
Remark :
- LOD : Limit of Detection
- "u" : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
- Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
- Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any way without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO.,LTD. An ALS limited Company



ISO/IEC 17025
Accreditation No. 10311/47

Analysis / Test Report

Client : Oaktree Company Limited
2, North Sathorn Road, Silom, Bangrak, Bangkok Thailand 10500
P/O : บริษัท ออคิดรี จำกัด
Project Name :
Project Location :

Lot ID: 2646680
Date Received : Jun 01, 2026
Date Reported : Jun 20, 2026
Report Number : 3601863-1

Page 1 of 1

Sample Number : 2646680-13
Sample Date : Jun 01, 2026 11:50 AM
Sample Description : Consumption Water
Location : Kitchen
Date Analysis Commenced : Jun 01, 2026
Condition of Sample : Contained in two plastic bottles, sample containers comply to pretreatment - preservation standards (APHA, USEPA)

Analyte	Unit	LOD	LOQ (LOR)	Result	Method	Testing Location
Microbiological Testing						
<i>Escherichia coli</i>	in 100 mL	-	-	Not Detected	Standard Methods for the Examination of Water and Wastewater, APHA, AWWA & WEF, 24th ed., 2023, part 9221 F	Bangkok

Sampling By : Altipon Yaso

- Remark :
- LOD : Limit of Detection
 - " $\leq$ " : Lower than LOQ (Limit of Quantitation) / LOR (Limit of Reporting)
 - Analyte(s) marked * is/are not included in scope of Accreditation ISO/IEC 17025.
 - Sampling is not included in scope of accreditation ISO/IEC 17025

Results apply to the sample(s) as submitted, unless the sampling was conducted by ALS. The report shall not be reproduced or used in any way without the written approval of the laboratory.

Approved by

Scientist (3)

ADDRESS 104 Phatthanakan 40, Phatthanakan Rd., Khwaeng Phatthanakan, Khet Suan Luang, Bangkok 10250 Thailand | PHONE +66 0 2760 3000 | FAX +66 0 2760 3197
ALS LABORATORY GROUP (THAILAND) CO., LTD. An ALS limited Company

Life Sciences

www.alsglobal.com

RIGHT SOLUTIONS RIGHT PARTNER

7941-101/ EMAIL

S:\Reports\AL_NSG.rpt (5:20PM)
