


๓. สรุปผลการทำงานของระบบบำบัดน้ำเสียเป็นรายเดือน

- (๑) ปริมาณการใช้ไฟฟ้าของระบบบำบัดน้ำเสีย (หน่วย) ระบบที่ 1 = 1,140.00
- (๒) ปริมาณน้ำใช้ทุกกิจกรรมในแหล่งกำเนิดมลพิษ (ลบ.ม.) ระบบที่ 1 = 1,210.00
- (๓) ปริมาณน้ำเสียที่เข้าระบบบำบัดน้ำเสีย (ลบ.ม.) ระบบที่ 1 = 1,465.10
- (๔) การระบายน้ำทิ้งจากระบบบำบัดน้ำเสีย ระบบที่ 1 = 1,465.10
- (๕) ปริมาณสารเคมีหรือสารสกัดชีวภาพที่ใช้ (ลิตรหรือกิโลกรัม) 0.24
- (๖) การทำงานของระบบบำบัดน้ำเสียและอุปกรณ์
- ระบบบำบัดน้ำเสีย ☒ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องสูบน้ำ ☒ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องเติมอากาศ ☒ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องกวน/ผสมน้ำเสีย ☐ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องกวน/ผสมสารเคมี ☐ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องสูบละกอน ☒ ปกติ ☐ ผิดปกติ (ระบุ)
 - อื่นๆ ☐ ปกติ ☐ ผิดปกติ (ระบุ)
- (๗) ปริมาณตะกอนส่วนเกินจากระบบบำบัดน้ำเสียที่นำไปกำจัด (ลบ.ม.)
- (๘) ปัญหา อุปสรรค และแนวทางแก้ไข -


- คำเตือน ๑. เจ้าของหรือผู้ครอบครองแหล่งกำเนิดมลพิษ ผู้ควบคุมระบบบำบัดน้ำเสีย หรือผู้รับจ้างให้บริการบำบัดน้ำเสียผู้ใดไม่จัดเก็บสถิติข้อมูล หรือไม่ทำบันทึกหรือรายงานตามมาตรา ๘๐ ต้องระวางโทษจำคุกไม่เกินหนึ่งเดือน หรือปรับไม่เกินหนึ่งหมื่นบาทหรือทั้งจำทั้งปรับตามมาตรา ๑๐๖
๒. ผู้ควบคุมระบบบำบัดน้ำเสียหรือผู้รับจ้างให้บริการบำบัดน้ำเสียผู้ใดทำบันทึกหรือรายงานโดยแสดงข้อความอันเป็นเท็จต้องระวางโทษจำคุกไม่เกินหนึ่งปี หรือปรับไม่เกินหนึ่งแสนบาท หรือทั้งจำทั้งปรับตามมาตรา ๑๐๗

แบบบันทึกรายละเอียดของสถิติและข้อมูลซึ่งแสดงผลการทำงานของระบบบำบัดน้ำเสีย
ของแหล่งกำเนิดมลพิษ

แหล่งกำเนิดมลพิษตั้งอยู่เลขที่ 108 หมู่ที่ อาคารชุด ไอริส แอเวนิว อาคาร 5 ถนน
ลาดกระบัง เขต/ตำบล เขต/อำเภอ จังหวัด
กรุงเทพมหานคร โทรศัพท์ 0 2118 6162 โทรสาร โดยมี (นาย /นาง/
นางสาว) นางสาวทรรศวรรณ จุลเอี่ยม เป็นเจ้าของหรือผู้ครอบครองแหล่งกำเนิดมลพิษ
ประกอบกิจการประเภท (ข) อาคารสูง ประกอบด้วย 1 อาคาร จำนวน 253 ห้องชุด ใบอนุญาต
เลขที่ (ถ้ามี) 17/2556 ออกให้โดย หิมตอายุ
สำนักงานที่ดินกรุงเทพมหานคร สาขาเขตลาดกระบัง
ซึ่งมีแผนผังแสดงการทำงานของระบบบำบัดน้ำเสีย ดังนี้

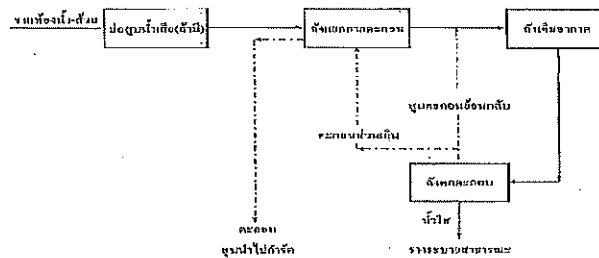

FLOW DIAGRAM FOR WASTEWATER TREATMENT PLANT

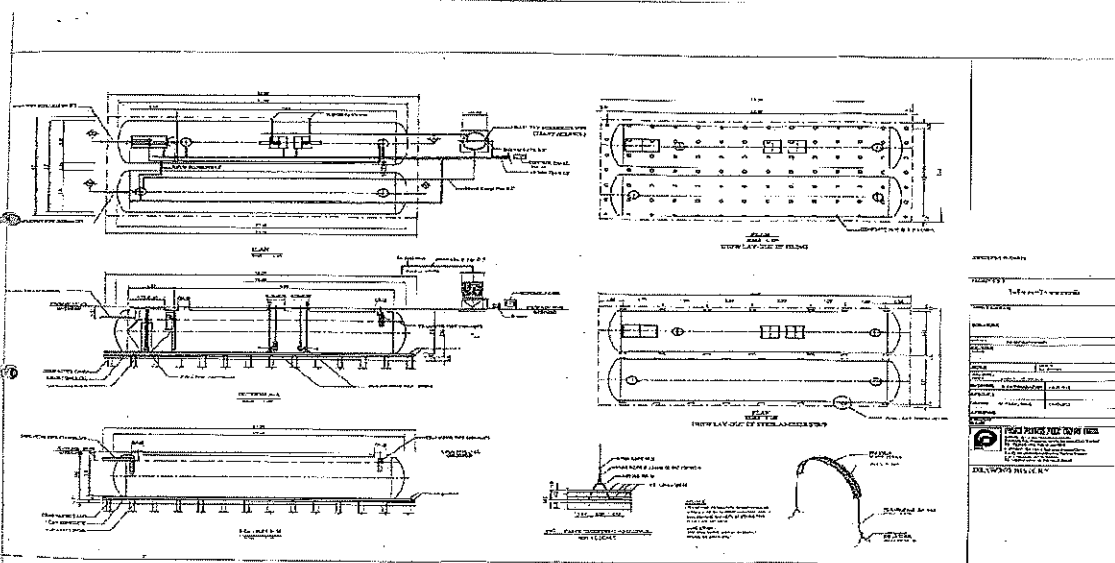

ได้จัดเก็บสถิติและข้อมูลแสดงผลการทำงานของระบบบำบัดน้ำเสียปรากฏตามตาราง ดังนี้

สถิติและข้อมูลที่เกิดขึ้นจากแหล่งกำเนิดมลพิษ														
วัน เดือน ปี	ปริมาณการใช้ไฟฟ้าของระบบบำบัดน้ำเสีย (หน่วย)	ปริมาณน้ำใช้ในทุกกิจกรรมแหล่งกำเนิดมลพิษ (ลบ.ม.)	ปริมาณเสียที่เข้าระบบบำบัดน้ำเสีย(ลบ.ม.)	การระบายน้ำทิ้งจากระบบบำบัดน้ำเสีย(ระบายน้ไม่ระบาย)	ปริมาณสารเคมีหรือสารสกัดชีวภาพที่ใช้ (ชื่อปริมาณ) (ลิตรหรือ กิโลกรัม)	การทำงานของระบบบำบัดน้ำเสีย							ปริมาณตะกอนส่วนเกินที่เกิดขึ้นจากระบบบำบัดน้ำเสียที่นำไปกำจัด (ลบ.ม.)	ปัญหาอุปสรรคและแนวทางแก้ไข
						ระบบบำบัดน้ำเสีย (ปกติ/ผิดปกติ)	เครื่องสูบน้ำ (ปกติ/ผิดปกติ)	เครื่องเติมอากาศ (ปกติ/ผิดปกติ)	เครื่องกรองกากมวลรวม/สารเคมี (ปกติ/ผิดปกติ)	เครื่องสูบลดทอน (ปกติ/ผิดปกติ)	อื่นๆ (ระบุ) (ปกติ/ผิดปกติ)			
														ลายมือชื่อผู้บันทึก
11/12/67	40	62	91.1	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
12/12/67	30	29	66.3	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
13/12/67	40	71	46.1	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
14/12/67	30	67	46.4	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
15/12/67	40	46	45.1	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
16/12/67	40	38	42.4	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
17/12/67	40	29	89.3	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
18/12/67	30	72	55.5	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
19/12/67	40	53	41.3	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
20/12/67	30	50	49.4	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
21/12/67	40	86	68.8	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา
22/12/67	30	69	54.1	ระบาย	0.00	ปกติ	ปกติ	-	-	ปกติ	-	-	-	เจษฎา

สถิติและข้อมูลที่เกี่ยวข้องกับจากแหล่งกำเนิดมลพิษ														
วัน เดือน ปี	ปริมาณการใช้ไฟฟ้าของระบบบำบัดน้ำเสีย (หน่วย)	ปริมาณน้ำใช้ ในทุกกิจกรรมของแหล่งกำเนิดมลพิษ (ลบ.ม.)	ปริมาณน้ำเสียที่เข้าระบบบำบัดน้ำเสีย (ลบ.ม.)	การระบายน้ำทิ้งจากระบบบำบัดน้ำเสีย (ระบาย/ไม่ระบาย)	ปริมาณสารเคมีหรือสารสกัดชีวภาพที่ใช้ (ชื่อ/ปริมาณ) (ลดหรือก็โลกรั้ม)	การทำงานของระบบบำบัดน้ำเสีย							ปริมาณตะกอนส่วนเกินที่เกิดขึ้นจากระบบบำบัดน้ำเสียที่นำไปกำจัด (ลบ.ม.)	ปัญหาอุปสรรคและแนวทางแก้ไข
						เครื่องสูบน้ำ (ปกติ/ผิดปกติ)	เครื่องเติมอากาศ (ปกติ/ผิดปกติ)	เครื่องกวน/ผสมน้ำเสีย (ปกติ/ผิดปกติ)	เครื่องกรอง (ปกติ/ผิดปกติ)	เครื่องสูบล้าง (ปกติ/ผิดปกติ)	เครื่องสูบล้าง (ปกติ/ผิดปกติ)	เครื่องสูบล้าง (ปกติ/ผิดปกติ)		
23/12/67	40	62	30.1	ระบาย	0.00	ปกติ	ปกติ	-	-	-	ปกติ	-	-	เจษฎา
24/12/67	30	29	55.1	ระบาย	0.00	ปกติ	ปกติ	-	-	-	ปกติ	-	-	เจษฎา
25/12/67	40	71	52.2	ระบาย	0.00	ปกติ	ปกติ	-	-	-	ปกติ	-	-	เจษฎา
26/12/67	30	67	40.5	ระบาย	0.00	ปกติ	ปกติ	-	-	-	ปกติ	-	-	เจษฎา
27/12/67	40	46	36.1	ระบาย	0.00	ปกติ	ปกติ	-	-	-	ปกติ	-	-	เจษฎา
28/12/67	40	38	43.4	ระบาย	0.00	ปกติ	ปกติ	-	-	-	ปกติ	-	-	เจษฎา
29/12/67	40	38	42.4	ระบาย	0.00	ปกติ	ปกติ	-	-	-	ปกติ	-	-	เจษฎา
30/12/67	30	36	29.3	ระบาย	0.00	ปกติ	ปกติ	-	-	-	ปกติ	-	-	เจษฎา
31/12/67	40	87	71.1	ระบาย	0.00	ปกติ	ปกติ	-	-	-	ปกติ	-	-	เจษฎา

- หมายเหตุ ๑.ให้กรอสถิติและข้อมูลเฉพาะในกรณีที่มีสถิติและข้อมูลนั้นๆ ในแต่ละวัน
 ๒.ในกรณีระบบบำบัดน้ำเสียที่มีการติดตั้งเครื่องตรวจวัดคุณภาพน้ำทิ้งแบบอัตโนมัติให้แนบผลการตรวจวัดคุณภาพน้ำทิ้งทุกวันแยกตามพารามิเตอร์ที่ตรวจวัด และทำการสรุปผลเป็นสถิติและข้อมูลรายเดือน

ขอรับรองว่าการบันทึกสถิติและข้อมูลตามตารางข้างต้นถูกต้องทุกประการ

.....
 ทวีพรพรรณ จุลเอี่ยม เจ้าของหรือผู้ครอบครองแหล่งกำเนิดมลพิษ
 (นางสาวทวีพรพรรณ จุลเอี่ยม)

.....ผู้ควบคุมระบบบำบัดน้ำเสีย
 (.....)

ใบอนุญาตเลขที่ หมดอายุ ออกให้โดย

.....ผู้รับจ้างให้บริการบำบัดน้ำเสีย
 (.....)

ใบอนุญาตเลขที่ หมดอายุ ออกให้โดย

รายงานสรุปผลการทำงานของระบบบำบัดน้ำเสีย

๑. ข้อมูลทั่วไป

แหล่งกำเนิดมลพิษตั้งอยู่เลขที่ 108 หมู่ที่ - ซอย - ถนน ลาดกระบัง แขวง/ตำบล
 ลาดกระบัง เขต/อำเภอ ลาดกระบัง จังหวัด กรุงเทพมหานคร โทรศัพท์ 0-2118 6162 โทรสาร -
 โดยมี (นาง/นาง/นางสาว) นางสาวทรรศวรรณ จุลเอี่ยม เป็นเจ้าของหรือผู้ครอบครอง
 แหล่งกำเนิดมลพิษ ประกอบกิจการประเภท (ข) อควารูด 1 อควารูด จำนวน 253 ห้องชุด ใบอนุญาต
 เลขที่ (ถ้ามี) 17/2556 ออกให้โดย หมดอายุ
 สำนักงานที่ดินกรุงเทพมหานคร สาขาลาดกระบัง

ในการนี้ขอรายงานสรุปผลการทำงานของระบบบำบัดน้ำเสียของแหล่งกำเนิดมลพิษสำหรับ
 เดือน ธันวาคม พ.ศ. 2568 ตามที่ได้กำหนดในมาตรา ๘๐ แห่งพระราชบัญญัติส่งเสริมและรักษา
 คุณภาพสิ่งแวดล้อมแห่งชาติ พ.ศ. ๒๕๓๕ ในฐานะ

ทรรศวรรณ จุลเอี่ยม
 เจ้าของหรือผู้ครอบครองแหล่งกำเนิดมลพิษ
 (นางสาวทรรศวรรณ จุลเอี่ยม)

..... ผู้ควบคุมระบบบำบัดน้ำเสีย
 (.....)

ใบอนุญาตเลขที่ หมดอายุ ออกให้โดย

..... ผู้รับจ้างให้บริการบำบัดน้ำเสีย
 (.....)

ใบอนุญาตเลขที่ หมดอายุ ออกให้โดย

๒. ข้อมูลเกี่ยวกับระบบบำบัดน้ำเสีย และแหล่งรองรับน้ำทิ้ง

(๑) ประเภท/ชนิดของระบบบำบัดน้ำเสีย ระบบที่ 1 ชีวภาพผสม (Combined Bio-Treatment)

ความสามารถในการรองรับน้ำเสียของระบบบำบัดน้ำเสีย ระบบที่ 1 = 200 ลบ.ม./วัน

(๒) การทำงานของระบบบำบัดน้ำเสีย ☒ แบบต่อเนื่องระบบที่ 1=24 ชั่วโมง/วัน

☐ แบบไม่ต่อเนื่อง (ระบุ)

(๓) อุปกรณ์และเครื่องมือที่ใช้ในระบบบำบัดน้ำเสีย ☒ เครื่องสูบน้ำ ☒ เครื่องเติมอากาศ

☐ เครื่องกวนผสมน้ำเสีย ☐ เครื่องกวนผสมสารเคมี ☒ เครื่องสูบละกอน ☐ อื่น ๆ (ระบุ)

(๔) แหล่งรองรับน้ำทิ้ง (ระบุ) ท่อสาธารณะกรุงเทพมหานคร บริเวณด้านหน้าถนนลาดกระบัง

(๕) วิธีจัดการตะกอนที่เกิดขึ้นจากระบบบำบัดน้ำเสียและวิธีการกำจัด

ระบบที่ 1 จ้างรถสูบละกอนไปทิ้งยังระบบกำจัดตะกอนไปทิ้ง

๓. สรุปผลการทำงานของระบบบำบัดน้ำเสียเป็นรายเดือน

- (๑) ปริมาณการใช้ไฟฟ้าของระบบบำบัดน้ำเสีย (หน่วย) ระบบที่ 1 = 1,210.00
- (๒) ปริมาณน้ำใช้ทุกกิจกรรมในแหล่งกำเนิดมลพิษ (ลบ.ม.) ระบบที่ 1 = 1,331.20
- (๓) ปริมาณน้ำเสียที่เข้าระบบบำบัดน้ำเสีย (ลบ.ม.) ระบบที่ 1 = 1,554.50
- (๔) การระบายน้ำทิ้งจากระบบบำบัดน้ำเสีย ระบบที่ 1 = 1,554.50
- (๕) ปริมาณสารเคมีหรือสารสกัดชีวภาพที่ใช้ (ลิตรหรือกิโลกรัม) 0.24
- (๖) การทำงานของระบบบำบัดน้ำเสียและอุปกรณ์
- ระบบบำบัดน้ำเสีย ☒ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องสูบน้ำ ☒ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องเติมอากาศ ☒ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องกวนผสมน้ำเสีย ☐ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องกวนผสมสารเคมี ☐ ปกติ ☐ ผิดปกติ (ระบุ)
 - เครื่องสูบลตะกอน ☒ ปกติ ☐ ผิดปกติ (ระบุ)
 - อื่นๆ ☐ ปกติ ☐ ผิดปกติ (ระบุ)
- (๗) ปริมาณตะกอนส่วนเกินจากระบบบำบัดน้ำเสียที่นำไปกำจัด (ลบ.ม.)
- (๘) ปัญหา อุปสรรค และแนวทางแก้ไข

- คำเตือน ๑. เจ้าของหรือผู้ครอบครองแหล่งกำเนิดมลพิษ ผู้ควบคุมระบบบำบัดน้ำเสีย หรือผู้รับจ้างให้บริการบำบัดน้ำเสียผู้ใดไม่จัดเก็บสถิติข้อมูล หรือไม่ทำบันทึกหรือรายงานตามมาตรา ๘๐ ต้องระวางโทษจำคุกไม่เกินหนึ่งเดือน หรือปรับไม่เกินหนึ่งหมื่นบาทหรือทั้งจำทั้งปรับตามมาตรา ๑๐๖
๒. ผู้ควบคุมระบบบำบัดน้ำเสียหรือผู้รับจ้างให้บริการบำบัดน้ำเสียผู้ใดทำบันทึกหรือรายงานโดยแสดงข้อความอันเป็นเท็จต้องระวางโทษจำคุกไม่เกินหนึ่งปี หรือปรับไม่เกินหนึ่งแสนบาท หรือทั้งจำทั้งปรับตามมาตรา ๑๐๗

ภาคผนวก ๒

เอกสารตรวจเช็คระบบป้องกันอัคคีภัย และเตือนภัย

ใบตรวจเช็คตู้จ่ายไฟหลัก MDB

Date 3/09/16

MDB (Main Distribution Board)

	Description	Time		Description	Time
		09.00 H.			
Tower2	Voltage Phase R (Volt)	398.2		Voltage Phase R (Volt)	392.0
	Voltage Phase S (Volt)	396.0		Voltage Phase S (Volt)	398.6
	Voltage Phase T (Volt)	392.6		Voltage Phase T (Volt)	392.2
	Current Phase R (Amp)	42.08		Current Phase R (Amp)	26.24
	Current Phase S (Amp)	46.12		Current Phase S (Amp)	62.88
	Current Phase T (Amp)	68.02		Current Phase T (Amp)	58.64
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.68		Energy (kw)	46.88
	PF	0.98		PF	0.98
	Kwh	60999/6		Kwh	61023/6
	Recorded by	8.		Recorded by	8.
Tower3	Voltage Phase R (Volt)	396.4		Voltage Phase R (Volt)	398.3
	Voltage Phase S (Volt)	392.6		Voltage Phase S (Volt)	396.9
	Voltage Phase T (Volt)	399.3		Voltage Phase T (Volt)	398.1
	Current Phase R (Amp)	68.06		Current Phase R (Amp)	72.96
	Current Phase S (Amp)	52.24		Current Phase S (Amp)	68.48
	Current Phase T (Amp)	48.30		Current Phase T (Amp)	62.10
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.96		Energy (kw)	42.66
	PF	0.98		PF	0.98
	Kwh	2942		Kwh	4228142
	Recorded by	8.		Recorded by	8.
Tower4	Voltage Phase R (Volt)	398.2		Voltage Phase R (Volt)	392.0
	Voltage Phase S (Volt)	396.0		Voltage Phase S (Volt)	398.6
	Voltage Phase T (Volt)	392.6		Voltage Phase T (Volt)	392.2
	Current Phase R (Amp)	42.08		Current Phase R (Amp)	26.24
	Current Phase S (Amp)	46.12		Current Phase S (Amp)	62.88
	Current Phase T (Amp)	68.02		Current Phase T (Amp)	58.64
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.68		Energy (kw)	46.88
	PF	0.98		PF	0.98
	Kwh	60999/6		Kwh	61023/6
	Recorded by	8.		Recorded by	8.
Tower5	Voltage Phase R (Volt)	396.4		Voltage Phase R (Volt)	398.3
	Voltage Phase S (Volt)	392.6		Voltage Phase S (Volt)	396.9
	Voltage Phase T (Volt)	399.3		Voltage Phase T (Volt)	398.1
	Current Phase R (Amp)	68.06		Current Phase R (Amp)	72.96
	Current Phase S (Amp)	52.24		Current Phase S (Amp)	68.48
	Current Phase T (Amp)	48.30		Current Phase T (Amp)	62.10
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.96		Energy (kw)	42.66
	PF	0.98		PF	0.98
	Kwh	2942		Kwh	4228142
	Recorded by	8.		Recorded by	8.

Remark =

Date 10/06/18

MDB (Main Distribution Board)

	Description	Time		Description	Time
		09.00 u.			09.00 u.
Tower2	Voltage Phase R (Volt)	396.2	Tower4	Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	398.1		Voltage Phase S (Volt)	396.4
	Voltage Phase T (Volt)	399.2		Voltage Phase T (Volt)	399.2
	Current Phase R (Amp)	68.26		Current Phase R (Amp)	96.22
	Current Phase S (Amp)	54.12		Current Phase S (Amp)	86.40
	Current Phase T (Amp)	60.11		Current Phase T (Amp)	61.12
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.93		Energy (kw)	42.66
	PF	0.98		PF	0.98
	Kwh	611485		Kwh	611389
	Recorded by	8		Recorded by	8
Tower3	Voltage Phase R (Volt)	392.5	Tower5	Voltage Phase R (Volt)	396.0
	Voltage Phase S (Volt)	398.1		Voltage Phase S (Volt)	398.4
	Voltage Phase T (Volt)	396.4		Voltage Phase T (Volt)	399.9
	Current Phase R (Amp)	62.96		Current Phase R (Amp)	86.29
	Current Phase S (Amp)	38.42		Current Phase S (Amp)	98.42
	Current Phase T (Amp)	51.02		Current Phase T (Amp)	56.12
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.92		Energy (kw)	42.29
	PF	0.98		PF	0.98
	Kwh	3002		Kwh	1240068
	Recorded by	8		Recorded by	8

Remark =

.....

Date 12/01/18

MDB (Main Distribution Board)

	Description	Time	Tower4	Description	Time
Tower2	Voltage Phase R (Volt)	09.00 H.	Tower4	Voltage Phase R (Volt)	09.00 H.
	Voltage Phase S (Volt)	396.2		Voltage Phase S (Volt)	398.1
	Voltage Phase T (Volt)	392.1		Voltage Phase T (Volt)	396.0
	Current Phase R (Amp)	396.8		Current Phase R (Amp)	399.4
	Current Phase S (Amp)	36.92		Current Phase S (Amp)	101.98
	Current Phase T (Amp)	58.44		Current Phase T (Amp)	68.12
	Frequency (49.5 - 50.5 Hz)	66.52		Frequency (49.5 - 50.5 Hz)	62.94
	Energy (kw)	60.00		Energy (kw)	50.00
	PF	62.98		PF	62.96
	Kwh	0.98		Kwh	2.98
Tower3	Recorded by	6195468	Tower5	Recorded by	6125668
		8			8
	Voltage Phase R (Volt)	398.2		Voltage Phase R (Volt)	390.6
	Voltage Phase S (Volt)	398.0		Voltage Phase S (Volt)	392.2
	Voltage Phase T (Volt)	396.4		Voltage Phase T (Volt)	396.4
	Current Phase R (Amp)	32.96		Current Phase R (Amp)	32.98
	Current Phase S (Amp)	48.19		Current Phase S (Amp)	41.11
	Current Phase T (Amp)	52.08		Current Phase T (Amp)	68.93
	Frequency (49.5 - 50.5 Hz)	60.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	62.66		Energy (kw)	62.96
Tower5	PF	0.98		PF	0.98
	Kwh	3054		Kwh	1261810
	Recorded by	8		Recorded by	8

Remark =

Date 24/02/2016

MDB (Main Distribution Board)

	Description	Time	Tower	Description	Time
Tower2	Voltage Phase R (Volt)	09.00 H.	Tower4	Voltage Phase R (Volt)	09.00 H.
	Voltage Phase S (Volt)	396.4		Voltage Phase S (Volt)	396.2
	Voltage Phase T (Volt)	398.2		Voltage Phase T (Volt)	398.0
	Current Phase R (Amp)	399.0		Current Phase R (Amp)	395.6
	Current Phase S (Amp)	68.26		Current Phase S (Amp)	92.68
	Current Phase T (Amp)	66.93		Current Phase T (Amp)	68.32
	Frequency (49.5 - 50.5 Hz)	38.46		Frequency (49.5 - 50.5 Hz)	42.42
	Energy (kw)	60.00		Energy (kw)	60.00
	PF	62.66		PF	62.96
	Kwh	0.98		Kwh	0.98
Tower3	Recorded by	6136786	Tower5	Recorded by	6137120
	Voltage Phase R (Volt)	8		Voltage Phase R (Volt)	8
	Voltage Phase S (Volt)	394.1		Voltage Phase S (Volt)	398.2
	Voltage Phase T (Volt)	396.2		Voltage Phase T (Volt)	398.0
	Current Phase R (Amp)	396.8		Current Phase R (Amp)	396.1
	Current Phase S (Amp)	86.98		Current Phase S (Amp)	68.29
	Current Phase T (Amp)	52.48		Current Phase T (Amp)	48.10
	Frequency (49.5 - 50.5 Hz)	60.12		Frequency (49.5 - 50.5 Hz)	60.28
	Energy (kw)	60.00		Energy (kw)	60.00
	PF	62.68		PF	62.96
Tower5	Kwh	0.98		Kwh	0.98
	Recorded by	3992		Recorded by	1263616
		8			8

Remark =

MDB (Main Distribution Board)

Date 15.01.2016

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	396.2	09.00 u.	Voltage Phase R (Volt)	396.0
	Voltage Phase S (Volt)	397.0		Voltage Phase S (Volt)	398.6
	Voltage Phase T (Volt)	397.8		Voltage Phase T (Volt)	397.2
	Current Phase R (Amp)	92.68		Current Phase R (Amp)	98.26
	Current Phase S (Amp)	98.32		Current Phase S (Amp)	68.25
	Current Phase T (Amp)	58.06		Current Phase T (Amp)	96.15
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.82		Energy (kw)	42.92
	PF	0.98		PF	0.98
	Kwh	6148524		Kwh	6148789
Tower3	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	394.2		Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	396.8		Voltage Phase S (Volt)	396.1
	Voltage Phase T (Volt)	397.0		Voltage Phase T (Volt)	398.9
	Current Phase R (Amp)	66.26		Current Phase R (Amp)	66.52
	Current Phase S (Amp)	54.98		Current Phase S (Amp)	50.66
	Current Phase T (Amp)	46.38		Current Phase T (Amp)	48.32
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.69		Energy (kw)	42.92
	PF	0.98		PF	0.98
Tower4	Kwh	5182		Kwh	1225508
	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	394.2		Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	396.8		Voltage Phase S (Volt)	396.1
	Voltage Phase T (Volt)	397.0		Voltage Phase T (Volt)	398.9
	Current Phase R (Amp)	66.26		Current Phase R (Amp)	66.52
	Current Phase S (Amp)	54.98		Current Phase S (Amp)	50.66
	Current Phase T (Amp)	46.38		Current Phase T (Amp)	48.32
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.69		Energy (kw)	42.92
Tower5	PF	0.98		PF	0.98
	Kwh	5182		Kwh	1225508
	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	394.2		Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	396.8		Voltage Phase S (Volt)	396.1
	Voltage Phase T (Volt)	397.0		Voltage Phase T (Volt)	398.9
	Current Phase R (Amp)	66.26		Current Phase R (Amp)	66.52
	Current Phase S (Amp)	54.98		Current Phase S (Amp)	50.66
	Current Phase T (Amp)	46.38		Current Phase T (Amp)	48.32
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
Tower6	Energy (kw)	42.69		Energy (kw)	42.92
	PF	0.98		PF	0.98
	Kwh	5182		Kwh	1225508
	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	394.2		Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	396.8		Voltage Phase S (Volt)	396.1
	Voltage Phase T (Volt)	397.0		Voltage Phase T (Volt)	398.9
	Current Phase R (Amp)	66.26		Current Phase R (Amp)	66.52
	Current Phase S (Amp)	54.98		Current Phase S (Amp)	50.66
	Current Phase T (Amp)	46.38		Current Phase T (Amp)	48.32

Remark =

Date 2008/08/16

MDB (Main Distribution Board)

	Description	Time	Tower	Description	Time
Tower2	Voltage Phase R (Volt)	396.2	Tower4	Voltage Phase R (Volt)	396.2
	Voltage Phase S (Volt)	398.4		Voltage Phase S (Volt)	398.0
	Voltage Phase T (Volt)	399.0		Voltage Phase T (Volt)	392.4
	Current Phase R (Amp)	39.06		Current Phase R (Amp)	36.24
	Current Phase S (Amp)	39.18		Current Phase S (Amp)	38.12
	Current Phase T (Amp)	38.92		Current Phase T (Amp)	36.14
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.66		Energy (kw)	42.69
	PF	0.98		PF	0.99
	Kwh	616020.7		Kwh	616062.1
Tower3	Recorded by	8	Tower5	Recorded by	8
	Voltage Phase R (Volt)	392.6		Voltage Phase R (Volt)	399.1
	Voltage Phase S (Volt)	398.1		Voltage Phase S (Volt)	398.2
	Voltage Phase T (Volt)	396.2		Voltage Phase T (Volt)	399.4
	Current Phase R (Amp)	30.21		Current Phase R (Amp)	32.92
	Current Phase S (Amp)	62.36		Current Phase S (Amp)	68.44
	Current Phase T (Amp)	58.16		Current Phase T (Amp)	65.02
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.92		Energy (kw)	42.68
	PF	0.98		PF	0.98
Tower4	Kwh	3225	Tower5	Kwh	1288400
	Recorded by	8		Recorded by	8
	Remark =			Remark =	

MDB (Main Distribution Board)

Date 15/09/18

Tower2		Tower4		Tower5	
Description		Time		Description	
Voltage Phase R (Volt)		09.00 u.		Voltage Phase R (Volt)	
Voltage Phase S (Volt)		398.2		Voltage Phase S (Volt)	
Voltage Phase T (Volt)		398.0		Voltage Phase T (Volt)	
Current Phase R (Amp)		399.6		Current Phase R (Amp)	
Current Phase S (Amp)		62.24		Current Phase S (Amp)	
Current Phase T (Amp)		58.42		Current Phase T (Amp)	
Frequency (49.5 - 50.5 Hz)		66.30		Frequency (49.5 - 50.5 Hz)	
Energy (kw)		50.00		Energy (kw)	
PF		42.96		PF	
Kwh		0.98		Kwh	
Recorded by		6182149		Recorded by	
		8			
Tower3		Tower5		Tower5	
Voltage Phase R (Volt)		30160		Voltage Phase R (Volt)	
Voltage Phase S (Volt)		3019.2		Voltage Phase S (Volt)	
Voltage Phase T (Volt)		3019.8		Voltage Phase T (Volt)	
Current Phase R (Amp)		68.32		Current Phase R (Amp)	
Current Phase S (Amp)		59.61		Current Phase S (Amp)	
Current Phase T (Amp)		61.12		Current Phase T (Amp)	
Frequency (49.5 - 50.5 Hz)		50.00		Frequency (49.5 - 50.5 Hz)	
Energy (kw)		42.62		Energy (kw)	
PF		0.98		PF	
Kwh		3289		Kwh	
Recorded by		8		Recorded by	
Time		09.00 u.		Time	
Voltage Phase R (Volt)		398.2		Voltage Phase R (Volt)	
Voltage Phase S (Volt)		398.1		Voltage Phase S (Volt)	
Voltage Phase T (Volt)		399.6		Voltage Phase T (Volt)	
Current Phase R (Amp)		100.92		Current Phase R (Amp)	
Current Phase S (Amp)		68.55		Current Phase S (Amp)	
Current Phase T (Amp)		84.16		Current Phase T (Amp)	
Frequency (49.5 - 50.5 Hz)		50.00		Frequency (49.5 - 50.5 Hz)	
Energy (kw)		42.92		Energy (kw)	
PF		0.98		PF	
Kwh		6182149		Kwh	
Recorded by		8		Recorded by	

Remark =

.....

MDB (Main Distribution Board)

Date 22/08/16

Tower2	Description	Time		Tower4	Description	Time	
			09.00 H.				09.00 H.
Tower2	Voltage Phase R (Volt)		396.8	Tower4	Voltage Phase R (Volt)		398.0
	Voltage Phase S (Volt)		398.0		Voltage Phase S (Volt)		399.6
	Voltage Phase T (Volt)		396.8		Voltage Phase T (Volt)		390.8
	Current Phase R (Amp)		92.95		Current Phase R (Amp)		98.11
	Current Phase S (Amp)		98.12		Current Phase S (Amp)		96.18
	Current Phase T (Amp)		60.35		Current Phase T (Amp)		68.32
	Frequency (49.5 - 50.5 Hz)		50.00		Frequency (49.5 - 50.5 Hz)		50.00
	Energy (kw)		62.96		Energy (kw)		122.90
	PF		0.98		PF		0.98
	Kwh		6184095		Kwh		6184449
Tower3	Recorded by		8	Tower5	Recorded by		8
	Voltage Phase R (Volt)		396.8		Voltage Phase R (Volt)		396.1
	Voltage Phase S (Volt)		398.0		Voltage Phase S (Volt)		396.8
	Voltage Phase T (Volt)		399.2		Voltage Phase T (Volt)		397.5
	Current Phase R (Amp)		92.95		Current Phase R (Amp)		92.68
	Current Phase S (Amp)		60.10		Current Phase S (Amp)		61.12
	Current Phase T (Amp)		58.11		Current Phase T (Amp)		59.11
	Frequency (49.5 - 50.5 Hz)		50.00		Frequency (49.5 - 50.5 Hz)		50.00
	Energy (kw)		62.92		Energy (kw)		42.98
	PF		0.98		PF		0.98
Tower5	Kwh		3548		Kwh		131192
	Recorded by		8		Recorded by		8

Remark =

Date 29/08/2016

MDB (Main Distribution Board)

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	396.5	09.00 H.	Voltage Phase R (Volt)	09.00 H.
	Voltage Phase S (Volt)	397.1		Voltage Phase S (Volt)	396.8
	Voltage Phase T (Volt)	397.0		Voltage Phase T (Volt)	397.2
	Current Phase R (Amp)	32.11		Current Phase R (Amp)	38.90
	Current Phase S (Amp)	68.20		Current Phase S (Amp)	62.16
	Current Phase T (Amp)	52.16		Current Phase T (Amp)	58.44
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.92		Energy (kw)	42.99
	PF	0.98		PF	0.98
	Kwh	619656		Kwh	6196214
Tower3	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	390.6		Voltage Phase R (Volt)	396.8
	Voltage Phase S (Volt)	396.8		Voltage Phase S (Volt)	396.8
	Voltage Phase T (Volt)	397.1		Voltage Phase T (Volt)	397.4
	Current Phase R (Amp)	96.54		Current Phase R (Amp)	43.06
	Current Phase S (Amp)	32.16		Current Phase S (Amp)	58.44
	Current Phase T (Amp)	60.11		Current Phase T (Amp)	62.82
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.99		Energy (kw)	42.96
	PF	0.98		PF	0.98
Tower4	Kwh	3406		Kwh	1323020
	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	390.6		Voltage Phase R (Volt)	396.8
	Voltage Phase S (Volt)	396.8		Voltage Phase S (Volt)	396.8
	Voltage Phase T (Volt)	397.1		Voltage Phase T (Volt)	397.4
	Current Phase R (Amp)	96.54		Current Phase R (Amp)	43.06
	Current Phase S (Amp)	32.16		Current Phase S (Amp)	58.44
	Current Phase T (Amp)	60.11		Current Phase T (Amp)	62.82
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.99		Energy (kw)	42.96
Tower5	PF	0.98		PF	0.98
	Kwh	3406		Kwh	1323020
	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	390.6		Voltage Phase R (Volt)	396.8
	Voltage Phase S (Volt)	396.8		Voltage Phase S (Volt)	396.8
	Voltage Phase T (Volt)	397.1		Voltage Phase T (Volt)	397.4
	Current Phase R (Amp)	96.54		Current Phase R (Amp)	43.06
	Current Phase S (Amp)	32.16		Current Phase S (Amp)	58.44
	Current Phase T (Amp)	60.11		Current Phase T (Amp)	62.82
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
Tower5	Energy (kw)	42.99		Energy (kw)	42.96
	PF	0.98		PF	0.98
	Kwh	3406		Kwh	1323020
	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	390.6		Voltage Phase R (Volt)	396.8
	Voltage Phase S (Volt)	396.8		Voltage Phase S (Volt)	396.8
	Voltage Phase T (Volt)	397.1		Voltage Phase T (Volt)	397.4
	Current Phase R (Amp)	96.54		Current Phase R (Amp)	43.06
	Current Phase S (Amp)	32.16		Current Phase S (Amp)	58.44
	Current Phase T (Amp)	60.11		Current Phase T (Amp)	62.82

Remark =

MDB (Main Distribution Board)

Date 09/09/2016

Tower2	Description	Time	Tower4	Description	Time
Tower2	Voltage Phase R (Volt)	398.2	Tower4	Voltage Phase R (Volt)	398.1
	Voltage Phase S (Volt)	396.0		Voltage Phase S (Volt)	396.0
	Voltage Phase T (Volt)	390.6		Voltage Phase T (Volt)	396.3
	Current Phase R (Amp)	82.92		Current Phase R (Amp)	89.40
	Current Phase S (Amp)	58.16		Current Phase S (Amp)	41.12
	Current Phase T (Amp)	60.10		Current Phase T (Amp)	58.92
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.62		Energy (kw)	42.46
	PF	0.98		PF	0.98
	Kwh	6208488		Kwh	6208062
Tower3	Recorded by	8	Tower5	Recorded by	8
	Voltage Phase R (Volt)	396.2		Voltage Phase R (Volt)	396.1
	Voltage Phase S (Volt)	398.4		Voltage Phase S (Volt)	398.2
	Voltage Phase T (Volt)	399.1		Voltage Phase T (Volt)	399.1
	Current Phase R (Amp)	66.09		Current Phase R (Amp)	72.98
	Current Phase S (Amp)	68.92		Current Phase S (Amp)	60.10
	Current Phase T (Amp)	54.12		Current Phase T (Amp)	59.46
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.92		Energy (kw)	42.96
	PF	0.98		PF	0.98
Tower3	Kwh	3467	Tower5	Kwh	1334868
	Recorded by	8		Recorded by	8

Remark =

Date 01/02/2016

MDB (Main Distribution Board)

	Description	Time	Tower4	Description	Time
		09.00 H.			09.00 H.
Tower2	Voltage Phase R (Volt)	378.0	Tower4	Voltage Phase R (Volt)	396.2
	Voltage Phase S (Volt)	379.6		Voltage Phase S (Volt)	392.8
	Voltage Phase T (Volt)	374.8		Voltage Phase T (Volt)	399.9
	Current Phase R (Amp)	67.52		Current Phase R (Amp)	72.72
	Current Phase S (Amp)	56.12		Current Phase S (Amp)	86.54
	Current Phase T (Amp)	68.79		Current Phase T (Amp)	65.92
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.76		Energy (kw)	42.96
	PF	0.98		PF	0.98
	Kwh	6220236		Kwh	6217558
	Recorded by	8	Recorded by	8	
Tower3	Voltage Phase R (Volt)	396.1	Tower5	Voltage Phase R (Volt)	398.1
	Voltage Phase S (Volt)	394.2		Voltage Phase S (Volt)	396.8
	Voltage Phase T (Volt)	396.6		Voltage Phase T (Volt)	396.2
	Current Phase R (Amp)	68.69		Current Phase R (Amp)	62.98
	Current Phase S (Amp)	69.88		Current Phase S (Amp)	60.28
	Current Phase T (Amp)	52.92		Current Phase T (Amp)	62.00
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.96		Energy (kw)	42.98
	PF	0.98		PF	0.98
	Kwh	3526		Kwh	1346814
	Recorded by	8	Recorded by	8	

Remark =

Date 18/02/2018

MDB (Main Distribution Board)

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	398.2	09.00 u.	Voltage Phase R (Volt)	398.4
	Voltage Phase S (Volt)	398.0		Voltage Phase S (Volt)	398.2
	Voltage Phase T (Volt)	399.2		Voltage Phase T (Volt)	391.6
	Current Phase R (Amp)	48.03		Current Phase R (Amp)	47.86
	Current Phase S (Amp)	46.22		Current Phase S (Amp)	62.41
	Current Phase T (Amp)	60.11		Current Phase T (Amp)	58.83
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.96		Energy (kw)	42.96
	PF	0.98		PF	0.98
	Kwh	6832089		Kwh	6234006
Tower3	Recorded by	H		Recorded by	H
	Voltage Phase R (Volt)	398.7		Voltage Phase R (Volt)	396.2
	Voltage Phase S (Volt)	396.0		Voltage Phase S (Volt)	392.1
	Voltage Phase T (Volt)	398.9		Voltage Phase T (Volt)	399.3
	Current Phase R (Amp)	62.36		Current Phase R (Amp)	88.29
	Current Phase S (Amp)	48.92		Current Phase S (Amp)	62.14
	Current Phase T (Amp)	41.12		Current Phase T (Amp)	58.06
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.96		Energy (kw)	42.92
	PF	0.98		PF	0.98
Tower5	Kwh	3588		Kwh	1358610
	Recorded by	H		Recorded by	H
	Voltage Phase R (Volt)	398.7		Voltage Phase R (Volt)	396.2
	Voltage Phase S (Volt)	396.0		Voltage Phase S (Volt)	392.1
	Voltage Phase T (Volt)	398.9		Voltage Phase T (Volt)	399.3
	Current Phase R (Amp)	62.36		Current Phase R (Amp)	88.29
	Current Phase S (Amp)	48.92		Current Phase S (Amp)	62.14
	Current Phase T (Amp)	41.12		Current Phase T (Amp)	58.06
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.96		Energy (kw)	42.92
	PF	0.98		PF	0.98
	Kwh	3588		Kwh	1358610
	Recorded by	H		Recorded by	H

Remark =

Date 26/09/16

MDB (Main Distribution Board)

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	2974.1	09.00 u.	Voltage Phase R (Volt)	2976.8
	Voltage Phase S (Volt)	2976.8		Voltage Phase S (Volt)	2979.0
	Voltage Phase T (Volt)	2972.4		Voltage Phase T (Volt)	2978.2
	Current Phase R (Amp)	26.41		Current Phase R (Amp)	26.16
	Current Phase S (Amp)	27.27		Current Phase S (Amp)	27.02
	Current Phase T (Amp)	22.17		Current Phase T (Amp)	22.32
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.96		Energy (kw)	42.96
	PF	0.98		PF	0.98
	Kwh	6243850		Kwh	6243183
Tower3	Recorded by			Recorded by	
	Voltage Phase R (Volt)	2976.2		Voltage Phase R (Volt)	2978.2
	Voltage Phase S (Volt)	2978.4		Voltage Phase S (Volt)	2979.0
	Voltage Phase T (Volt)	2978.2		Voltage Phase T (Volt)	2976.2
	Current Phase R (Amp)	22.98		Current Phase R (Amp)	22.16
	Current Phase S (Amp)	28.16		Current Phase S (Amp)	28.92
	Current Phase T (Amp)	29.32		Current Phase T (Amp)	26.32
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.00		Energy (kw)	42.92
	PF	0.98		PF	0.98
Tower4	Kwh	3646		Kwh	1390462
	Recorded by			Recorded by	
	Voltage Phase R (Volt)	2976.2		Voltage Phase R (Volt)	2978.2
	Voltage Phase S (Volt)	2978.4		Voltage Phase S (Volt)	2979.0
	Voltage Phase T (Volt)	2978.2		Voltage Phase T (Volt)	2976.2
	Current Phase R (Amp)	22.98		Current Phase R (Amp)	22.16
	Current Phase S (Amp)	28.16		Current Phase S (Amp)	28.92
	Current Phase T (Amp)	29.32		Current Phase T (Amp)	26.32
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.00		Energy (kw)	42.92
Tower5	PF	0.98		PF	0.98
	Kwh	3646		Kwh	1390462
	Recorded by			Recorded by	
	Voltage Phase R (Volt)	2976.2		Voltage Phase R (Volt)	2978.2
	Voltage Phase S (Volt)	2978.4		Voltage Phase S (Volt)	2979.0
	Voltage Phase T (Volt)	2978.2		Voltage Phase T (Volt)	2976.2
	Current Phase R (Amp)	22.98		Current Phase R (Amp)	22.16
	Current Phase S (Amp)	28.16		Current Phase S (Amp)	28.92
	Current Phase T (Amp)	29.32		Current Phase T (Amp)	26.32
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00

Remark =

Date 20/01/2018

MDB (Main Distribution Board)

Tower2	Description	Time		Tower4	Description	Time	
		09.00 H.				09.00 H.	
Tower2	Voltage Phase R (Volt)	396.2		Tower4	Voltage Phase R (Volt)	396.0	
	Voltage Phase S (Volt)	398.3			Voltage Phase S (Volt)	399.8	
	Voltage Phase T (Volt)	399.6			Voltage Phase T (Volt)	399.2	
	Current Phase R (Amp)	86.32			Current Phase R (Amp)	87.58	
	Current Phase S (Amp)	89.30			Current Phase S (Amp)	62.16	
	Current Phase T (Amp)	46.92			Current Phase T (Amp)	38.11	
	Frequency (49.5 - 50.5 Hz)	50.00			Frequency (49.5 - 50.5 Hz)	50.00	
	Energy (kw)	42.92			Energy (kw)	42.92	
	PF	0.98			PF	0.98	
	Kwh	625569			Kwh	625569	
Tower3	Recorded by	8		Tower5	Recorded by	8	
	Voltage Phase R (Volt)	398.2			Voltage Phase R (Volt)	399.0	
	Voltage Phase S (Volt)	396.0			Voltage Phase S (Volt)	398.0	
	Voltage Phase T (Volt)	394.8			Voltage Phase T (Volt)	396.5	
	Current Phase R (Amp)	61.13			Current Phase R (Amp)	92.93	
	Current Phase S (Amp)	87.25			Current Phase S (Amp)	64.30	
	Current Phase T (Amp)	68.11			Current Phase T (Amp)	58.62	
	Frequency (49.5 - 50.5 Hz)	50.00			Frequency (49.5 - 50.5 Hz)	50.00	
	Energy (kw)	42.96			Energy (kw)	42.96	
	PF	0.98			PF	0.98	
Tower4	Kwh	3698		Tower5	Kwh	1382298	
	Recorded by	8			Recorded by	8	

Remark =

MDB (Main Distribution Board)

Date 09/01/2016

	Description	Time	Tower4	Description	Time
		09.00 u.			09.00 u.
Tower2	Voltage Phase R (Volt)	396.8	Tower4	Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	396.2		Voltage Phase S (Volt)	397.7
	Voltage Phase T (Volt)	397.1		Voltage Phase T (Volt)	398.3
	Current Phase R (Amp)	68.24		Current Phase R (Amp)	88.32
	Current Phase S (Amp)	62.48		Current Phase S (Amp)	57.68
	Current Phase T (Amp)	56.42		Current Phase T (Amp)	82.11
	Frequency (49.5 - 50.5 Hz)	60.00		Frequency (49.5 - 50.5 Hz)	60.00
	Energy(kw)	42.98		Energy (kw)	42.92
	PF	0.98		PF	0.98
	Kwh	6267046		Kwh	6266760
	Recorded by	X		Recorded by	X
Tower3	Voltage Phase R (Volt)	398.2	Tower5	Voltage Phase R (Volt)	398.1
	Voltage Phase S (Volt)	396.8		Voltage Phase S (Volt)	396.8
	Voltage Phase T (Volt)	397.0		Voltage Phase T (Volt)	398.0
	Current Phase R (Amp)	82.98		Current Phase R (Amp)	62.14
	Current Phase S (Amp)	60.12		Current Phase S (Amp)	48.32
	Current Phase T (Amp)	62.48		Current Phase T (Amp)	56.18
	Frequency (49.5 - 50.5 Hz)	60.00		Frequency (49.5 - 50.5 Hz)	60.00
	Energy (kw)	42.96		Energy (kw)	42.98
	PF	0.98		PF	0.98
	Kwh	396.1		Kwh	1394123
	Recorded by	X		Recorded by	X

Remark =

Date 16/09/16

MDB (Main Distribution Board)

240

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	09.00 H.	Tower4	Voltage Phase R (Volt)	09.00 H.
	Voltage Phase S (Volt)	398.2		Voltage Phase S (Volt)	399.2
	Voltage Phase T (Volt)	396.1		Voltage Phase T (Volt)	396.8
	Current Phase R (Amp)	399.2		Current Phase R (Amp)	397.1
	Current Phase S (Amp)	62.58		Current Phase S (Amp)	78.12
	Current Phase T (Amp)	58.32		Current Phase T (Amp)	69.14
	Frequency (49.5 - 50.5 Hz)	48.50		Frequency (49.5 - 50.5 Hz)	56.28
	Energy (kw)	20.00		Energy (kw)	50.00
	PF	42.92		PF	42.96
	Kwh	0.98		Kwh	0.98
Tower3	Recorded by	6299452	Tower5	Recorded by	6298903
	Voltage Phase R (Volt)	8		Voltage Phase R (Volt)	8
	Voltage Phase S (Volt)	396.9		Voltage Phase S (Volt)	398.9
	Voltage Phase T (Volt)	396.2		Voltage Phase T (Volt)	398.1
	Current Phase R (Amp)	398.0		Current Phase R (Amp)	397.8
	Current Phase S (Amp)	68.52		Current Phase S (Amp)	69.28
	Current Phase T (Amp)	46.48		Current Phase T (Amp)	48.65
	Frequency (49.5 - 50.5 Hz)	50.96		Frequency (49.5 - 50.5 Hz)	52.16
	Energy (kw)	50.00		Energy (kw)	50.00
	PF	42.96		PF	42.69
Tower4	Recorded by	3821	Tower5	Recorded by	1405969
	Kwh	8		Kwh	8
	Recorded by	8		Recorded by	8

Remark =

Date 22/09/2018

MDB (Main Distribution Board)

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	396.4	Tower4	Voltage Phase R (Volt)	392.1
	Voltage Phase S (Volt)	398.0		Voltage Phase S (Volt)	398.3
	Voltage Phase T (Volt)	396.8		Voltage Phase T (Volt)	397.5
	Current Phase R (Amp)	68.36		Current Phase R (Amp)	102.36
	Current Phase S (Amp)	69.28		Current Phase S (Amp)	28.84
	Current Phase T (Amp)	62.11		Current Phase T (Amp)	56.66
	Frequency (49.5 - 50.5 Hz)	60.00		Frequency (49.5 - 50.5 Hz)	60.00
	Energy (kw)	42.96		Energy (kw)	42.96
	PF	0.98		PF	0.98
	Kwh	6291441		Kwh	6290154
Tower3	Recorded by	8	Tower5	Recorded by	8
	Voltage Phase R (Volt)	398.1		Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	399.0		Voltage Phase S (Volt)	398.0
	Voltage Phase T (Volt)	397.8		Voltage Phase T (Volt)	398.6
	Current Phase R (Amp)	58.42		Current Phase R (Amp)	26.92
	Current Phase S (Amp)	62.34		Current Phase S (Amp)	68.11
	Current Phase T (Amp)	46.98		Current Phase T (Amp)	67.04
	Frequency (49.5 - 50.5 Hz)	60.00		Frequency (49.5 - 50.5 Hz)	60.00
	Energy (kw)	62.98		Energy (kw)	62.96
	PF	0.98		PF	0.98
Tower4	Kwh	3849	Tower5	Kwh	1418819
	Recorded by	8		Recorded by	8

Remark =

Date 30/01/2016

MDB (Main Distribution Board)

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	398.1	Tower4	Voltage Phase R (Volt)	398.6
	Voltage Phase S (Volt)	396.0		Voltage Phase S (Volt)	396.5
	Voltage Phase T (Volt)	399.4		Voltage Phase T (Volt)	399.8
	Current Phase R (Amp)	96.20		Current Phase R (Amp)	96.12
	Current Phase S (Amp)	58.16		Current Phase S (Amp)	58.36
	Current Phase T (Amp)	60.42		Current Phase T (Amp)	59.33
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	62.96		Energy (kw)	62.96
	PF	0.98		PF	0.98
	Kwh	6303189		Kwh	6302143
Tower3	Recorded by	X	Tower5	Recorded by	X
	Voltage Phase R (Volt)	398.0		Voltage Phase R (Volt)	398.0
	Voltage Phase S (Volt)	399.6		Voltage Phase S (Volt)	399.8
	Voltage Phase T (Volt)	396.8		Voltage Phase T (Volt)	398.5
	Current Phase R (Amp)	62.60		Current Phase R (Amp)	64.52
	Current Phase S (Amp)	51.16		Current Phase S (Amp)	48.16
	Current Phase T (Amp)	48.20		Current Phase T (Amp)	52.38
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.97		Energy (kw)	42.96
	PF	0.98		PF	0.98
Tower4	Kwh	3942	Tower5	Kwh	1429609
	Recorded by	X		Recorded by	X

Remark =

.....

Date 6/10/1969

MDB (Main Distribution Board)

248

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	399.0	09.00 H.	Voltage Phase R (Volt)	399.2
	Voltage Phase S (Volt)	396.2		Voltage Phase S (Volt)	396.4
	Voltage Phase T (Volt)	398.2		Voltage Phase T (Volt)	399.6
	Current Phase R (Amp)	42.68		Current Phase R (Amp)	46.32
	Current Phase S (Amp)	49.28		Current Phase S (Amp)	49.64
	Current Phase T (Amp)	60.06		Current Phase T (Amp)	46.91
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	49.82		Energy (kw)	69.92
	PF	0.98		PF	0.98
	Kwh	6314185		Kwh	6313912
Tower3	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	396.8		Voltage Phase R (Volt)	392.1
	Voltage Phase S (Volt)	392.2		Voltage Phase S (Volt)	392.3
	Voltage Phase T (Volt)	399.0		Voltage Phase T (Volt)	399.2
	Current Phase R (Amp)	20.43		Current Phase R (Amp)	68.25
	Current Phase S (Amp)	54.58		Current Phase S (Amp)	52.61
	Current Phase T (Amp)	60.89		Current Phase T (Amp)	42.11
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.49		Energy (kw)	42.91
	PF	0.98		PF	0.98
Tower4	Kwh	4002		Kwh	1491584
	Recorded by	8		Recorded by	8
	Voltage Phase R (Volt)	396.8		Voltage Phase R (Volt)	392.1
	Voltage Phase S (Volt)	392.2		Voltage Phase S (Volt)	392.3
	Voltage Phase T (Volt)	399.0		Voltage Phase T (Volt)	399.2
	Current Phase R (Amp)	20.43		Current Phase R (Amp)	68.25
	Current Phase S (Amp)	54.58		Current Phase S (Amp)	52.61
	Current Phase T (Amp)	60.89		Current Phase T (Amp)	42.11
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.49		Energy (kw)	42.91
Tower5	PF	0.98		PF	0.98
	Kwh	4002		Kwh	1491584
	Recorded by	8		Recorded by	8

Remark =

Date 13/11/2018

MDB (Main Distribution Board)

	Description	Time	Tower4	Description	Time
		09.00 H.			09.00 H.
Tower2	Voltage Phase R (Volt)	396.2	Tower5	Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	399.0		Voltage Phase S (Volt)	392.4
	Voltage Phase T (Volt)	398.4		Voltage Phase T (Volt)	396.1
	Current Phase R (Amp)	32.06		Current Phase R (Amp)	44.36
	Current Phase S (Amp)	60.12		Current Phase S (Amp)	69.41
	Current Phase T (Amp)	62.12		Current Phase T (Amp)	58.02
	Frequency (49.5 - 50.5 Hz)	60.00		Frequency (49.5 - 50.5 Hz)	60.00
	Energy (kw)	42.68		Energy (kw)	42.68
	PF	0.98		PF	0.98
	Kwh	6325817		Kwh	1455429
	Recorded by	8		Recorded by	71
Tower3	Voltage Phase R (Volt)	398.2	Tower5	Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	399.2		Voltage Phase S (Volt)	392.4
	Voltage Phase T (Volt)	392.6		Voltage Phase T (Volt)	396.1
	Current Phase R (Amp)	42.94		Current Phase R (Amp)	44.36
	Current Phase S (Amp)	58.22		Current Phase S (Amp)	69.41
	Current Phase T (Amp)	62.06		Current Phase T (Amp)	58.02
	Frequency (49.5 - 50.5 Hz)	60.00		Frequency (49.5 - 50.5 Hz)	60.00
	Energy (kw)	42.66		Energy (kw)	42.68
	PF	0.98		PF	0.98
	Kwh	4060		Kwh	1455429
	Recorded by	71		Recorded by	71

Remark =

Date 20/10/2016

MDB (Main Distribution Board)

	Description	Time		Description	Time
		09.00 H.			
Tower2	Voltage Phase R (Volt)	397.0		Voltage Phase R (Volt)	396.7
	Voltage Phase S (Volt)	397.6		Voltage Phase S (Volt)	396.2
	Voltage Phase T (Volt)	396.2		Voltage Phase T (Volt)	398.4
	Current Phase R (Amp)	62.34		Current Phase R (Amp)	98.26
	Current Phase S (Amp)	68.42		Current Phase S (Amp)	95.02
	Current Phase T (Amp)	66.30		Current Phase T (Amp)	69.11
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.67		Energy (kw)	42.66
	PF	0.98		PF	0.98
	Kwh	636.664		Kwh	653.7086
	Recorded by	S		Recorded by	S
Tower3	Voltage Phase R (Volt)	396.2		Voltage Phase R (Volt)	398.2
	Voltage Phase S (Volt)	398.2		Voltage Phase S (Volt)	396.2
	Voltage Phase T (Volt)	397.0		Voltage Phase T (Volt)	399.0
	Current Phase R (Amp)	68.43		Current Phase R (Amp)	68.62
	Current Phase S (Amp)	69.46		Current Phase S (Amp)	48.90
	Current Phase T (Amp)	62.00		Current Phase T (Amp)	60.90
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.66		Energy (kw)	42.68
	PF	0.98		PF	0.98
	Kwh	611.1		Kwh	1265.918
	Recorded by	S		Recorded by	S
Tower4	Voltage Phase R (Volt)			Voltage Phase R (Volt)	
	Voltage Phase S (Volt)			Voltage Phase S (Volt)	
	Voltage Phase T (Volt)			Voltage Phase T (Volt)	
	Current Phase R (Amp)			Current Phase R (Amp)	
	Current Phase S (Amp)			Current Phase S (Amp)	
	Current Phase T (Amp)			Current Phase T (Amp)	
	Frequency (49.5 - 50.5 Hz)			Frequency (49.5 - 50.5 Hz)	
	Energy (kw)			Energy (kw)	
	PF			PF	
	Kwh			Kwh	
	Recorded by			Recorded by	
Tower5	Voltage Phase R (Volt)			Voltage Phase R (Volt)	
	Voltage Phase S (Volt)			Voltage Phase S (Volt)	
	Voltage Phase T (Volt)			Voltage Phase T (Volt)	
	Current Phase R (Amp)			Current Phase R (Amp)	
	Current Phase S (Amp)			Current Phase S (Amp)	
	Current Phase T (Amp)			Current Phase T (Amp)	
	Frequency (49.5 - 50.5 Hz)			Frequency (49.5 - 50.5 Hz)	
	Energy (kw)			Energy (kw)	
	PF			PF	
	Kwh			Kwh	
	Recorded by			Recorded by	

Remark =

Date 24/01/2016

MDB (Main Distribution Board)

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	396.8	09.00 H.	Voltage Phase R (Volt)	398.6
	Voltage Phase S (Volt)	399.1		Voltage Phase S (Volt)	396.2
	Voltage Phase T (Volt)	396.2		Voltage Phase T (Volt)	390.3
	Current Phase R (Amp)	82.68		Current Phase R (Amp)	98.20
	Current Phase S (Amp)	48.12		Current Phase S (Amp)	82.38
	Current Phase T (Amp)	58.02		Current Phase T (Amp)	68.11
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.68		Energy (kw)	42.82
	PF	0.98		PF	0.98
	Kwh	6347560		Kwh	6349200
Tower3	Recorded by	N		Recorded by	8
	Voltage Phase R (Volt)	392.0		Voltage Phase R (Volt)	396.2
	Voltage Phase S (Volt)	396.2		Voltage Phase S (Volt)	392.8
	Voltage Phase T (Volt)	397.1		Voltage Phase T (Volt)	394.2
	Current Phase R (Amp)	82.98		Current Phase R (Amp)	68.90
	Current Phase S (Amp)	61.12		Current Phase S (Amp)	52.16
	Current Phase T (Amp)	59.10		Current Phase T (Amp)	48.11
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.62		Energy (kw)	42.82
	PF	0.98		PF	0.98
Tower4	Kwh	6182		Kwh	159916
	Recorded by	7		Recorded by	8
	Voltage Phase R (Volt)	392.0		Voltage Phase R (Volt)	396.2
	Voltage Phase S (Volt)	396.2		Voltage Phase S (Volt)	392.8
	Voltage Phase T (Volt)	397.1		Voltage Phase T (Volt)	394.2
	Current Phase R (Amp)	82.98		Current Phase R (Amp)	68.90
	Current Phase S (Amp)	61.12		Current Phase S (Amp)	52.16
	Current Phase T (Amp)	59.10		Current Phase T (Amp)	48.11
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.62		Energy (kw)	42.82
Tower5	PF	0.98		PF	0.98
	Kwh	6182		Kwh	159916
	Recorded by	7		Recorded by	8

Remark =

Date 5/8/2016

MDB (Main Distribution Board)

	Description	Time		Tower4	Description	Time	
			09.00 H.				09.00 H.
Tower2	Voltage Phase R (Volt)	396.2		Tower4	Voltage Phase R (Volt)	396.2	
	Voltage Phase S (Volt)	397.0			Voltage Phase S (Volt)	397.6	
	Voltage Phase T (Volt)	398.2			Voltage Phase T (Volt)	398.2	
	Current Phase R (Amp)	48.68			Current Phase R (Amp)	100.23	
	Current Phase S (Amp)	52.92			Current Phase S (Amp)	88.48	
	Current Phase T (Amp)	60.06			Current Phase T (Amp)	86.51	
	Frequency (49.5 - 50.5 Hz)	50.00			Frequency (49.5 - 50.5 Hz)	50.00	
	Energy (kw)	42.82			Energy (kw)	42.89	
	PF	0.98			PF	0.98	
	Kwh	63710.90			Kwh	63610.96	
	Recorded by	H			Recorded by	H	
Tower3	Voltage Phase R (Volt)	394.2		Tower5	Voltage Phase R (Volt)	396.2	
	Voltage Phase S (Volt)	396.8			Voltage Phase S (Volt)	398.2	
	Voltage Phase T (Volt)	399.0			Voltage Phase T (Volt)	399.2	
	Current Phase R (Amp)	80.56			Current Phase R (Amp)	68.22	
	Current Phase S (Amp)	56.38			Current Phase S (Amp)	50.68	
	Current Phase T (Amp)	62.85			Current Phase T (Amp)	46.92	
	Frequency (49.5 - 50.5 Hz)	50.00			Frequency (49.5 - 50.5 Hz)	50.00	
	Energy (kw)	42.96			Energy (kw)	42.66	
	PF	0.98			PF	0.98	
	Kwh	4230			Kwh	42341.6	
	Recorded by	H			Recorded by	H	

Remark =

Date 12/05/2016

MDB (Main Distribution Board)

Tower2	Description	Time		Tower4	Description	Time	
			09.00 u.				09.00 u.
Tower2	Voltage Phase R (Volt)		396.8	Tower4	Voltage Phase R (Volt)		398.1
	Voltage Phase S (Volt)		398.7		Voltage Phase S (Volt)		396.9
	Voltage Phase T (Volt)		399.0		Voltage Phase T (Volt)		396.9
	Current Phase R (Amp)		38.60		Current Phase R (Amp)		38.65
	Current Phase S (Amp)		60.19		Current Phase S (Amp)		82.69
	Current Phase T (Amp)		58.26		Current Phase T (Amp)		56.18
	Frequency (49.5 - 50.5 Hz)		50.00		Frequency (49.5 - 50.5 Hz)		50.00
	Energy (kw)		42.82		Energy (kw)		62.69
	PF		0.98		PF		0.98
	Kwh		6383042		Kwh		6382882
Tower3	Recorded by		X	Tower5	Recorded by		X
	Voltage Phase R (Volt)		398.6		Voltage Phase R (Volt)		392.6
	Voltage Phase S (Volt)		396.8		Voltage Phase S (Volt)		394.0
	Voltage Phase T (Volt)		398.6		Voltage Phase T (Volt)		396.1
	Current Phase R (Amp)		38.69		Current Phase R (Amp)		38.65
	Current Phase S (Amp)		58.32		Current Phase S (Amp)		68.96
	Current Phase T (Amp)		64.60		Current Phase T (Amp)		62.18
	Frequency (49.5 - 50.5 Hz)		50.00		Frequency (49.5 - 50.5 Hz)		50.00
	Energy (kw)		42.68		Energy (kw)		52.98
	PF		0.98		PF		0.98
Tower3	Kwh		4348	Tower5	Kwh		1500988
	Recorded by		46		Recorded by		X

Remark =

Date 19/08/2018

MDB (Main Distribution Board)

240

	Description	Time		Description	Time
Tower2	Voltage Phase R (Volt)	09.00 u.	Tower4	Voltage Phase R (Volt)	09.00 u.
	Voltage Phase S (Volt)	397.6		Voltage Phase S (Volt)	396.9
	Voltage Phase T (Volt)	399.0		Voltage Phase T (Volt)	396.4
	Current Phase R (Amp)	396.2		Current Phase R (Amp)	399.5
	Current Phase S (Amp)	397.68		Current Phase S (Amp)	397.56
	Current Phase T (Amp)	62.24		Current Phase T (Amp)	48.09
	Frequency (49.5 - 50.5 Hz)	66.30		Frequency (49.5 - 50.5 Hz)	64.4
	Energy (kw)	50.00		Energy (kw)	50.00
	PF	42.69		PF	42.69
	Kwh	0.98		Kwh	0.98
Tower3	Recorded by	6394512	Tower5	Recorded by	6386573
	Voltage Phase R (Volt)	398.2		Voltage Phase R (Volt)	397.2
	Voltage Phase S (Volt)	396.2		Voltage Phase S (Volt)	397.2
	Voltage Phase T (Volt)	397.6		Voltage Phase T (Volt)	397.2
	Current Phase R (Amp)	69.86		Current Phase R (Amp)	68.62
	Current Phase S (Amp)	68.42		Current Phase S (Amp)	68.50
	Current Phase T (Amp)	68.26		Current Phase T (Amp)	60.20
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.68		Energy (kw)	42.64
	PF	0.98		PF	0.98
Tower4	Kwh	44.00		Kwh	1512891
	Recorded by	48		Recorded by	48
	Voltage Phase R (Volt)	398.2		Voltage Phase R (Volt)	397.2
	Voltage Phase S (Volt)	396.2		Voltage Phase S (Volt)	397.2
Tower5	Voltage Phase T (Volt)	397.6		Voltage Phase T (Volt)	397.2
	Current Phase R (Amp)	69.86		Current Phase R (Amp)	68.62
	Current Phase S (Amp)	68.42		Current Phase S (Amp)	68.50
	Current Phase T (Amp)	68.26		Current Phase T (Amp)	60.20
Tower6	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
	Energy (kw)	42.68		Energy (kw)	42.64
	PF	0.98		PF	0.98
	Kwh	44.00		Kwh	1512891
Tower7	Recorded by	48		Recorded by	48
	Voltage Phase R (Volt)	398.2		Voltage Phase R (Volt)	397.2
	Voltage Phase S (Volt)	396.2		Voltage Phase S (Volt)	397.2
	Voltage Phase T (Volt)	397.6		Voltage Phase T (Volt)	397.2
Tower8	Current Phase R (Amp)	69.86		Current Phase R (Amp)	68.62
	Current Phase S (Amp)	68.42		Current Phase S (Amp)	68.50
	Current Phase T (Amp)	68.26		Current Phase T (Amp)	60.20
	Frequency (49.5 - 50.5 Hz)	50.00		Frequency (49.5 - 50.5 Hz)	50.00
Tower9	Energy (kw)	42.68		Energy (kw)	42.64
	PF	0.98		PF	0.98
	Kwh	44.00		Kwh	1512891
	Recorded by	48		Recorded by	48

Remark =

Date 26/06/2018

MDB (Main Distribution Board)

Tower2	Description	Time		Tower4	Description	Time	
			09.00 H.				09.00 H.
Tower2	Voltage Phase R (Volt)	398.1		Tower4	Voltage Phase R (Volt)	398.0	
	Voltage Phase S (Volt)	396.8			Voltage Phase S (Volt)	398.6	
	Voltage Phase T (Volt)	392.1			Voltage Phase T (Volt)	390.9	
	Current Phase R (Amp)	92.68			Current Phase R (Amp)	98.20	
	Current Phase S (Amp)	98.12			Current Phase S (Amp)	98.36	
	Current Phase T (Amp)	98.02			Current Phase T (Amp)	68.22	
	Frequency (49.5 - 50.5 Hz)	50.00			Frequency (49.5 - 50.5 Hz)	50.00	
	Energy (kw)	42.69			Energy (kw)	40.68	
	PF	0.98			PF	0.98	
	Kwh	6559248			Kwh	6008330	
Tower3	Recorded by	Y		Tower5	Recorded by	Y	
	Voltage Phase R (Volt)	396.2			Voltage Phase R (Volt)	396.2	
	Voltage Phase S (Volt)	398.1			Voltage Phase S (Volt)	398.3	
	Voltage Phase T (Volt)	398.0			Voltage Phase T (Volt)	398.2	
	Current Phase R (Amp)	92.82			Current Phase R (Amp)	96.90	
	Current Phase S (Amp)	62.04			Current Phase S (Amp)	56.82	
	Current Phase T (Amp)	58.10			Current Phase T (Amp)	48.12	
	Frequency (49.5 - 50.5 Hz)	50.00			Frequency (49.5 - 50.5 Hz)	50.00	
	Energy (kw)	42.68			Energy (kw)	48.69	
	PF	0.99			PF	0.98	
Tower3	Kwh	4290			Kwh	1594567	
	Recorded by	Y			Recorded by	Y	
	Remark =						

ใบตรวจเช็คและบำรุงรักษา Emergency Lighting

รายงานการปฏิบัติตามเงื่อนไขของมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อม

ประจำเดือน กรกฎาคม

Equipment Code : EML Brand : Osany Model : NAU300BHZ LED Capacity : 2 x 12 VDC LED 2 x 5 W Location : 1-4

Floor	Place	Code	รายการเช็ค									Remark
			แบตเตอรี่	หลอดไฟ	Fuse AC	Fuse DC	Switch Fuse	Switch On	Switch Off	Charger Bat.	อุณหภูมิ	
4	ST-1	EML-31	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-32	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	EE Room	EML-33	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-34	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-35	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-36	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	ST-2	EML-37	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	ST-1	EML-38	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-39	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	EE Room	EML-40	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-41	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-42	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-43	AB	✓	✓	✓	✓	✓	✓	✓	✓	
3	ST-2	EML-44	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	ST-1	EML-45	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EML-46	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	EE Room	EML-47	AB	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EML-48	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EML-49	AB	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EML-50	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	ST-2	EML-51	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	ST-1	EML-52	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	corridor	EML-53	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	corridor	EML-54	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	Pump Room	EML-55	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	car park	EML-56	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	car park	EML-57	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	car park	EML-58	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	ST-2	EML-59	✓	✓	✓	✓	✓	✓	✓	✓	✓	

Recommendation/Remark :

จัดทำโดย : นิติบุคคลอาคารชุด ไอรিস แอเวนิว อาคาร ๒-๕
รายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ครั้งที่ ๒ (รอบเดือนกรกฎาคม - ธันวาคม ๒๕๖๔)

ประจำเดือน สิงหาคม

Equipment Code : EML Brand : Sunny Model : RAU2000HZ LED Capacity : 2x12 VDC L20 2x3 W Location : 1-4

Floor	Place	Cells	รายการเช็ค									Remark
			แบตเตอรี่	พวงมาลัย	Fans AC	Fans DC	Switch Fan	Switch On	Switch Off	Charger Bat.	สัญญาณเตือน	
4	ST-1	EML-31	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-32	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	EE Room	EML-33	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-34	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-35	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-36	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	ST-2	EML-37	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	ST-1	EML-38	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-39	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	EE Room	EML-40	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-41	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-42	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-43	AB	✓	✓	✓	✓	✓	✓	✓	✓	
3	ST-2	EML-44	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	ST-1	EML-45	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EML-46	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	EE Room	EML-47	AB	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EML-48	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EML-49	AB	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EML-50	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	ST-2	EML-51	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	ST-1	EML-52	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	corridor	EML-53	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	corridor	EML-54	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	Pump Room	EML-55	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	car park	EML-56	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	car park	EML-57	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	car park	EML-58	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	ST-2	EML-59	✓	✓	✓	✓	✓	✓	✓	✓	✓	

Recommendations/Remark:

จัดทำโดย : นิติบุคคลอาคารชุด ไอริส แอเวนิว อาคาร ๒-๕
รายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ครั้งที่ ๒ (รอบเดือนกรกฎาคม - ธันวาคม ๒๕๖๔)

รายงานการปฏิบัติตามเงื่อนไขของมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อม

ประจำเดือน กันยายน

Equipment Code : EML Brand : Govee Model : RAU2001BHZ LED Capacity : 2x12 VDC 1.80 1x3 W Location : 1-4

Floor	Place	Code	รายการเช็ค									Remark
			เปิดไฟ	หลอดไฟ	Fans AC	Fans DC	Switch Fan	Switch On	Switch Off	Charger Bat.	แบตเตอรี่เต็ม	
4	ST-1	EML-31	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	corridor	EML-32	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	EE Room	EML-33	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	corridor	EML-34	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	corridor	EML-35	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	corridor	EML-36	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	ST-2	EML-37	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	ST-1	EML-38	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	corridor	EML-39	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	EE Room	EML-40	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	corridor	EML-41	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	corridor	EML-42	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	corridor	EML-43	AB	✓	✓	✓	✓	✓	✓	2	✓	
3	ST-2	EML-44	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	ST-1	EML-45	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	corridor	EML-46	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	EE Room	EML-47	AB	✓	✓	✓	✓	✓	✓	2	✓	
2	corridor	EML-48	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	corridor	EML-49	AB	✓	✓	✓	✓	✓	✓	2	✓	
2	corridor	EML-50	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	ST-2	EML-51	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	ST-1	EML-52	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	corridor	EML-53	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	corridor	EML-54	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	Pump Room	EML-55	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	car park	EML-56	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	car park	EML-57	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	car park	EML-58	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	ST-2	EML-59	✓	✓	✓	✓	✓	✓	✓	2	✓	

Recommendation/Remark :

จัดทำโดย : นิติบุคคลอาคารชุด ไอรিস แอเวนิว อาคาร ๒-๕
รายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ครั้งที่ ๒ (รอบเดือนกรกฎาคม - ธันวาคม ๒๕๖๔)

ประจำเดือน ตุลาคม

Equipment Code : EML Brand : Sunway Model : HAU2000MHZ LED Capacity : 2x12 VDC 1.20 2x 5 W Location : 1-4

Floor	Place	Code	รายการเช็ค									Remark
			เปลี่ยนไฟ	ขดขโมย	Fans AC	Fans DC	Switch Fan	Switch On	Switch Off	Charge Bat	ใช้งานปกติ	
4	ST-1	EML-31	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	corridor	EML-32	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	EE Room	EML-33	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	corridor	EML-34	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	corridor	EML-35	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	corridor	EML-36	✓	✓	✓	✓	✓	✓	✓	2	✓	
4	ST-2	EML-37	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	ST-1	EML-38	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	corridor	EML-39	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	EE Room	EML-40	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	corridor	EML-41	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	corridor	EML-42	✓	✓	✓	✓	✓	✓	✓	2	✓	
3	corridor	EML-43	AB	✓	✓	✓	✓	✓	✓	2	✓	
3	ST-2	EML-44	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	ST-1	EML-45	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	corridor	EML-46	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	EE Room	EML-47	AB	✓	✓	✓	✓	✓	✓	2	✓	
2	corridor	EML-48	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	corridor	EML-49	AB	✓	✓	✓	✓	✓	✓	2	✓	
2	corridor	EML-50	✓	✓	✓	✓	✓	✓	✓	2	✓	
2	ST-2	EML-51	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	ST-1	EML-52	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	corridor	EML-53	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	corridor	EML-54	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	Pump Room	EML-55	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	car park	EML-56	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	car park	EML-57	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	car park	EML-58	✓	✓	✓	✓	✓	✓	✓	2	✓	
1	ST-2	EML-59	✓	✓	✓	✓	✓	✓	✓	2	✓	

Recommendation/Remark :

รายงานการปฏิบัติตามเงื่อนไขของมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อม

ประจำเดือน พฤศจิกายน

Equipment Code : EML Brand : Sonny Model : RAU2000HZ LED Capacity : 2x12 VOC 1.801x3 W Location : 1-4

Floor	Place	Code	รายการเช็ค									Remark
			แสงไฟ	พัดลม	Fans AC	Fans DC	Switch Fans	Switch DC	Switch BT	Charger Fan	อุณหภูมิ	
4	ST-1	EML-31	✓	✓	✓	✓	✓	✓	✓	22	✓	
4	corridor	EML-32	✓	✓	✓	✓	✓	✓	✓	22	✓	
4	EE Room	EML-33	✓	✓	✓	✓	✓	✓	✓	22	✓	
4	corridor	EML-34	✓	✓	✓	✓	✓	✓	✓	22	✓	
4	corridor	EML-35	✓	✓	✓	✓	✓	✓	✓	22	✓	
4	corridor	EML-36	✓	✓	✓	✓	✓	✓	✓	22	✓	
4	ST-2	EML-37	✓	✓	✓	✓	✓	✓	✓	22	✓	
3	ST-1	EML-38	✓	✓	✓	✓	✓	✓	✓	22	✓	
3	corridor	EML-39	✓	✓	✓	✓	✓	✓	✓	22	✓	
3	EE Room	EML-40	✓	✓	✓	✓	✓	✓	✓	22	✓	
3	corridor	EML-41	✓	✓	✓	✓	✓	✓	✓	22	✓	
3	corridor	EML-42	✓	✓	✓	✓	✓	✓	✓	22	✓	
3	corridor	EML-43	AB	✓	✓	✓	✓	✓	✓	22	✓	
3	ST-2	EML-44	✓	✓	✓	✓	✓	✓	✓	22	✓	
2	ST-1	EML-45	✓	✓	✓	✓	✓	✓	✓	22	✓	
2	corridor	EML-46	✓	✓	✓	✓	✓	✓	✓	22	✓	
2	EE Room	EML-47	AB	✓	✓	✓	✓	✓	✓	22	✓	
2	corridor	EML-48	✓	✓	✓	✓	✓	✓	✓	22	✓	
2	corridor	EML-49	AB	✓	✓	✓	✓	✓	✓	22	✓	
2	corridor	EML-50	✓	✓	✓	✓	✓	✓	✓	22	✓	
2	ST-2	EML-51	✓	✓	✓	✓	✓	✓	✓	22	✓	
1	ST-1	EML-52	✓	✓	✓	✓	✓	✓	✓	22	✓	
1	corridor	EML-53	✓	✓	✓	✓	✓	✓	✓	22	✓	
1	corridor	EML-54	✓	✓	✓	✓	✓	✓	✓	22	✓	
1	Pump Room	EML-55	✓	✓	✓	✓	✓	✓	✓	22	✓	
1	car park	EML-56	✓	✓	✓	✓	✓	✓	✓	22	✓	
1	car park	EML-57	✓	✓	✓	✓	✓	✓	✓	22	✓	
1	car park	EML-58	✓	✓	✓	✓	✓	✓	✓	22	✓	
1	ST-2	EML-59	✓	✓	✓	✓	✓	✓	✓	22	✓	

Recommendations/Remarks:

จัดทำโดย : นิติบุคคลอาคารชุด ไอรিস แอเวนิว อาคาร ๒-๕
รายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ครั้งที่ ๒ (รอบเดือนกรกฎาคม - ธันวาคม ๒๕๖๘)

รายงานการปฏิบัติตามเงื่อนไขของมาตรการป้องกันและแก้ไขผลกระทบสิ่งแวดล้อม

ประจำเดือน ธันวาคม

Equipment Code: EML Brand: Sonney Model: RAU3000HZ LED Capacity: 2x12 VDC LED 2x3 W Location: 1-4

Floor	Place	Code	ตรวจสอบ									Remark
			เปิดไฟ	หลอดไฟ	Fans AC	Fans DC	Switch Fan	Switch On	Switch Off	Charger Bat.	แบตเตอรี่	
4	ST-1	EML-31	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-32	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	EE Room	EML-33	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-34	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EML-35	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	corridor	EVL-36	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	ST-2	EVL-37	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	ST-1	EML-38	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-39	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	EE Room	EML-40	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-41	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-42	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	corridor	EML-43	AB	✓	✓	✓	✓	✓	✓	✓	✓	
3	ST-2	EML-44	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	ST-1	EML-45	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EVL-46	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	EE Room	EVL-47	AB	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EVL-48	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EVL-49	AB	✓	✓	✓	✓	✓	✓	✓	✓	
2	corridor	EML-50	✓	✓	✓	✓	✓	✓	✓	✓	✓	
2	ST-2	EML-51	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	ST-1	EML-52	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	corridor	EML-53	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	corridor	EML-54	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	Pump Room	EML-55	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	car park	EML-56	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	car park	EVL-57	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	car park	EML-58	✓	✓	✓	✓	✓	✓	✓	✓	✓	
1	ST-2	EML-59	✓	✓	✓	✓	✓	✓	✓	✓	✓	

Recommendations/Remark:

จัดทำโดย : นิติบุคคลอาคารชุด ไอริส แอเวนิว อาคาร ๒-๕
รายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ครั้งที่ ๒ (รอบเดือนกรกฎาคม - ธันวาคม ๒๕๖๘)

ใบตรวจเช็คและบำรุงรักษา ตู้ดับเพลิง

ประจำเดือน กรกฎาคม

Item	Code	Description	Status	Remarks	ผู้เกี่ยวข้อง					ดำเนินการ				Status
					นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	
1	IR-01													
2	IR-02/IR-03													
3	IR-04/IR-05													
4	IR-06													
5	IR-07													
6	IR-08													
7	IR-09/IR-10													
8	IR-11/IR-12													
9	IR-13/IR-14													
10	IR-15													
11	IR-16													
12	IR-17/IR-18													
13	IR-19/IR-20													
14	IR-21													
15	IR-22/IR-23													
16	IR-24													
17	IR-25													
18	IR-26													
19	IR-27/IR-28													
20	IR-29/IR-30													
21	IR-31													
22	IR-32/IR-33													
23	IR-34													
24	IR-35													
25	IR-36													
26	IR-37/IR-38													
27	IR-39/IR-40													
28	IR-41													
29	IR-42/IR-43													
30	IR-44													
31	IR-45													
32	IR-46/IR-47													
33	IR-48													
34	IR-49/IR-50													
35	IR-51													
36	IR-52													
37	IR-53/IR-54													
38	IR-55													
39	IR-56													
40	IR-57/IR-58													
41	IR-59/IR-60													
42	IR-61													
43	IR-62/IR-63													
44	IR-64													
45	IR-65													
46	IR-66													
47	IR-67/IR-68													
48	IR-69/IR-70													
49	IR-71													
50	IR-72/IR-73													
51	IR-74													
52	IR-75													
53	IR-76/IR-77													
54	IR-78/IR-79													
55	IR-80													

รวมทั้งหมด/Total

ประจำเดือน สิงหาคม

Floor	Code	กิจกรรม	ชนิดพืช	วัสดุปลูก	ผู้ให้บริการ					ชนิดไม้				Remarks
					ไม้ประดับ	ไม้ยืนต้น	ไม้เลื้อย	ไม้พุ่ม	ไม้ดอก	ไม้ผล	ไม้ใบ	ไม้ดอก	ไม้ใบ	
4	FE-401/16-412	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
4	FE-404	✓								✓	✓	✓	✓	
4	FE-405	✓								✓	✓	✓	✓	
4	FE-406	✓								✓	✓	✓	✓	
4	FE-407/16-413	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	FE-301/16-308	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	FE-309	✓								✓	✓	✓	✓	
3	FE-310	✓								✓	✓	✓	✓	
3	FE-311	✓								✓	✓	✓	✓	
3	FE-312/16-319	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	
3	FE-313	✓								✓	✓	✓	✓	
3	FE-314	✓								✓	✓	✓	✓	
3	FE-315	✓								✓	✓	✓	✓	
3	FE-316	✓								✓	✓	✓	✓	
3	FE-317	✓								✓	✓	✓	✓	
3	FE-318	✓								✓	✓	✓	✓	
3	FE-319	✓								✓	✓	✓	✓	
3	FE-320	✓								✓	✓	✓	✓	
3	FE-321	✓								✓	✓	✓	✓	
3	FE-322	✓								✓	✓	✓	✓	
3	FE-323	✓								✓	✓	✓	✓	
3	FE-324	✓								✓	✓	✓	✓	
3	FE-325	✓								✓	✓	✓	✓	
3	FE-326	✓								✓	✓	✓	✓	
3	FE-327	✓								✓	✓	✓	✓	
3	FE-328	✓								✓	✓	✓	✓	
3	FE-329	✓								✓	✓	✓	✓	
3	FE-330	✓								✓	✓	✓	✓	
3	FE-331	✓								✓	✓	✓	✓	
3	FE-332	✓								✓	✓	✓	✓	
3	FE-333	✓								✓	✓	✓	✓	
3	FE-334	✓								✓	✓	✓	✓	
3	FE-335	✓								✓	✓	✓	✓	
3	FE-336	✓								✓	✓	✓	✓	
3	FE-337	✓								✓	✓	✓	✓	
3	FE-338	✓								✓	✓	✓	✓	
3	FE-339	✓								✓	✓	✓	✓	
3	FE-340	✓								✓	✓	✓	✓	
3	FE-341	✓								✓	✓	✓	✓	
3	FE-342	✓								✓	✓	✓	✓	

Remarks/Remarks

ประจำเดือน กันยายน

No.	Code	Status	Remarks	Action	Action Item					Action Item				Status
					Check	Design	Proc.	Install	Test	Check	Design	Proc.	Install	
4	PHC-013/F-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
4	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
4	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
4	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
4	PHC-013/F-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
3	PHC-013/F-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
3	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
3	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
3	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
3	PHC-013/F-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
4	PHC-013/F-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
2	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
1	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
1	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
1	PHC-013/F-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
1	PHC-013/F-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
1	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
1	FL-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
1	PHC-013/F-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N
1	PHC-013/F-401	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	N

Signature of the Engineer

จัดทำโดย : นิติบุคคลอาคารชุด ไอริส แอเวนิว อาคาร ๒-๕

รายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ครั้งที่ ๒ (รอบเดือนกรกฎาคม - ธันวาคม ๒๕๖๔)

ประจำเดือน ตุลาคม

No.	Code	Location	Status	Remarks	Frequency					Frequency				Total
					Monthly	Quarterly	Half Yearly	Yearly	Other	Monthly	Quarterly	Half Yearly	Yearly	
1	FE-01		✓							✓	✓	✓	✓	2
2	FE-02		✓		✓	✓	✓	✓	✓	✓	✓	✓	✓	2
3	FE-03		✓		✓	✓	✓	✓	✓	✓	✓	✓	✓	2
4	FE-04		✓							✓	✓	✓	✓	2
5	FE-05		✓							✓	✓	✓	✓	2
6	FE-06		✓							✓	✓	✓	✓	2
7	FE-07		✓		✓	✓	✓	✓	✓	✓	✓	✓	✓	2
8	FE-08		✓		✓	✓	✓	✓	✓	✓	✓	✓	✓	2
9	FE-09		✓							✓	✓	✓	✓	2
10	FE-10		✓							✓	✓	✓	✓	2
11	FE-11		✓							✓	✓	✓	✓	2
12	FE-12		✓		✓	✓	✓	✓	✓	✓	✓	✓	✓	2
13	FE-13		✓							✓	✓	✓	✓	2
14	FE-14		✓							✓	✓	✓	✓	2
15	FE-15		✓							✓	✓	✓	✓	2
16	FE-16		✓							✓	✓	✓	✓	2
17	FE-17		✓		✓	✓	✓	✓	✓	✓	✓	✓	✓	2
18	FE-18		✓		✓	✓	✓	✓	✓	✓	✓	✓	✓	2
19	FE-19		✓							✓	✓	✓	✓	2
20	FE-20		✓							✓	✓	✓	✓	2
21	FE-21		✓							✓	✓	✓	✓	2
22	FE-22		✓							✓	✓	✓	✓	2
23	FE-23		✓							✓	✓	✓	✓	2
24	FE-24		✓							✓	✓	✓	✓	2
25	FE-25		✓							✓	✓	✓	✓	2
26	FE-26		✓							✓	✓	✓	✓	2
27	FE-27		✓							✓	✓	✓	✓	2
28	FE-28		✓							✓	✓	✓	✓	2
29	FE-29		✓							✓	✓	✓	✓	2
30	FE-30		✓							✓	✓	✓	✓	2

Remediation/Recovery

ประจำเดือน พฤศจิกายน

Date	Code	Date check	Status	Type	ปริมาณ					จำนวน				Remark
					ปริมาณ (kg)	ค่าเฉลี่ย	ค่าต่ำ	ค่าสูง	ค่าเฉลี่ย	จำนวน	ค่าเฉลี่ย	ค่าต่ำ	ค่าสูง	
Nov	PR-001	✓								✓	✓	✓	22	
Nov	PR-002	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	22	
Nov	PR-003	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	22	
Nov	PR-004	✓								✓	✓	✓	22	
Nov	PR-005	✓								✓	✓	✓	22	
Nov	PR-006	✓								✓	✓	✓	22	
Nov	PR-007	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	22	
Nov	PR-008	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	22	
Nov	PR-009	✓								✓	✓	✓	22	
Nov	PR-010	✓								✓	✓	✓	22	
Nov	PR-011	✓								✓	✓	✓	22	
Nov	PR-012	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	22	
Nov	PR-013	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	22	
Nov	PR-014	✓								✓	✓	✓	22	
Nov	PR-015	✓								✓	✓	✓	22	
Nov	PR-016	✓								✓	✓	✓	22	
Nov	PR-017	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	22	
Nov	PR-018	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	22	
Nov	PR-019	✓								✓	✓	✓	22	
Nov	PR-020	✓								✓	✓	✓	22	
Nov	PR-021	✓								✓	✓	✓	22	
Nov	PR-022	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	22	

Prepared by: / Reviewed by:

จัดทำโดย : นิติบุคคลอาคารชุด ไอริส แอเวนิว อาคาร ๒-๕

รายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ครั้งที่ ๒ (รอบเดือนกรกฎาคม - ธันวาคม ๒๕๖๔)

ประจำเดือน ธันวาคม

Index	Code	ดำเนินการ	ตรวจสอบ	ผู้ตรวจ	ผู้ตรวจ					ผู้ตรวจ				รวม
					นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	นายสมชาย	
4	ENC-403FE-003	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	2
4	FE-404	✓								✓	✓	✓	✓	2
4	FE-405	✓								✓	✓	✓	✓	2
4	FE-406	✓								✓	✓	✓	✓	2
4	ENC-401FE-003	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	2
1	ENC-501FE-004	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	2
1	FE-502	✓								✓	✓	✓	✓	2
2	FE-503	✓								✓	✓	✓	✓	2
2	FE-504	✓								✓	✓	✓	✓	2
1	ENC-301FE-003	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	2
1	ENC-501FE-004	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	2
1	FE-505	✓								✓	✓	✓	✓	2
2	FE-506	✓								✓	✓	✓	✓	2
1	FE-507	✓								✓	✓	✓	✓	2
2	ENC-501FE-004	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	2
1	ENC-501FE-004	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	2
1	FE-508	✓								✓	✓	✓	✓	2
1	FE-509	✓								✓	✓	✓	✓	2
1	ENC-501FE-004	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	2

Enclosed/Included

จัดทำโดย : นิติบุคคลอาคารชุด ไอรিস แอเวนิว อาคาร ๒-๕

รายงานการวิเคราะห์ผลกระทบสิ่งแวดล้อม ครั้งที่ ๒ (รอบเดือนกรกฎาคม - ธันวาคม ๒๕๖๔)

ใบตรวจเช็ค FIRE ALARM CONTROL PANEL

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เชนส์ พร็อพเพอร์ตี้ เวิลด์ จำกัด
CHS PROPERTY WORLD CO., LTD.

รหัสงาน		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์		1. <u>อัคร</u> 2.			
วันที่ปฏิบัติ <u>๑๑ ก.ค. ๖๘</u>		3. 4.			
ชื่ออาคาร <u>๑</u>		5. 6.			
ชื่อผู้ควบคุม <u>อัคร</u>		ชื่อผู้ตรวจสอบ <u>100/11</u>			
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>19.6</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>19.3</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>24.9</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>0.98</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>230</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATOR	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



กรมโยธาธิการและผังเมือง
THAILAND PUBLIC WORKS DEPT.

รหัสงาน.....		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์.....		1. <u>IMB</u> 2.			
วันที่ปฏิบัติ <u>29.10.68</u>		3. 4.			
ชื่ออาคาร <u>9</u>		5. 6.			
ชื่อผู้ควบคุม <u>IMB</u>		ชื่อผู้ตรวจสอบ <u>100/99</u>			
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>192</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>13.4</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>26.2</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>0.98</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>230</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

.....

.....

.....

บันทึกผลการปฏิบัติ

- ☒ 1. ปฏิบัติงานเสร็จเรียบร้อย
- ☒ 2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เพรสเซอร์ เทคโนโลยี จำกัด
PRESSURE WORLD CO., LTD.

รหัสงาน.....		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์.....		1. 11/10/11/15 2.			
วันที่ปฏิบัติ 29 ก.อ. 68		3. 4.			
		5. 6.			
ชื่ออาคาร 4		ชื่อผู้ควบคุม 11/10/11/15		ชื่อผู้ตรวจสอบ 100%	
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 132 VDC	✓			
	ตรวจเช็ค BATTERY No2 132 VDC	✓			
	ตรวจเช็ค BATTERY รวม 260 VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY 0.98 VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ 250 VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATOR	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			
หมายเหตุ					

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL


 กระทรวงสาธารณสุข
 กรมสุขภาพจิต กรมสุขภาพจิต

รหัสงาน		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์		1. <u>อ.กมล</u>	2.		
วันที่ปฏิบัติ <u>๑๙. ๑๑. ๖๕</u>		3.	4.		
ชื่ออาคาร <u>5</u>		5.	6.		
ชื่อผู้ควบคุม <u>อ.กมล</u>		ชื่อผู้ตรวจสอบ <u>อ.กมล</u>			
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>13.8</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>13.6</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>๑๕.6</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>๐.๙๙</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>๑๕๐</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL


 กระทรวงสาธารณสุข
 กรมสุขภาพจิต กรมสุขภาพจิต กรมสุขภาพจิต

รหัสงาน		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์		1. <u>อ.ส.อ.</u> 2.			
วันที่ปฏิบัติ <u>16/5.ค./68</u>		3. 4.			
		5. 6.			
ชื่ออาคาร <u>9</u>		ชื่อผู้ควบคุม <u>อ.ส.อ.</u>		ชื่อผู้ตรวจสอบ <u>10/9</u>	
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>196</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>199</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>196.0</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>098</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>230</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งผิดปกติ (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เซ็นเซอร์ เทคโนโลยี จำกัด
644/45 ซอยสุขุมวิท 101/10

รหัสงาน.....		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์.....		1. <u>สมชาย</u> 2.			
วันที่ปฏิบัติ <u>26/10/68</u>		3. 4.			
ชื่ออาคาร <u>5</u>		5. 6.			
ชื่อผู้ควบคุม <u>สมชาย</u>		ชื่อผู้ตรวจสอบ <u>สมชาย</u>			
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>13.8</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>12.8</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>26.6</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>0.98</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>250</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อยแล้ว



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท ทรานส์ เทคโนโลยี จำกัด
69/69 หมู่ 10 ต.บางนา จ.สมุทรปราการ

รหัสงาน		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์		1. 11/12/1401 2.			
วันที่ปฏิบัติ		3. 4.			
		5. 6.			
ชื่ออาคาร ๒		ชื่อผู้ควบคุม 11/12/1401		ชื่อผู้ตรวจสอบ 1007	
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 13.6 VDC	✓			
	ตรวจเช็ค BATTERY No2 13.6 VDC	✓			
	ตรวจเช็ค BATTERY รวม 26.0 VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY 0.9 VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ 230 VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

.....

.....

.....

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อยแล้ว



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL


 กรมอนามัย กระทรวงสาธารณสุข
 กรมอนามัย กระทรวงสาธารณสุข

รหัสงาน		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์		1. <u>019004</u> 2.			
วันที่ปฏิบัติ <u>08/10/62</u>		3. 4.			
ชื่ออาคาร <u>5</u>		5. 6.			
ชื่อผู้ควบคุม <u>0454</u>		ชื่อผู้ตรวจสอบ <u>10579</u>			
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>19.8</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>19.6</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>28.8</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>0.79</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>250</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



กรุงเทพมหานคร
FIRE DEPARTMENT OF BANGKOK

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>ด.ส.น.</u> 2.
วันที่ปฏิบัติ <u>26/ก.ย./68</u>	3. 4.
ชื่ออาคาร <u>2</u> ชื่อผู้ควบคุม <u>ด.ส.น.</u> ชื่อผู้ตรวจสอบ <u>100/ก.ย.</u>	5. 6.

		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>13.6</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>13.6</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>27.2</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>0.98</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>230</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งผิดปกติ (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เซ็นเซอร์ เทคโนโลยี จำกัด
SENSE PROTECT WORLD CO., LTD.

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>ทศอ</u> 2.
วันที่ปฏิบัติ <u>26 / ๗.๐. / ๖๔</u>	3. 4.
ชื่ออาคาร <u>๑</u> ชื่อผู้ควบคุม <u>ทศอ</u> ชื่อผู้ตรวจสอบ <u>1๐๐/๑</u>	5. 6.

ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
-------	--------	----	-------	-----------	----------

FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>15.๕</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>1๕.๕</u> VDC	✓			
	ตรวจเช็ค BATTERYรวม <u>๑๕.๐</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>๐.๙๘</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>๑๕๐</u> VAC	✓			
5	ตรวจเช็คไฟ SHOWตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL

บริษัท เซ็นเซอร์ เทคโนโลยี จำกัด
SENSE TECHNOLOGY CO., LTD.

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. 1163/155 2.
วันที่ปฏิบัติ 26 / 11 / 65	3. 4.
	5. 6.

ชื่ออาคาร 4	ชื่อผู้ควบคุม 1163/155	ชื่อผู้ตรวจสอบ 10079
-------------	------------------------	----------------------

ผลการตรวจเช็ค		หมายเหตุ	
ลำดับ	รายการ	ดี	แก้ไข

FIRE ALARM CONTROL PANEL			
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓	
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓	
3	ตรวจเช็ค BATTERY No1 190 VDC	✓	
	ตรวจเช็ค BATTERY No2 13.2 VDC	✓	
	ตรวจเช็ค BATTERYรวม 24.8 VDC	✓	
	ตรวจเช็คไฟชาร์จ BATTERY 0.98 VDC	✓	
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ 220 VAC	✓	
5	ตรวจเช็คไฟ SHOWตู้ FCP	✓	
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓	
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓	
8	ตรวจเช็คสภาพตู้ FCP	✓	
9	ตรวจสอบอุปกรณ์ Manual	✓	
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓	

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เซ็นเซอร์ เทคโนโลยี จำกัด
SENSE PROPERTY MONITOR CO., LTD.

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>01967</u> 2.
วันที่ปฏิบัติ <u>26 / 0.0 / 68</u>	3. 4.
	5. 6.

ชื่ออาคาร <u>5</u>	ชื่อผู้ควบคุม <u>01967</u>	ชื่อผู้ตรวจสอบ <u>10999</u>
--------------------	----------------------------	-----------------------------

		ผลการตรวจเช็ค		
ลำดับ	รายการ	ดี	แก้ไข	หมายเหตุ

FIRE ALARM CONTROL PANEL

1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>13.2</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>13.6</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>26.2</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>0.98</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>230</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL


 บริษัท เซ็นส์ อีแอสเทิร์น จำกัด
 SENSES PROPERTY SOLUTION CO., LTD.

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>ด.กฤษ</u> 2.
วันที่ปฏิบัติ	3. 4.
วันที่ปฏิบัติ <u>24/07/65</u>	5. 6.
ชื่ออาคาร <u>2</u>	ชื่อผู้ควบคุม <u>ด.กฤษ</u> ชื่อผู้ตรวจสอบ <u>10979</u>

		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>13.6</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>190</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>203</u> VDC	✓			
	ตรวจเช็คไฟสำรอง BATTERY <u>678</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>990</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งผิดปกติ (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท ฟูมฟาย จำกัด
FUMFAY CO., LTD.

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>ทนาย</u> 2.
วันที่ปฏิบัติ <u>๑๕/๑๑/๕๘</u>	3. 4.
ชื่ออาคาร <u>๑</u>	5. 6.
ชื่อผู้ควบคุม <u>ทนาย</u>	ชื่อผู้ตรวจสอบ <u>100%</u>

ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
-------	--------	----	-------	-----------	----------

FIRE ALARM CONTROL PANEL

1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1..... <u>13.6</u> VDC	✓			
	ตรวจเช็ค BATTERY No2..... <u>13.6</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม..... <u>13.6</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY..... <u>0.98</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>230</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เจริญรุ่งเรือง จำกัด
FIRE ALARM CONTROL PANEL

รหัสงาน		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์		1. 11/50/155 2.			
วันที่ปฏิบัติ 17/10/68		3. 4.			
ชื่ออาคาร 4		ชื่อผู้ควบคุม 11/50/155 ชื่อผู้ตรวจสอบ 10079			
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 15.6 VDC	✓			
	ตรวจเช็ค BATTERY No2 19.8 VDC	✓			
	ตรวจเช็ค BATTERY รวม 24.8 VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY 0.98 VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ 230 VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL

บริษัท เจริญรุ่งเรือง จำกัด
123/45 ถนนสุขุมวิท กรุงเทพฯ 10110

รหัสงาน		รายชื่อพนักงานที่ปฏิบัติงาน			
รหัสอุปกรณ์		1. ๐๑๖๓ 2.			
วันที่ปฏิบัติ ๑๖ / ๓.๑ / ๖๕		3. 4.			
ชื่ออาคาร ๖		5. 6.			
ชื่อผู้ควบคุม ๐๑๖๓		ชื่อผู้ตรวจสอบ ๑๐๑๑			
		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1..... 13.6 VDC	✓			
	ตรวจเช็ค BATTERY No2..... 13.6 VDC	✓			
	ตรวจเช็ค BATTERYรวม..... 25.2 VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY..... ๐.๗๘ VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ ๑๖๐ VAC	✓			
5	ตรวจเช็คไฟ SHOWตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			
หมายเหตุ					

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เอนจิเนียริง เทคโนโลยี จำกัด
67/25 ถนนสุขุมวิท แขวงคลองเตย เขตคลองเตย กรุงเทพฯ 10110

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>01/0000</u> 2.
วันที่ปฏิบัติ <u>26 / พ.ย. / 68</u>	3. 4.
ชื่ออาคาร <u>2</u> ชื่อผู้ควบคุม <u>01/0000</u> ชื่อผู้ตรวจสอบ <u>0000</u>	5. 6.

		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>13.0</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>13.2</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>26.0</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>0.9V</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>9.30</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL

บริษัท เจริญรุ่งเรือง จำกัด
FIRE ALARM CONTROL PANEL

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>1005</u> 2.
วันที่ปฏิบัติ <u>26 / 11 / 68</u>	3. 4.
ชื่ออาคาร <u>2</u>	5. 6.
ชื่อผู้ควบคุม <u>1005</u>	ชื่อผู้ตรวจสอบ <u>1005</u>

ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
-------	--------	----	-------	-----------	----------

FIRE ALARM CONTROL PANEL

1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>138</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>150</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>260</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>0.9</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>230</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ

- ☒ 1. ปฏิบัติงานเสร็จเรียบร้อย
 ☒ 2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL


 กระทรวงสาธารณสุข
 กรมสุขภาพจิต

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>1/10/1/1/1</u> 2.
วันที่ปฏิบัติ <u>96/11/18</u>	3. 4.
ชื่ออาคาร <u>5</u> ชื่อผู้ควบคุม <u>1/10/1/1/1</u> ชื่อผู้ตรวจสอบ <u>100%</u>	5. 6.

		ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
FIRE ALARM CONTROL PANEL					
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>13.0</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>13.2</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>14.9</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>2.9</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>230</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งผิดปกติ (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เซ็นเซอร์ เทคโนโลยี จำกัด
Sensors Technology Public Co., Ltd.

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>เอกวิ</u> 2.
วันที่ปฏิบัติ <u>26/11/18</u>	3. 4.
ชื่ออาคาร <u>5</u> ชื่อผู้ควบคุม <u>เอกวิ</u> ชื่อผู้ตรวจสอบ <u>10091</u>	5. 6.

ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
-------	--------	----	-------	-----------	----------

FIRE ALARM CONTROL PANEL

1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>13.6</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>13.2</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>13.0</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>0.9V</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>9.50</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เซ็นเซอร์ เทคโนโลยี จำกัด
SENSE PROTECT WORLD CO., LTD.

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>กฤษกร</u> 2.
วันที่ปฏิบัติ <u>๑๖/๐๓/๖๗</u>	3. 4.
ชื่ออาคาร <u>๑</u>	5. 6.
ชื่อผู้ควบคุม <u>กฤษกร</u>	ชื่อผู้ตรวจสอบ <u>กฤษกร</u>

ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
-------	--------	----	-------	-----------	----------

FIRE ALARM CONTROL PANEL

1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>190</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>19.2</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>150</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>๐๙๗</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>050</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

.....

.....

.....

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL

บริษัท ฟูมฟอส จำกัด
FUMFOS COMPANY LIMITED CO., LTD.

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน	
รหัสอุปกรณ์	1. <u>ไกรธ</u>	2.
วันที่ปฏิบัติ <u>28/5.6/64</u>	3.	4.
ชื่ออาคาร <u>9</u>	5.	6.
ชื่อผู้ควบคุม <u>ไกรธ</u>	ชื่อผู้ตรวจสอบ <u>100571</u>	

ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
-------	--------	----	-------	-----------	----------

FIRE ALARM CONTROL PANEL

1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1..... <u>12.8</u> VDC	✓			
	ตรวจเช็ค BATTERY No2..... <u>13.0</u> VDC	✓			
	ตรวจเช็ค BATTERYรวม..... <u>95.0</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY..... <u>0.98</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ..... <u>0.80</u> VAC	✓			
5	ตรวจเช็คไฟ SHOWตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เพรสเซอร์ เวิลด์ จำกัด
PRESSURE WORLD CO., LTD.

รหัสงาน.....	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์.....	1. <u>11/591-1-1051</u> 2.
วันที่ปฏิบัติ <u>05 / 8.7 / 91</u>	3. 4.
ชื่ออาคาร <u>5</u> ชื่อผู้ควบคุม <u>11/591-1-1051</u> ชื่อผู้ตรวจสอบ <u>1002910</u>	5. 6.

ผลการตรวจเช็ค			
ลำดับ	รายการ	ดี	แก้ไข

FIRE ALARM CONTROL PANEL			
ลำดับ	รายการ	ดี	แก้ไข
1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓	
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓	
3	ตรวจเช็ค BATTERY No1 <u>190</u> VDC	✓	
	ตรวจเช็ค BATTERY No2 <u>192</u> VDC	✓	
	ตรวจเช็ค BATTERY รวม <u>382</u> VDC	✓	
	ตรวจเช็คไฟชาร์จ BATTERY <u>09%</u> VDC	✓	
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>230</u> VAC	✓	
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓	
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓	
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓	
8	ตรวจเช็คสภาพตู้ FCP	✓	
9	ตรวจสอบอุปกรณ์ Manual	✓	
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓	

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย



2. ปฏิบัติงานแล้วเสร็จพบสิ่งที่ต้องแก้ไขอีก (CM)

ตารางตรวจเช็ค FIRE ALARM CONTROL PANEL



บริษัท เจริญรุ่งเรือง จำกัด
CHANG PONGSANG PAPER CO., LTD.

รหัสงาน	รายชื่อพนักงานที่ปฏิบัติงาน
รหัสอุปกรณ์	1. <u>01/25</u> 2.
วันที่ปฏิบัติ <u>๑๕/๐๓/๕๕</u>	3. 4.
ชื่ออาคาร <u>5</u> ชื่อผู้ควบคุม <u>01/25</u> ชื่อผู้ตรวจสอบ <u>100/๕๕</u>	5. 6.

ลำดับ	รายการ	ดี	แก้ไข	อาการเสีย	หมายเหตุ
-------	--------	----	-------	-----------	----------

FIRE ALARM CONTROL PANEL

1	ตรวจเช็คจุดต่อ และ SOCKET สาย	✓			
2	ตรวจเช็คสภาพสายสัญญาณภายในตู้	✓			
3	ตรวจเช็ค BATTERY No1 <u>19.๐</u> VDC	✓			
	ตรวจเช็ค BATTERY No2 <u>19.๐</u> VDC	✓			
	ตรวจเช็ค BATTERY รวม <u>16.๐</u> VDC	✓			
	ตรวจเช็คไฟชาร์จ BATTERY <u>๑๑๕</u> VDC	✓			
4	ตรวจเช็คแรงดันที่จ่ายให้ระบบ <u>๑๕๐</u> VAC	✓			
5	ตรวจเช็คไฟ SHOW ตู้ FCP	✓			
6	ตรวจเช็คจอแสดงผล (LCD DISPLAY)	✓			
7	ตรวจเช็คชุด GRAPHIC ANNUNCIATER	✓			
8	ตรวจเช็คสภาพตู้ FCP	✓			
9	ตรวจสอบอุปกรณ์ Manual	✓			
10	ทดสอบ FUNCTION การทำงานที่ตู้ FCP	✓			

หมายเหตุ

บันทึกผลการปฏิบัติ



1. ปฏิบัติงานเสร็จเรียบร้อย




2. ปฏิบัติงานแล้วเสร็จพบสิ่งผิดปกติ (CM)


ภาคผนวก ๓

รายงานการใช้ระบบไฟฟ้า และประปา ประจำวัน


แผนภูมิแสดงการจดบันทึกมีเตอร์น้ำส่วนกลาง ประจำเดือน กรกฎาคม

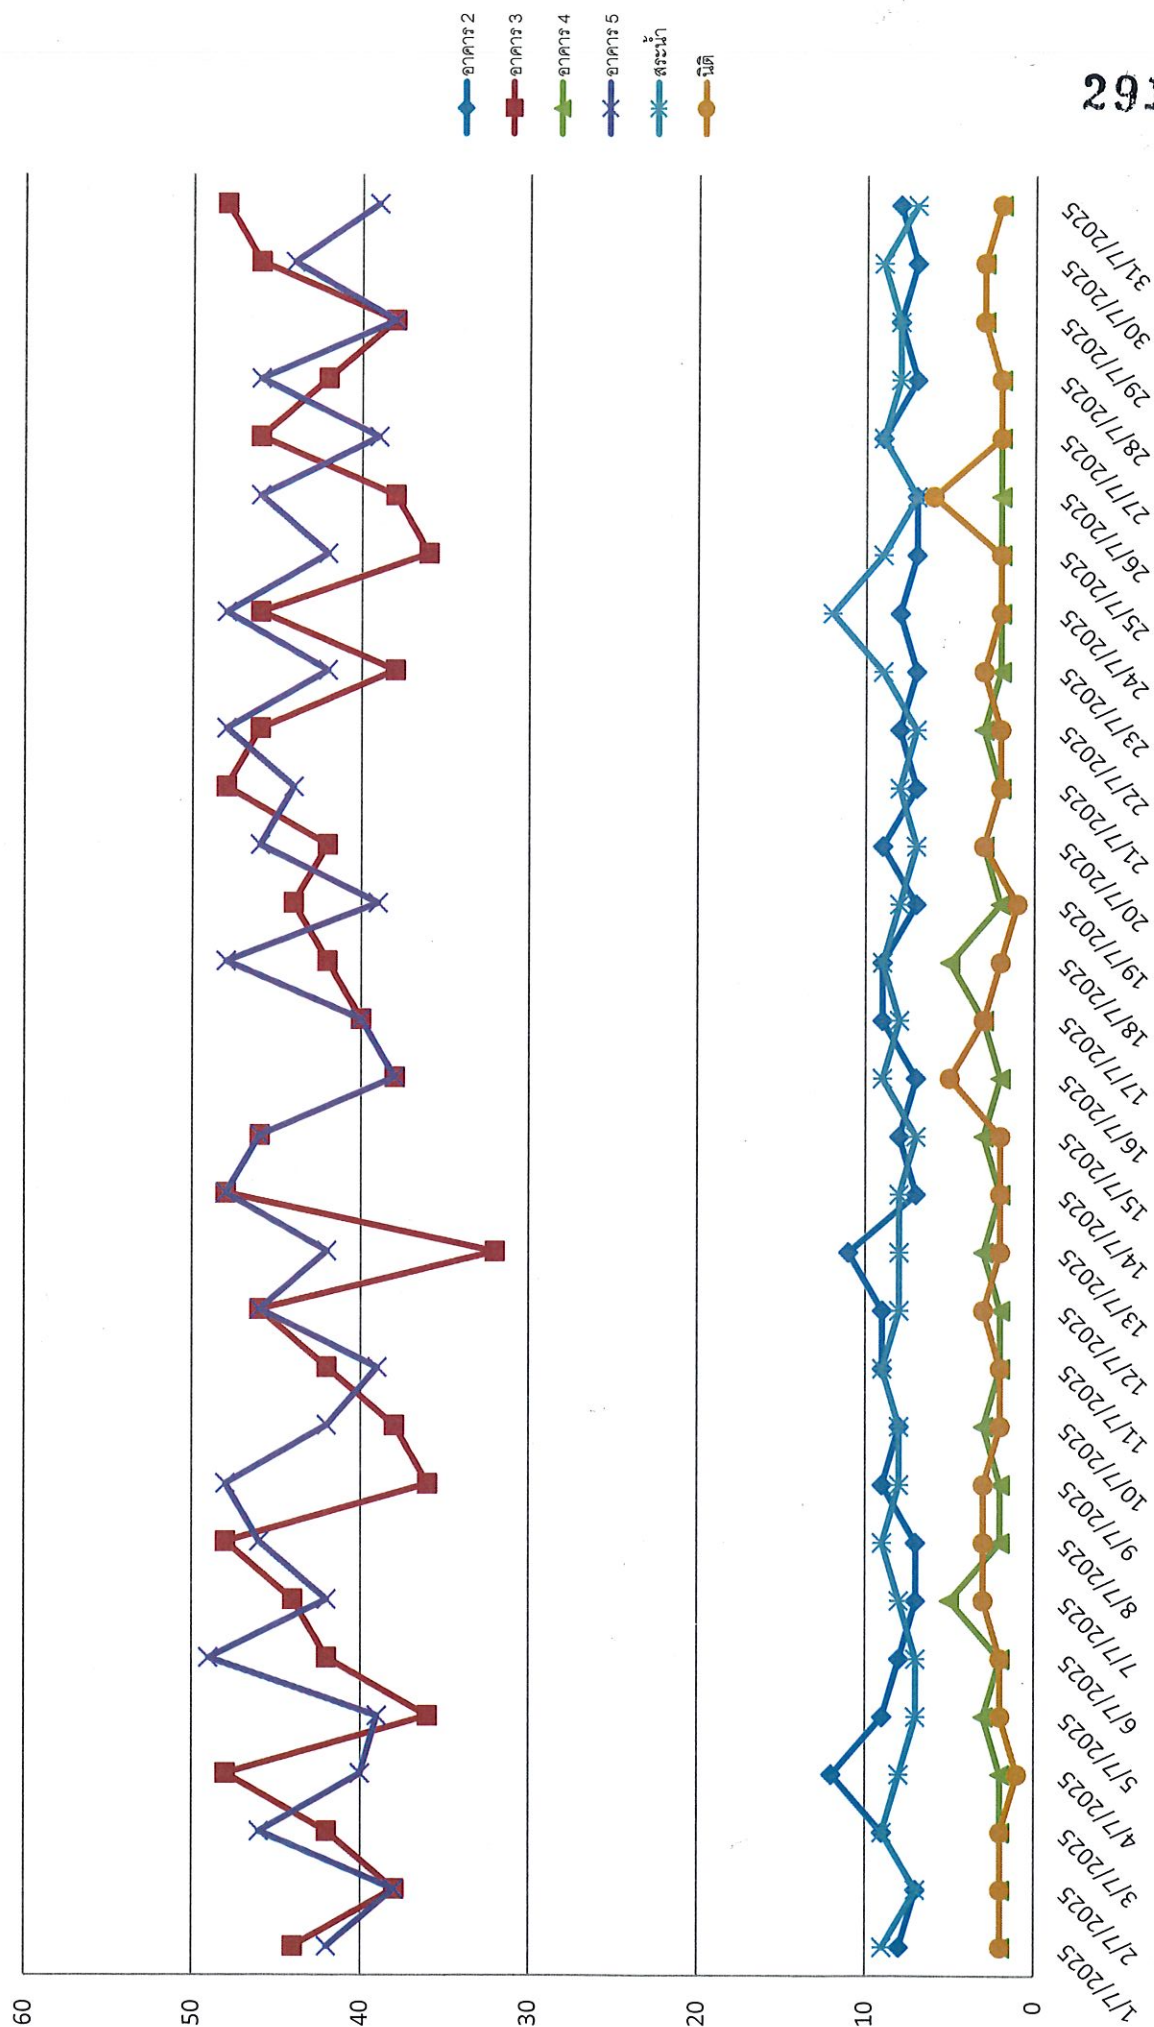


แผนภูมิแสดงการจดบันทึกมีเตอร์น้ำส่วนกลาง ประจำเดือน สิงหาคม

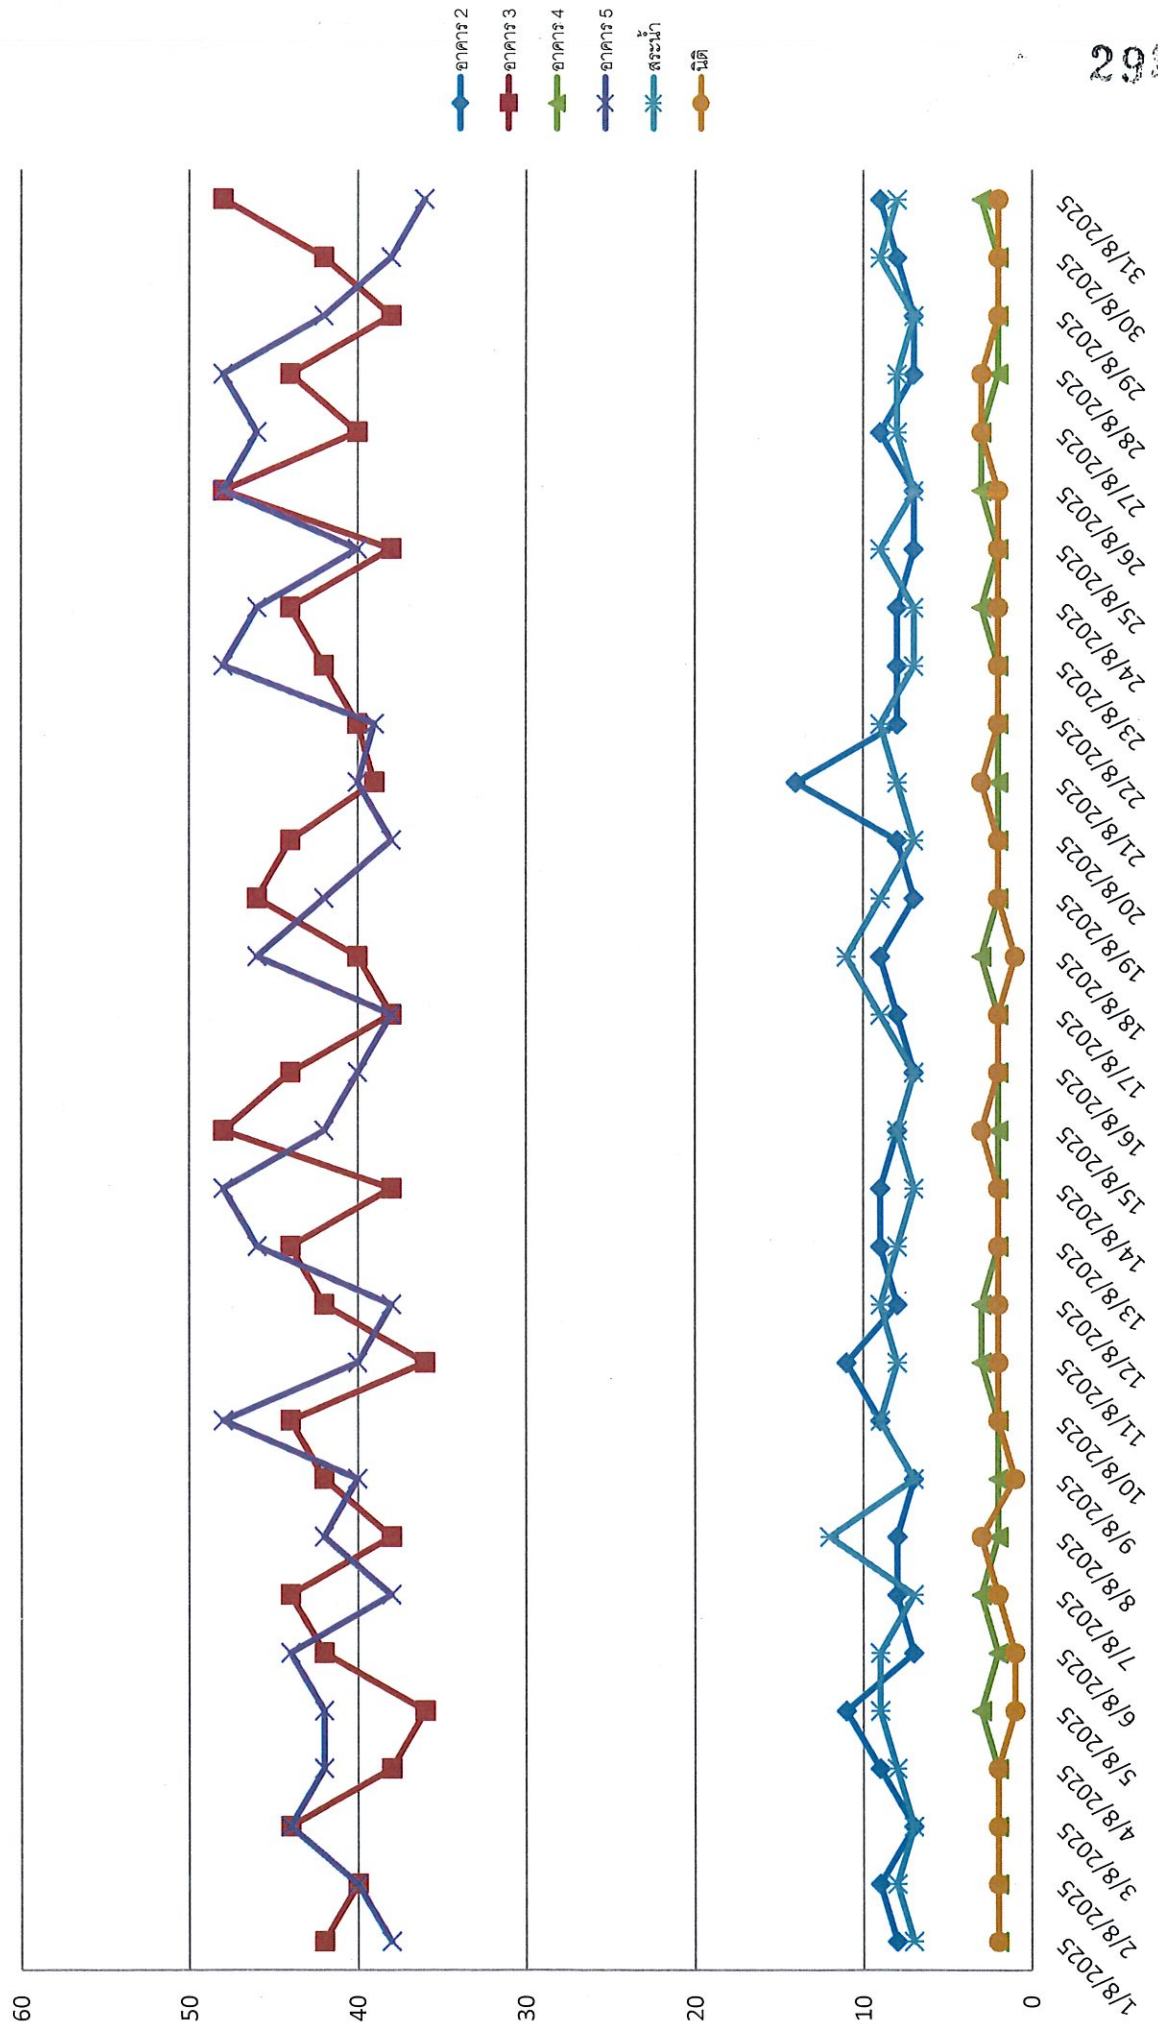


แผนภูมิแสดงการจดบันทึกมีเตอร์น้ำส่วนกลาง ประจำเดือน กันยายน

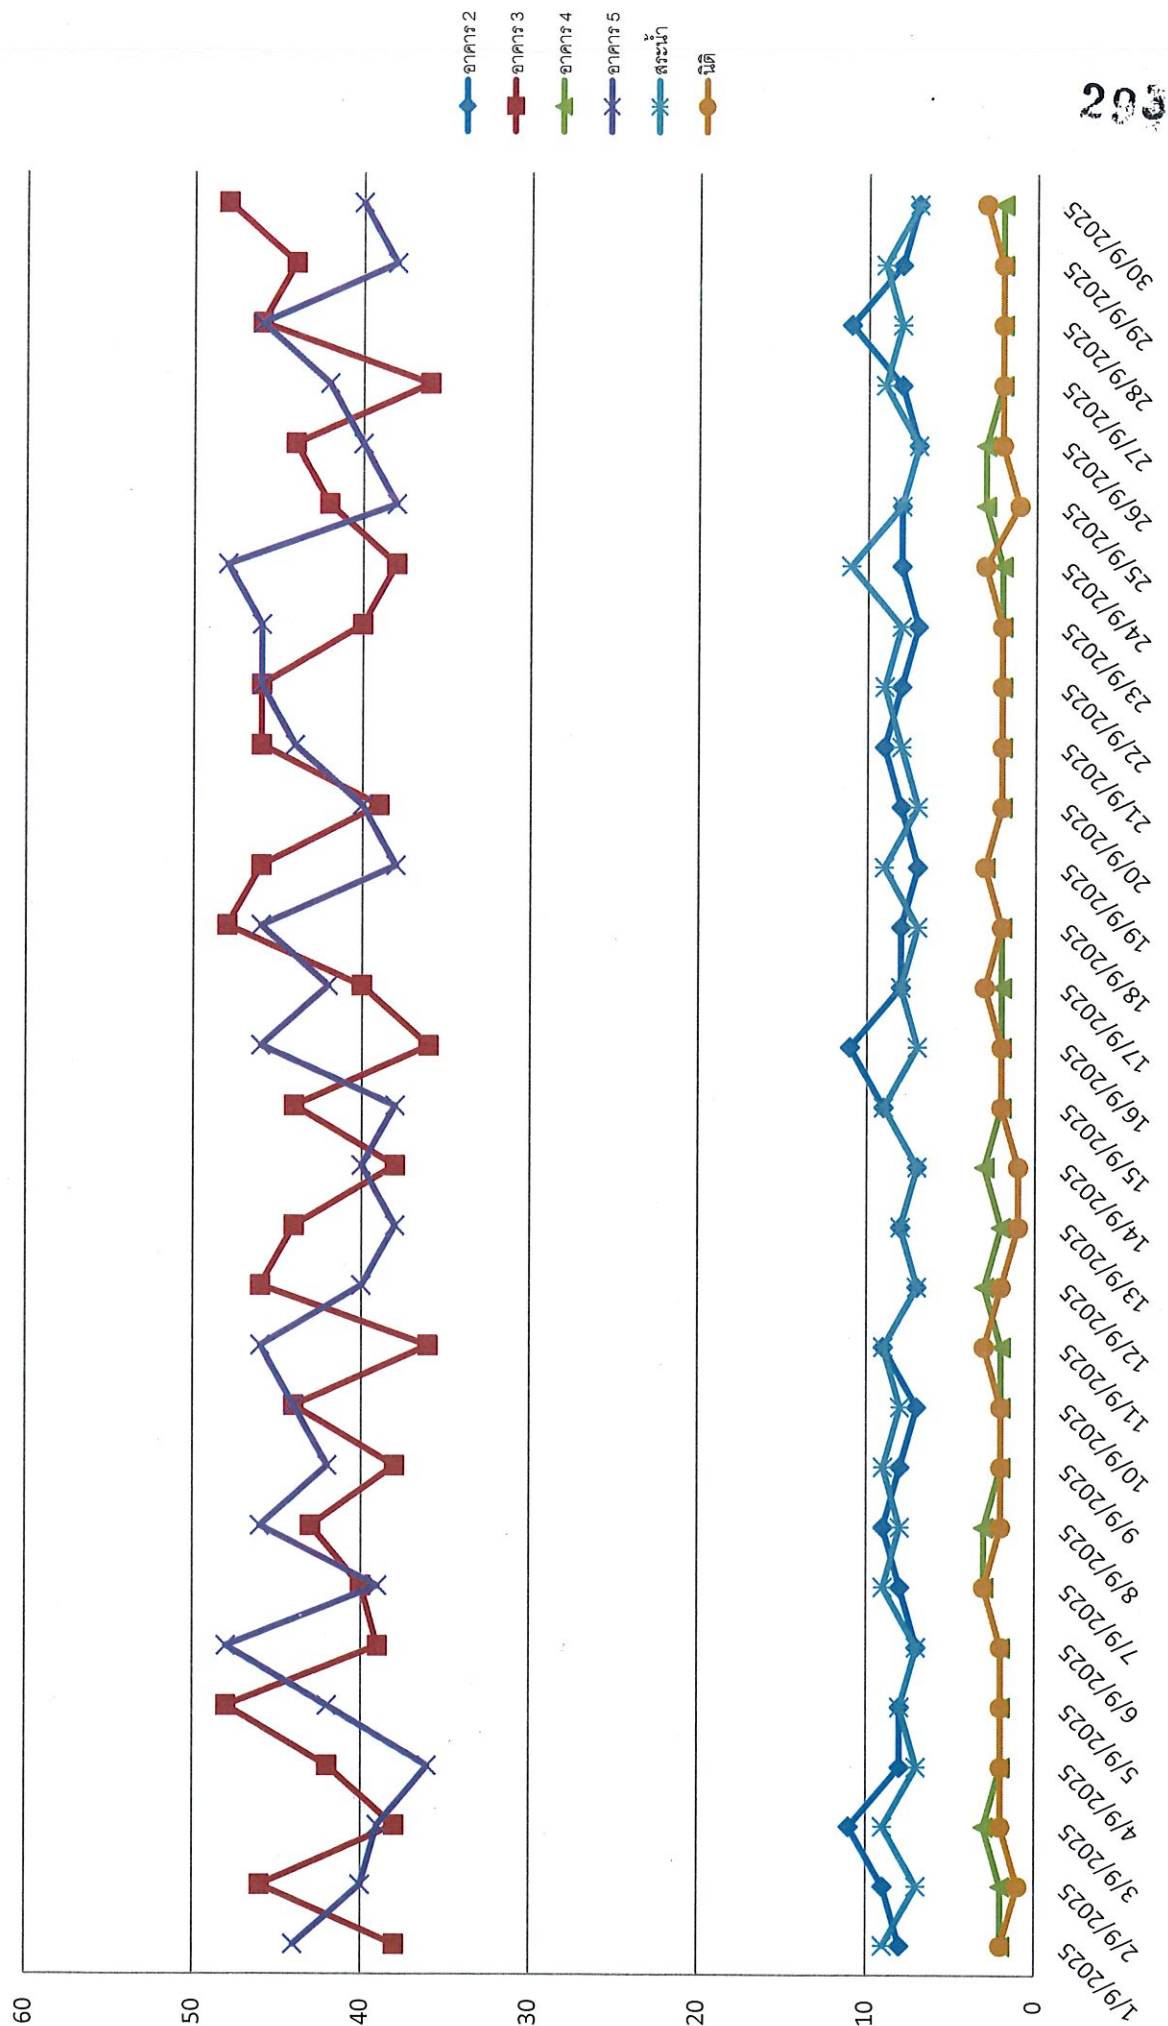


แผนภูมิแสดงการจดบันทึกมีเตอร์น้ำส่วนกลาง ประจำเดือน ตุลาคม

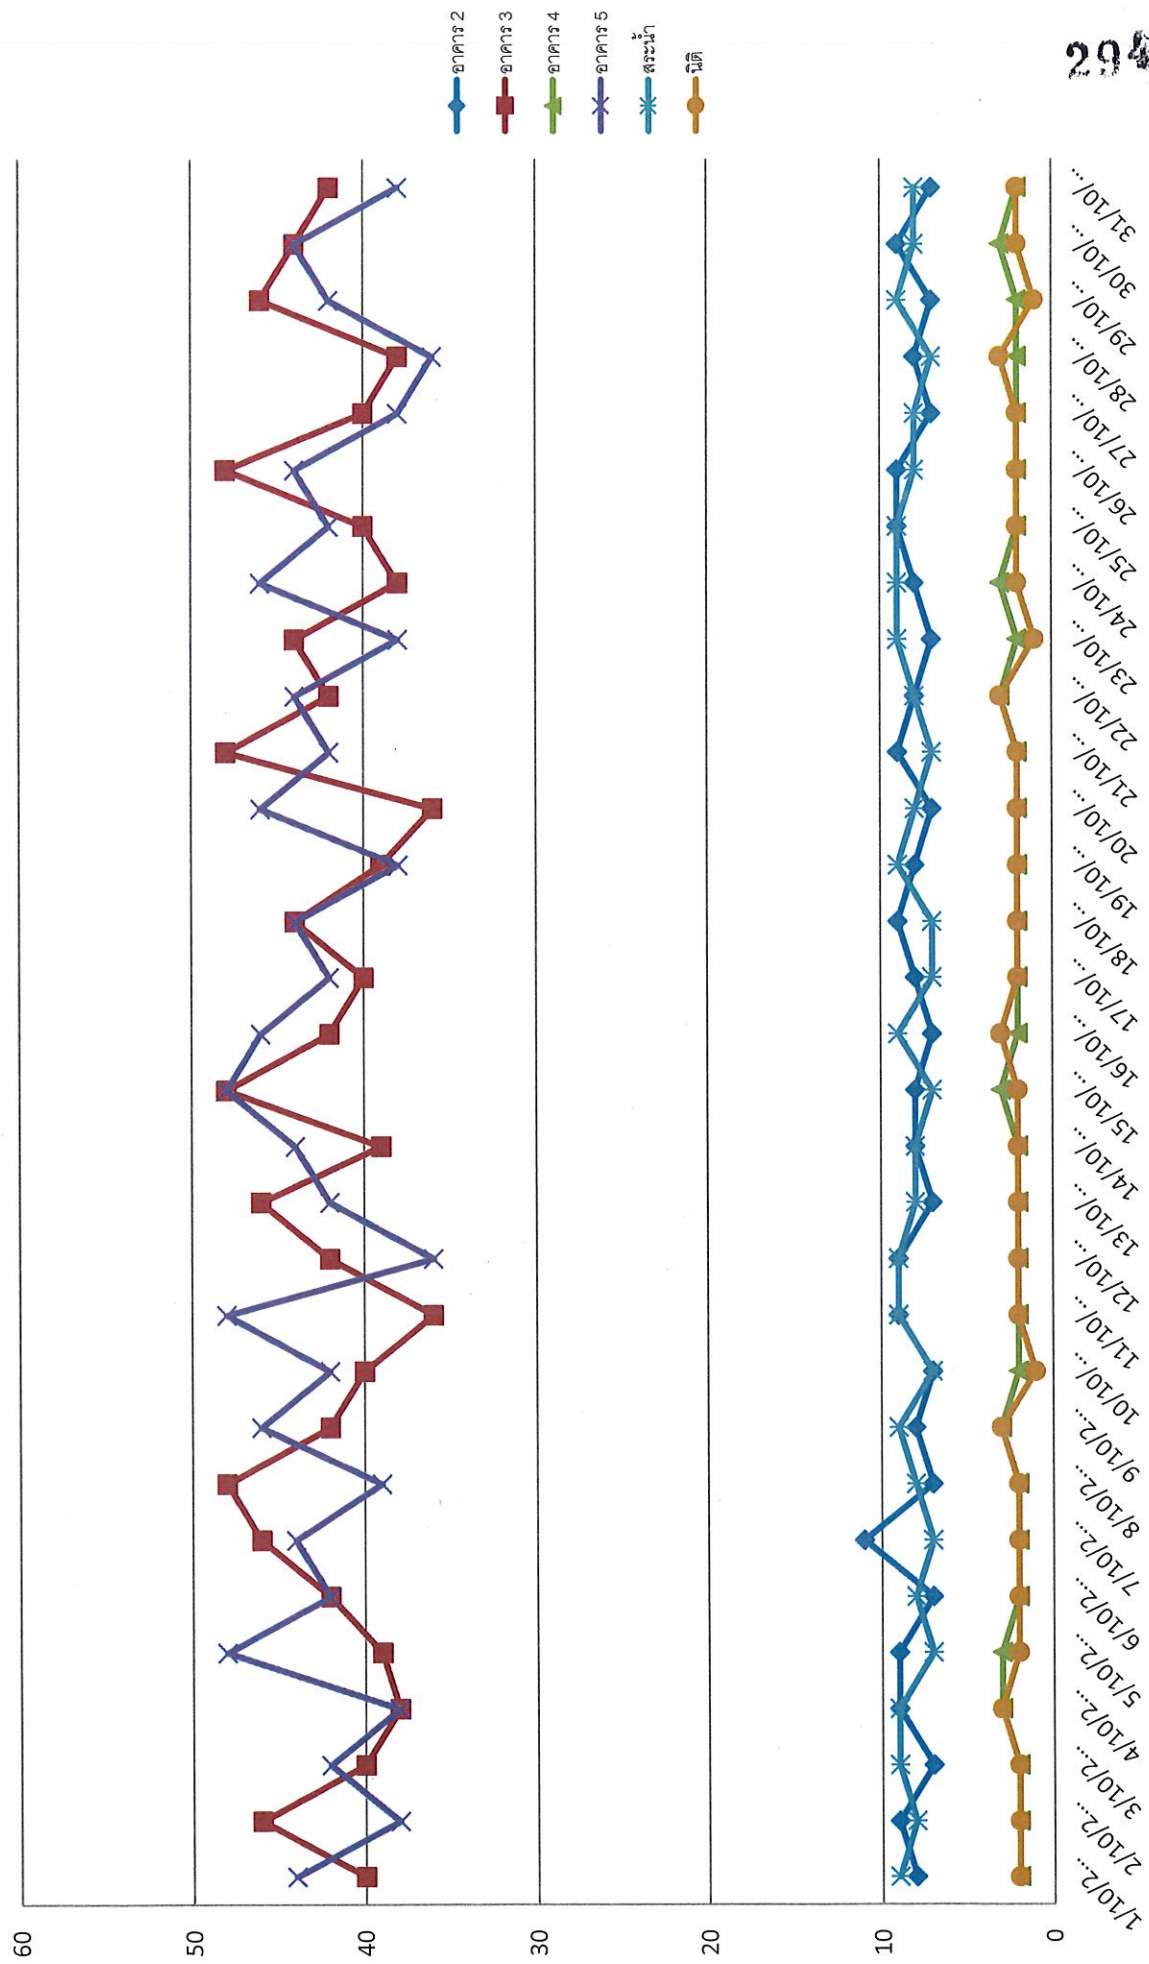


แผนภูมิแสดงการจดบันทึกมีเตอร์น้ำส่วนกลาง ประจำเดือน พฤศจิกายน

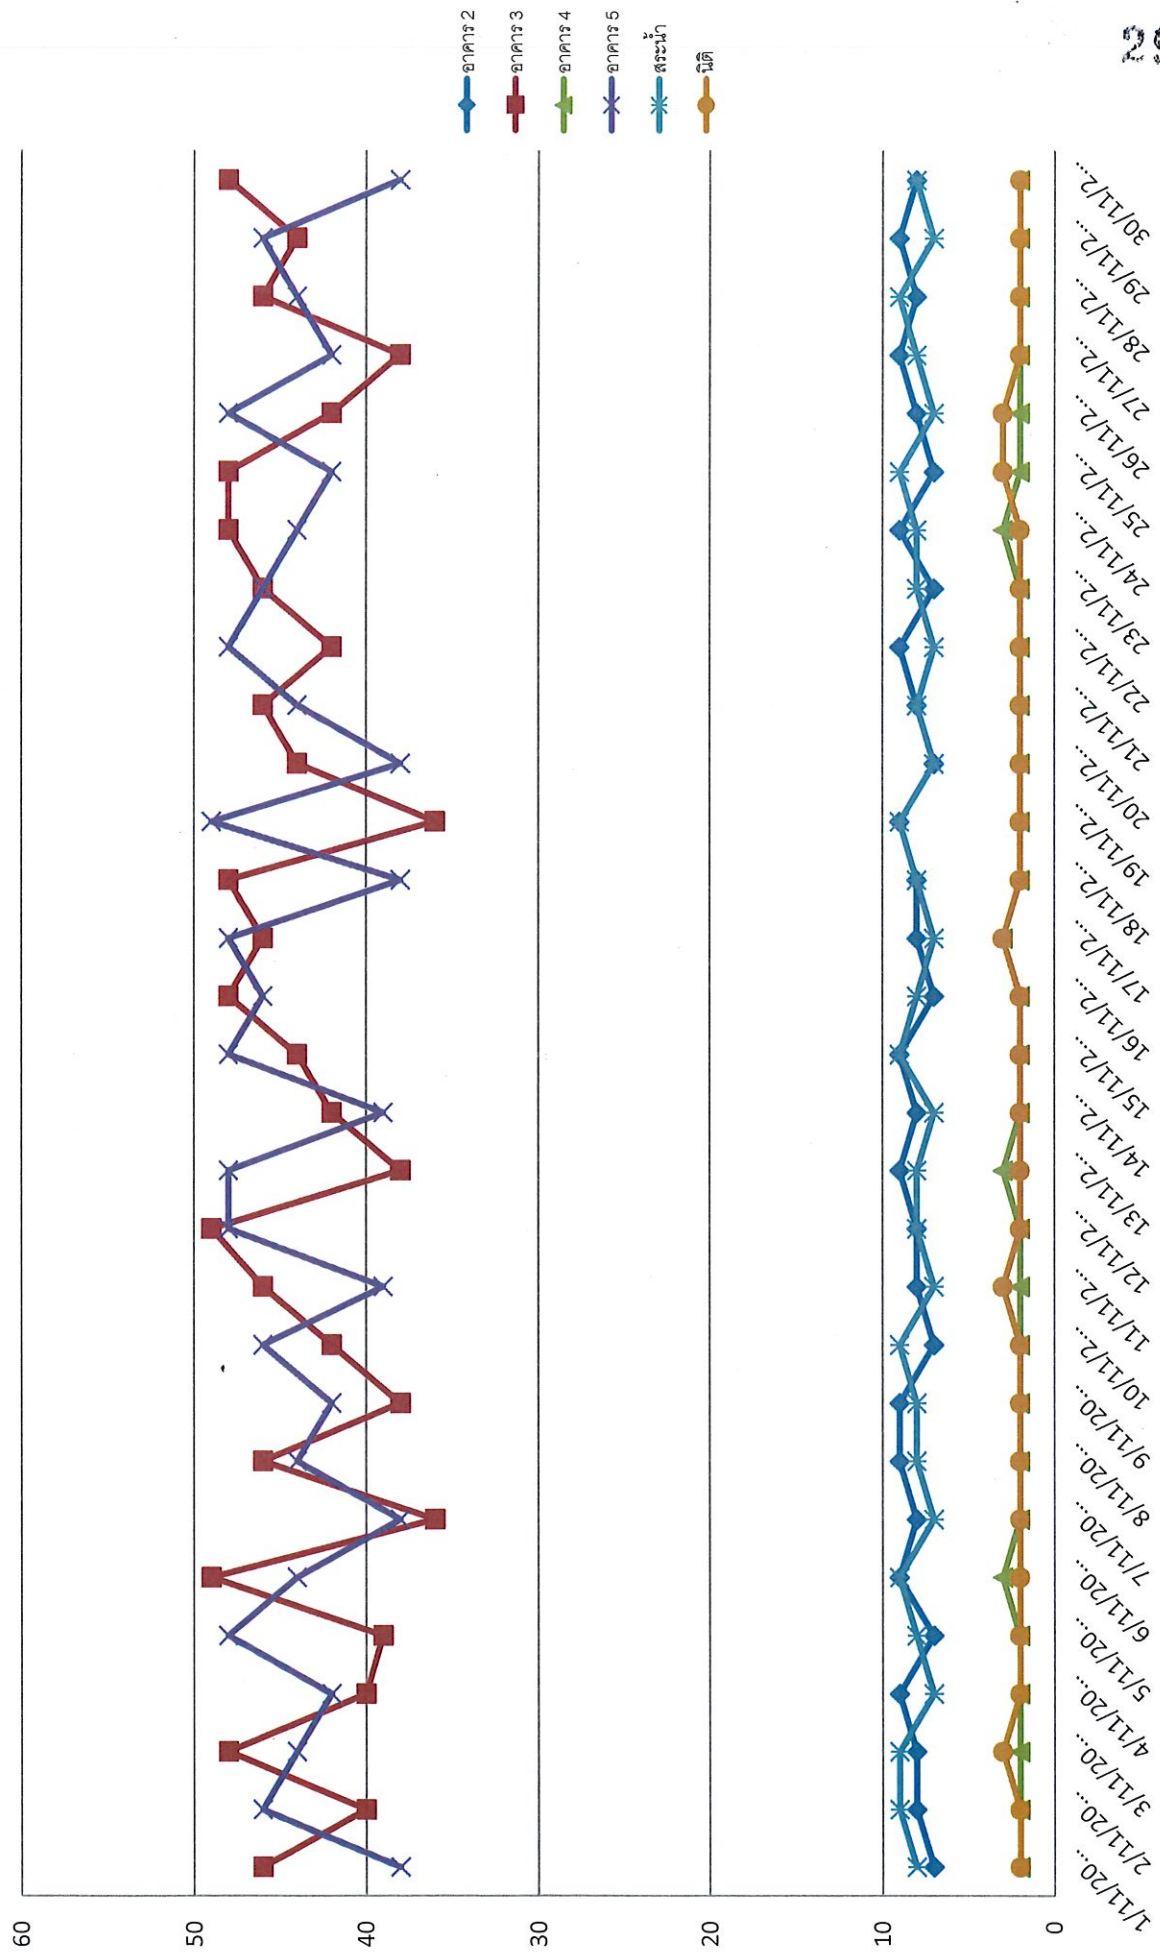


แผนภูมิแสดงการจดบันทึกมีเตอร์น้ำส่วนกลาง ประจำเดือน ธันวาคม

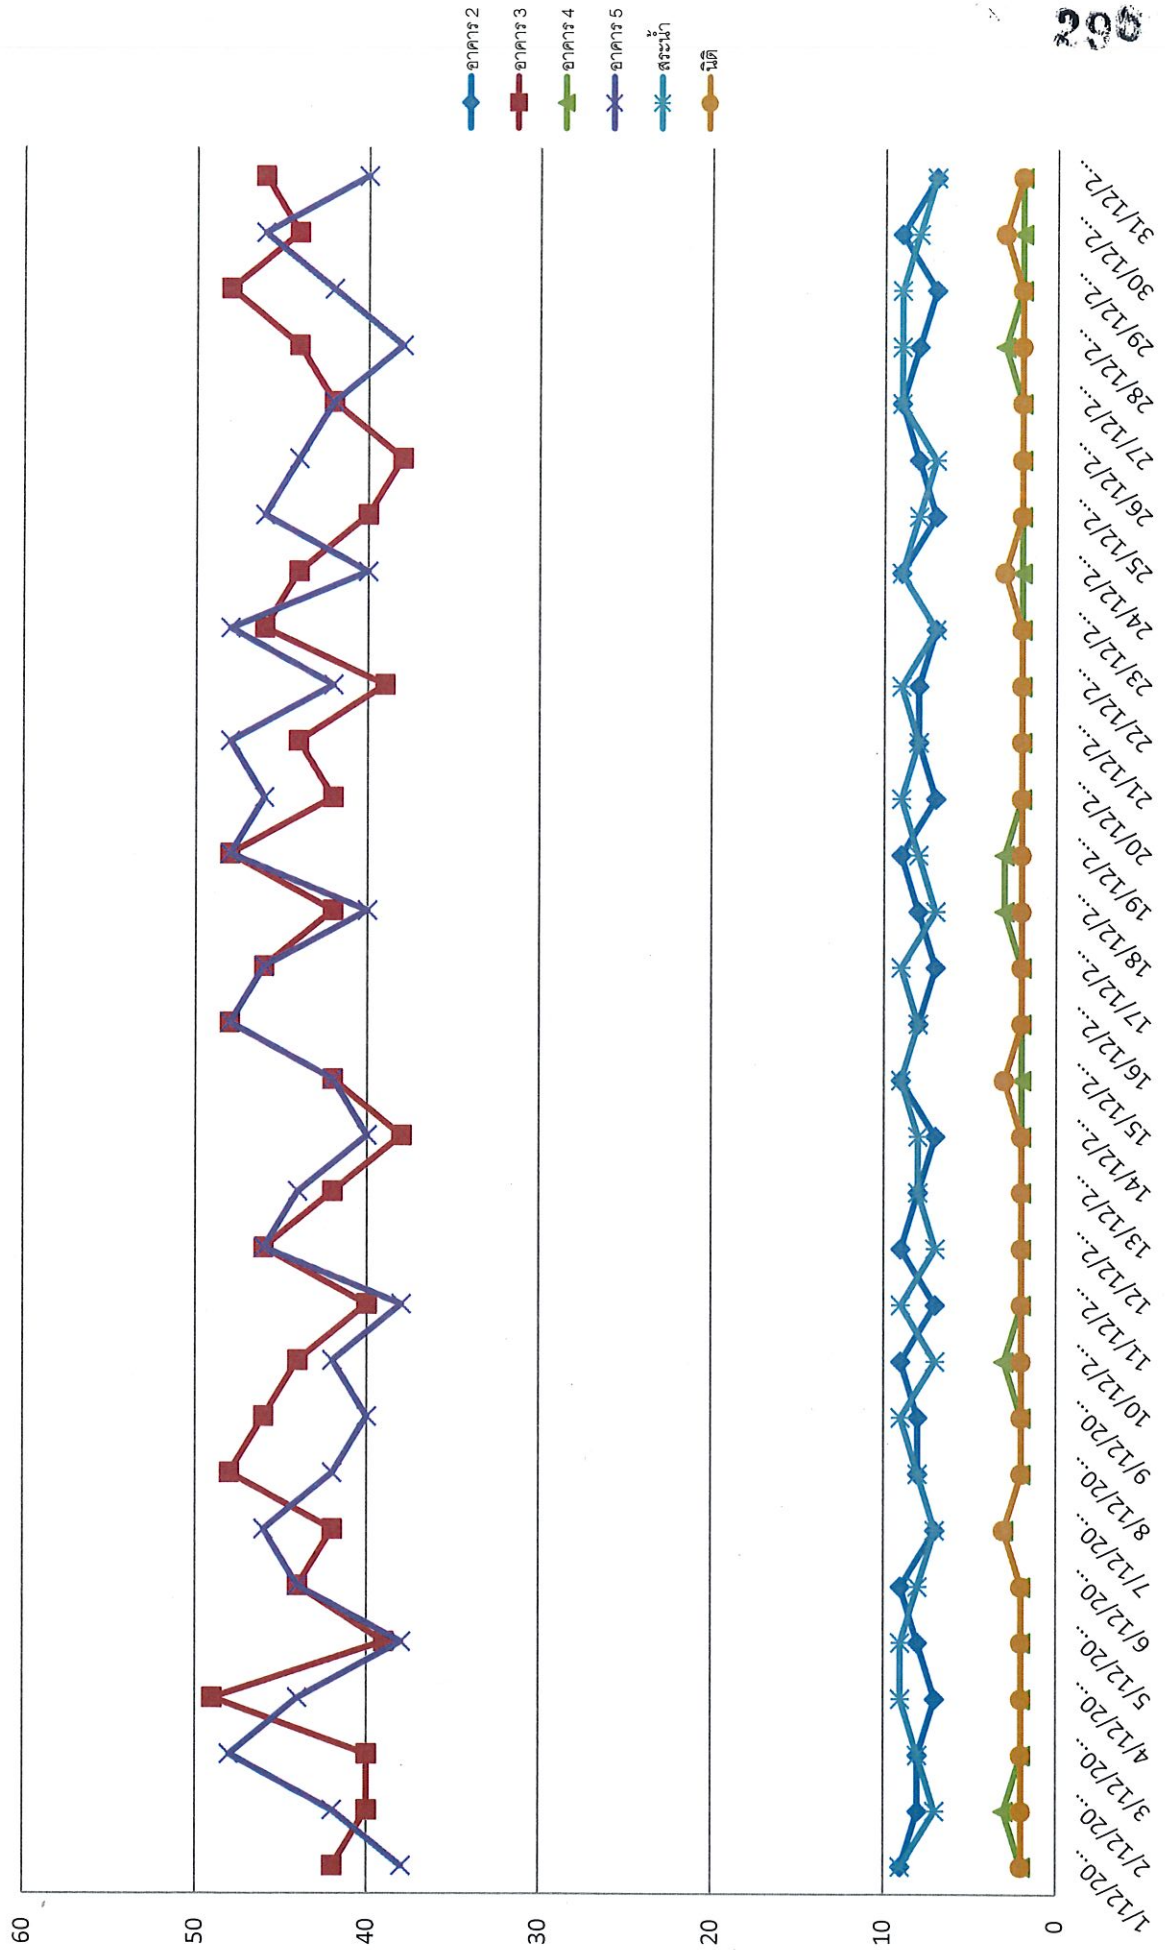


แผนภูมิแสดงการจดบันทึกมีเตอร์ไฟฟ้าส่วนกลาง ประจำเดือน กรกฎาคม

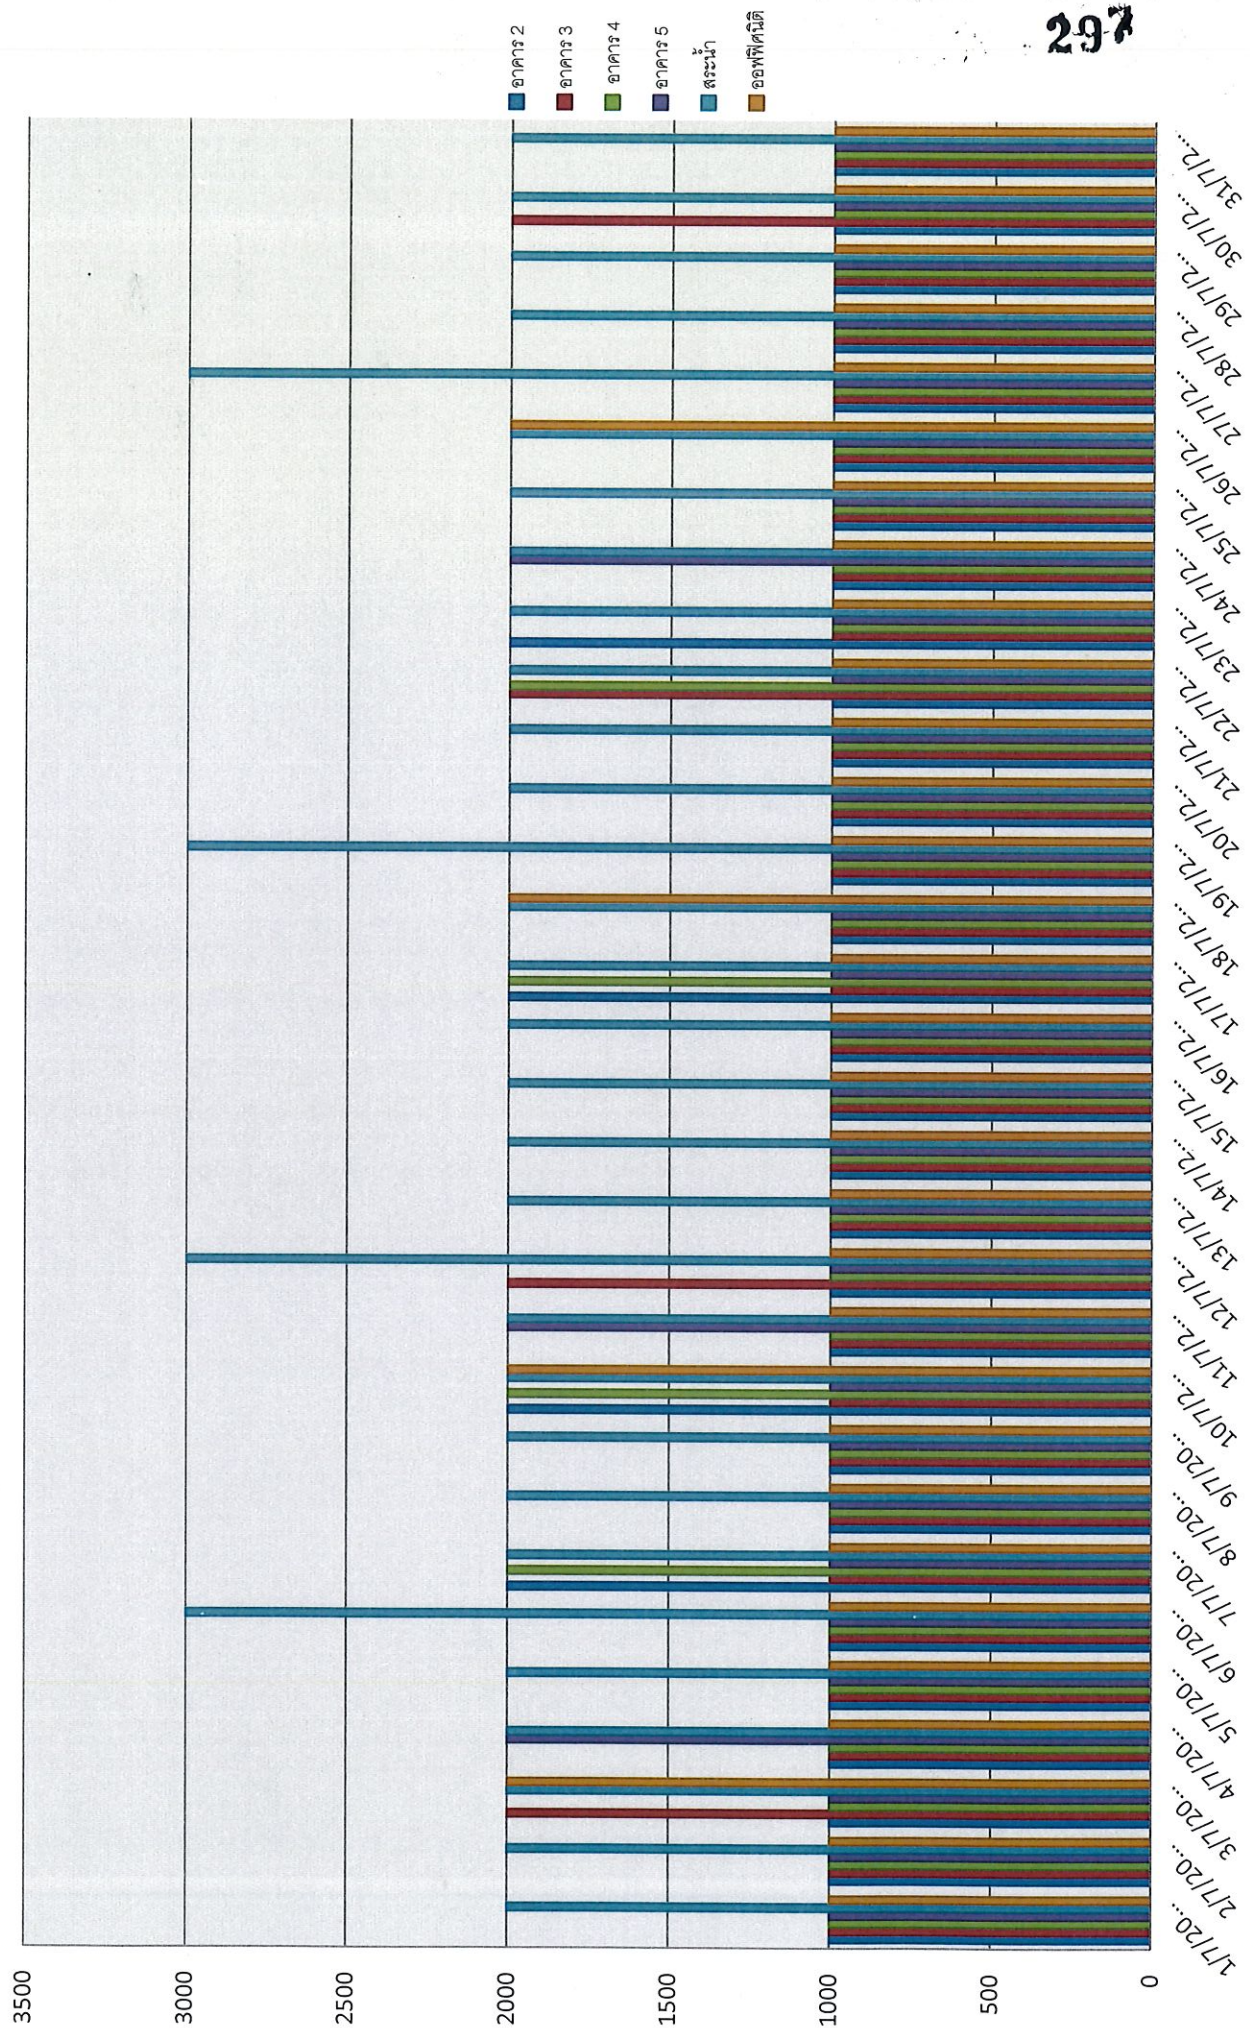


แผนภูมิแสดงการจดบันทึกมีเตอร์ไฟฟ้าส่วนกลาง ประจำเดือน สิงหาคม

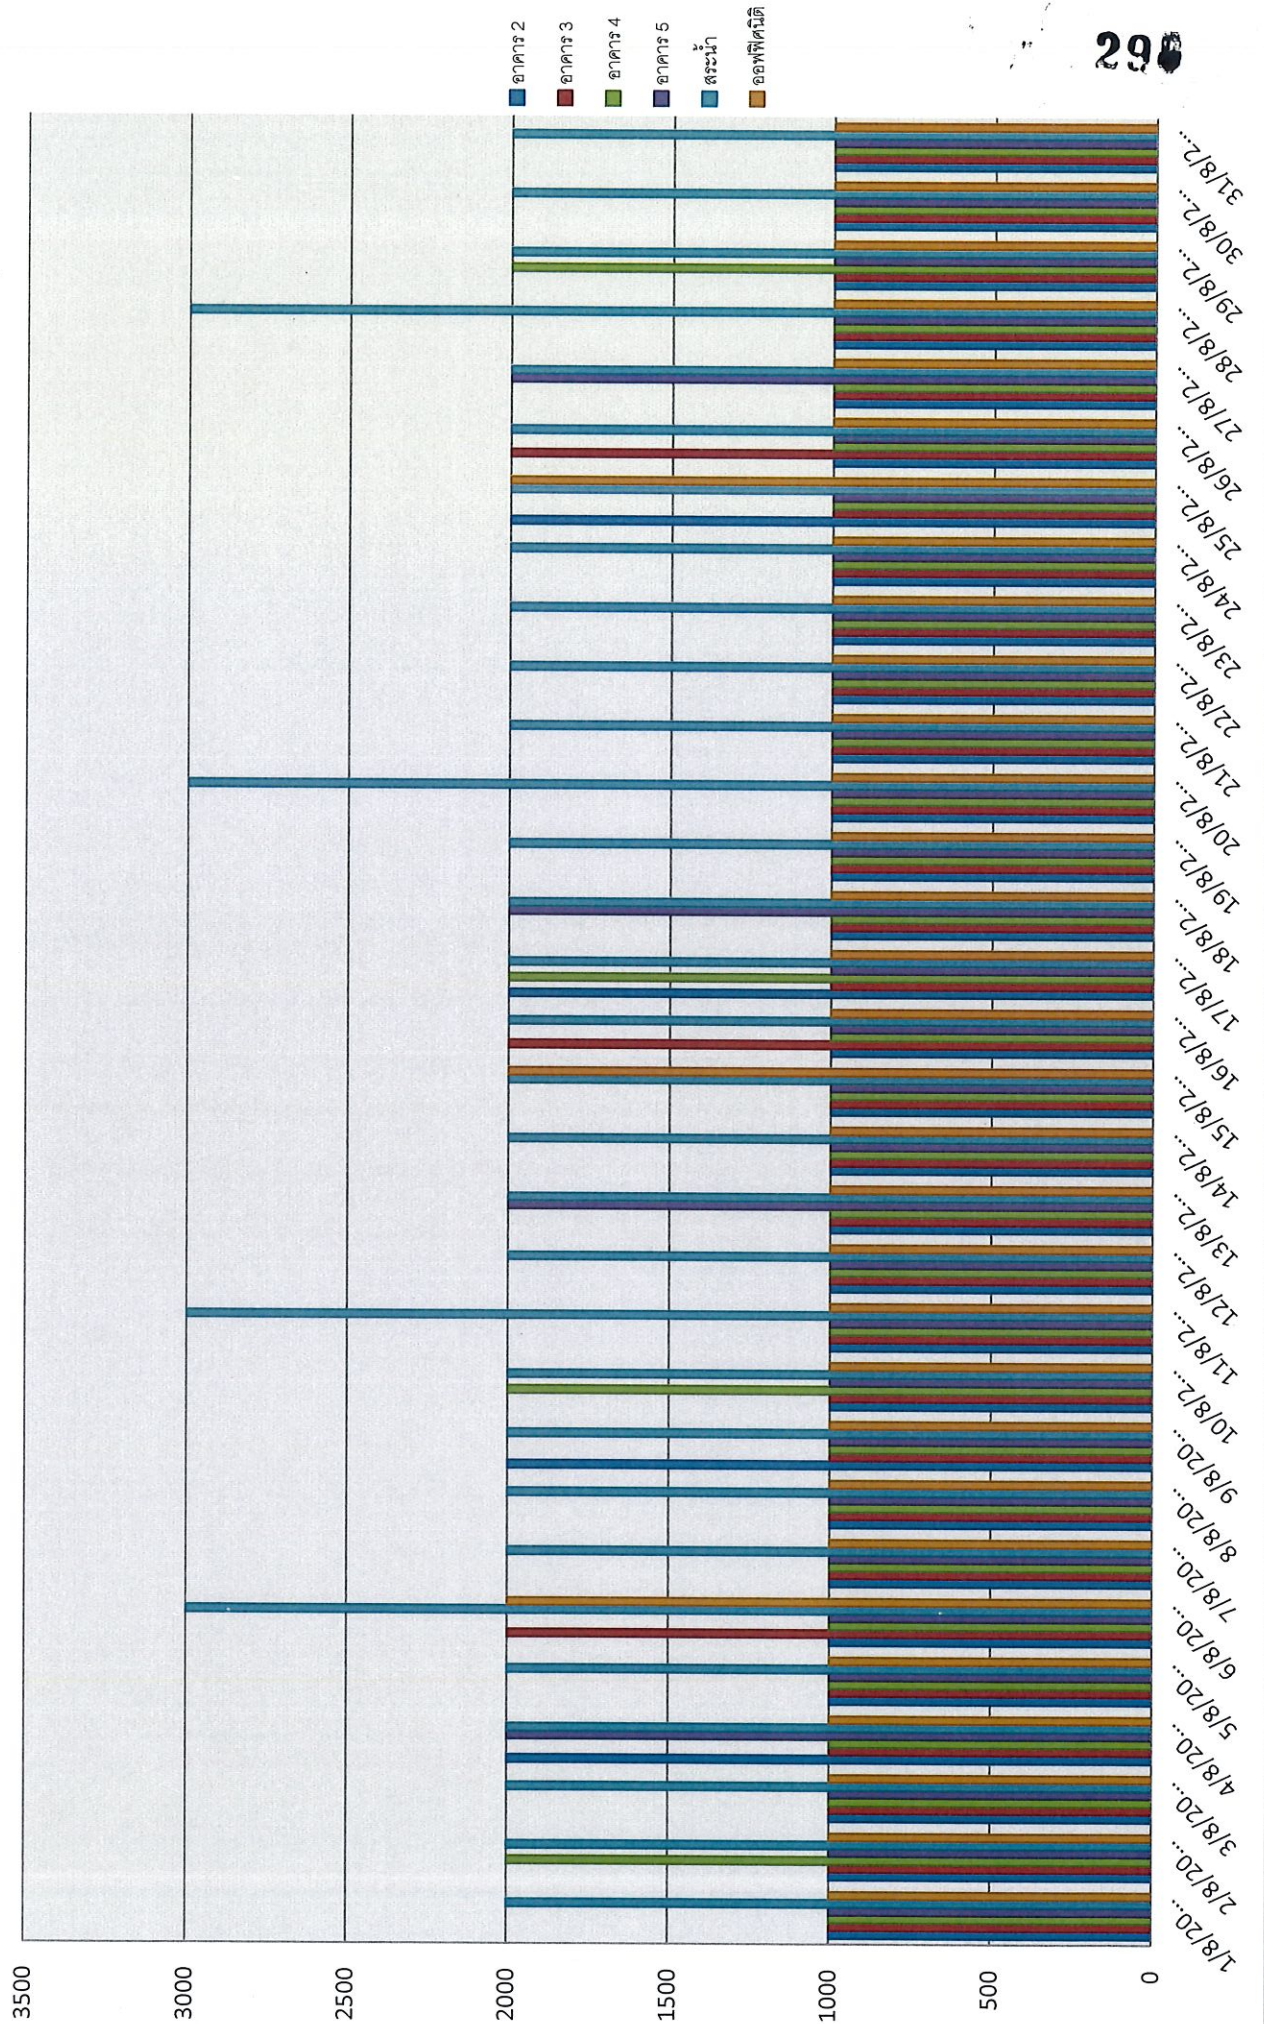

แผนภูมิแสดงการจดบันทึกมีเตอร์ไฟฟ้าส่วนกลาง ประจำเดือน กันยายน

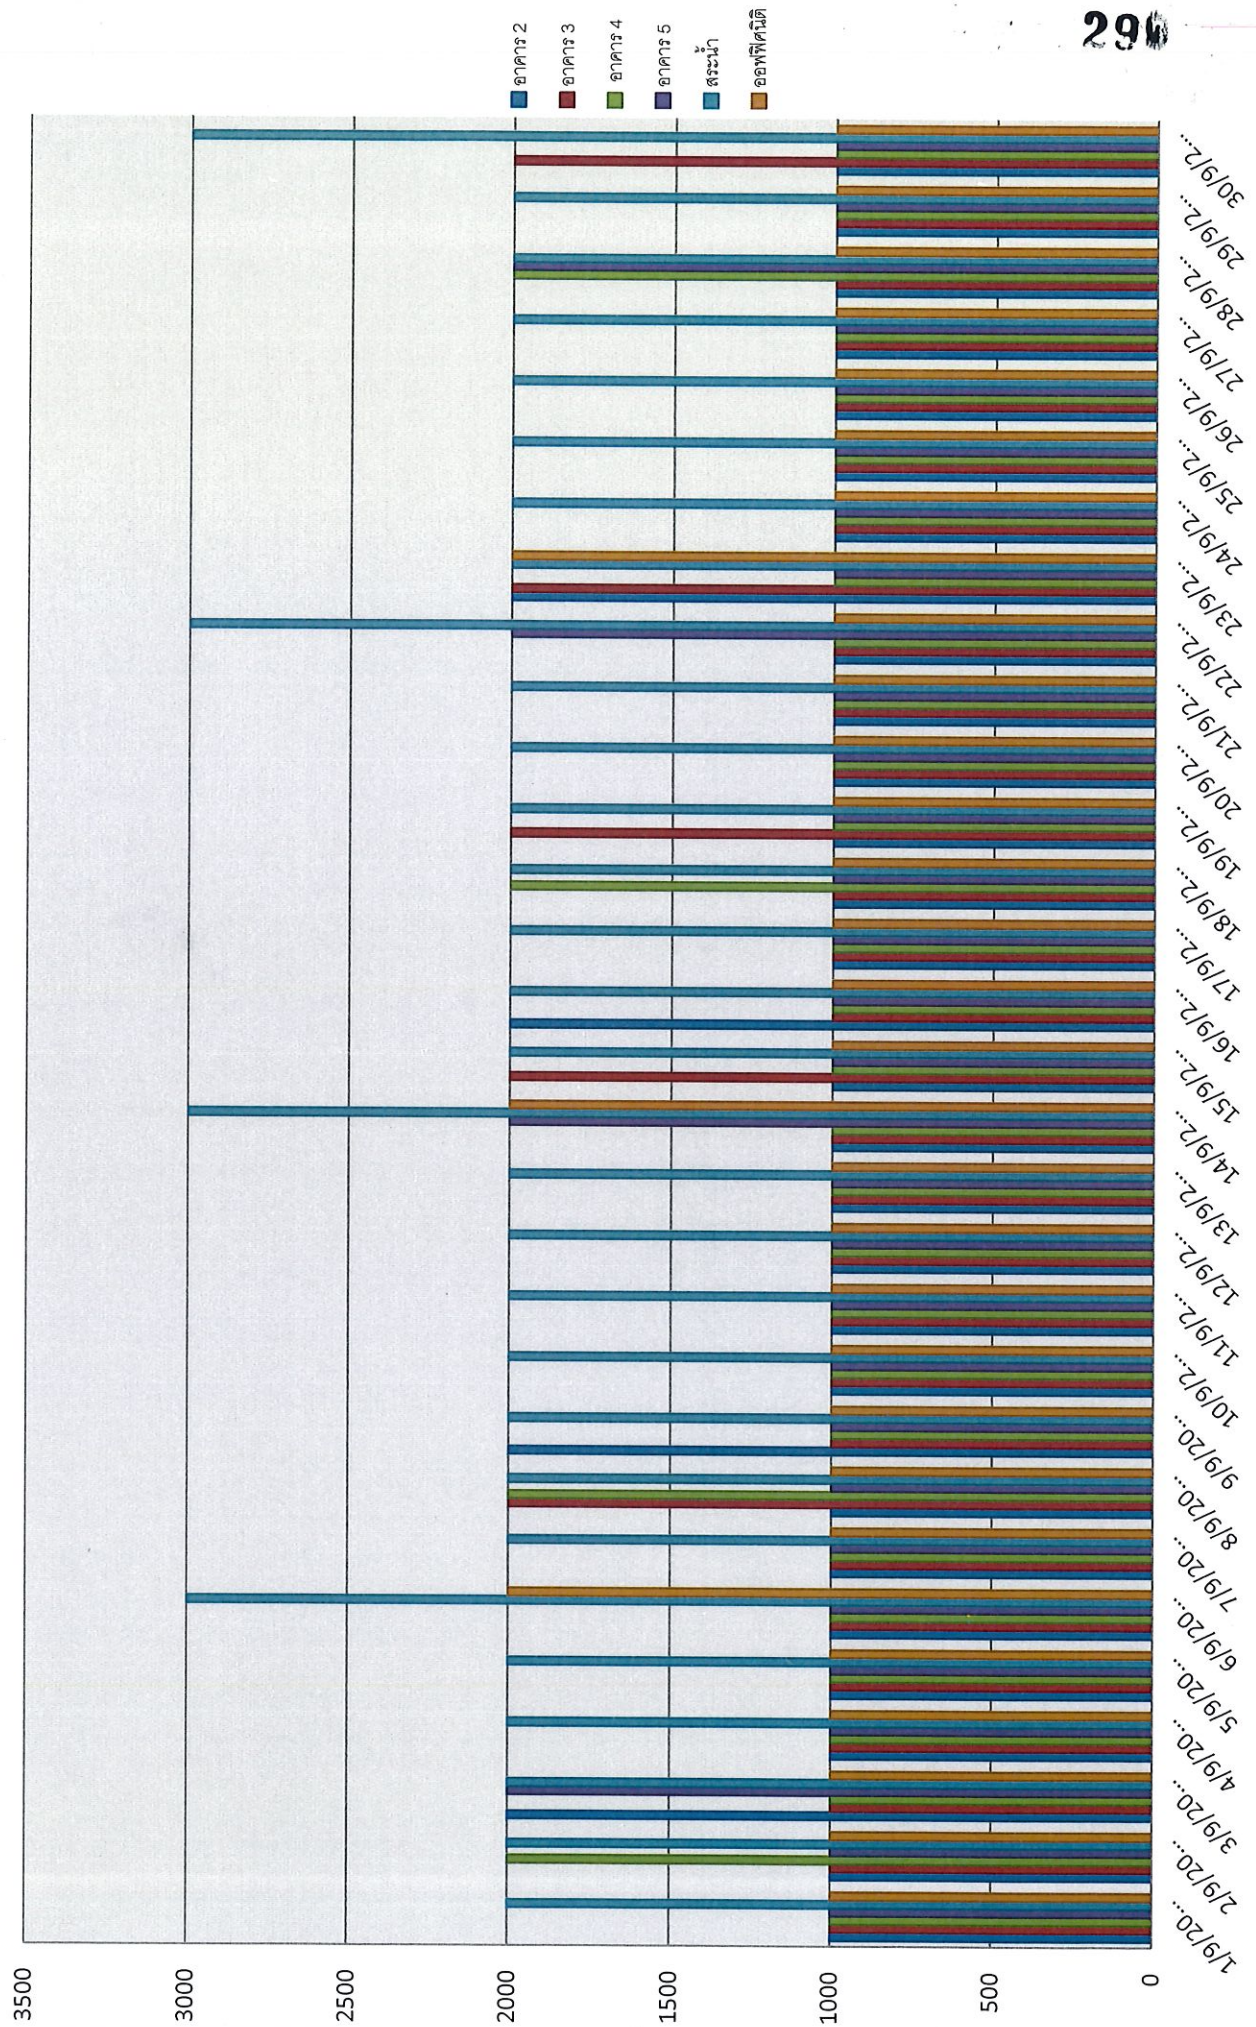

แผนภูมิแสดงการจดบันทึกมีเตอร์ไฟฟ้าส่วนกลาง ประจำเดือน ตุลาคม

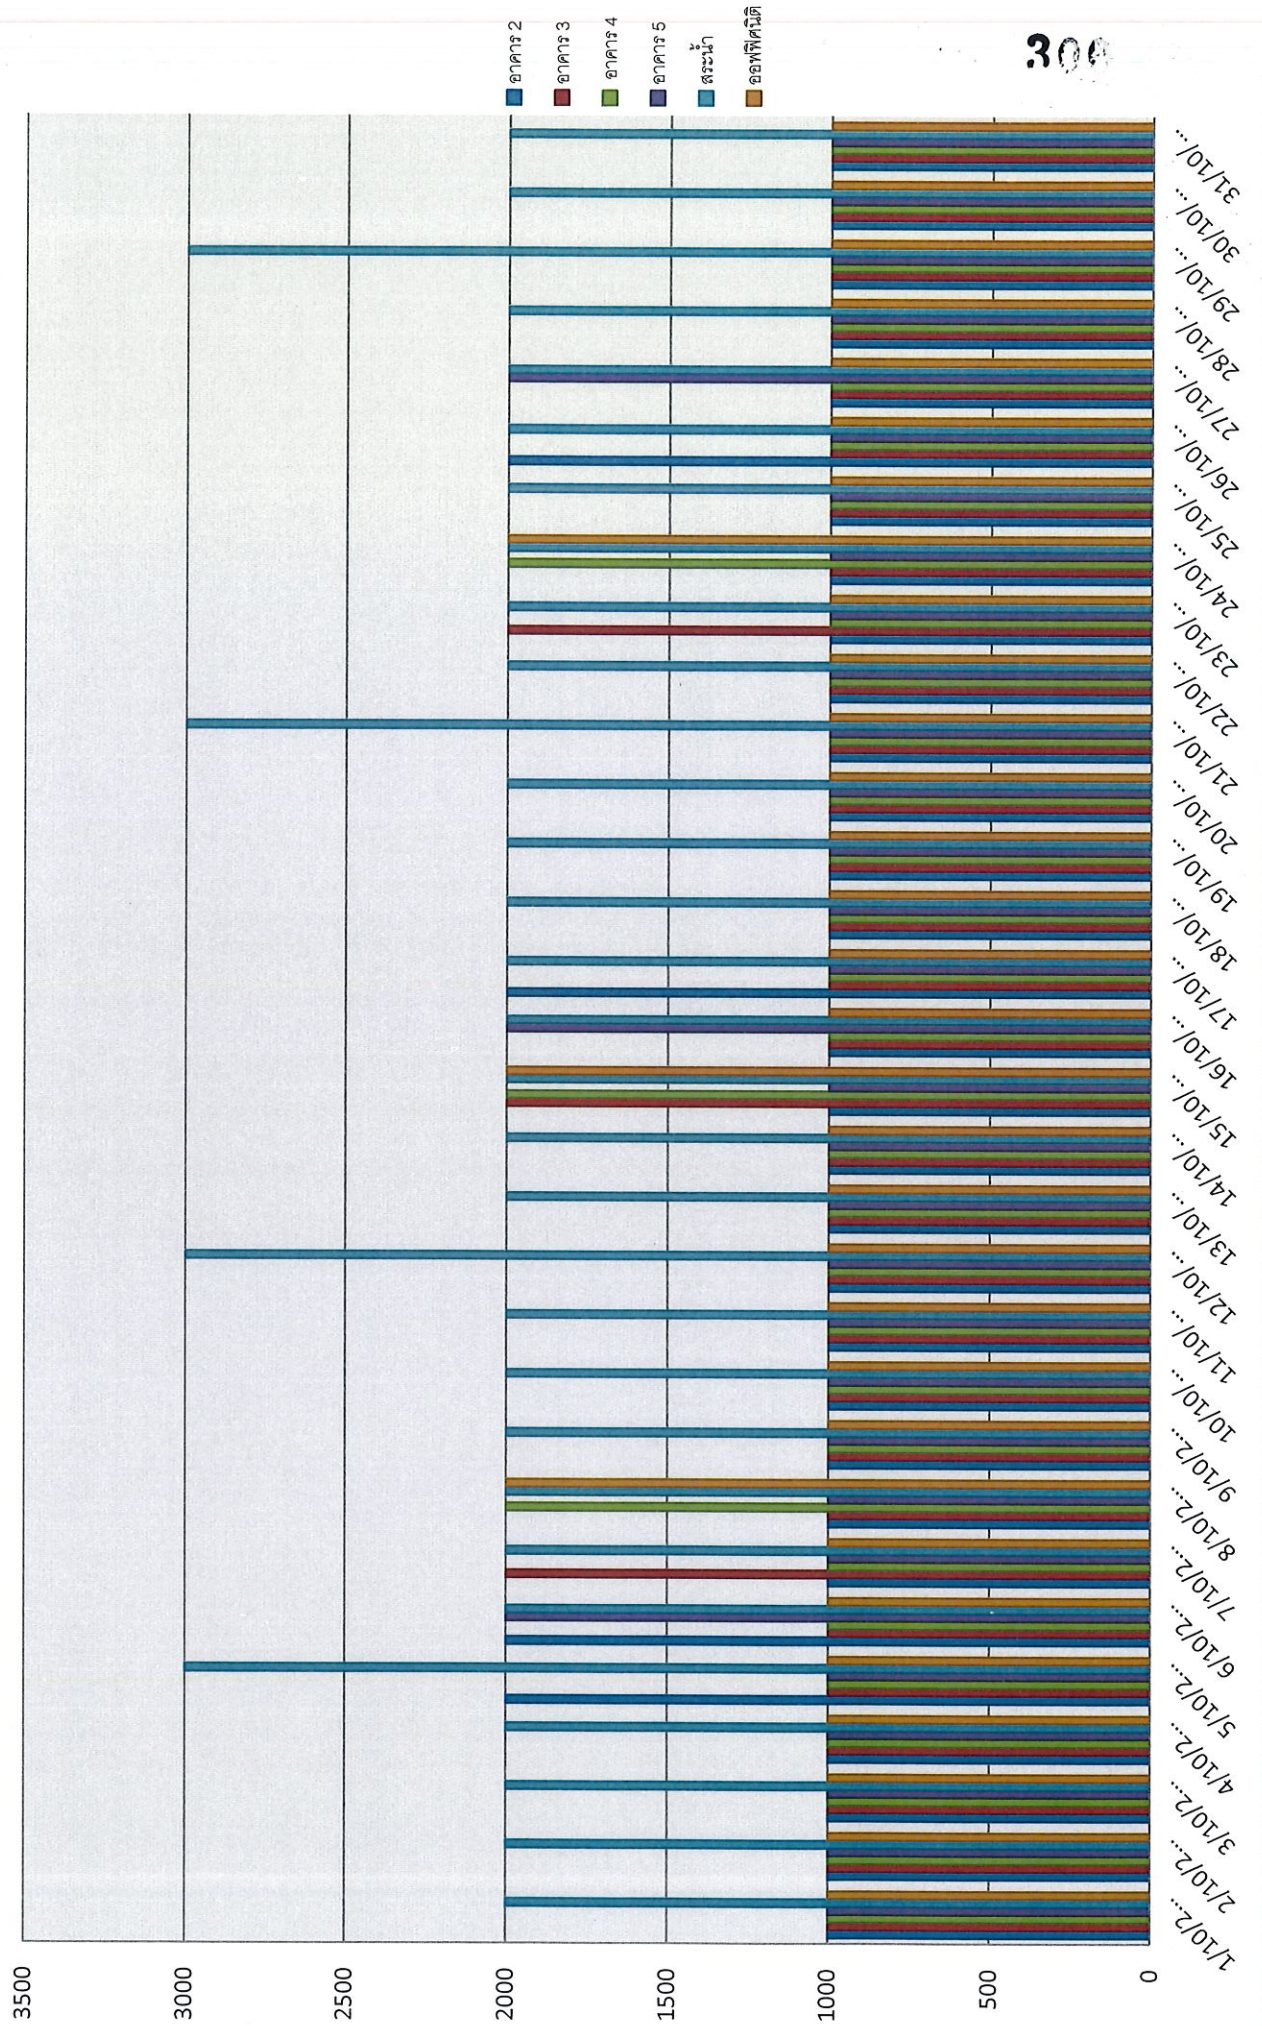

แผนภูมิแสดงการจดบันทึกมีเตอร์ไฟฟ้าส่วนกลาง ประจำเดือน พฤศจิกายน

