เอกสารแนบที่ 3

ใบรายงานผลการตรวจวัดสิ่งแวดล้อม

เอกสารแนบที่ 3-1 ใบรายงานผลการตรวจวัดคุณภาพอากาศด้วยระบบ AAQMS

เอกสารแนบที่ 3-2 ใบรายงานผลการตรวจสอบความถูกต้องด้วยระบบ AAQMS

เอกสารแนบที่ 3-3 ใบรายงานผลการตรวจวัดระดับเสียงในบรรยากาศ

เอกสารแนบที่ 3-4 ใบรายงานผลการตรวจวัดคุณภาพน้ำผิวดิน

เอกสารแนบที่ 3-5 ใบรายงานผลการตรวจวัดคุณภาพน้ำทิ้ง

เอกสารแนบที่ 3-6 ใบรายงานผลการตรวจวัดคุณภาพน้ำในบ่อยิปซั่มและบ่อสังเกตการณ์

เอกสารแนบที่ 3-7 ใบรายงานผลการตรวจวัดคุณภาพดิน

เอกสารแนบที่ 3-8 ใบรายงานผลการตรวจวัดนิเวศวิทยาทางน้ำ

เอกสารแนบที่ 3-9 ใบรายงานผลการตรวจวัดระดับเสียงในสถานประกอบการ

เอกสารแนบที่ 3-10 ใบรายงานผลการตรวจวัดปริมาณเสียงสะสม

เอกสารแนบที่ 3-11 ใบรายงานผลการตรวจวัดระดับความเข้มของแสงสว่างในสถานประกอบการ

เอกสารแนบที่ 3-12 ใบรายงานผลการตรวจวัดระดับความร้อนในสถานประกอบการ

เอกสารแนบที่ 3-13 ใบรายงานผลการตรวจวัดคุณภาพอากาศในสถานประกอบการ

เอกสารแนบที่ 3-1

ใบรายงานผลการตรวจวัดคุณภาพอากาศด้วยระบบ AAQMS

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : January

MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Jan 26	70	62	3	2 - 5	2 - 22	3 - 80
2 Jan 26	53	51	3	2 - 4	3 - 20	2 - 79
3 Jan 26	53	49	3	2 - 4	4 - 22	4 - 79
4 Jan 26	67	57	3	2 - 4	3 - 21	5 - 84
5 Jan 26	55	50	3	2 - 4	3 - 33	4 - 79
6 Jan 26	63	58	3	3 - 4	5 - 19	7 - 88
7 Jan 26	59	53	3	3 - 4	5 - 21	6 - 83
8 Jan 26	66	57	3	3 - 4	4 - 20	13 - 75
9 Jan 26	62	56	3	3 - 4	3 - 13	5 - 71
10 Jan 26	71	64	4	3 - 5	3 - 22	3 - 81
11 Jan 26	65	59	3	3 - 7	3 - 19	8 - 78
12 Jan 26	66	63	4	3 - 5	3 - 18	9 - 77
13 Jan 26	78	71	4	3 - 5	4 - 19	12 - 88
14 Jan 26	77	78	4	3 - 5	5 - 19	7 - 89
15 Jan 26	72	61	3	3 - 5	2 - 24	3 - 72
16 Jan 26	51	51	3	2 - 5	3 - 14	4 - 80
17 Jan 26	40	35	3	2 - 3	2 - 18	2 - 61
18 Jan 26	47	46	3	3 - 5	2 - 12	2 - 86
19 Jan 26	61	56	3	3 - 5	3 - 17	3 - 75
20 Jan 26	58	52	3	2 - 4	3 - 18	3 - 73
21 Jan 26	58	51	3	3 - 4	3 - 23	2 - 71
22 Jan 26	48	45	3	3 - 4	3 - 25	2 - 76
23 Jan 26	59	54	4	3 - 5	4 - 22	2 - 81
24 Jan 26	67	56	3	3 - 5	5 - 22	3 - 80
25 Jan 26	58	56	3	3 - 5	3 - 21	4 - 88
26 Jan 26	70	64	4	3 - 7	4 - 30	5 - 93
27 Jan 26	84	76	4	3 - 6	6 - 34	3 - 93
28 Jan 26	73	64	3	3 - 6	4 - 23	5 - 93
29 Jan 26	72	65	4	3 - 7	4 - 25	3 - 93
30 Jan 26	66	62	3	3 - 5	3 - 16	4 - 80
31 Jan 26	70	61	3	3 - 4	3 - 19	2 - 85
Range	40 - 84	35 - 78	3 - 4	2 - 7	2 - 34	2 - 93
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	31	31	31	31	31	31
Monitoring Hour	742	744	711	711	711	706
Ambient Air Quality Standard	330 (200)	120 (100)	120 (50)	300 (100)	170 (120)	100 (100)

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : January


MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Jan 26	19.4	33.3	25.3	38	100	77	1,007	1,012	1,009	0.0
2 Jan 26	19.8	32.1	25.2	34	100	73	1,010	1,014	1,012	0.0
3 Jan 26	19.2	30.2	24.4	41	99	76	1,010	1,016	1,013	0.0
4 Jan 26	18.7	30.7	24.0	40	100	79	1,010	1,016	1,013	0.0
5 Jan 26	19.0	31.0	24.2	37	100	75	1,011	1,016	1,013	0.0
6 Jan 26	18.8	30.7	24.4	43	99	76	1,011	1,016	1,013	0.0
7 Jan 26	19.5	28.5	23.5	47	99	75	1,013	1,017	1,015	0.0
8 Jan 26	17.7	27.2	21.8	40	99	71	1,014	1,019	1,016	0.0
9 Jan 26	15.7	26.5	20.5	38	99	73	1,014	1,018	1,016	0.0
10 Jan 26	14.9	28.3	20.7	27	99	70	1,012	1,017	1,015	0.0
11 Jan 26	15.0	28.2	21.0	33	99	71	1,014	1,019	1,016	0.0
12 Jan 26	15.5	29.1	21.8	36	99	71	1,013	1,018	1,015	0.0
13 Jan 26	16.9	30.9	23.2	35	99	70	1,011	1,017	1,014	0.0
14 Jan 26	18.3	32.7	24.2	35	99	74	1,009	1,015	1,012	0.0
15 Jan 26	18.8	33.7	25.2	36	100	75	1,008	1,014	1,011	0.0
16 Jan 26	20.4	34.1	26.2	38	100	77	1,007	1,012	1,010	0.0
17 Jan 26	21.3	33.7	26.8	38	100	77	1,005	1,011	1,008	0.0
18 Jan 26	20.8	33.9	26.7	36	100	77	1,005	1,010	1,007	0.0
19 Jan 26	21.6	34.2	26.8	30	100	73	1,006	1,011	1,008	0.0
20 Jan 26	22.2	33.3	26.6	50	100	83	1,007	1,012	1,009	0.0
21 Jan 26	22.9	31.3	26.4	54	100	86	1,009	1,013	1,011	0.0
22 Jan 26	22.2	32.2	26.0	39	100	80	1,011	1,015	1,013	0.0
23 Jan 26	19.5	32.7	25.6	26	99	63	1,012	1,017	1,014	0.0
24 Jan 26	19.7	31.8	24.6	29	100	70	1,012	1,017	1,014	0.0
25 Jan 26	18.1	32.6	24.4	29	99	69	1,011	1,015	1,013	0.0
26 Jan 26	18.3	32.7	24.7	29	99	70	1,011	1,016	1,013	0.0
27 Jan 26	19.2	32.8	25.0	31	100	72	1,011	1,016	1,013	0.0
28 Jan 26	19.0	32.8	25.0	29	99	71	1,011	1,016	1,013	0.0
29 Jan 26	19.1	34.1	25.5	31	99	69	1,010	1,015	1,013	0.0
30 Jan 26	20.2	33.7	26.3	39	100	73	1,010	1,016	1,013	0.0
31 Jan 26	21.5	33.2	27.1	48	100	77	1,011	1,016	1,013	0.0
Total	14.9	34.2	24.6	26	100	74	1,005	1,019	1,012	0.0
Day	31			31			31			31
Hours	744			744			744			744

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/January/2026	STATION : Ban Don Mod Tanoi

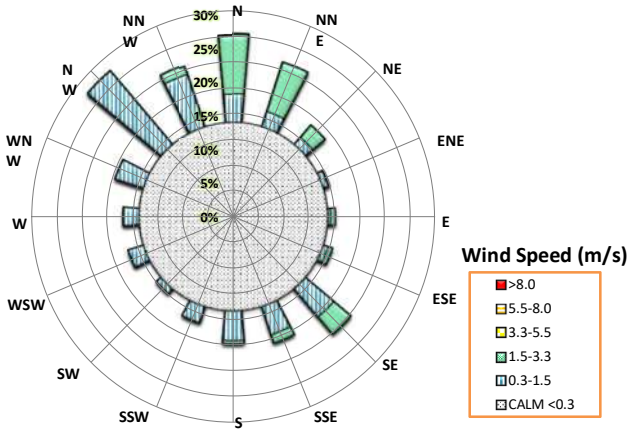

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	4.23%	8.78%	0.16%	0.00%	0.00%	**13.17%**
NNE	2.35%	7.68%	0.00%	0.00%	0.00%	**10.03%**
NE	1.41%	2.35%	0.00%	0.00%	0.00%	**3.76%**
ENE	0.78%	0.16%	0.00%	0.00%	0.00%	**0.94%**
E	0.47%	0.63%	0.00%	0.00%	0.00%	**1.10%**
ESE	0.78%	0.63%	0.00%	0.00%	0.00%	**1.41%**
SE	5.49%	3.29%	0.00%	0.00%	0.00%	**8.78%**
SSE	4.39%	1.25%	0.00%	0.00%	0.00%	**5.64%**
S	4.39%	0.47%	0.00%	0.00%	0.00%	**4.86%**
SSW	2.51%	0.00%	0.00%	0.00%	0.00%	**2.51%**
SW	0.94%	0.00%	0.00%	0.00%	0.00%	**0.94%**
WSW	2.35%	0.00%	0.00%	0.00%	0.00%	**2.35%**
W	2.35%	0.00%	0.00%	0.00%	0.00%	**2.35%**
WNW	4.39%	0.00%	0.00%	0.00%	0.00%	**4.39%**
NW	14.26%	0.00%	0.00%	0.00%	0.00%	**14.26%**
NNW	8.15%	1.41%	0.00%	0.00%	0.00%	**9.56%**
	59.25%	**26.65%**	**0.16%**	**0.00%**	**0.00%**	**86.05%**

No. of Monitored Hours	744	Hours	No. of Calm	89	Hours
No. of Monitored Days	31	Days	Calm (%)	13.95%	
Missing Data	106	Hours	Average Wind Speed	1.03	m/s
No. of Valid Data	638	Hours	Maximum Wind Speed	3.40	m/s
			Prevailing Wind Direction		NW

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : January

MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Jan 26	86	73	3	3 - 4	3 - 32	7 - 73
2 Jan 26	75	58	3	2 - 4	3 - 30	8 - 72
3 Jan 26	66	54	3	3 - 4	3 - 28	7 - 70
4 Jan 26	64	49	3	3 - 4	3 - 26	11 - 76
5 Jan 26	68	57	3	3 - 4	3 - 23	11 - 70
6 Jan 26	71	58	3	3 - 4	4 - 21	11 - 71
7 Jan 26	63	49	3	3 - 4	4 - 17	12 - 71
8 Jan 26	64	54	3	3 - 4	4 - 16	18 - 69
9 Jan 26	65	56	3	3 - 4	4 - 37	11 - 64
10 Jan 26	75	66	4	3 - 6	5 - 39	7 - 70
11 Jan 26	79	72	3	3 - 6	4 - 26	15 - 70
12 Jan 26	72	62	4	3 - 5	4 - 32	8 - 67
13 Jan 26	80	67	3	3 - 5	4 - 26	10 - 78
14 Jan 26	86	76	4	3 - 6	5 - 22	13 - 94
15 Jan 26	76	64	3	3 - 5	2 - 24	7 - 66
16 Jan 26	60	52	3	3 - 5	4 - 18	8 - 74
17 Jan 26	53	41	3	3 - 5	3 - 13	7 - 69
18 Jan 26	61	49	3	3 - 5	2 - 14	7 - 78
19 Jan 26	71	60	3	3 - 5	3 - 19	10 - 70
20 Jan 26	69	56	3	2 - 3	3 - 17	8 - 70
21 Jan 26	65	55	2	2 - 3	3 - 23	3 - 58
22 Jan 26	66	57	3	2 - 3	4 - 24	4 - 74
23 Jan 26	78	67	3	2 - 4	3 - 33	4 - 71
24 Jan 26	74	63	3	2 - 6	4 - 31	5 - 71
25 Jan 26	70	59	3	2 - 5	3 - 21	7 - 71
26 Jan 26	79	68	3	2 - 6	4 - 30	4 - 73
27 Jan 26	92	78	3	2 - 6	5 - 31	4 - 90
28 Jan 26	88	80	3	2 - 5	4 - 32	5 - 84
29 Jan 26	79	68	3	2 - 6	5 - 25	4 - 87
30 Jan 26	78	68	3	2 - 5	3 - 18	6 - 71
31 Jan 26	75	63	3	2 - 4	3 - 15	4 - 76
Range	53 - 92	41 - 80	2 - 4	2 - 6	2 - 39	3 - 94
Number of times (exceeded standard)	0	0	0	0	0	0
Total Monitoring Day	31	31	31	31	31	31
Total Monitoring Hour	744	744	714	714	714	714
Ambient Air Quality Standard	330 (200)	120 (100)	120 (50)	300 (100)	170 (120)	100 (100)

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : January


MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Temperature (° C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Jan 26	19.7	31.8	25.2	42	99	76	1,008	1,012	1,010	0.0
2 Jan 26	19.8	32.2	25.4	34	99	70	1,010	1,014	1,012	0.0
3 Jan 26	19.3	30.5	24.6	42	98	73	1,011	1,016	1,013	0.0
4 Jan 26	18.7	30.8	24.4	41	97	73	1,011	1,016	1,013	0.0
5 Jan 26	18.9	31.2	24.4	38	98	71	1,011	1,016	1,013	0.0
6 Jan 26	19.5	31.0	24.7	43	90	70	1,011	1,016	1,013	0.0
7 Jan 26	19.7	28.5	23.7	49	95	71	1,013	1,017	1,015	0.0
8 Jan 26	17.8	27.2	21.9	41	94	68	1,014	1,019	1,016	0.0
9 Jan 26	15.9	26.3	20.7	39	91	67	1,014	1,018	1,016	0.0
10 Jan 26	15.1	28.3	21.0	30	94	65	1,013	1,017	1,015	0.0
11 Jan 26	15.1	28.2	21.3	34	93	66	1,014	1,019	1,016	0.0
12 Jan 26	16.0	29.4	22.2	36	86	63	1,013	1,018	1,015	0.0
13 Jan 26	16.9	30.8	23.4	35	93	66	1,011	1,017	1,014	0.0
14 Jan 26	18.4	31.9	24.4	36	96	68	1,009	1,015	1,012	0.0
15 Jan 26	19.4	31.9	25.2	39	99	73	1,008	1,014	1,011	0.0
16 Jan 26	20.5	32.7	26.2	41	99	76	1,007	1,012	1,010	0.0
17 Jan 26	21.8	33.6	27.0	36	99	76	1,005	1,011	1,008	0.0
18 Jan 26	21.1	34.1	27.1	37	99	74	1,005	1,010	1,007	0.0
19 Jan 26	21.7	34.2	27.0	31	99	71	1,006	1,011	1,008	0.0
20 Jan 26	22.3	32.3	26.4	51	99	82	1,007	1,011	1,009	0.0
21 Jan 26	23.2	31.4	26.7	53	99	82	1,009	1,013	1,011	0.0
22 Jan 26	22.7	31.3	26.3	44	99	79	1,011	1,015	1,013	0.0
23 Jan 26	19.8	32.1	25.5	28	99	65	1,013	1,017	1,015	0.0
24 Jan 26	20.1	31.4	25.0	29	93	63	1,012	1,018	1,015	0.0
25 Jan 26	18.3	32.4	24.8	28	95	62	1,011	1,015	1,013	0.0
26 Jan 26	18.6	32.5	25.0	29	99	65	1,011	1,016	1,013	0.0
27 Jan 26	19.0	33.1	25.5	31	96	66	1,011	1,016	1,013	0.0
28 Jan 26	19.2	32.6	25.3	30	98	67	1,011	1,016	1,013	0.0
29 Jan 26	19.3	32.7	25.6	32	99	65	1,010	1,015	1,013	0.0
30 Jan 26	20.2	32.8	26.3	41	99	71	1,011	1,016	1,013	0.0
31 Jan 26	22.1	33.2	27.3	48	99	76	1,011	1,016	1,013	0.0
Total	15.1	34.2	24.8	28	99	70	1,005	1,019	1,013	0.0
Day	31			31			31			31
Hours	744			744			744			744

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/January/2026 STATION : Wat Bang Gado

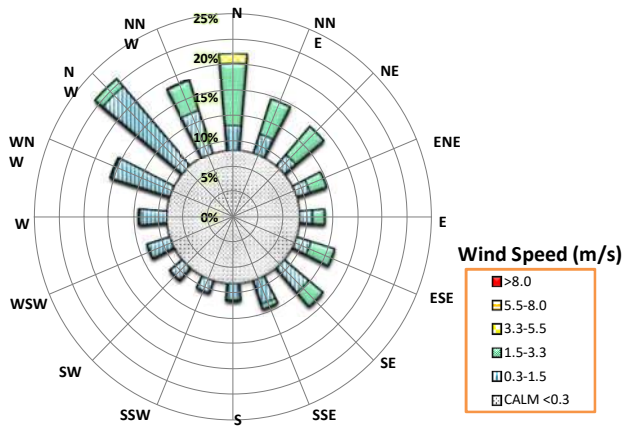

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	3.09%	7.80%	1.21%	0.00%	0.00%	12.10%
NNE	2.55%	4.57%	0.00%	0.00%	0.00%	7.12%
NE	1.88%	4.57%	0.00%	0.00%	0.00%	6.45%
ENE	1.75%	2.15%	0.00%	0.00%	0.00%	3.90%
E	1.61%	1.48%	0.00%	0.00%	0.00%	3.09%
ESE	1.88%	3.09%	0.00%	0.00%	0.00%	4.97%
SE	4.03%	2.28%	0.00%	0.00%	0.00%	6.32%
SSE	3.09%	0.67%	0.00%	0.00%	0.00%	3.76%
S	2.02%	0.13%	0.00%	0.00%	0.00%	2.15%
SSW	1.61%	0.00%	0.00%	0.00%	0.00%	1.61%
SW	2.02%	0.00%	0.00%	0.00%	0.00%	2.02%
WSW	2.96%	0.00%	0.00%	0.00%	0.00%	2.96%
W	3.36%	0.13%	0.00%	0.00%	0.00%	3.49%
WNW	7.66%	0.13%	0.00%	0.00%	0.00%	7.80%
NW	13.04%	1.21%	0.00%	0.00%	0.00%	14.25%
NNW	5.78%	3.76%	0.13%	0.00%	0.00%	9.68%
	58.33%	31.99%	1.34%	0.00%	0.00%	91.67%

No. of Monitored Hours	744	Hours	No. of Calm	62	Hours
No. of Monitored Days	31	Days	Calm (%)	8.33%	
Missing Data	0	Hours	Average Wind Speed	1.27	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	4.00	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	NW	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : January

MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Jan 26	68	55	3	2 - 4	4 - 35	3 - 99
2 Jan 26	60	47	3	2 - 4	4 - 30	3 - 93
3 Jan 26	60	46	3	2 - 5	5 - 30	4 - 93
4 Jan 26	60	47	3	2 - 5	4 - 28	11 - 106*
5 Jan 26	63	48	3	2 - 4	3 - 24	16 - 92
6 Jan 26	71	53	3	2 - 4	0 - 13	11 - 105*
7 Jan 26	69	50	3	3 - 5	17 - 33	14 - 99
8 Jan 26	69	50	3	3 - 5	7 - 24	26 - 91
9 Jan 26	66	62	4	2 - 5	5 - 40	8 - 86
10 Jan 26	71	58	3	2 - 6	6 - 33	3 - 99
11 Jan 26	71	60	3	2 - 7	5 - 43	15 - 95
12 Jan 26	67	57	3	2 - 5	5 - 37	13 - 96
13 Jan 26	73	65	3	3 - 4	5 - 34	8 - 113*
14 Jan 26	76	62	4	3 - 5	5 - 31	13 - 119*
15 Jan 26	63	63	3	2 - 5	3 - 28	5 - 88
16 Jan 26	54	47	3	2 - 4	4 - 23	4 - 84
17 Jan 26	45	40	3	2 - 3	4 - 13	1 - 76
18 Jan 26	51	47	3	2 - 3	3 - 17	1 - 91
19 Jan 26	64	55	3	2 - 4	4 - 22	5 - 89
20 Jan 26	65	54	3	2 - 4	3 - 29	8 - 90
21 Jan 26	58	52	3	2 - 7	2 - 21	1 - 75
22 Jan 26	64	52	3	2 - 4	5 - 33	2 - 89
23 Jan 26	71	62	3	2 - 6	4 - 31	2 - 92
24 Jan 26	73	61	3	2 - 6	5 - 46	3 - 93
25 Jan 26	61	53	3	2 - 4	4 - 35	4 - 92
26 Jan 26	71	63	3	2 - 6	4 - 31	8 - 102*
27 Jan 26	89	76	3	2 - 5	8 - 47	3 - 133*
28 Jan 26	81	72	3	2 - 6	6 - 54	2 - 114*
29 Jan 26	78	66	3	2 - 6	3 - 32	9 - 98
30 Jan 26	70	63	3	2 - 4	4 - 27	5 - 94
31 Jan 26	63	56	3	2 - 4	4 - 25	3 - 99
Range	45 - 89	40 - 76	3 - 4	2 - 7	0 - 54	1 - 133*
Number of times (exceeded standard)	0	0	0	0	0	7
Total Day	31	31	31	31	31	31
Monitoring Hour	742	742	711	711	679	711
Ambient Air Quality Standard	330 (200)	120 (100)	120 (50)	300 (100)	170 (120)	100 (100)

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : January


MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Jan 26	20.0	32.9	25.6	38	89	67	1,007	1,011	1,009	0.0
2 Jan 26	20.5	32.1	25.5	35	89	63	1,009	1,013	1,011	0.0
3 Jan 26	20.2	29.6	24.7	43	79	64	1,010	1,016	1,013	0.0
4 Jan 26	19.0	30.0	24.4	43	86	67	1,010	1,015	1,013	0.0
5 Jan 26	19.4	30.6	24.7	39	86	63	1,010	1,015	1,013	0.0
6 Jan 26	20.1	30.4	25.0	44	77	63	1,011	1,015	1,013	0.0
7 Jan 26	21.0	28.3	24.3	47	75	61	1,012	1,017	1,015	0.0
8 Jan 26	19.3	26.8	22.6	42	71	57	1,013	1,018	1,016	0.0
9 Jan 26	17.2	26.0	21.2	39	74	58	1,013	1,018	1,016	0.0
10 Jan 26	16.1	28.1	21.4	32	83	58	1,012	1,017	1,014	0.0
11 Jan 26	15.9	28.0	21.5	34	81	59	1,014	1,019	1,016	0.0
12 Jan 26	17.3	29.1	22.6	37	71	57	1,013	1,018	1,015	0.0
13 Jan 26	17.4	30.5	23.6	36	83	61	1,010	1,017	1,013	0.0
14 Jan 26	19.4	32.5	24.3	36	81	63	1,009	1,014	1,011	0.0
15 Jan 26	19.4	33.1	25.6	38	88	66	1,008	1,013	1,010	0.0
16 Jan 26	20.7	33.7	26.6	38	87	68	1,007	1,012	1,009	0.0
17 Jan 26	21.9	33.5	27.1	39	97	72	1,004	1,010	1,007	0.0
18 Jan 26	21.0	34.3	26.9	37	92	68	1,004	1,009	1,007	0.0
19 Jan 26	21.6	33.8	27.2	33	87	64	1,005	1,010	1,008	0.0
20 Jan 26	23.0	33.0	27.1	49	97	73	1,007	1,011	1,009	0.0
21 Jan 26	23.2	33.0	27.1	49	93	73	1,009	1,013	1,010	0.0
22 Jan 26	22.5	31.9	26.3	39	96	71	1,010	1,015	1,012	0.0
23 Jan 26	20.4	31.9	25.6	29	86	57	1,012	1,017	1,014	0.0
24 Jan 26	20.2	31.1	25.0	32	81	57	1,012	1,017	1,014	0.0
25 Jan 26	18.2	32.3	25.0	30	84	57	1,010	1,015	1,012	0.0
26 Jan 26	18.5	32.9	25.2	29	85	59	1,010	1,015	1,013	0.0
27 Jan 26	19.7	32.5	25.4	35	84	61	1,011	1,016	1,013	0.0
28 Jan 26	19.7	32.1	25.3	31	89	62	1,011	1,015	1,013	0.0
29 Jan 26	19.6	33.4	25.8	32	82	59	1,010	1,014	1,012	0.0
30 Jan 26	20.5	33.8	26.7	40	85	63	1,010	1,015	1,012	0.0
31 Jan 26	22.1	34.1	27.7	43	94	67	1,010	1,015	1,012	0.0
Total	15.9	34.3	25.1	29	97	63	1,004	1,019	1,012	0.0
Day	31			31			31			31
Hours	742			742			742			742

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/January/2026	STATION : Ban Klong Klae

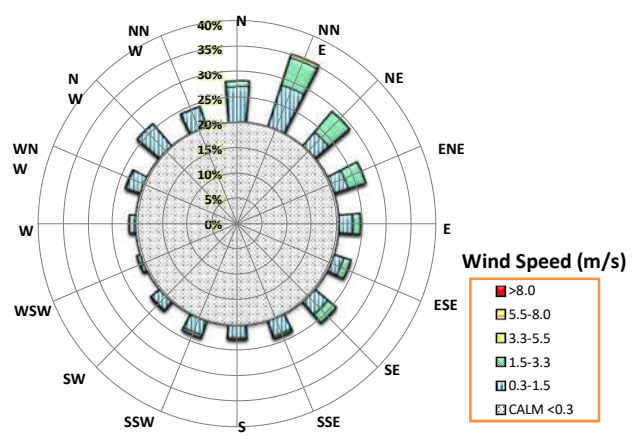

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	7.14%	1.08%	0.00%	0.00%	0.00%	8.22%
NNE	8.76%	5.80%	0.67%	0.00%	0.00%	15.23%
NE	3.64%	5.39%	0.00%	0.00%	0.00%	9.03%
ENE	2.96%	3.64%	0.00%	0.00%	0.00%	6.60%
E	2.83%	1.48%	0.00%	0.00%	0.00%	4.31%
ESE	2.02%	1.48%	0.00%	0.00%	0.00%	3.50%
SE	3.37%	2.16%	0.00%	0.00%	0.00%	5.53%
SSE	3.23%	0.40%	0.00%	0.00%	0.00%	3.64%
S	2.43%	0.27%	0.00%	0.00%	0.00%	2.70%
SSW	2.96%	0.54%	0.00%	0.00%	0.00%	3.50%
SW	2.16%	0.13%	0.00%	0.00%	0.00%	2.29%
WSW	0.67%	0.00%	0.00%	0.00%	0.00%	0.67%
W	1.21%	0.00%	0.00%	0.00%	0.00%	1.21%
WNW	2.96%	0.13%	0.00%	0.00%	0.00%	3.10%
NW	5.80%	0.00%	0.00%	0.00%	0.00%	5.80%
NNW	4.31%	0.00%	0.00%	0.00%	0.00%	4.31%
	56.47%	22.51%	0.67%	0.00%	0.00%	79.65%

No. of Monitored Hours	744	Hours	No. of Calm	151	Hours
No. of Monitored Days	31	Days	Calm (%)	20.35%	
Missing Data	2	Hours	Average Wind Speed	0.99	m/s
No. of Valid Data	742	Hours	Maximum Wind Speed	3.80	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	NNE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : January

MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Jan 26	76	65	1	1 - 2	2 - 13	6 - 60
2 Jan 26	55	49	1	1 - 2	3 - 11	5 - 58
3 Jan 26	60	50	1	1 - 2	3 - 14	8 - 58
4 Jan 26	62	48	1	1 - 2	3 - 13	11 - 63
5 Jan 26	59	50	1	1 - 2	3 - 14	13 - 58
6 Jan 26	67	57	2	1 - 3	4 - 14	12 - 64
7 Jan 26	61	52	1	1 - 2	3 - 11	9 - 63
8 Jan 26	62	50	2	1 - 2	3 - 11	15 - 61
9 Jan 26	63	56	2	2 - 3	3 - 11	12 - 59
10 Jan 26	68	60	2	2 - 4	3 - 15	12 - 64
11 Jan 26	73	65	2	2 - 5	3 - 14	16 - 63
12 Jan 26	64	59	2	1 - 3	3 - 20	10 - 61
13 Jan 26	77	68	2	1 - 3	3 - 11	9 - 71
14 Jan 26	83	76	2	1 - 4	4 - 15	13 - 85
15 Jan 26	71	65	1	1 - 3	2 - 14	5 - 61
16 Jan 26	54	51	1	1 - 2	3 - 10	7 - 62
17 Jan 26	48	42	1	1 - 2	2 - 8	5 - 51
18 Jan 26	60	50	1	1 - 3	2 - 8	5 - 62
19 Jan 26	64	55	1	1 - 3	2 - 12	7 - 62
20 Jan 26	57	51	1	1 - 2	2 - 11	6 - 58
21 Jan 26	61	54	1	1 - 2	3 - 13	5 - 59
22 Jan 26	55	46	1	1 - 2	3 - 14	5 - 67
23 Jan 26	60	53	1	1 - 3	3 - 14	5 - 64
24 Jan 26	67	56	1	1 - 4	4 - 14	6 - 65
25 Jan 26	62	52	2	1 - 3	2 - 13	7 - 68
26 Jan 26	71	65	2	1 - 4	3 - 14	8 - 71
27 Jan 26	81	70	2	1 - 4	4 - 16	5 - 82
28 Jan 26	76	68	2	1 - 3	3 - 15	5 - 71
29 Jan 26	71	63	2	1 - 4	4 - 15	7 - 70
30 Jan 26	74	65	2	1 - 4	2 - 11	6 - 57
31 Jan 26	72	64	1	1 - 2	3 - 12	5 - 57
Range	48 - 83	42 - 76	1 - 2	1 - 5	2 - 20	5 - 85
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	31	31	31	31	31	31
Monitoring Hour	744	744	711	711	711	711
Ambient Air Quality Standard	330 (200)	120 (100)	120 (50)	300 (100)	170 (120)	100 (100)

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : January


MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Jan 26	19.1	32.5	24.7	39	100	79	1,006	1,010	1,008	0.0
2 Jan 26	19.9	31.4	24.6	37	100	76	1,008	1,012	1,010	0.0
3 Jan 26	19.2	29.3	23.9	45	100	78	1,009	1,015	1,012	0.0
4 Jan 26	18.9	30.1	23.7	42	100	81	1,009	1,014	1,012	0.0
5 Jan 26	19.1	30.0	24.4	40	100	73	1,009	1,014	1,012	0.0
6 Jan 26	21.9	30.0	26.3	45	99	68	1,010	1,013	1,011	0.0
7 Jan 26	20.1	27.7	23.5	50	99	74	1,011	1,016	1,014	0.0
8 Jan 26	18.2	26.2	21.8	43	99	71	1,013	1,017	1,015	0.0
9 Jan 26	16.5	25.6	20.3	40	100	74	1,012	1,017	1,015	0.0
10 Jan 26	15.1	27.6	20.4	29	100	72	1,011	1,015	1,013	0.0
11 Jan 26	15.5	27.3	20.8	35	100	73	1,013	1,018	1,015	0.0
12 Jan 26	15.7	28.4	21.6	38	100	71	1,012	1,017	1,014	0.0
13 Jan 26	17.2	30.0	22.8	37	100	73	1,009	1,016	1,012	0.0
14 Jan 26	18.1	32.2	24.1	36	100	76	1,008	1,013	1,010	0.0
15 Jan 26	18.7	32.5	24.8	38	100	76	1,007	1,013	1,010	0.0
16 Jan 26	20.2	33.5	26.0	38	100	78	1,006	1,011	1,008	0.0
17 Jan 26	21.0	33.5	26.5	39	100	78	1,004	1,009	1,006	0.0
18 Jan 26	20.7	33.5	26.4	37	100	78	1,003	1,008	1,006	0.0
19 Jan 26	21.0	33.4	26.3	32	100	75	1,004	1,009	1,007	0.0
20 Jan 26	22.1	32.6	26.2	53	100	85	1,006	1,010	1,008	0.0
21 Jan 26	22.7	31.8	26.4	51	100	86	1,008	1,011	1,009	0.0
22 Jan 26	21.6	31.3	25.6	41	100	82	1,009	1,014	1,011	0.0
23 Jan 26	19.2	31.8	24.8	28	100	69	1,011	1,016	1,013	0.0
24 Jan 26	19.2	30.7	24.2	32	100	71	1,011	1,016	1,013	0.0
25 Jan 26	17.9	32.6	24.2	29	100	69	1,009	1,014	1,011	0.0
26 Jan 26	18.3	32.0	24.3	30	100	71	1,009	1,015	1,012	0.0
27 Jan 26	19.0	31.8	24.6	33	100	73	1,010	1,015	1,012	0.0
28 Jan 26	19.1	31.6	24.5	31	100	73	1,010	1,014	1,012	0.0
29 Jan 26	18.7	33.3	25.1	32	100	70	1,009	1,013	1,011	0.0
30 Jan 26	19.8	33.0	26.0	40	100	74	1,009	1,014	1,011	0.0
31 Jan 26	21.3	33.3	26.8	47	100	77	1,009	1,014	1,011	0.0
Total	15.1	33.5	24.4	28	100	75	1,003	1,018	1,011	0.0
Day	31			31			31			31
Hours	727			727			727			727

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/January/2026 STATION : Ban Chao Nua

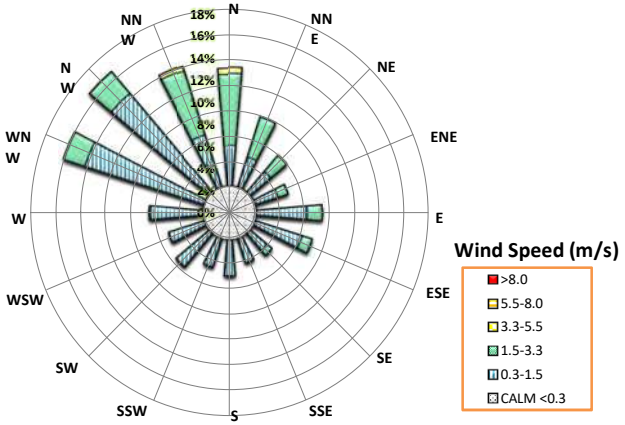

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	3.63%	6.45%	0.54%	0.00%	0.00%	10.62%
NNE	2.82%	3.76%	0.00%	0.00%	0.00%	6.59%
NE	2.42%	1.88%	0.00%	0.00%	0.00%	4.30%
ENE	2.15%	0.94%	0.00%	0.00%	0.00%	3.09%
E	4.57%	1.34%	0.00%	0.00%	0.00%	5.91%
ESE	4.44%	0.94%	0.00%	0.00%	0.00%	5.38%
SE	2.02%	0.54%	0.00%	0.00%	0.00%	2.55%
SSE	2.28%	0.00%	0.00%	0.00%	0.00%	2.28%
S	3.23%	0.00%	0.00%	0.00%	0.00%	3.23%
SSW	2.69%	0.00%	0.00%	0.00%	0.00%	2.69%
SW	3.90%	0.00%	0.00%	0.00%	0.00%	3.90%
WSW	3.36%	0.00%	0.00%	0.00%	0.00%	3.36%
W	4.70%	0.13%	0.00%	0.00%	0.00%	4.84%
WNW	11.29%	2.02%	0.00%	0.00%	0.00%	13.31%
NW	11.56%	2.55%	0.00%	0.00%	0.00%	14.11%
NNW	4.97%	6.05%	0.40%	0.00%	0.00%	11.42%
	70.03%	26.61%	0.94%	0.00%	0.00%	97.58%

No. of Monitored Hours	744	Hours	No. of Calm	18	Hours
No. of Monitored Days	31	Days	Calm (%)	2.42%	
Missing Data	0	Hours	Average Wind Speed	1.15	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	4.10	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	NW	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : February

MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Feb 26	70	59	3	3 - 5	3 - 18	2 - 100
2 Feb 26	71	63	4	3 - 5	3 - 20	5 - 85
3 Feb 26	48	44	4	3 - 4	5 - 16	5 - 90
4 Feb 26	67	57	4	3 - 5	2 - 31	6 - 74
5 Feb 26	56	53	3	3 - 5	2 - 14	3 - 87
6 Feb 26	52	48	4	3 - 5	2 - 16	3 - 86
7 Feb 26	36	34	3	3 - 4	2 - 10	2 - 69
8 Feb 26	34	31	3	3	2 - 6	4 - 47
9 Feb 26	39	37	3	3 - 4	1 - 10	11 - 72
10 Feb 26	56	N/A	4	3 - 6	4 - 22	2 - 97
11 Feb 26	71	69	4	3 - 5	3 - 31	2 - 100
12 Feb 26	74	73	4	3 - 5	4 - 17	4 - 91
13 Feb 26	36	29	3	3	2 - 12	6 - 62
14 Feb 26	37	N/A	3	3 - 4	2 - 10	2 - 63
15 Feb 26	29	N/A	3	3	2 - 11	2 - 58
16 Feb 26	54	N/A	3	3 - 4	2 - 12	2 - 77
17 Feb 26	45	N/A	3	3	1 - 8	3 - 53
18 Feb 26	36	N/A	3	3	3 - 17	5 - 64
19 Feb 26	83	N/A	3	3 - 5	4 - 26	2 - 85
20 Feb 26	51	N/A	4	3 - 6	5 - 20	2 - 91
21 Feb 26	20	N/A	3	3 - 5	3 - 13	2 - 77
22 Feb 26	20	N/A	3	3 - 5	2 - 11	2 - 72
23 Feb 26	17	N/A	3	3 - 4	2 - 9	2 - 66
24 Feb 26	18	N/A	3	3	2 - 7	9 - 45
25 Feb 26	16	N/A	3	3 - 5	2 - 10	5 - 69
26 Feb 26	N/A	41	3	3 - 5	2 - 9	7 - 66
27 Feb 26	30	28	3	3	2 - 9	2 - 50
28 Feb 26	21	18	N/A	N/A	1 - 7	2 - 46
Range	16 - 83	18 - 73	3 - 4	3 - 6	1 - 31	2 - 100
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	27	15	27	27	28	28
Monitoring Hour	633	348	618	618	644	641
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : February


MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Temperature (° C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Feb 26	22.1	33.3	26.7	41	100	80	1,011	1,016	1,013	0.0
2 Feb 26	20.3	32.8	26.2	29	100	68	1,011	1,016	1,014	0.0
3 Feb 26	23.0	31.8	26.4	44	99	69	1,012	1,017	1,014	0.0
4 Feb 26	21.1	33.7	26.7	36	99	72	1,011	1,016	1,013	0.0
5 Feb 26	21.3	35.8	27.5	33	100	72	1,009	1,014	1,012	0.0
6 Feb 26	22.3	35.8	28.0	32	100	73	1,007	1,013	1,010	0.0
7 Feb 26	22.2	36.4	28.0	34	100	76	1,007	1,012	1,009	0.0
8 Feb 26	23.1	35.3	28.2	44	100	81	1,008	1,013	1,010	0.0
9 Feb 26	22.6	32.7	26.5	43	100	86	1,010	1,013	1,011	15.6
10 Feb 26	21.2	33.9	26.6	40	100	78	1,009	1,014	1,012	0.0
11 Feb 26	21.6	34.9	27.6	37	100	76	1,010	1,016	1,012	0.0
12 Feb 26	22.4	35.8	27.9	37	100	78	1,009	1,014	1,011	0.0
13 Feb 26	23.3	35.8	28.3	42	100	80	1,008	1,012	1,010	0.0
14 Feb 26	23.3	34.7	28.2	48	100	82	1,007	1,011	1,009	0.0
15 Feb 26	23.5	35.3	28.4	48	100	81	1,007	1,011	1,009	0.0
16 Feb 26	23.9	35.9	28.9	48	100	79	1,005	1,011	1,008	0.0
17 Feb 26	24.8	35.1	29.2	49	100	81	1,006	1,011	1,008	0.0
18 Feb 26	23.5	30.8	26.8	63	100	93	1,009	1,013	1,010	9.8
19 Feb 26	23.1	35.4	28.1	37	100	80	1,010	1,014	1,012	0.0
20 Feb 26	23.2	35.0	28.0	38	100	78	1,009	1,015	1,012	0.0
21 Feb 26	22.6	36.4	28.6	36	100	74	1,005	1,011	1,008	0.0
22 Feb 26	23.8	36.8	29.0	36	100	73	1,003	1,009	1,006	0.0
23 Feb 26	23.2	36.6	28.9	43	100	79	1,003	1,009	1,006	0.0
24 Feb 26	24.9	35.0	29.0	54	100	84	1,004	1,009	1,007	0.0
25 Feb 26	23.8	34.6	28.5	48	100	84	1,005	1,011	1,008	0.0
26 Feb 26	23.6	35.2	28.0	46	100	85	1,003	1,010	1,007	20.8
27 Feb 26	23.2	34.6	27.5	47	100	86	1,002	1,008	1,005	2.0
28 Feb 26	23.4	37.0	29.0	39	100	78	1,003	1,008	1,005	0.0
Total	20.3	37.0	27.9	29	100	79	1,002	1,017	1,010	48.2
Day	28			28			28			28
Hours	672			672			672			672

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-28/February/2026	STATION : Ban Don Mod Tanoi

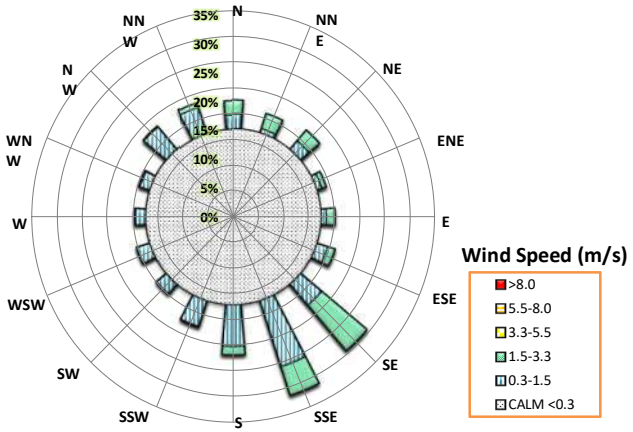

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	2.53%	2.38%	0.00%	0.00%	0.00%	**4.91%**
NNE	0.74%	2.68%	0.00%	0.00%	0.00%	**3.42%**
NE	1.93%	2.38%	0.00%	0.00%	0.00%	**4.32%**
ENE	0.89%	0.74%	0.00%	0.00%	0.00%	**1.64%**
E	0.89%	1.49%	0.00%	0.00%	0.00%	**2.38%**
ESE	1.93%	1.34%	0.00%	0.00%	0.00%	**3.27%**
SE	4.76%	10.27%	0.00%	0.00%	0.00%	**15.03%**
SSE	11.90%	5.21%	0.00%	0.00%	0.00%	**17.11%**
S	7.14%	1.49%	0.00%	0.00%	0.00%	**8.63%**
SSW	4.61%	0.15%	0.00%	0.00%	0.00%	**4.76%**
SW	2.23%	0.00%	0.00%	0.00%	0.00%	**2.23%**
WSW	2.38%	0.00%	0.00%	0.00%	0.00%	**2.38%**
W	1.79%	0.15%	0.00%	0.00%	0.00%	**1.93%**
WNW	1.79%	0.30%	0.00%	0.00%	0.00%	**2.08%**
NW	5.06%	0.15%	0.00%	0.00%	0.00%	**5.21%**
NNW	4.76%	0.74%	0.00%	0.00%	0.00%	**5.51%**
	55.36%	**29.46%**	**0.00%**	**0.00%**	**0.00%**	**84.82%**

No. of Monitored Hours	672	Hours	No. of Calm	102	Hours
No. of Monitored Days	28	Days	Calm (%)	15.18%	
Missing Data	0	Hours	Average Wind Speed	1.12	m/s
No. of Valid Data	672	Hours	Maximum Wind Speed	3.30	m/s
			Prevailing Wind Direction	SSE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : February

MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Feb 26	75	63	3	2 - 4	4 - 22	5 - 86
2 Feb 26	N/A	N/A	3	2 - 4	4 - 18	4 - 73
3 Feb 26	N/A	N/A	3	2 - 3	5 - 25	5 - 69
4 Feb 26	N/A	N/A	3	2 - 4	3 - 25	4 - 61
5 Feb 26	67	59	2	2 - 3	3 - 22	5 - 70
6 Feb 26	56	45	2	2 - 4	3 - 18	4 - 69
7 Feb 26	49	37	2	2 - 4	3 - 13	3 - 57
8 Feb 26	40	28	2	2	1 - 6	8 - 44
9 Feb 26	43	34	2	2 - 3	2 - 13	12 - 67
10 Feb 26	70	61	3	2 - 5	3 - 21	3 - 83
11 Feb 26	80	72	3	2 - 4	3 - 21	3 - 89
12 Feb 26	76	66	3	2 - 4	4 - 23	4 - 79
13 Feb 26	47	34	2	2 - 3	2 - 9	6 - 55
14 Feb 26	50	38	2	2 - 3	3 - 9	4 - 59
15 Feb 26	43	30	2	2 - 3	2 - 11	4 - 54
16 Feb 26	63	50	2	2 - 3	2 - 14	5 - 66
17 Feb 26	51	39	2	2	2 - 9	6 - 46
18 Feb 26	43	31	2	2	3 - 25	8 - 59
19 Feb 26	76	65	3	2 - 3	5 - 31	5 - 83
20 Feb 26	82	72	3	2 - 4	4 - 28	4 - 99
21 Feb 26	69	58	2	2 - 3	4 - 18	8 - 71
22 Feb 26	57	47	2	2 - 4	2 - 10	7 - 67
23 Feb 26	47	33	2	2 - 3	3 - 12	6 - 60
24 Feb 26	48	34	2	2	2 - 8	11 - 45
25 Feb 26	55	41	2	2 - 3	2 - 11	9 - 59
26 Feb 26	49	37	2	2 - 4	2 - 9	9 - 58
27 Feb 26	38	24	2	2 - 3	2 - 11	3 - 44
28 Feb 26	33	19	2	2 - 3	2 - 8	3 - 45
Range	33 - 82	19 - 72	2 - 3	2 - 5	1 - 31	3 - 99
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	25	25	28	28	28	28
Monitoring Hour	600	600	644	644	644	644
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : February


MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Temperature (° C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Feb 26	22.6	33.2	26.9	39	99	79	1,011	1,016	1,013	0.0
2 Feb 26	20.6	32.6	26.4	31	99	67	1,011	1,016	1,014	0.0
3 Feb 26	23.0	31.7	26.5	46	90	67	1,012	1,017	1,014	0.0
4 Feb 26	21.6	33.3	27.1	38	91	67	1,011	1,016	1,013	0.0
5 Feb 26	21.9	34.6	27.6	35	93	68	1,009	1,015	1,012	0.0
6 Feb 26	22.9	36.2	28.3	32	99	72	1,007	1,013	1,011	0.0
7 Feb 26	22.6	34.7	27.8	37	99	75	1,007	1,012	1,009	0.0
8 Feb 26	23.8	33.5	27.9	51	99	82	1,008	1,013	1,010	0.4
9 Feb 26	23.0	31.5	26.6	44	99	83	1,010	1,014	1,011	0.4
10 Feb 26	21.4	33.8	27.1	39	99	74	1,010	1,014	1,012	0.0
11 Feb 26	21.9	35.0	28.1	37	99	72	1,010	1,016	1,012	0.0
12 Feb 26	22.7	34.5	28.0	39	99	74	1,009	1,014	1,011	0.0
13 Feb 26	23.4	34.5	28.2	46	99	80	1,008	1,013	1,010	0.0
14 Feb 26	23.8	33.4	28.1	53	99	81	1,007	1,011	1,009	0.0
15 Feb 26	24.0	34.1	28.4	52	99	81	1,007	1,011	1,009	0.0
16 Feb 26	24.5	35.5	29.1	45	99	77	1,005	1,011	1,008	0.0
17 Feb 26	25.2	33.4	29.0	56	99	80	1,007	1,011	1,008	0.0
18 Feb 26	25.0	31.7	27.4	64	99	91	1,009	1,013	1,010	0.6
19 Feb 26	23.8	34.3	28.4	41	99	77	1,010	1,014	1,012	0.0
20 Feb 26	23.8	34.5	28.5	39	99	74	1,009	1,015	1,012	0.0
21 Feb 26	23.0	34.6	28.5	38	97	72	1,005	1,011	1,008	0.0
22 Feb 26	24.5	37.0	29.1	35	99	73	1,002	1,009	1,006	0.0
23 Feb 26	24.0	34.5	28.7	49	99	79	1,003	1,009	1,006	0.0
24 Feb 26	25.5	33.3	28.8	60	99	85	1,004	1,009	1,007	0.0
25 Feb 26	24.1	34.6	28.6	49	99	82	1,005	1,011	1,008	0.0
26 Feb 26	24.1	35.0	28.0	50	99	86	1,003	1,010	1,007	4.0
27 Feb 26	23.9	33.8	28.0	48	99	83	1,002	1,008	1,005	0.0
28 Feb 26	24.1	35.7	29.1	41	99	77	1,003	1,008	1,005	0.0
Total	20.6	37.0	28.0	31	99	77	1,002	1,017	1,010	5.4
Day	28			28			28			28
Hours	672			672			672			672

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-28/February/2026 STATION : Wat Bang Gado

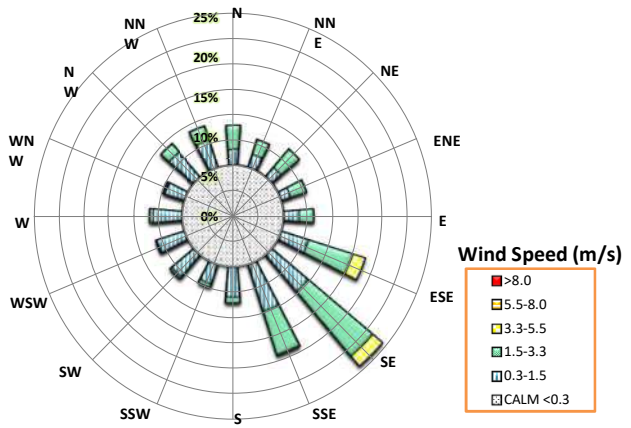

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	1.93%	2.98%	0.00%	0.00%	0.00%	4.91%
NNE	1.64%	1.93%	0.00%	0.00%	0.00%	3.57%
NE	1.49%	2.98%	0.00%	0.00%	0.00%	4.46%
ENE	1.19%	2.08%	0.00%	0.00%	0.00%	3.27%
E	1.93%	1.79%	0.00%	0.00%	0.00%	3.72%
ESE	3.57%	5.80%	1.64%	0.00%	0.00%	11.01%
SE	5.95%	10.57%	1.64%	0.00%	0.00%	18.15%
SSE	6.10%	5.65%	0.15%	0.00%	0.00%	11.90%
S	3.72%	0.74%	0.00%	0.00%	0.00%	4.46%
SSW	2.53%	0.45%	0.00%	0.00%	0.00%	2.98%
SW	3.57%	0.30%	0.00%	0.00%	0.00%	3.87%
WSW	3.57%	0.15%	0.00%	0.00%	0.00%	3.72%
W	3.57%	0.45%	0.00%	0.00%	0.00%	4.02%
WNW	2.53%	0.15%	0.15%	0.00%	0.00%	2.83%
NW	4.02%	1.34%	0.00%	0.00%	0.00%	5.36%
NNW	3.57%	1.79%	0.00%	0.00%	0.00%	5.36%
	50.89%	39.14%	3.57%	0.00%	0.00%	93.60%

No. of Monitored Hours	672	Hours	No. of Calm	43	Hours
No. of Monitored Days	28	Days	Calm (%)	6.40%	
Missing Data	0	Hours	Average Wind Speed	1.44	m/s
No. of Valid Data	672	Hours	Maximum Wind Speed	4.80	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	SE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : February

MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Feb 26	76	68	3	2 - 4	5 - 43	2 - 107*
2 Feb 26	75	64	3	2 - 5	5 - 35	4 - 102*
3 Feb 26	65	54	3	3 - 4	7 - 36	6 - 105*
4 Feb 26	59	47	3	2 - 5	4 - 39	3 - 85
5 Feb 26	66	59	3	2 - 4	3 - 30	8 - 106*
6 Feb 26	55	45	3	2 - 3	3 - 25	1 - 92
7 Feb 26	41	36	3	2 - 3	3 - 24	2 - 84
8 Feb 26	33	27	2	2 - 3	1 - 10	3 - 57
9 Feb 26	37	33	3	2 - 3	1 - 25	5 - 80
10 Feb 26	65	56	3	2 - 5	5 - 32	1 - 97
11 Feb 26	69	63	4	3 - 7	4 - 32	1 - 116*
12 Feb 26	74	64	3	2 - 5	4 - 24	8 - 109*
13 Feb 26	43	39	3	2 - 3	2 - 19	3 - 71
14 Feb 26	43	37	3	2 - 3	3 - 17	1 - 75
15 Feb 26	41	35	3	2 - 6	2 - 14	1 - 76
16 Feb 26	62	53	3	2 - 6	3 - 14	1 - 96
17 Feb 26	48	41	3	2 - 3	2 - 12	6 - 59
18 Feb 26	38	29	3	2 - 3	4 - 32	4 - 74
19 Feb 26	73	65	3	2 - 5	4 - 34	1 - 92
20 Feb 26	80	70	3	3 - 5	5 - 43	2 - 108*
21 Feb 26	64	54	3	2 - 5	3 - 29	1 - 82
22 Feb 26	58	44	3	2 - 5	3 - 12	8 - 75
23 Feb 26	42	35	3	2 - 3	3 - 13	4 - 77
24 Feb 26	40	35	3	2 - 3	2 - 11	10 - 55
25 Feb 26	46	39	3	3 - 5	4 - 16	5 - 73
26 Feb 26	42	37	3	3 - 7	3 - 18	6 - 68
27 Feb 26	27	20	3	2 - 4	4 - 13	1 - 59
28 Feb 26	20	19	3	2 - 3	2 - 14	1 - 49
Range	20 - 80	19 - 70	2 - 4	2 - 7	1 - 43	1 - 116*
Number of times (exceeded standard)	0	0	0	0	0	7
Total Day	28	28	28	28	28	28
Monitoring Hour	672	672	643	643	643	643
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : February


MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Temperature (° C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Feb 26	22.5	32.7	26.9	44	89	70	1,011	1,016	1,013	0.0
2 Feb 26	21.6	32.2	26.6	31	85	60	1,011	1,016	1,013	0.0
3 Feb 26	22.6	31.1	26.5	45	76	62	1,012	1,016	1,014	0.0
4 Feb 26	22.5	33.0	27.3	38	77	60	1,010	1,015	1,013	0.0
5 Feb 26	21.8	35.5	27.9	35	82	62	1,008	1,014	1,011	0.0
6 Feb 26	22.8	36.1	28.4	33	89	66	1,007	1,013	1,010	0.0
7 Feb 26	23.1	35.9	28.5	35	89	63	1,006	1,012	1,009	0.0
8 Feb 26	23.5	34.3	28.0	47	96	74	1,008	1,012	1,010	4.2
9 Feb 26	23.4	30.9	26.3	48	99	80	1,009	1,013	1,011	9.0
10 Feb 26	21.5	33.4	26.9	42	97	72	1,009	1,014	1,011	0.0
11 Feb 26	22.4	34.3	27.8	38	90	67	1,009	1,015	1,012	0.0
12 Feb 26	22.7	34.9	28.2	38	89	68	1,009	1,014	1,011	0.0
13 Feb 26	23.8	35.3	28.6	43	96	73	1,007	1,012	1,009	0.0
14 Feb 26	23.9	35.0	28.4	49	96	75	1,007	1,011	1,009	0.0
15 Feb 26	24.1	35.4	28.7	46	96	73	1,006	1,011	1,008	0.0
16 Feb 26	24.3	35.9	29.4	44	92	70	1,005	1,010	1,007	0.0
17 Feb 26	25.0	34.8	29.3	49	90	71	1,006	1,010	1,008	0.0
18 Feb 26	25.6	31.2	27.6	59	89	79	1,008	1,012	1,010	0.4
19 Feb 26	24.0	35.2	28.5	39	92	70	1,010	1,014	1,011	0.0
20 Feb 26	24.0	34.7	28.6	42	88	66	1,009	1,014	1,011	0.0
21 Feb 26	23.1	36.1	29.0	37	90	65	1,004	1,011	1,008	0.0
22 Feb 26	24.2	36.6	29.4	36	91	67	1,002	1,008	1,006	0.0
23 Feb 26	23.7	36.2	29.2	43	90	70	1,003	1,009	1,006	0.0
24 Feb 26	25.3	35.3	29.1	49	91	75	1,004	1,009	1,007	0.0
25 Feb 26	24.4	34.3	28.9	47	87	72	1,005	1,010	1,008	0.0
26 Feb 26	24.4	35.3	27.9	47	99	80	1,002	1,009	1,006	11.0
27 Feb 26	23.9	35.5	27.8	46	99	82	1,002	1,008	1,005	13.6
28 Feb 26	23.6	35.3	29.0	47	99	76	1,002	1,007	1,005	0.0
Total	21.5	36.6	28.2	31	99	70	1,002	1,016	1,009	38.2
Day	28			28			28			28
Hours	672			672			672			672

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-28/February/2026	STATION : Ban Klong Klae

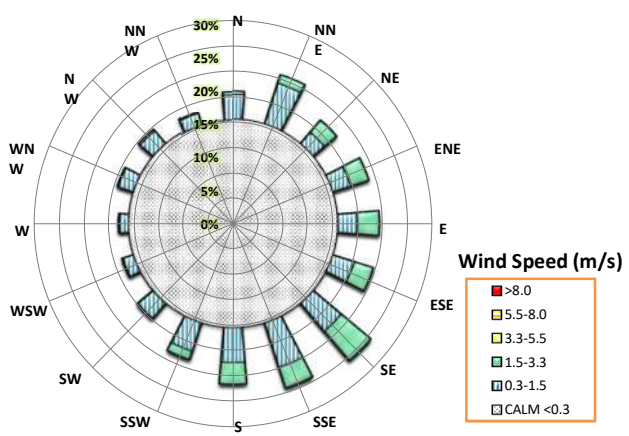

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	3.72%	0.45%	0.00%	0.00%	0.00%	**4.17%**
NNE	6.40%	1.34%	0.00%	0.00%	0.00%	**7.74%**
NE	2.23%	2.38%	0.00%	0.00%	0.00%	**4.61%**
ENE	2.83%	2.83%	0.00%	0.00%	0.00%	**5.65%**
E	2.98%	3.27%	0.00%	0.00%	0.00%	**6.25%**
ESE	3.42%	2.98%	0.00%	0.00%	0.00%	**6.40%**
SE	5.51%	5.80%	0.00%	0.00%	0.00%	**11.31%**
SSE	6.99%	3.27%	0.00%	0.00%	0.00%	**10.27%**
S	5.21%	3.27%	0.00%	0.00%	0.00%	**8.48%**
SSW	4.46%	1.34%	0.00%	0.00%	0.00%	**5.80%**
SW	2.98%	0.15%	0.00%	0.00%	0.00%	**3.13%**
WSW	1.64%	0.15%	0.00%	0.00%	0.00%	**1.79%**
W	1.34%	0.15%	0.00%	0.00%	0.00%	**1.49%**
WNW	2.38%	0.15%	0.00%	0.00%	0.00%	**2.53%**
NW	2.53%	0.30%	0.00%	0.00%	0.00%	**2.83%**
NNW	1.79%	0.15%	0.00%	0.00%	0.00%	**1.93%**
	56.40%	**27.98%**	**0.00%**	**0.00%**	**0.00%**	**84.38%**

No. of Monitored Hours	672	Hours	No. of Calm	105	Hours
No. of Monitored Days	28	Days	Calm (%)	15.63%	
Missing Data	0	Hours	Average Wind Speed	1.10	m/s
No. of Valid Data	672	Hours	Maximum Wind Speed	3.20	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	SE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : February

MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Feb 26	70	59	1	1 - 2	3 - 9	5 - 60
2 Feb 26	69	59	2	1 - 3	3 - 10	5 - 51
3 Feb 26	56	49	2	1 - 2	4 - 13	7 - 54
4 Feb 26	61	49	2	1 - 3	2 - 12	5 - 48
5 Feb 26	64	55	1	1 - 3	2 - 14	5 - 73
6 Feb 26	51	45	1	1 - 2	2 - 7	7 - 69
7 Feb 26	38	34	1	1 - 2	2 - 7	6 - 62
8 Feb 26	31	24	1	1 - 2	2 - 5	7 - 43
9 Feb 26	38	31	1	1 - 2	1 - 10	11 - 63
10 Feb 26	63	55	1	1 - 3	4 - 18	5 - 72
11 Feb 26	69	61	2	1 - 3	3 - 14	4 - 81
12 Feb 26	68	61	2	1 - 3	3 - 12	5 - 67
13 Feb 26	37	34	1	1 - 2	2 - 9	7 - 47
14 Feb 26	43	35	1	1 - 2	2 - 9	4 - 49
15 Feb 26	35	26	1	1	2 - 8	5 - 45
16 Feb 26	61	51	1	1 - 3	2 - 8	4 - 57
17 Feb 26	42	37	1	1	2 - 6	6 - 48
18 Feb 26	38	30	1	1	2 - 15	7 - 55
19 Feb 26	66	59	1	1 - 2	4 - 12	6 - 71
20 Feb 26	70	62	2	1 - 3	4 - 12	5 - 81
21 Feb 26	59	50	1	1 - 2	2 - 12	5 - 58
22 Feb 26	52	46	1	1 - 2	2 - 8	5 - 50
23 Feb 26	41	35	1	1 - 2	2 - 7	5 - 50
24 Feb 26	39	34	1	1	1 - 4	9 - 44
25 Feb 26	46	39	1	1 - 3	2 - 7	10 - 50
26 Feb 26	43	36	1	1 - 2	2 - 7	11 - 48
27 Feb 26	27	20	1	1 - 2	2 - 7	8 - 35
28 Feb 26	24	16	1	1 - 2	2 - 6	8 - 32
Range	24 - 70	16 - 62	1 - 2	1 - 3	1 - 18	4 - 81
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	28	28	28	28	28	28
Monitoring Hour	672	672	645	645	645	645
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : February


MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Feb 26	21.9	32.7	26.3	43	100	82	1,010	1,015	1,012	0.0
2 Feb 26	20.6	32.4	25.9	30	100	71	1,010	1,015	1,012	0.0
3 Feb 26	22.7	30.6	25.9	47	99	72	1,011	1,015	1,013	0.0
4 Feb 26	22.1	32.2	26.3	39	100	73	1,009	1,015	1,012	0.0
5 Feb 26	21.5	35.0	27.3	34	100	73	1,008	1,013	1,010	0.0
6 Feb 26	21.9	35.3	27.7	33	100	74	1,006	1,012	1,009	0.0
7 Feb 26	21.8	35.3	27.7	35	100	76	1,005	1,011	1,008	0.0
8 Feb 26	23.1	34.2	27.8	47	100	82	1,007	1,011	1,009	0.0
9 Feb 26	22.8	31.7	26.2	45	100	87	1,008	1,012	1,010	24.6
10 Feb 26	21.4	32.9	26.3	42	100	80	1,008	1,013	1,010	0.0
11 Feb 26	21.5	34.0	27.0	38	100	78	1,008	1,014	1,011	0.0
12 Feb 26	22.1	35.3	27.6	37	100	79	1,008	1,013	1,010	0.0
13 Feb 26	23.1	34.8	28.0	45	100	81	1,006	1,011	1,008	0.0
14 Feb 26	23.2	33.9	27.8	51	100	83	1,006	1,010	1,008	0.0
15 Feb 26	23.4	34.5	28.1	50	100	82	1,005	1,010	1,007	0.0
16 Feb 26	23.7	34.9	28.6	47	100	80	1,004	1,009	1,006	0.0
17 Feb 26	24.7	33.8	28.8	52	100	82	1,005	1,009	1,007	0.0
18 Feb 26	24.0	30.9	26.9	63	100	93	1,007	1,011	1,009	4.8
19 Feb 26	23.4	34.2	27.7	41	100	82	1,009	1,013	1,010	0.0
20 Feb 26	23.1	33.8	27.7	43	100	80	1,008	1,013	1,010	0.0
21 Feb 26	23.1	35.2	28.3	38	100	75	1,003	1,010	1,007	0.0
22 Feb 26	23.6	36.7	28.8	36	100	75	1,001	1,007	1,005	0.0
23 Feb 26	23.1	35.2	28.6	45	100	81	1,002	1,008	1,005	0.0
24 Feb 26	24.9	34.5	28.7	52	100	85	1,003	1,008	1,006	0.0
25 Feb 26	24.4	34.3	28.3	48	100	85	1,004	1,009	1,007	0.0
26 Feb 26	23.7	34.6	27.7	49	100	88	1,001	1,008	1,005	25.8
27 Feb 26	23.7	33.8	27.5	48	100	86	1,001	1,007	1,004	2.0
28 Feb 26	23.4	35.7	28.7	41	100	79	1,001	1,006	1,004	0.0
Total	20.6	36.7	27.6	30	100	80	1,001	1,015	1,008	57.2
Day	28			28			28			28
Hours	672			672			672			672

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-28/February/2026 STATION : Ban Chao Nua

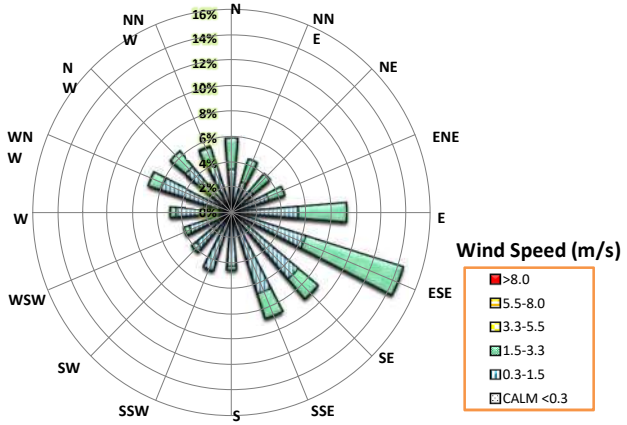

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	3.27%	2.53%	0.00%	0.00%	0.00%	5.80%
NNE	2.38%	1.93%	0.00%	0.00%	0.00%	4.32%
NE	2.08%	1.79%	0.00%	0.00%	0.00%	3.87%
ENE	2.98%	1.34%	0.00%	0.00%	0.00%	4.32%
E	5.21%	3.87%	0.00%	0.00%	0.00%	9.08%
ESE	6.10%	8.18%	0.00%	0.00%	0.00%	14.29%
SE	6.85%	2.08%	0.00%	0.00%	0.00%	8.93%
SSE	6.70%	2.08%	0.00%	0.00%	0.00%	8.78%
S	4.17%	0.30%	0.00%	0.00%	0.00%	4.46%
SSW	4.76%	0.00%	0.00%	0.00%	0.00%	4.76%
SW	3.57%	0.45%	0.00%	0.00%	0.00%	4.02%
WSW	3.42%	0.45%	0.00%	0.00%	0.00%	3.87%
W	4.32%	0.45%	0.00%	0.00%	0.00%	4.76%
WNW	5.80%	1.04%	0.00%	0.00%	0.00%	6.85%
NW	4.61%	1.64%	0.00%	0.00%	0.00%	6.25%
NNW	3.87%	1.49%	0.00%	0.00%	0.15%	5.51%
	70.09%	29.61%	0.00%	0.00%	0.15%	99.85%

No. of Monitored Hours	672	Hours	No. of Calm	1	Hours
No. of Monitored Days	28	Days	Calm (%)	0.15%	
Missing Data	0	Hours	Average Wind Speed	50.58	m/s
No. of Valid Data	672	Hours	Maximum Wind Speed	33222.70	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	ESE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : March

MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Mar 26	21	20	N/A	N/A	1 - 8	2 - 49
2 Mar 26	35	30	N/A	N/A	2 - 10	3 - 52
3 Mar 26	48	46	N/A	N/A	2 - 15	3 - 65
4 Mar 26	55	51	N/A	N/A	2 - 20	11 - 72
5 Mar 26	68	66	N/A	N/A	2 - 12	2 - 66
6 Mar 26	55	52	N/A	N/A	2 - 19	4 - 58
7 Mar 26	40	39	N/A	N/A	3 - 18	3 - 93
8 Mar 26	38	36	N/A	N/A	2 - 18	2 - 62
9 Mar 26	43	42	N/A	2 - 3	3 - 26	2 - 95
10 Mar 26	71	51	3	2 - 4	5 - 17	2 - 92
11 Mar 26	65	59	3	2 - 5	5 - 14	4 - 98
12 Mar 26	57	49	2	2 - 3	2 - 15	11 - 74
13 Mar 26	35	N/A	2	2 - 4	2 - 14	2 - 95
14 Mar 26	39	N/A	2	2 - 3	2 - 21	9 - 108*
15 Mar 26	62	N/A	3	2 - 4	3 - 28	8 - 88
16 Mar 26	53	N/A	3	2 - 3	2 - 11	6 - 72
17 Mar 26	31	27	2	2 - 3	2 - 9	8 - 65
18 Mar 26	35	N/A	2	2 - 3	1 - 10	5 - 54
19 Mar 26	34	N/A	2	2 - 4	1 - 7	3 - 47
20 Mar 26	42	38	2	2 - 3	1 - 13	4 - 48
21 Mar 26	35	33	2	2 - 3	1 - 9	3 - 49
22 Mar 26	37	33	2	2 - 2	1 - 5	11 - 54
23 Mar 26	34	31	2	2 - 3	1 - 6	13 - 49
24 Mar 26	33	31	2	2 - 2	1 - 7	10 - 45
25 Mar 26	35	30	2	2 - 2	1 - 6	9 - 50
26 Mar 26	37	34	2	2 - 3	2 - 8	9 - 62
27 Mar 26	39	34	2	2 - 3	1 - 7	13 - 53
28 Mar 26	38	36	2	2 - 3	1 - 7	7 - 51
29 Mar 26	35	29	2	2 - 3	1 - 6	15 - 42
30 Mar 26	28	24	3	2 - 3	1 - 7	8 - 35
31 Mar 26	34	29	3	2 - 3	1 - 9	5 - 43
Range	21 - 71	20 - 66	2 - 3	2 - 5	1 - 28	2 - 108*
Number of times (exceeded standard)	0	0	0	0	0	1
Total Day	31	25	22	23	31	31
Monitoring Hour	726	570	504	504	711	711
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : March


MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Mar 26	23.3	37.2	29.3	38	100	74	1,003	1,009	1,006	0.0
2 Mar 26	23.8	38.2	29.8	29	100	70	1,004	1,010	1,007	0.0
3 Mar 26	23.0	37.7	29.2	27	100	69	1,004	1,010	1,007	0.0
4 Mar 26	22.4	37.9	28.5	19	99	56	1,004	1,010	1,007	0.0
5 Mar 26	22.2	36.3	28.8	31	99	67	1,005	1,009	1,007	0.0
6 Mar 26	24.7	35.6	28.7	40	100	79	1,007	1,012	1,009	0.0
7 Mar 26	24.7	35.5	29.2	38	100	74	1,008	1,013	1,010	0.0
8 Mar 26	24.1	35.0	28.7	42	100	78	1,007	1,012	1,010	0.0
9 Mar 26	24.0	36.6	29.3	36	100	74	1,008	1,013	1,010	0.0
10 Mar 26	23.2	35.0	28.6	27	99	70	1,009	1,015	1,012	1.0
11 Mar 26	25.6	33.0	28.8	51	99	76	1,008	1,013	1,011	0.0
12 Mar 26	25.0	33.3	28.4	46	99	71	1,007	1,013	1,010	0.0
13 Mar 26	23.4	32.6	26.3	47	100	88	1,008	1,013	1,010	16.6
14 Mar 26	22.2	33.7	27.3	42	100	77	1,009	1,015	1,012	0.0
15 Mar 26	23.6	35.6	28.8	37	99	74	1,009	1,014	1,011	0.0
16 Mar 26	23.6	36.0	29.0	36	100	74	1,007	1,013	1,010	0.0
17 Mar 26	24.5	36.0	29.2	40	100	76	1,007	1,012	1,010	0.0
18 Mar 26	24.0	35.2	28.8	41	100	76	1,007	1,013	1,010	0.0
19 Mar 26	24.3	35.6	29.3	44	94	71	1,007	1,012	1,010	0.0
20 Mar 26	24.0	34.5	28.4	51	94	76	1,007	1,011	1,009	0.0
21 Mar 26	23.8	36.9	29.6	44	95	72	1,007	1,012	1,009	0.0
22 Mar 26	24.4	38.1	30.1	38	91	69	1,007	1,011	1,009	0.0
23 Mar 26	25.6	37.7	30.6	45	92	71	1,006	1,011	1,009	0.0
24 Mar 26	25.6	37.3	30.8	47	91	70	1,005	1,009	1,007	0.0
25 Mar 26	25.0	37.4	30.7	45	90	68	1,006	1,010	1,008	0.0
26 Mar 26	25.1	35.8	29.5	49	91	73	1,005	1,010	1,007	0.0
27 Mar 26	N/A	N/A	N/A	N/A	N/A	N/A	1,005	1,010	1,007	0.0
28 Mar 26	N/A	N/A	N/A	N/A	N/A	N/A	1,004	1,009	1,007	0.0
29 Mar 26	N/A	N/A	N/A	N/A	N/A	N/A	1,006	1,011	1,008	0.0
30 Mar 26	N/A	N/A	N/A	N/A	N/A	N/A	1,006	1,010	1,008	0.0
31 Mar 26	26.6	37.0	32.4	47	99	69	1,005	1,011	1,008	0.0
Total	22.2	38.2	29.2	19	100	73	1,003	1,015	1,009	17.6
Day	27			27			31			31
Hours	625			625			744			743

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/March/2026	STATION : Ban Don Mod Tanoi

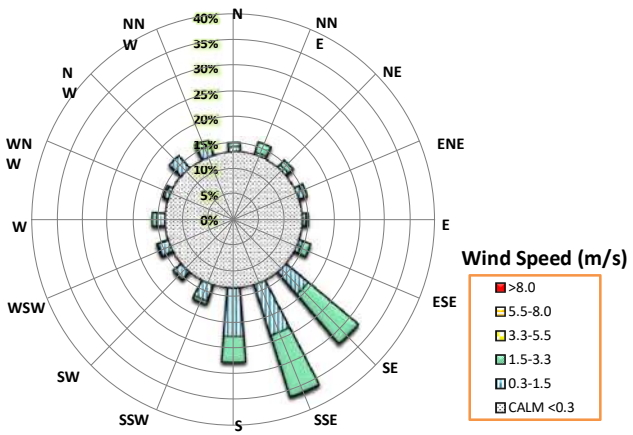

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	0.94%	0.81%	0.00%	0.00%	0.00%	1.75%
NNE	0.54%	2.02%	0.00%	0.00%	0.00%	2.55%
NE	0.67%	1.21%	0.00%	0.00%	0.00%	1.88%
ENE	1.08%	0.67%	0.00%	0.00%	0.00%	1.75%
E	0.81%	0.40%	0.00%	0.00%	0.00%	1.21%
ESE	0.81%	1.61%	0.00%	0.00%	0.00%	2.42%
SE	5.78%	12.77%	0.00%	0.00%	0.00%	18.55%
SSE	10.48%	12.63%	0.13%	0.00%	0.00%	23.25%
S	9.54%	5.11%	0.00%	0.00%	0.00%	14.65%
SSW	3.36%	0.67%	0.00%	0.00%	0.00%	4.03%
SW	2.02%	0.00%	0.00%	0.00%	0.00%	2.02%
WSW	2.15%	0.27%	0.00%	0.00%	0.00%	2.42%
W	1.61%	0.94%	0.00%	0.00%	0.00%	2.55%
WNW	0.81%	0.40%	0.00%	0.00%	0.00%	1.21%
NW	3.09%	0.00%	0.00%	0.00%	0.00%	3.09%
NNW	3.09%	0.13%	0.00%	0.00%	0.00%	3.23%
	46.77%	39.65%	0.13%	0.00%	0.00%	86.56%

No. of Monitored Hours	744	Hours	No. of Calm	100	Hours
No. of Monitored Days	31	Days	Calm (%)	13.44%	
Missing Data	0	Hours	Average Wind Speed	1.35	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	3.50	m/s
			Prevailing Wind Direction	SSE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : March

MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Mar 26	37	20	2	2 - 3	1 - 9	4 - 46
2 Mar 26	47	31	2	2 - 3	2 - 11	5 - 55
3 Mar 26	57	44	2	2 - 3	2 - 12	7 - 61
4 Mar 26	67	57	2	2 - 3	2 - 15	5 - 70
5 Mar 26	76	63	2	2 - 4	2 - 17	9 - 63
6 Mar 26	62	50	3	2 - 7	2 - 14	7 - 54
7 Mar 26	53	42	3	2 - 4	4 - 13	5 - 83
8 Mar 26	58	46	2	2 - 6	2 - 23	4 - 61
9 Mar 26	57	43	3	2 - 3	3 - 25	4 - 87
10 Mar 26	70	56	3	2 - 4	4 - 19	4 - 88
11 Mar 26	61	47	3	2 - 4	5 - 15	5 - 89
12 Mar 26	N/A	N/A	N/A	2 - 3	3 - 12	25 - 70
13 Mar 26	60	48	3	2 - 4	3 - 23	6 - 84
14 Mar 26	52	39	3	2 - 3	3 - 24	8 - 95
15 Mar 26	66	56	3	2 - 4	2 - 18	8 - 77
16 Mar 26	57	49	2	2 - 3	2 - 14	13 - 67
17 Mar 26	43	31	2	2 - 3	2 - 9	10 - 59
18 Mar 26	45	34	2	2 - 4	2 - 10	6 - 52
19 Mar 26	42	28	2	2 - 3	1 - 13	5 - 44
20 Mar 26	52	37	2	2 - 3	2 - 12	10 - 49
21 Mar 26	46	36	2	2 - 3	2 - 11	5 - 46
22 Mar 26	44	34	2	2 - 3	1 - 6	15 - 52
23 Mar 26	43	32	2	2	1 - 7	14 - 43
24 Mar 26	41	29	2	2	2 - 6	12 - 48
25 Mar 26	43	30	2	2	1 - 7	10 - 48
26 Mar 26	49	39	2	2	2 - 6	14 - 61
27 Mar 26	45	35	2	2 - 3	1 - 6	13 - 53
28 Mar 26	48	37	2	2	1 - 7	11 - 51
29 Mar 26	41	29	2	2	1 - 5	18 - 43
30 Mar 26	37	23	2	2	1 - 5	10 - 37
31 Mar 26	41	32	2	2	2 - 8	8 - 47
Range	37 - 76	20 - 63	2 - 3	2 - 7	1 - 25	4 - 95
Number of times (exceeded standard)	0	0	0	0	0	0
Total Monitoring Day	30	30	30	31	31	31
Total Monitoring Hour	720	720	690	690	702	702
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : March


MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Temperature (° C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Mar 26	24.4	36.0	29.7	37	99	71	1,003	1,009	1,006	0.0
2 Mar 26	25.0	37.1	30.2	32	95	67	1,004	1,010	1,007	0.0
3 Mar 26	24.1	37.6	29.6	24	95	63	1,004	1,010	1,007	0.0
4 Mar 26	24.0	36.7	29.1	20	85	50	1,004	1,010	1,007	0.0
5 Mar 26	22.5	34.9	28.2	33	94	66	1,005	1,009	1,007	0.0
6 Mar 26	25.1	33.5	28.5	46	99	79	1,007	1,012	1,009	0.0
7 Mar 26	24.9	33.9	29.3	45	99	74	1,008	1,013	1,010	0.0
8 Mar 26	24.7	34.4	28.5	42	99	80	1,007	1,012	1,010	5.6
9 Mar 26	24.6	35.0	29.4	40	99	75	1,008	1,013	1,010	0.0
10 Mar 26	24.2	34.3	29.0	40	99	70	1,009	1,015	1,012	0.0
11 Mar 26	25.8	33.2	29.2	48	99	74	1,008	1,013	1,011	0.0
12 Mar 26	23.1	32.7	29.2	36	90	63	1,007	1,012	1,009	0.0
13 Mar 26	23.8	32.8	27.1	49	99	84	1,008	1,013	1,011	2.4
14 Mar 26	22.6	33.3	27.8	44	99	74	1,009	1,015	1,012	0.0
15 Mar 26	24.5	34.9	29.2	37	98	69	1,009	1,015	1,012	0.0
16 Mar 26	24.4	34.3	29.0	40	99	73	1,007	1,013	1,010	0.0
17 Mar 26	25.3	34.2	29.0	43	99	76	1,007	1,012	1,010	0.0
18 Mar 26	24.3	33.8	28.7	47	99	77	1,007	1,013	1,010	0.0
19 Mar 26	24.7	33.8	28.9	47	94	73	1,007	1,012	1,010	0.0
20 Mar 26	24.1	32.9	28.1	56	94	76	1,007	1,011	1,009	0.0
21 Mar 26	24.4	34.2	29.0	49	92	74	1,007	1,012	1,009	0.0
22 Mar 26	25.0	35.2	29.6	44	88	70	1,007	1,011	1,009	0.0
23 Mar 26	26.1	34.9	29.9	52	90	73	1,006	1,011	1,009	0.0
24 Mar 26	25.8	34.5	29.9	52	90	73	1,005	1,009	1,007	0.0
25 Mar 26	25.6	34.8	29.9	51	87	70	1,006	1,010	1,008	0.0
26 Mar 26	25.9	36.4	30.2	46	88	71	1,005	1,010	1,007	0.0
27 Mar 26	26.0	35.4	29.9	44	90	71	1,005	1,010	1,007	0.0
28 Mar 26	25.4	34.9	29.7	47	92	71	1,004	1,009	1,007	0.0
29 Mar 26	25.9	34.7	29.8	43	85	66	1,006	1,011	1,008	0.0
30 Mar 26	24.6	33.4	29.0	52	89	71	1,006	1,010	1,008	0.0
31 Mar 26	24.4	35.0	29.2	53	91	75	1,005	1,011	1,008	0.0
Total	22.5	37.6	29.1	20	99	72	1,003	1,015	1,009	8.0
Day	31			31			31			31
Hours	735			735			735			735

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/March/2026 STATION : Wat Bang Gado

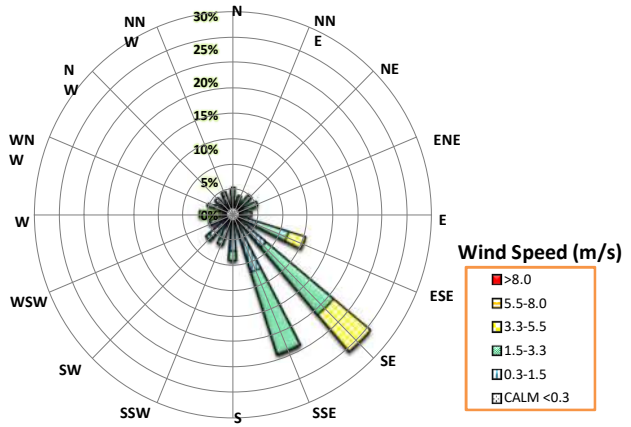

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	1.50%	1.50%	0.00%	0.00%	0.00%	2.99%
NNE	0.41%	1.50%	0.00%	0.00%	0.00%	1.90%
NE	1.09%	1.63%	0.00%	0.00%	0.00%	2.72%
ENE	0.82%	2.18%	0.00%	0.00%	0.00%	2.99%
E	0.41%	1.50%	0.00%	0.00%	0.00%	1.90%
ESE	2.86%	5.03%	2.59%	0.00%	0.00%	10.48%
SE	5.58%	13.20%	7.21%	0.00%	0.00%	25.99%
SSE	8.16%	12.79%	0.14%	0.00%	0.00%	21.09%
S	4.63%	1.36%	0.00%	0.00%	0.00%	5.99%
SSW	3.13%	0.82%	0.00%	0.00%	0.00%	3.95%
SW	3.67%	0.54%	0.00%	0.00%	0.00%	4.22%
WSW	2.45%	0.27%	0.00%	0.00%	0.00%	2.72%
W	2.31%	1.63%	0.00%	0.00%	0.00%	3.95%
WNW	1.90%	1.09%	0.00%	0.00%	0.00%	2.99%
NW	2.45%	0.00%	0.00%	0.00%	0.00%	2.45%
NNW	2.18%	0.54%	0.00%	0.00%	0.00%	2.72%
	43.54%	45.58%	9.93%	0.00%	0.00%	99.05%

No. of Monitored Hours	744	Hours	No. of Calm	7	Hours
No. of Monitored Days	31	Days	Calm (%)	0.95%	
Missing Data	9	Hours	Average Wind Speed	1.83	m/s
No. of Valid Data	735	Hours	Maximum Wind Speed	4.90	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	SE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : March

MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Mar 26	21	16	3	3	2 - 17	1 - 60
2 Mar 26	32	31	3	3	3 - 16	1 - 69
3 Mar 26	46	42	3	3 - 5	3 - 19	3 - 77
4 Mar 26	54	50	3	3 - 4	3 - 18	3 - 81
5 Mar 26	67	66	3	3 - 4	2 - 12	14 - 75
6 Mar 26	52	49	3	3 - 4	2 - 17	5 - 63
7 Mar 26	40	38	3	3 - 5	3 - 13	1 - 99
8 Mar 26	40	33	3	3 - 5	2 - 20	1 - 69
9 Mar 26	43	42	3	3 - 5	2 - 32	3 - 101*
10 Mar 26	63	54	4	3 - 6	5 - 20	7 - 107*
11 Mar 26	63	56	4	3 - 6	5 - 19	15 - 111*
12 Mar 26	50	40	3	3 - 4	2 - 12	28 - 76
13 Mar 26	57	52	3	3 - 5	3 - 22	2 - 105*
14 Mar 26	40	36	4	3 - 5	4 - 36	18 - 127*
15 Mar 26	60	53	4	3 - 6	5 - 28	4 - 101*
16 Mar 26	48	44	3	3 - 5	2 - 24	6 - 79
17 Mar 26	33	30	3	3 - 4	2 - 9	6 - 64
18 Mar 26	32	26	3	3 - 4	2 - 13	4 - 66
19 Mar 26	21	N/A	4	3 - 6	1 - 12	3 - 46
20 Mar 26	45	43	4	3 - 5	2 - 13	12 - 58
21 Mar 26	41	38	4	4 - 5	1 - 14	4 - 62
22 Mar 26	37	33	4	4	2 - 10	17 - 65
23 Mar 26	35	34	4	4	2 - 9	18 - 62
24 Mar 26	34	29	4	4	2 - 9	10 - 66
25 Mar 26	35	31	4	4	2 - 12	9 - 60
26 Mar 26	43	39	4	4	2 - 9	13 - 77
27 Mar 26	40	36	4	4	2 - 8	18 - 69
28 Mar 26	41	36	4	4	2 - 13	12 - 63
29 Mar 26	34	27	4	4 - 5	1 - 10	21 - 53
30 Mar 26	28	26	4	4	1 - 8	12 - 47
31 Mar 26	32	28	4	4	2 - 9	9 - 61
Range	21 - 67	16 - 66	3 - 4	3 - 6	1 - 36	1 - 127*
Number of times (exceeded standard)	0	0	0	0	0	6
Total Day	31	30	31	31	31	31
Monitoring Hour	738	717	716	716	716	709
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : March


MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Mar 26	24.3	35.8	29.8	47	92	70	1,003	1,008	1,005	0.0
2 Mar 26	25.3	37.0	30.5	35	92	63	1,004	1,009	1,006	0.0
3 Mar 26	24.1	37.7	30.1	28	87	59	1,004	1,009	1,007	0.0
4 Mar 26	22.2	38.0	29.2	21	74	50	1,003	1,010	1,007	0.0
5 Mar 26	23.1	36.3	28.9	34	80	59	1,004	1,009	1,007	0.0
6 Mar 26	24.7	34.3	28.8	45	93	70	1,006	1,011	1,009	0.0
7 Mar 26	24.8	33.8	29.4	42	95	68	1,007	1,012	1,010	0.0
8 Mar 26	24.6	35.4	29.4	39	88	67	1,007	1,012	1,009	0.0
9 Mar 26	24.6	36.3	29.8	35	91	65	1,008	1,012	1,010	0.0
10 Mar 26	24.7	36.1	29.5	39	86	62	1,009	1,014	1,011	0.0
11 Mar 26	26.0	33.7	29.3	50	83	67	1,007	1,013	1,010	0.0
12 Mar 26	25.0	34.0	29.0	44	82	62	1,006	1,012	1,009	0.0
13 Mar 26	23.2	32.0	27.4	49	91	71	1,008	1,013	1,010	0.2
14 Mar 26	22.4	34.4	27.7	41	93	69	1,009	1,014	1,011	4.8
15 Mar 26	24.7	34.4	29.2	39	84	62	1,008	1,014	1,011	0.0
16 Mar 26	24.5	35.6	29.4	39	89	66	1,007	1,012	1,009	0.0
17 Mar 26	24.8	35.5	29.6	40	91	67	1,007	1,011	1,009	0.0
18 Mar 26	24.9	35.6	29.5	42	90	68	1,007	1,012	1,010	0.0
19 Mar 26	20.5	34.8	28.9	45	92	69	1,006	1,012	1,009	0.0
20 Mar 26	24.7	34.0	28.4	51	89	72	1,007	1,011	1,009	0.0
21 Mar 26	24.2	35.9	29.5	46	90	69	1,006	1,011	1,009	0.0
22 Mar 26	25.3	36.3	30.0	40	84	67	1,006	1,011	1,009	0.0
23 Mar 26	26.2	35.8	30.3	48	87	70	1,005	1,011	1,008	0.0
24 Mar 26	25.7	35.6	30.4	48	88	69	1,004	1,009	1,007	0.0
25 Mar 26	26.0	36.1	30.5	47	82	66	1,006	1,009	1,007	0.0
26 Mar 26	26.2	37.7	30.6	42	86	67	1,004	1,010	1,007	0.0
27 Mar 26	26.1	36.9	30.4	39	86	67	1,004	1,009	1,006	0.0
28 Mar 26	25.8	36.0	30.2	43	87	65	1,004	1,009	1,006	0.0
29 Mar 26	26.4	36.0	30.3	40	78	61	1,005	1,010	1,007	0.0
30 Mar 26	24.9	34.9	29.8	46	84	66	1,005	1,010	1,007	0.0
31 Mar 26	24.3	35.6	29.7	49	89	70	1,004	1,011	1,008	0.0
Total	20.5	38.0	29.5	21	95	66	1,003	1,014	1,008	5.0
Day	31			31			31			31
Hours	743			743			744			744

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/March/2026	STATION : Ban Klong Klae

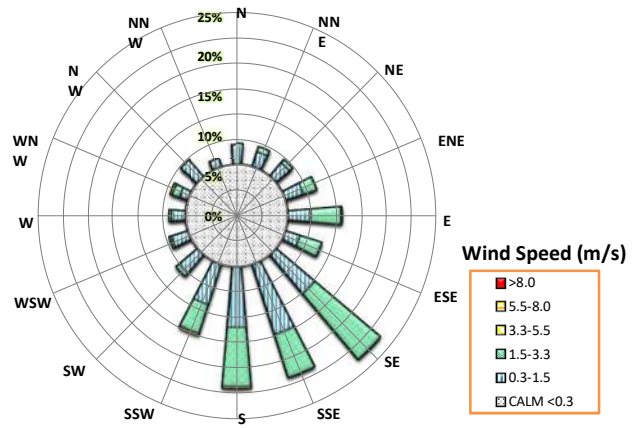

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	2.55%	0.00%	0.00%	0.00%	0.00%	2.55%
NNE	1.88%	0.67%	0.00%	0.00%	0.00%	2.55%
NE	2.15%	0.54%	0.00%	0.00%	0.00%	2.69%
ENE	2.28%	1.75%	0.00%	0.00%	0.00%	4.03%
E	2.82%	3.76%	0.13%	0.00%	0.00%	6.72%
ESE	1.88%	2.82%	0.00%	0.00%	0.00%	4.70%
SE	6.32%	10.75%	0.00%	0.00%	0.00%	17.07%
SSE	9.14%	5.65%	0.00%	0.00%	0.00%	14.78%
S	7.53%	7.39%	0.27%	0.00%	0.00%	15.19%
SSW	5.24%	3.76%	0.27%	0.00%	0.00%	9.27%
SW	2.96%	0.54%	0.00%	0.00%	0.00%	3.49%
WSW	2.15%	0.27%	0.00%	0.00%	0.00%	2.42%
W	1.75%	0.27%	0.00%	0.00%	0.00%	2.02%
WNW	1.08%	0.94%	0.27%	0.00%	0.00%	2.28%
NW	2.69%	0.00%	0.00%	0.00%	0.00%	2.69%
NNW	1.08%	0.00%	0.00%	0.00%	0.00%	1.08%
	53.49%	39.11%	0.94%	0.00%	0.00%	93.55%

No. of Monitored Hours	744	Hours	No. of Calm	48	Hours
No. of Monitored Days	31	Days	Calm (%)	6.45%	
Missing Data	0	Hours	Average Wind Speed	1.39	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	4.50	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	SE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : March

MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Mar 26	26	21	1	1	1 - 8	8 - 38
2 Mar 26	42	30	1	1 - 2	1 - 7	9 - 39
3 Mar 26	51	44	1	1 - 2	1 - 7	10 - 46
4 Mar 26	59	52	1	1 - 2	1 - 10	16 - 48
5 Mar 26	67	59	1	1 - 3	2 - 8	9 - 58
6 Mar 26	50	45	1	1 - 3	1 - 12	10 - 54
7 Mar 26	44	39	2	1 - 3	3 - 11	9 - 77
8 Mar 26	42	33	1	1 - 2	2 - 11	10 - 56
9 Mar 26	52	42	1	1 - 2	2 - 13	9 - 77
10 Mar 26	58	48	2	1 - 3	3 - 13	10 - 81
11 Mar 26	N/A	N/A	N/A	1 - 3	5 - 29	13 - 82
12 Mar 26	54	42	1	1 - 2	2 - 11	17 - 62
13 Mar 26	57	49	1	1 - 2	3 - 14	7 - 76
14 Mar 26	46	37	1	1 - 2	2 - 17	6 - 86
15 Mar 26	75	64	2	1 - 3	3 - 37	7 - 70
16 Mar 26	78	61	1	1 - 2	2 - 31	8 - 58
17 Mar 26	50	39	1	1	1 - 16	7 - 50
18 Mar 26	51	39	1	1 - 2	1 - 21	6 - 53
19 Mar 26	53	38	1	1 - 3	1 - 19	5 - 45
20 Mar 26	60	45	1	1 - 2	1 - 14	6 - 43
21 Mar 26	58	43	1	1 - 2	1 - 20	5 - 43
22 Mar 26	52	43	1	1	1 - 17	9 - 46
23 Mar 26	47	36	1	1	1 - 9	9 - 41
24 Mar 26	36	29	1	1	1 - 4	9 - 43
25 Mar 26	39	28	1	1	1 - 5	9 - 43
26 Mar 26	43	40	1	1 - 2	1 - 5	9 - 53
27 Mar 26	44	36	1	1	1 - 5	10 - 45
28 Mar 26	46	38	1	1	1 - 5	8 - 44
29 Mar 26	40	34	1	1 - 2	1 - 4	16 - 38
30 Mar 26	35	25	1	1	1 - 4	8 - 34
31 Mar 26	37	32	1	1	1 - 5	6 - 38
Range	26 - 78	21 - 64	1 - 2	1 - 3	1 - 37	5 - 86
Number of times (exceeded standard)	0	0	0	0	0	0
Total Monitoring Day	30	30	30	31	31	31
Total Monitoring Hour	720	720	691	691	708	708
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : March


MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Mar 26	24.0	35.5	29.3	41	100	74	1,002	1,007	1,004	0.0
2 Mar 26	24.8	37.3	29.9	31	100	70	1,003	1,008	1,005	0.0
3 Mar 26	23.6	36.5	29.1	28	100	69	1,003	1,009	1,006	0.0
4 Mar 26	23.1	36.9	28.7	19	99	54	1,003	1,009	1,006	0.0
5 Mar 26	21.1	35.1	27.7	34	100	72	1,003	1,008	1,006	0.0
6 Mar 26	24.5	33.7	28.2	43	100	81	1,005	1,010	1,008	0.0
7 Mar 26	24.4	34.2	28.8	42	100	76	1,006	1,011	1,009	0.0
8 Mar 26	24.0	35.2	28.5	40	100	78	1,006	1,011	1,008	0.0
9 Mar 26	23.9	35.6	29.2	37	100	75	1,007	1,011	1,009	0.0
10 Mar 26	24.3	34.8	28.8	39	100	73	1,008	1,013	1,010	0.0
11 Mar 26	25.6	32.7	28.5	52	100	79	1,007	1,012	1,009	0.0
12 Mar 26	24.8	32.9	28.2	46	99	72	1,006	1,011	1,008	0.0
13 Mar 26	23.4	31.5	26.1	51	100	89	1,007	1,012	1,009	28.8
14 Mar 26	22.7	33.1	27.1	43	100	81	1,008	1,013	1,010	0.0
15 Mar 26	24.4	33.6	28.7	41	100	75	1,007	1,013	1,010	0.0
16 Mar 26	23.8	34.5	28.7	39	100	76	1,006	1,011	1,008	0.0
17 Mar 26	24.4	34.5	28.9	42	100	78	1,006	1,011	1,008	0.0
18 Mar 26	24.3	34.4	28.6	44	100	80	1,006	1,011	1,009	0.0
19 Mar 26	24.1	34.6	28.9	46	100	79	1,005	1,011	1,008	0.0
20 Mar 26	24.0	33.6	28.0	53	100	84	1,006	1,010	1,008	0.0
21 Mar 26	23.7	34.9	29.0	48	100	80	1,006	1,010	1,008	0.0
22 Mar 26	24.3	35.5	29.4	41	100	79	1,006	1,010	1,008	0.0
23 Mar 26	25.6	35.0	29.9	51	100	81	1,004	1,010	1,007	0.0
24 Mar 26	25.3	35.2	29.9	51	100	79	1,003	1,008	1,006	0.0
25 Mar 26	25.0	35.7	29.8	49	100	77	1,005	1,008	1,006	0.0
26 Mar 26	25.1	37.2	30.1	43	100	78	1,004	1,009	1,006	0.0
27 Mar 26	25.4	36.5	29.8	42	100	77	1,003	1,008	1,005	0.0
28 Mar 26	24.8	35.7	29.7	45	100	76	1,003	1,008	1,005	0.0
29 Mar 26	25.5	35.5	29.9	39	99	73	1,004	1,009	1,006	0.0
30 Mar 26	24.3	33.9	28.9	49	100	78	1,005	1,009	1,007	0.0
31 Mar 26	23.8	35.5	29.1	51	100	82	1,004	1,010	1,007	0.0
Total	21.1	37.3	28.9	19	100	77	1,002	1,013	1,007	28.8
Day	31			31			31			31
Hours	742			742			744			744

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/March/2026 STATION : Ban Chao Nua

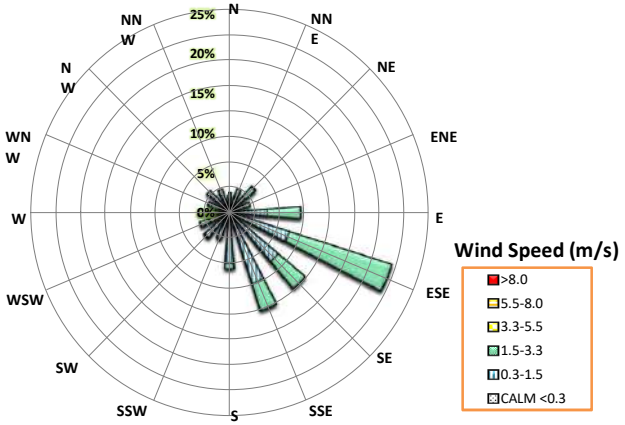

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	1.61%	0.81%	0.00%	0.00%	0.00%	2.42%
NNE	2.02%	1.08%	0.00%	0.00%	0.00%	3.09%
NE	2.55%	1.61%	0.13%	0.00%	0.00%	4.30%
ENE	1.88%	0.81%	0.00%	0.00%	0.00%	2.69%
E	4.70%	4.17%	0.00%	0.00%	0.00%	8.87%
ESE	7.80%	13.44%	0.00%	0.00%	0.00%	21.24%
SE	7.93%	4.44%	0.00%	0.00%	0.00%	12.37%
SSE	9.27%	3.49%	0.00%	0.00%	0.00%	12.77%
S	6.32%	0.67%	0.00%	0.00%	0.00%	6.99%
SSW	3.49%	0.00%	0.00%	0.00%	0.00%	3.49%
SW	4.03%	0.13%	0.00%	0.00%	0.00%	4.17%
WSW	2.69%	1.21%	0.00%	0.00%	0.00%	3.90%
W	2.69%	1.21%	0.00%	0.00%	0.00%	3.90%
WNW	2.42%	0.40%	0.00%	0.00%	0.00%	2.82%
NW	3.36%	0.40%	0.00%	0.00%	0.00%	3.76%
NNW	2.42%	0.81%	0.00%	0.00%	0.00%	3.23%
	65.19%	34.68%	0.13%	0.00%	0.00%	100.00%

No. of Monitored Hours	744	Hours	No. of Calm	0	Hours
No. of Monitored Days	31	Days	Calm (%)	0.00%	
Missing Data	0	Hours	Average Wind Speed	1.30	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	3.50	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	ESE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : April

MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Apr 26	35	32	2	2 - 3	1 - 7	3 - 50
2 Apr 26	35	33	2	2 - 3	1 - 6	6 - 40
3 Apr 26	N/A	32	2	2 - 3	1 - 5	6 - 49
4 Apr 26	N/A	42	3	2 - 4	2 - 8	3 - 60
5 Apr 26	N/A	53	3	2 - 4	1 - 7	6 - 75
6 Apr 26	N/A	52	3	2 - 3	2 - 8	7 - 70
7 Apr 26	N/A	42	3	2 - 3	1 - 7	3 - 64
8 Apr 26	54	53	3	2 - 3	2 - 8	3 - 73
9 Apr 26	52	48	2	2 - 3	1 - 8	5 - 51
10 Apr 26	37	36	2	2 - 3	1 - 7	3 - 52
11 Apr 26	38	37	3	2 - 4	2 - 9	2 - 67
12 Apr 26	49	45	3	2 - 3	2 - 6	3 - 70
13 Apr 26	45	43	3	2 - 3	1 - 6	6 - 60
14 Apr 26	68	67	3	2 - 3	2 - 9	5 - 74
15 Apr 26	65	60	3	2 - 4	1 - 8	2 - 61
16 Apr 26	38	37	3	2 - 3	1 - 4	5 - 59
17 Apr 26	39	34	3	2 - 3	1 - 6	1 - 51
18 Apr 26	49	38	3	2 - 4	2 - 7	4 - 91
19 Apr 26	41	36	3	2 - 3	1 - 7	6 - 75
20 Apr 26	47	44	3	2 - 3	1 - 8	7 - 88
21 Apr 26	57	49	3	2 - 4	1 - 8	8 - 75
22 Apr 26	55	47	3	2 - 3	1 - 6	5 - 65
23 Apr 26	45	41	3	2 - 3	1 - 6	9 - 51
24 Apr 26	31	30	3	3	1 - 7	5 - 50
25 Apr 26	29	24	3	3	1 - 8	6 - 42
26 Apr 26	26	24	3	3	1 - 5	13 - 53
27 Apr 26	23	19	3	3	1 - 5	16 - 46
28 Apr 26	27	26	3	3	2 - 7	9 - 64
29 Apr 26	37	27	3	3	2 - 5	10 - 68
30 Apr 26	22	21	3	3	1 - 7	3 - 35
Range	22 - 68	19 - 67	2 - 3	2 - 4	1 - 9	1 - 91
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	25	30	30	30	30	30
Monitoring Hour	584	686	692	692	692	692
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : April


MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Apr 26	25.3	38.1	30.8	43	100	79	1,005	1,010	1,008	0.0
2 Apr 26	25.5	37.5	30.5	49	100	81	1,006	1,010	1,008	0.0
3 Apr 26	25.8	37.3	30.7	43	100	75	1,005	1,010	1,007	0.0
4 Apr 26	25.2	38.2	30.9	35	100	73	1,003	1,009	1,006	0.0
5 Apr 26	24.4	39.6	30.7	26	100	67	1,003	1,008	1,005	0.0
6 Apr 26	25.0	39.5	30.8	27	99	67	1,004	1,009	1,006	0.0
7 Apr 26	25.0	39.7	31.0	30	100	68	1,004	1,011	1,007	0.0
8 Apr 26	25.1	39.5	30.9	34	99	73	1,005	1,010	1,007	0.0
9 Apr 26	25.1	38.2	30.9	42	100	78	1,006	1,011	1,008	0.0
10 Apr 26	25.9	37.5	30.9	45	100	78	1,006	1,011	1,008	0.0
11 Apr 26	25.4	39.4	30.8	27	100	70	1,004	1,011	1,007	0.0
12 Apr 26	25.0	39.3	30.9	30	100	70	1,003	1,008	1,006	0.0
13 Apr 26	25.3	39.4	31.5	27	99	69	1,005	1,010	1,007	0.0
14 Apr 26	24.5	40.2	31.3	27	100	67	1,004	1,010	1,007	0.0
15 Apr 26	25.2	38.9	31.0	37	100	73	1,004	1,009	1,006	0.0
16 Apr 26	25.6	38.9	31.5	32	100	74	1,003	1,008	1,006	0.0
17 Apr 26	26.5	38.2	31.7	44	100	74	1,004	1,009	1,007	0.0
18 Apr 26	26.5	40.1	31.8	26	100	71	1,004	1,009	1,006	0.0
19 Apr 26	26.9	39.3	31.7	35	99	71	1,003	1,008	1,006	0.0
20 Apr 26	26.6	38.8	31.6	31	99	72	1,003	1,008	1,006	0.0
21 Apr 26	26.6	38.8	31.2	33	100	74	1,003	1,008	1,006	0.0
22 Apr 26	26.7	38.8	31.5	37	99	74	1,002	1,008	1,005	0.0
23 Apr 26	27.1	38.3	31.6	45	99	76	1,002	1,007	1,005	0.0
24 Apr 26	26.5	37.8	31.2	43	99	75	1,003	1,008	1,006	0.0
25 Apr 26	26.9	38.0	31.3	40	99	74	1,006	1,011	1,008	0.0
26 Apr 26	26.1	38.5	31.3	30	99	69	1,005	1,010	1,008	0.0
27 Apr 26	26.6	38.4	31.7	43	99	66	1,004	1,009	1,006	0.0
28 Apr 26	27.3	39.3	31.5	39	95	68	1,004	1,009	1,006	0.0
29 Apr 26	26.1	39.2	31.6	28	100	69	1,004	1,009	1,007	4.2
30 Apr 26	26.9	38.7	31.5	40	99	75	1,005	1,011	1,008	0.0
Total	24.4	40.2	31.2	26	100	72	1,002	1,011	1,007	4.2
Day	30			30			30			30
Hours	720			720			720			720

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-30/April/2026	STATION : Ban Don Mod Tanoi

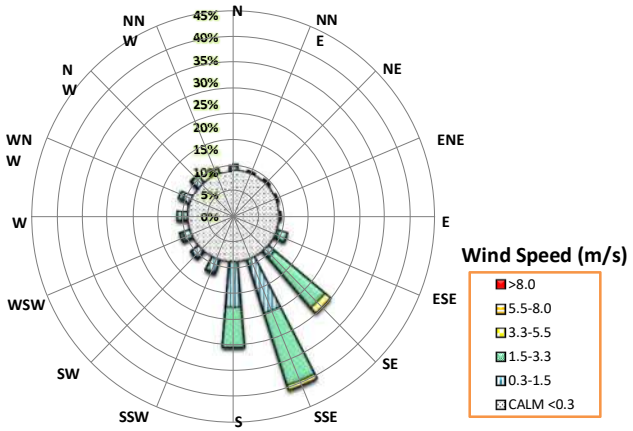

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	0.83%	0.56%	0.00%	0.00%	0.00%	1.39%
NNE	0.28%	0.14%	0.00%	0.00%	0.00%	0.42%
NE	0.28%	0.28%	0.00%	0.00%	0.00%	0.56%
ENE	0.28%	0.14%	0.00%	0.00%	0.00%	0.42%
E	0.28%	0.14%	0.00%	0.00%	0.00%	0.42%
ESE	0.56%	1.94%	0.00%	0.00%	0.00%	2.50%
SE	1.94%	14.58%	1.67%	0.00%	0.00%	18.19%
SSE	12.50%	16.81%	1.11%	0.00%	0.00%	30.42%
S	10.14%	8.89%	0.00%	0.00%	0.00%	19.03%
SSW	3.06%	0.28%	0.00%	0.00%	0.00%	3.33%
SW	2.08%	0.14%	0.00%	0.00%	0.00%	2.22%
WSW	1.81%	0.56%	0.00%	0.00%	0.00%	2.36%
W	1.25%	1.11%	0.00%	0.00%	0.00%	2.36%
WNW	1.81%	0.83%	0.00%	0.00%	0.00%	2.64%
NW	1.94%	0.28%	0.00%	0.00%	0.00%	2.22%
NNW	1.25%	0.14%	0.00%	0.00%	0.00%	1.39%
	40.28%	46.81%	2.78%	0.00%	0.00%	89.86%

No. of Monitored Hours	720	Hours	No. of Calm	73	Hours
No. of Monitored Days	30	Days	Calm (%)	10.14%	
Missing Data	0	Hours	Average Wind Speed	1.60	m/s
No. of Valid Data	720	Hours	Maximum Wind Speed	4.10	m/s
			Prevailing Wind Direction	SSE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : April

MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Apr 26	45	35	2	2	2 - 8	9 - 60
2 Apr 26	42	31	2	2	1 - 6	10 - 46
3 Apr 26	44	36	2	2	1 - 5	13 - 57
4 Apr 26	59	53	2	2 - 4	2 - 10	6 - 72
5 Apr 26	63	56	2	2 - 3	2 - 8	12 - 81
6 Apr 26	60	51	2	2 - 3	1 - 10	6 - 72
7 Apr 26	55	48	2	2 - 3	1 - 9	9 - 61
8 Apr 26	64	55	2	2 - 3	2 - 10	5 - 74
9 Apr 26	54	45	2	2	2 - 6	13 - 59
10 Apr 26	51	35	2	2	1 - 6	9 - 60
11 Apr 26	49	39	2	2 - 3	1 - 7	6 - 72
12 Apr 26	57	49	2	2 - 3	2 - 8	4 - 73
13 Apr 26	61	53	2	2 - 3	1 - 11	11 - 62
14 Apr 26	73	67	2	2 - 3	2 - 16	11 - 80
15 Apr 26	73	69	2	2 - 3	2 - 8	7 - 69
16 Apr 26	54	48	2	2 - 3	1 - 6	7 - 68
17 Apr 26	51	39	2	2 - 2	1 - 5	10 - 60
18 Apr 26	67	57	2	2 - 4	1 - 9	10 - 111*
19 Apr 26	55	51	2	2 - 3	1 - 6	13 - 81
20 Apr 26	58	51	2	2 - 3	1 - 7	11 - 84
21 Apr 26	72	65	2	2 - 3	1 - 10	7 - 89
22 Apr 26	61	53	2	2	1 - 8	9 - 71
23 Apr 26	52	41	2	2	1 - 6	13 - 55
24 Apr 26	46	35	2	2 - 3	1 - 11	9 - 63
25 Apr 26	38	28	2	2	1 - 6	11 - 48
26 Apr 26	39	27	2	2 - 3	1 - 8	15 - 57
27 Apr 26	34	22	2	2	1 - 6	17 - 52
28 Apr 26	N/A	N/A	N/A	2 - 3	2 - 3	14 - 49
29 Apr 26	44	33	2	2 - 3	1 - 12	11 - 73
30 Apr 26	38	30	2	2	1 - 7	9 - 43
Range	34 - 73	22 - 69	2	2 - 4	1 - 16	4 - 111*
Number of times (exceeded standard)	0	0	0	0	0	1
Total Day	29	29	29	30	30	30
Monitoring Hour	696	696	665	665	675	678
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : April


MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Apr 26	26.0	35.6	30.2	47	93	75	1,005	1,010	1,008	0.0
2 Apr 26	26.2	34.9	29.9	55	94	77	1,006	1,011	1,008	0.0
3 Apr 26	26.1	35.1	30.0	46	92	73	1,005	1,010	1,007	0.0
4 Apr 26	25.7	36.3	30.3	39	88	69	1,003	1,009	1,006	0.0
5 Apr 26	25.0	37.7	30.5	27	91	61	1,003	1,008	1,005	0.0
6 Apr 26	24.9	38.7	30.6	30	89	64	1,004	1,009	1,007	0.0
7 Apr 26	25.8	38.9	31.1	32	89	63	1,004	1,011	1,007	0.0
8 Apr 26	26.0	37.6	30.7	36	87	66	1,005	1,010	1,007	0.0
9 Apr 26	26.1	35.9	30.4	46	90	72	1,006	1,011	1,008	0.0
10 Apr 26	26.8	35.3	30.6	46	92	73	1,006	1,011	1,008	0.0
11 Apr 26	25.9	38.2	30.7	28	92	66	1,004	1,011	1,007	0.0
12 Apr 26	25.4	37.4	30.6	32	93	66	1,003	1,008	1,006	0.0
13 Apr 26	25.8	37.5	31.0	32	86	63	1,005	1,010	1,007	0.0
14 Apr 26	25.2	37.5	30.9	30	91	63	1,004	1,010	1,007	0.0
15 Apr 26	25.5	36.5	30.5	39	92	68	1,004	1,009	1,006	0.0
16 Apr 26	26.3	37.2	31.2	34	92	69	1,003	1,008	1,006	0.0
17 Apr 26	27.1	36.1	31.2	48	93	72	1,004	1,009	1,007	0.0
18 Apr 26	27.2	38.2	31.4	27	90	67	1,004	1,009	1,006	0.0
19 Apr 26	27.5	37.6	31.4	37	87	68	1,003	1,008	1,006	0.0
20 Apr 26	26.9	37.8	31.4	31	89	67	1,003	1,009	1,006	0.0
21 Apr 26	27.0	36.4	30.8	38	92	69	1,003	1,008	1,006	0.0
22 Apr 26	27.2	36.5	31.2	44	90	70	1,002	1,008	1,005	0.0
23 Apr 26	27.5	35.7	31.0	52	88	73	1,002	1,007	1,005	0.0
24 Apr 26	27.0	35.3	30.7	51	88	71	1,003	1,008	1,006	0.0
25 Apr 26	27.2	35.2	30.6	47	88	71	1,006	1,011	1,008	0.0
26 Apr 26	26.4	35.7	30.6	38	87	66	1,005	1,010	1,008	0.0
27 Apr 26	26.9	35.5	30.9	49	84	66	1,004	1,009	1,007	0.0
28 Apr 26	28.8	33.9	30.8	56	82	70	1,004	1,008	1,006	0.0
29 Apr 26	27.5	38.5	31.7	29	86	64	1,004	1,009	1,007	0.8
30 Apr 26	26.9	35.9	31.0	47	90	71	1,005	1,011	1,008	0.0
Total	24.9	38.9	30.8	27	94	68	1,002	1,011	1,007	0.8
Day	30			30			30			30
Hours	706			706			706			706

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-30/April/2026 STATION : Wat Bang Gado

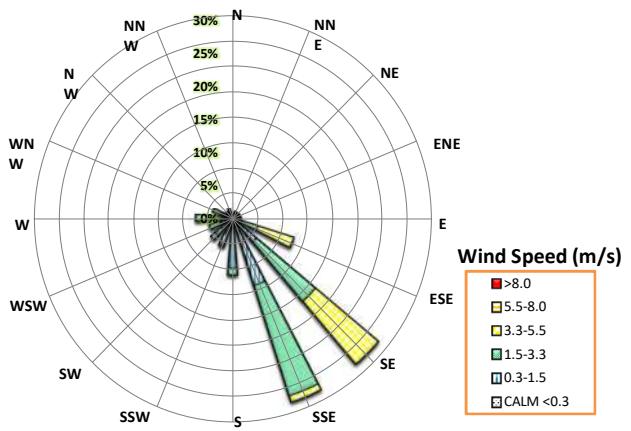

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	0.14%	0.00%	0.00%	0.00%	0.00%	0.14%
NNE	0.71%	0.00%	0.00%	0.00%	0.00%	0.71%
NE	0.57%	0.14%	0.00%	0.00%	0.00%	0.71%
ENE	0.57%	0.28%	0.00%	0.00%	0.00%	0.85%
E	0.42%	0.57%	0.00%	0.00%	0.00%	0.99%
ESE	0.57%	3.12%	5.67%	0.00%	0.00%	9.35%
SE	4.39%	11.61%	12.32%	0.00%	0.00%	28.33%
SSE	10.34%	17.28%	0.99%	0.00%	0.00%	28.61%
S	7.22%	0.99%	0.00%	0.00%	0.00%	8.22%
SSW	3.97%	0.28%	0.00%	0.00%	0.00%	4.25%
SW	3.12%	0.85%	0.00%	0.00%	0.00%	3.97%
WSW	1.56%	1.84%	0.00%	0.00%	0.00%	3.40%
W	2.41%	2.83%	0.00%	0.00%	0.00%	5.24%
WNW	1.42%	1.42%	0.00%	0.00%	0.00%	2.83%
NW	0.57%	0.28%	0.00%	0.00%	0.00%	0.85%
NNW	0.85%	0.42%	0.00%	0.00%	0.00%	1.27%
	38.81%	41.93%	18.98%	0.00%	0.00%	99.72%

No. of Monitored Hours	720	Hours	No. of Calm	2	Hours
No. of Monitored Days	30	Days	Calm (%)	0.28%	
Missing Data	14	Hours	Average Wind Speed	2.12	m/s
No. of Valid Data	706	Hours	Maximum Wind Speed	5.40	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	SSE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : April

MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Apr 26	41	36	4	4	3 - 9	10 - 70
2 Apr 26	36	29	4	4	2 - 10	8 - 55
3 Apr 26	37	34	4	4 - 5	2 - 7	11 - 63
4 Apr 26	48	40	4	4 - 5	3 - 11	8 - 77
5 Apr 26	64	56	4	4 - 5	3 - 13	6 - 92
6 Apr 26	60	48	4	4 - 5	2 - 13	9 - 85
7 Apr 26	56	51	4	4 - 5	2 - 13	4 - 80
8 Apr 26	59	53	5	4 - 6	3 - 9	4 - 102*
9 Apr 26	50	39	5	5	2 - 8	10 - 70
10 Apr 26	68	34	5	5	2 - 9	6 - 80
11 Apr 26	45	40	5	5 - 8	3 - 10	5 - 88
12 Apr 26	53	44	5	5	2 - 14	3 - 89
13 Apr 26	51	47	5	5 - 6	2 - 11	6 - 74
14 Apr 26	73	67	5	5 - 6	3 - 11	11 - 94
15 Apr 26	70	65	5	5 - 6	2 - 12	5 - 87
16 Apr 26	48	43	5	5 - 6	2 - 11	10 - 78
17 Apr 26	43	37	5	5	2 - 9	9 - 75
18 Apr 26	52	47	5	5 - 6	2 - 12	6 - 120*
19 Apr 26	52	48	5	5 - 6	1 - 10	15 - 97
20 Apr 26	57	50	5	5 - 6	2 - 14	13 - 112*
21 Apr 26	72	64	5	5 - 6	2 - 12	8 - 96
22 Apr 26	63	55	5	5 - 6	2 - 12	6 - 89
23 Apr 26	51	43	5	5	2 - 7	16 - 63
24 Apr 26	49	40	5	5 - 6	2 - 17	10 - 71
25 Apr 26	32	24	5	5	2 - 7	21 - 57
26 Apr 26	32	28	5	5 - 6	2 - 11	22 - 66
27 Apr 26	28	21	5	5	2 - 10	16 - 63
28 Apr 26	33	31	5	5 - 6	2 - 7	13 - 87
29 Apr 26	35	28	5	5 - 6	4 - 14	12 - 81
30 Apr 26	29	25	5	5 - 6	2 - 11	4 - 57
Range	28 - 73	21 - 67	4 - 5	4 - 8	1 - 17	3 - 120*
Number of times (exceeded standard)	0	0	0	0	0	3
Total Day	30	30	30	30	30	30
Monitoring Hour	720	720	691	691	691	691
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : April


MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Temperature (° C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Apr 26	25.9	36.7	30.5	42	89	70	1,005	1,010	1,007	0.0
2 Apr 26	26.1	36.3	30.3	49	91	73	1,005	1,010	1,008	0.0
3 Apr 26	26.1	36.5	30.4	44	89	69	1,004	1,009	1,007	0.0
4 Apr 26	25.9	37.7	30.9	34	89	66	1,003	1,008	1,005	0.0
5 Apr 26	25.0	38.4	30.8	26	90	59	1,003	1,007	1,005	0.0
6 Apr 26	25.1	39.0	31.1	28	83	59	1,004	1,009	1,006	0.0
7 Apr 26	25.4	38.9	31.4	31	88	60	1,004	1,010	1,007	0.0
8 Apr 26	25.8	38.6	31.1	36	85	64	1,005	1,009	1,007	0.0
9 Apr 26	25.6	37.4	30.8	41	89	69	1,006	1,010	1,008	0.0
10 Apr 26	26.5	36.2	31.0	44	90	69	1,005	1,010	1,008	0.0
11 Apr 26	25.9	38.4	31.2	25	90	62	1,004	1,010	1,007	0.0
12 Apr 26	25.7	38.4	31.3	28	89	62	1,003	1,008	1,005	0.0
13 Apr 26	25.3	38.5	31.3	31	86	62	1,005	1,009	1,007	0.0
14 Apr 26	24.8	38.7	31.5	29	85	59	1,004	1,009	1,006	0.0
15 Apr 26	25.6	37.4	30.8	39	86	66	1,003	1,008	1,005	0.0
16 Apr 26	26.7	37.2	31.5	34	89	66	1,003	1,008	1,005	0.0
17 Apr 26	27.1	37.3	31.6	40	90	67	1,003	1,009	1,006	0.0
18 Apr 26	26.8	38.7	31.8	27	90	64	1,003	1,008	1,006	0.0
19 Apr 26	27.7	37.2	31.8	38	83	64	1,003	1,008	1,006	0.0
20 Apr 26	27.0	37.6	31.6	32	84	63	1,003	1,008	1,006	0.0
21 Apr 26	27.1	37.4	31.3	34	86	65	1,003	1,008	1,005	0.0
22 Apr 26	27.4	37.3	31.6	41	87	66	1,002	1,008	1,005	0.0
23 Apr 26	27.7	37.1	31.6	47	83	68	1,002	1,007	1,005	0.0
24 Apr 26	27.3	36.1	31.2	47	83	67	1,003	1,008	1,005	0.0
25 Apr 26	27.6	36.3	31.0	43	82	67	1,005	1,010	1,007	0.0
26 Apr 26	26.4	37.0	31.1	37	80	62	1,005	1,010	1,007	0.0
27 Apr 26	27.4	36.8	31.6	44	80	61	1,004	1,009	1,006	0.0
28 Apr 26	27.4	37.7	31.6	42	78	63	1,003	1,008	1,006	0.0
29 Apr 26	25.2	38.0	31.5	31	90	62	1,004	1,008	1,006	13.8
30 Apr 26	26.9	36.4	31.3	44	90	67	1,005	1,010	1,008	0.0
Total	24.8	39.0	31.2	25	91	65	1,002	1,010	1,006	13.8
Day	30			30			30			30
Hours	720			720			720			720

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-30/April/2026 | **STATION : Ban Klong Klae**

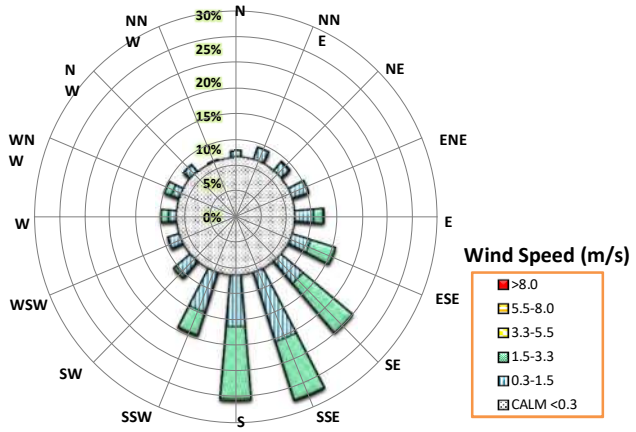

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	0.94%	0.00%	0.00%	0.00%	0.00%	**0.94%**
NNE	1.88%	0.00%	0.00%	0.00%	0.00%	**1.88%**
NE	1.61%	0.13%	0.00%	0.00%	0.00%	**1.75%**
ENE	2.55%	0.00%	0.00%	0.00%	0.00%	**2.55%**
E	2.82%	1.34%	0.13%	0.00%	0.00%	**4.30%**
ESE	2.96%	3.76%	0.00%	0.00%	0.00%	**6.72%**
SE	4.30%	9.54%	0.00%	0.00%	0.00%	**13.84%**
SSE	10.75%	9.01%	0.13%	0.00%	0.00%	**19.89%**
S	7.66%	10.62%	0.27%	0.00%	0.00%	**18.55%**
SSW	6.18%	3.49%	0.13%	0.00%	0.00%	**9.81%**
SW	2.82%	0.40%	0.00%	0.00%	0.00%	**3.23%**
WSW	1.75%	0.00%	0.00%	0.00%	0.00%	**1.75%**
W	1.21%	1.08%	0.00%	0.00%	0.00%	**2.28%**
WNW	1.21%	1.08%	0.00%	0.00%	0.00%	**2.28%**
NW	1.34%	0.00%	0.00%	0.00%	0.00%	**1.34%**
NNW	0.13%	0.00%	0.00%	0.00%	0.00%	**0.13%**
	50.13%	**40.46%**	**0.67%**	**0.00%**	**0.00%**	**91.26%**

No. of Monitored Hours	744	Hours	No. of Calm	65	Hours
No. of Monitored Days	31	Days	Calm (%)	8.74%	
Missing Data	0	Hours	Average Wind Speed	1.35	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	4.00	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	SSE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : April

MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Apr 26	41	33	1	1	2 - 5	5 - 49
2 Apr 26	41	32	1	1	1 - 5	7 - 39
3 Apr 26	49	37	1	1 - 2	1 - 5	8 - 44
4 Apr 26	58	46	1	1 - 2	2 - 6	8 - 53
5 Apr 26	64	56	1	1 - 2	1 - 4	8 - 65
6 Apr 26	81	63	1	1 - 2	2 - 8	10 - 57
7 Apr 26	96	73	1	1 - 2	1 - 9	5 - 59
8 Apr 26	57	51	1	1 - 2	2 - 6	5 - 64
9 Apr 26	53	43	1	1 - 2	1 - 6	8 - 46
10 Apr 26	44	35	1	1 - 2	1 - 5	6 - 50
11 Apr 26	39	35	1	1 - 2	1 - 6	5 - 57
12 Apr 26	56	48	1	1 - 2	1 - 5	5 - 55
13 Apr 26	57	49	1	1 - 2	1 - 3	10 - 47
14 Apr 26	76	67	1	1 - 2	2 - 4	11 - 62
15 Apr 26	65	60	1	1 - 2	1 - 5	5 - 53
16 Apr 26	52	46	1	1 - 2	1 - 4	6 - 50
17 Apr 26	44	37	1	1 - 2	1 - 5	8 - 47
18 Apr 26	57	52	2	1 - 3	1 - 5	9 - 81
19 Apr 26	51	43	1	1 - 2	1 - 5	9 - 67
20 Apr 26	63	51	1	1 - 2	1 - 8	8 - 68
21 Apr 26	71	64	1	1 - 2	1 - 5	9 - 63
22 Apr 26	60	57	1	1 - 2	1 - 7	7 - 56
23 Apr 26	54	42	1	1 - 2	1 - 5	10 - 45
24 Apr 26	44	38	1	1 - 2	1 - 6	9 - 48
25 Apr 26	33	25	1	1	1 - 5	10 - 39
26 Apr 26	32	26	1	1 - 2	1 - 6	12 - 45
27 Apr 26	33	23	1	1	1 - 5	12 - 41
28 Apr 26	35	26	1	1 - 2	2 - 5	10 - 58
29 Apr 26	38	30	1	1 - 2	2 - 5	9 - 58
30 Apr 26	31	23	1	1	1 - 6	6 - 36
Range	31 - 96	23 - 73	1 - 2	1 - 3	1 - 9	5 - 81
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	30	30	30	30	30	30
Monitoring Hour	718	720	691	691	690	691
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-

1) **Standards** = Ambient Air Quality Standards of the National Environment Board
2) **TSP** = Total Suspended Particulate
3) **PM-10** = Particulate Matter less than 10 μm
4) **SO_2** = Sulfur Dioxide
5) **NO_2** = Nitrogen Dioxide
6) **N/A** = Data not Available
7) ***** = Exeeding air quality standard
8) **-** = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : April


MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Temperature (° C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Apr 26	25.3	36.2	30.1	44	100	81	1,004	1,009	1,006	0.0
2 Apr 26	25.7	35.9	29.8	53	100	84	1,004	1,009	1,007	0.0
3 Apr 26	25.6	36.5	30.1	44	100	78	1,003	1,009	1,006	0.0
4 Apr 26	25.5	37.3	30.4	35	100	75	1,002	1,007	1,004	0.0
5 Apr 26	25.6	38.4	30.6	26	100	65	1,002	1,007	1,004	0.0
6 Apr 26	25.3	38.5	30.7	28	100	67	1,003	1,008	1,005	0.0
7 Apr 26	25.3	38.2	30.9	32	100	68	1,003	1,009	1,006	0.0
8 Apr 26	24.8	38.4	30.6	34	100	73	1,004	1,009	1,006	0.0
9 Apr 26	25.3	36.8	30.3	44	100	80	1,005	1,009	1,007	0.0
10 Apr 26	26.1	36.0	30.5	46	100	79	1,005	1,010	1,007	0.0
11 Apr 26	25.3	38.0	30.6	29	100	71	1,003	1,009	1,006	0.0
12 Apr 26	25.0	38.1	30.7	29	100	70	1,002	1,007	1,005	0.0
13 Apr 26	26.1	37.9	31.2	30	100	69	1,004	1,009	1,006	0.0
14 Apr 26	24.8	38.9	31.0	26	100	66	1,003	1,009	1,006	0.0
15 Apr 26	25.0	37.4	30.3	40	100	76	1,002	1,007	1,005	0.0
16 Apr 26	25.6	37.6	31.1	32	100	76	1,002	1,007	1,005	0.0
17 Apr 26	26.7	37.0	31.3	44	100	76	1,002	1,008	1,005	0.0
18 Apr 26	26.8	39.2	31.5	25	100	73	1,002	1,007	1,005	0.0
19 Apr 26	27.1	37.8	31.3	35	99	75	1,002	1,007	1,005	0.0
20 Apr 26	26.4	37.5	31.2	31	100	75	1,002	1,007	1,005	0.0
21 Apr 26	26.8	37.3	30.9	32	100	76	1,002	1,007	1,004	0.0
22 Apr 26	26.9	37.1	31.3	41	100	76	1,001	1,007	1,004	0.0
23 Apr 26	27.3	36.4	31.2	49	99	80	1,001	1,006	1,004	0.0
24 Apr 26	26.5	35.9	30.8	48	100	77	1,002	1,007	1,005	0.0
25 Apr 26	27.0	35.9	30.8	44	100	77	1,005	1,009	1,007	0.0
26 Apr 26	26.3	36.7	30.9	35	99	71	1,004	1,009	1,007	0.0
27 Apr 26	26.7	36.5	31.2	45	99	69	1,003	1,008	1,005	0.0
28 Apr 26	27.3	37.3	31.2	42	99	71	1,002	1,007	1,005	0.0
29 Apr 26	27.0	38.3	31.5	28	100	71	1,003	1,007	1,006	1.4
30 Apr 26	26.7	36.8	31.2	44	100	77	1,004	1,009	1,007	0.0
Total	24.8	39.2	30.8	25	100	74	1,001	1,010	1,005	1.4
Day	30			30			30			30
Hours	720			720			720			720

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-30/April/2026 STATION : Ban Chao Nua

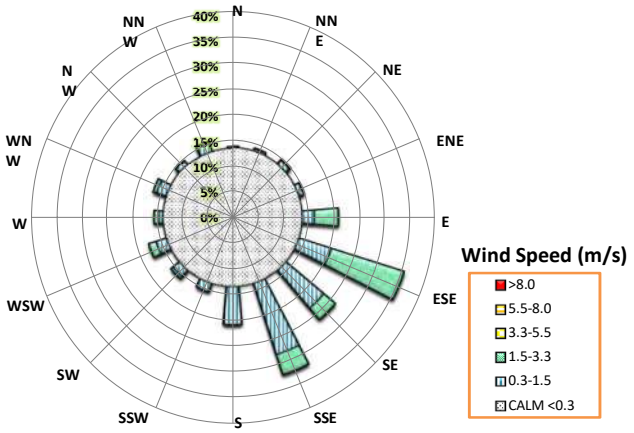

Wind Sector	Wind Speed (m/s)					
	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	0.27%	0.00%	0.00%	0.00%	0.00%	0.27%
NNE	0.40%	0.13%	0.00%	0.00%	0.00%	0.54%
NE	0.94%	0.27%	0.00%	0.00%	0.00%	1.21%
ENE	0.94%	0.13%	0.00%	0.00%	0.00%	1.08%
E	2.42%	4.70%	0.00%	0.00%	0.00%	7.12%
ESE	6.72%	15.05%	0.00%	0.00%	0.00%	21.77%
SE	9.81%	2.96%	0.00%	0.00%	0.00%	12.77%
SSE	14.78%	4.17%	0.00%	0.00%	0.00%	18.95%
S	7.53%	0.00%	0.00%	0.00%	0.00%	7.53%
SSW	1.75%	0.00%	0.00%	0.00%	0.00%	1.75%
SW	1.61%	0.54%	0.00%	0.00%	0.00%	2.15%
WSW	2.15%	1.48%	0.00%	0.00%	0.00%	3.63%
W	0.81%	0.94%	0.00%	0.00%	0.00%	1.75%
WNW	2.02%	0.67%	0.00%	0.00%	0.00%	2.69%
NW	0.94%	0.13%	0.00%	0.00%	0.00%	1.08%
NNW	2.02%	0.00%	0.00%	0.00%	0.00%	2.02%
	55.11%	31.18%	0.00%	0.00%	0.00%	86.29%

No. of Monitored Hours	744	Hours	No. of Calm	102	Hours
No. of Monitored Days	31	Days	Calm (%)	13.71%	
Missing Data	0	Hours	Average Wind Speed	1.18	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	3.30	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	ESE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : May

MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 May 26	28	26	3	3 - 4	1 - 8	16 - 67
2 May 26	23	22	3	3 - 4	1 - 8	9 - 61
3 May 26	27	25	3	3	1 - 9	4 - 57
4 May 26	25	24	3	3	1 - 8	4 - 43
5 May 26	17	16	3	3 - 4	1 - 8	14 - 70
6 May 26	21	20	3	3	1 - 7	3 - 56
7 May 26	18	16	3	3	1 - 6	8 - 46
8 May 26	21	20	3	3 - 4	2 - 8	13 - 59
9 May 26	30	29	3	3	2 - 11	15 - 83
10 May 26	25	22	3	3 - 4	1 - 7	17 - 66
11 May 26	23	20	3	3	2 - 7	8 - 58
12 May 26	23	20	3	3 - 4	1 - 9	6 - 39
13 May 26	13	11	3	3	1 - 7	4 - 35
14 May 26	12	11	3	3	1 - 7	2 - 37
15 May 26	18	13	3	3	1 - 9	2 - 41
16 May 26	16	14	3	3 - 4	1 - 8	2 - 48
17 May 26	10	8	3	3 - 4	0 - 5	6 - 33
18 May 26	14	11	3	3 - 4	1 - 5	7 - 40
19 May 26	17	14	3	3	1 - 7	9 - 35
20 May 26	20	20	3	3	1 - 7	9 - 48
21 May 26	N/A	N/A	2	0 - 3	1 - 6	2 - 32
22 May 26	24	17	0	0	2 - 7	4 - 40
23 May 26	14	18	0	0	1 - 9	1 - 42
24 May 26	16	13	0	0	1 - 7	5 - 40
25 May 26	19	17	1	0 - 9	1 - 8	1 - 37
26 May 26	22	17	2	2	2 - 9	2 - 40
27 May 26	16	15	2	1 - 2	1 - 10	4 - 50
28 May 26	24	19	1	1 - 2	2 - 11	3 - 42
29 May 26	26	23	1	1 - 2	2 - 11	2 - 45
30 May 26	25	21	1	1 - 2	2 - 8	4 - 52
31 May 26	19	18	1	1 - 2	1 - 7	5 - 46
Range	10 - 30	8 - 29	0 - 3	0 - 9	0 - 11	1 - 83
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	30	30	31	31	31	31
Monitoring Hour	693	694	710	710	710	710
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : May


MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 May 26	25.3	37.3	30.4	44	99	71	1,005	1,010	1,008	0.0
2 May 26	26.4	39.1	31.6	37	99	67	1,004	1,009	1,007	0.0
3 May 26	26.5	39.5	31.7	34	99	70	1,004	1,010	1,007	0.0
4 May 26	26.8	38.9	32.0	41	99	70	1,005	1,010	1,008	0.0
5 May 26	23.6	38.1	29.9	40	100	76	1,005	1,011	1,008	15.2
6 May 26	26.3	38.8	31.7	39	100	74	1,004	1,009	1,007	0.0
7 May 26	27.2	38.7	31.8	40	99	72	1,004	1,009	1,007	0.0
8 May 26	26.8	38.9	31.1	38	99	72	1,004	1,009	1,007	0.4
9 May 26	25.7	36.6	30.2	47	100	80	1,004	1,011	1,008	0.6
10 May 26	26.5	38.5	31.2	36	99	74	1,004	1,010	1,007	0.0
11 May 26	27.1	36.8	30.9	49	99	79	1,005	1,009	1,007	0.6
12 May 26	25.4	32.8	28.2	58	99	88	1,005	1,010	1,007	1.8
13 May 26	25.4	36.8	29.4	48	100	85	1,003	1,008	1,005	0.4
14 May 26	26.1	37.5	30.3	46	100	81	1,002	1,007	1,005	0.0
15 May 26	25.7	36.9	29.3	45	100	87	1,003	1,007	1,005	12.8
16 May 26	26.3	35.7	29.5	48	100	83	1,002	1,007	1,005	1.6
17 May 26	26.0	35.5	30.2	47	99	72	1,001	1,006	1,004	0.2
18 May 26	25.9	34.8	30.1	50	99	73	1,001	1,004	1,003	0.0
19 May 26	26.3	32.4	28.5	60	99	84	1,000	1,005	1,003	1.2
20 May 26	23.7	35.7	28.6	42	100	82	1,000	1,005	1,003	25.6
21 May 26	24.6	36.8	29.2	51	100	84	1,003	1,007	1,005	0.2
22 May 26	25.9	36.7	30.4	48	100	80	1,005	1,010	1,007	0.4
23 May 26	26.7	37.4	30.9	46	100	81	1,005	1,010	1,008	0.2
24 May 26	26.5	38.0	31.2	45	100	77	1,006	1,010	1,008	3.0
25 May 26	24.5	38.5	30.0	45	100	83	1,005	1,010	1,008	7.2
26 May 26	25.6	37.5	29.0	44	100	88	1,005	1,009	1,007	1.8
27 May 26	25.5	38.9	30.8	39	100	76	1,003	1,009	1,007	1.4
28 May 26	26.7	37.7	30.8	44	100	78	1,004	1,009	1,007	0.0
29 May 26	26.1	37.5	29.9	45	100	82	1,004	1,009	1,007	0.2
30 May 26	26.1	36.3	29.8	40	100	77	1,004	1,009	1,007	0.0
31 May 26	26.2	36.9	30.3	44	99	77	1,004	1,009	1,007	0.0
Total	23.6	39.5	30.3	34	100	78	1,000	1,011	1,006	74.8
Day	31			31			31			31
Hours	744			744			744			744

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/May/2026	STATION : Ban Don Mod Tanoi

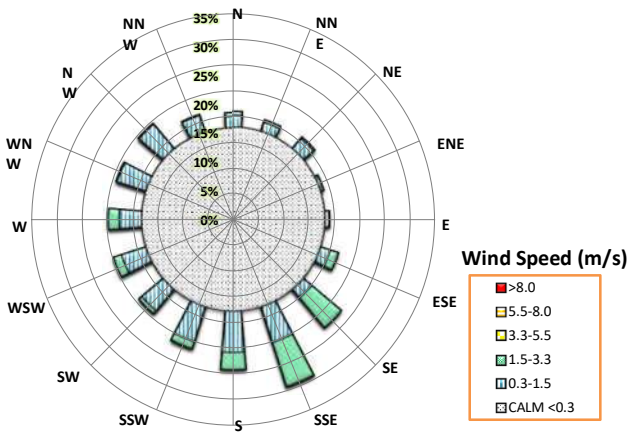

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	2.02%	0.67%	0.00%	0.00%	0.00%	**2.69%**
NNE	1.61%	0.40%	0.00%	0.00%	0.00%	**2.02%**
NE	2.28%	0.27%	0.00%	0.00%	0.00%	**2.55%**
ENE	0.54%	0.00%	0.00%	0.00%	0.00%	**0.54%**
E	0.67%	0.13%	0.00%	0.00%	0.00%	**0.81%**
ESE	1.75%	1.48%	0.00%	0.00%	0.00%	**3.23%**
SE	1.88%	6.72%	0.00%	0.00%	0.00%	**8.60%**
SSE	6.45%	7.93%	0.13%	0.00%	0.00%	**14.52%**
S	7.12%	2.96%	0.00%	0.00%	0.00%	**10.08%**
SSW	6.32%	1.21%	0.13%	0.00%	0.00%	**7.66%**
SW	4.84%	0.67%	0.00%	0.00%	0.00%	**5.51%**
WSW	4.44%	1.48%	0.00%	0.00%	0.00%	**5.91%**
W	3.90%	1.88%	0.00%	0.00%	0.00%	**5.78%**
WNW	5.24%	0.13%	0.00%	0.00%	0.00%	**5.38%**
NW	5.51%	0.13%	0.00%	0.00%	0.00%	**5.65%**
NNW	3.09%	0.13%	0.00%	0.00%	0.00%	**3.23%**
	57.66%	**26.21%**	**0.27%**	**0.00%**	**0.00%**	**84.14%**

No. of Monitored Hours	744	Hours	No. of Calm	118	Hours
No. of Monitored Days	31	Days	Calm (%)	15.86%	
Missing Data	0	Hours	Average Wind Speed	1.06	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	3.70	m/s
			Prevailing Wind Direction	SSE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : May

MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 May 26	39	21	2	2 - 3	1 - 6	20 - 73
2 May 26	37	24	2	2 - 3	1 - 10	11 - 62
3 May 26	39	33	2	2	1 - 8	9 - 58
4 May 26	40	37	2	2 - 3	1 - 7	11 - 52
5 May 26	33	29	2	2 - 3	1 - 9	18 - 80
6 May 26	35	34	2	2 - 3	2 - 13	5 - 67
7 May 26	37	33	2	2	2 - 9	8 - 56
8 May 26	31	25	2	2 - 3	1 - 14	13 - 64
9 May 26	42	31	2	2 - 3	2 - 8	25 - 83
10 May 26	40	28	2	2 - 3	2 - 7	23 - 74
11 May 26	37	32	2	2 - 3	2 - 8	13 - 59
12 May 26	33	N/A	2	2 - 3	2 - 8	15 - 42
13 May 26	27	N/A	2	2 - 3	1 - 10	5 - 39
14 May 26	28	N/A	2	2 - 3	1 - 10	5 - 46
15 May 26	28	N/A	2	2 - 3	1 - 9	4 - 43
16 May 26	30	N/A	2	2	1 - 10	4 - 45
17 May 26	26	N/A	2	2 - 3	1 - 7	8 - 34
18 May 26	26	N/A	2	2 - 3	2 - 8	7 - 37
19 May 26	30	N/A	2	2 - 3	2 - 12	8 - 35
20 May 26	35	N/A	2	2 - 3	2 - 8	13 - 45
21 May 26	40	27	2	2 - 3	2 - 10	4 - 34
22 May 26	33	18	2	2	2 - 10	6 - 30
23 May 26	32	18	2	2 - 3	2 - 9	N/A
24 May 26	28	13	2	2	2 - 8	N/A
25 May 26	32	19	2	2 - 3	2 - 11	N/A
26 May 26	33	16	2	2 - 3	3 - 11	N/A
27 May 26	27	15	2	2 - 3	2 - 9	N/A
28 May 26	36	17	2	2 - 3	2 - 14	N/A
29 May 26	39	23	2	2 - 3	2 - 12	N/A
30 May 26	34	20	2	2 - 3	3 - 9	N/A
31 May 26	33	17	2	2 - 3	2 - 8	N/A
Range	26 - 42	13 - 37	2	2 - 3	1 - 14	4 - 83
Number of times (exceeded standard)	0	0	0	0	0	0
Total Monitoring Day	31	22	31	31	31	22
Total Monitoring Hour	744	522	708	708	705	490
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : May


MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 May 26	25.4	34.7	30.0	51	88	69	1,005	1,010	1,008	0.0
2 May 26	26.6	36.7	30.9	41	86	66	1,004	1,010	1,007	0.0
3 May 26	26.6	38.4	31.6	37	85	65	1,004	1,010	1,007	0.0
4 May 26	27.5	36.6	31.6	46	87	67	1,005	1,010	1,008	0.0
5 May 26	23.4	35.6	29.6	47	97	72	1,005	1,011	1,008	26.8
6 May 26	27.1	36.0	31.2	46	92	70	1,004	1,009	1,007	0.0
7 May 26	27.8	36.4	31.3	45	89	70	1,004	1,009	1,007	0.0
8 May 26	26.9	36.2	30.4	44	87	69	1,004	1,010	1,007	0.0
9 May 26	26.3	36.2	30.5	49	89	72	1,004	1,011	1,008	0.0
10 May 26	26.2	36.4	30.9	42	91	70	1,004	1,010	1,008	0.0
11 May 26	27.2	34.6	30.6	54	86	72	1,005	1,009	1,008	0.0
12 May 26	25.9	31.5	28.2	61	91	79	1,005	1,010	1,007	1.2
13 May 26	25.7	35.0	29.2	53	92	79	1,003	1,008	1,006	1.2
14 May 26	26.5	34.8	30.0	54	95	77	1,002	1,008	1,005	0.0
15 May 26	26.6	34.8	29.3	52	92	77	1,003	1,007	1,005	3.6
16 May 26	26.2	34.9	29.2	52	94	78	1,002	1,007	1,005	7.0
17 May 26	26.4	35.3	30.3	48	91	68	1,001	1,006	1,004	0.0
18 May 26	26.3	34.2	30.1	52	89	69	1,001	1,005	1,003	0.0
19 May 26	26.9	31.9	28.7	62	84	73	1,000	1,005	1,003	2.2
20 May 26	24.8	34.7	28.6	49	95	76	1,000	1,005	1,003	12.2
21 May 26	25.4	34.4	29.2	55	97	78	1,003	1,007	1,005	0.0
22 May 26	26.6	35.2	30.1	49	92	74	1,005	1,010	1,007	0.0
23 May 26	26.9	35.9	30.6	51	95	76	1,005	1,010	1,008	0.0
24 May 26	26.6	35.5	31.0	50	91	72	1,006	1,011	1,008	0.0
25 May 26	25.0	37.3	29.8	44	96	78	1,005	1,010	1,008	20.2
26 May 26	25.9	36.2	29.1	50	96	80	1,005	1,009	1,007	2.4
27 May 26	26.0	36.9	30.9	44	88	68	1,003	1,009	1,007	0.0
28 May 26	27.5	35.3	30.5	52	92	72	1,004	1,009	1,007	0.0
29 May 26	25.5	35.7	29.5	49	95	78	1,004	1,009	1,007	4.2
30 May 26	26.1	35.5	29.5	46	97	75	1,004	1,009	1,007	0.0
31 May 26	25.1	36.3	29.9	47	93	74	1,004	1,009	1,007	4.0
Total	23.4	38.4	30.1	37	97	73	1,000	1,011	1,007	85.0
Day	31			31			31			31
Hours	744			744			744			744

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/May/2026 STATION : Wat Bang Gado

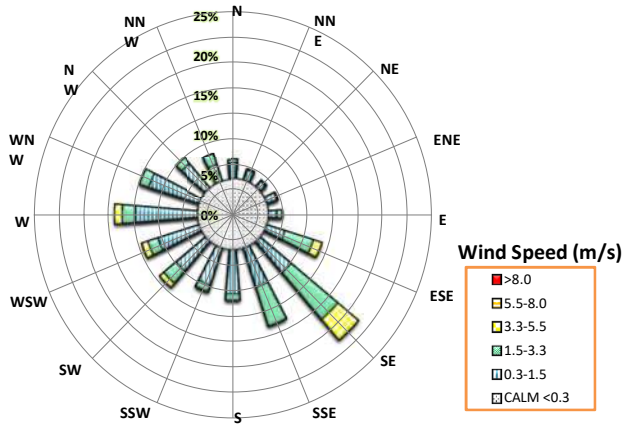

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	2.02%	0.40%	0.00%	0.00%	0.00%	2.42%
NNE	1.34%	0.13%	0.00%	0.00%	0.00%	1.48%
NE	0.94%	0.13%	0.00%	0.00%	0.00%	1.08%
ENE	1.34%	0.13%	0.00%	0.00%	0.00%	1.48%
E	1.08%	0.67%	0.00%	0.00%	0.00%	1.75%
ESE	2.42%	3.76%	1.08%	0.00%	0.00%	7.26%
SE	5.11%	7.66%	3.36%	0.00%	0.00%	16.13%
SSE	5.11%	5.11%	0.00%	0.00%	0.00%	10.22%
S	5.51%	0.81%	0.00%	0.00%	0.00%	6.32%
SSW	4.84%	0.81%	0.13%	0.00%	0.00%	5.78%
SW	4.84%	2.02%	0.67%	0.00%	0.00%	7.53%
WSW	5.38%	1.34%	0.81%	0.00%	0.00%	7.53%
W	7.80%	1.61%	0.94%	0.00%	0.00%	10.35%
WNW	6.59%	1.21%	0.00%	0.00%	0.00%	7.80%
NW	3.90%	0.94%	0.00%	0.00%	0.00%	4.84%
NNW	2.15%	1.48%	0.00%	0.00%	0.00%	3.63%
	60.35%	28.23%	6.99%	0.00%	0.00%	95.56%

No. of Monitored Hours	744	Hours	No. of Calm	33	Hours
No. of Monitored Days	31	Days	Calm (%)	4.44%	
Missing Data	0	Hours	Average Wind Speed	1.47	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	5.00	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	SE	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : May

MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 May 26	30	23	5	5 - 6	2 - 10	27 - 89
2 May 26	25	24	5	5 - 6	2 - 13	14 - 71
3 May 26	30	24	5	5 - 7	2 - 14	8 - 70
4 May 26	30	26	5	5 - 6	2 - 10	13 - 67
5 May 26	22	15	5	5 - 6	2 - 13	19 - 91
6 May 26	28	27	5	5 - 6	3 - 15	4 - 74
7 May 26	25	22	3	1 - 5	2 - 15	7 - 71
8 May 26	22	19	1	1 - 2	3 - 14	18 - 92
9 May 26	30	26	1	1 - 2	4 - 15	27 - 96
10 May 26	27	24	1	1 - 2	3 - 13	37 - 97
11 May 26	28	24	2	1 - 3	2 - 15	14 - 81
12 May 26	23	20	1	1 - 2	2 - 12	16 - 60
13 May 26	15	14	1	1 - 2	2 - 17	7 - 57
14 May 26	23	19	1	1 - 2	2 - 15	3 - 54
15 May 26	17	13	1	1 - 2	3 - 18	4 - 57
16 May 26	20	14	1	1 - 2	3 - 15	4 - 70
17 May 26	11	8	1	1 - 2	2 - 10	16 - 48
18 May 26	13	10	1	1 - 2	3 - 13	12 - 52
19 May 26	14	11	2	1 - 4	2 - 10	23 - 53
20 May 26	22	18	1	1 - 2	2 - 14	16 - 65
21 May 26	27	23	2	1 - 8	2 - 16	6 - 52
22 May 26	24	20	2	1 - 2	2 - 15	4 - 58
23 May 26	24	20	1	1 - 2	2 - 13	5 - 55
24 May 26	17	13	2	2	2 - 11	9 - 61
25 May 26	19	16	2	2	2 - 15	5 - 61
26 May 26	26	22	2	2	2 - 18	3 - 69
27 May 26	16	13	2	2	2 - 13	15 - 74
28 May 26	20	16	2	2	1 - 16	12 - 60
29 May 26	25	21	2	2	1 - 13	3 - 57
30 May 26	27	21	2	2	3 - 15	3 - 76
31 May 26	24	20	2	2 - 3	3 - 15	5 - 66
Range	11 - 30	8 - 27	1 - 5	1 - 8	1 - 18	3 - 97
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	31	31	31	31	31	31
Monitoring Hour	744	741	711	711	711	703
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : May


MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 May 26	26.3	36.0	30.5	47	81	65	1,004	1,010	1,008	0.0
2 May 26	27.1	37.8	31.7	35	81	61	1,003	1,009	1,007	0.0
3 May 26	27.2	38.6	31.9	35	81	61	1,003	1,009	1,007	0.0
4 May 26	27.8	37.5	32.0	42	81	64	1,004	1,010	1,007	0.0
5 May 26	24.0	35.9	30.1	46	95	70	1,004	1,010	1,008	10.6
6 May 26	27.2	37.2	31.7	40	89	66	1,003	1,008	1,006	0.0
7 May 26	28.3	37.8	32.1	41	85	64	1,003	1,008	1,006	0.0
8 May 26	27.3	37.8	31.2	41	81	65	1,003	1,009	1,007	0.0
9 May 26	26.3	35.4	30.5	49	88	70	1,004	1,010	1,007	0.8
10 May 26	26.3	37.4	31.1	41	92	67	1,004	1,009	1,007	2.2
11 May 26	27.6	35.9	30.9	48	81	68	1,005	1,009	1,007	0.0
12 May 26	25.4	33.6	28.6	54	94	76	1,005	1,010	1,007	2.2
13 May 26	25.5	35.7	29.4	48	99	78	1,002	1,007	1,005	19.8
14 May 26	26.6	37.5	30.5	48	99	77	1,002	1,007	1,005	0.0
15 May 26	26.3	35.3	29.6	51	99	77	1,002	1,006	1,005	15.2
16 May 26	27.1	35.9	29.8	50	91	75	1,002	1,006	1,005	8.4
17 May 26	26.6	34.5	30.4	51	88	67	1,001	1,006	1,004	0.0
18 May 26	26.7	34.4	30.2	52	86	68	1,000	1,004	1,003	0.0
19 May 26	27.2	32.2	29.2	60	74	68	1,000	1,005	1,002	0.0
20 May 26	24.8	36.6	29.3	40	99	72	1,000	1,004	1,002	23.0
21 May 26	25.3	35.0	29.1	53	99	80	1,003	1,007	1,005	0.4
22 May 26	26.3	36.5	30.5	52	96	75	1,005	1,009	1,007	0.2
23 May 26	27.2	37.6	31.2	48	95	75	1,005	1,010	1,008	0.0
24 May 26	27.1	37.0	31.5	49	96	72	1,005	1,010	1,008	9.4
25 May 26	27.4	38.5	30.9	43	98	74	1,004	1,009	1,007	0.2
26 May 26	26.6	36.8	30.3	48	94	74	1,004	1,008	1,007	0.0
27 May 26	26.9	38.7	31.8	39	79	62	1,003	1,009	1,006	0.0
28 May 26	27.9	37.6	31.3	44	81	65	1,004	1,009	1,007	0.0
29 May 26	26.0	37.0	29.9	41	90	74	1,003	1,009	1,007	1.0
30 May 26	26.4	36.4	29.8	44	96	73	1,004	1,009	1,007	0.0
31 May 26	25.7	36.3	30.0	46	90	72	1,003	1,009	1,006	2.6
Total	24.0	38.7	30.5	35	99	70	1,000	1,010	1,006	96.0
Day	31			31			31			31
Hours	744			744			744			744

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/May/2026 | **STATION : Ban Klong Klae**

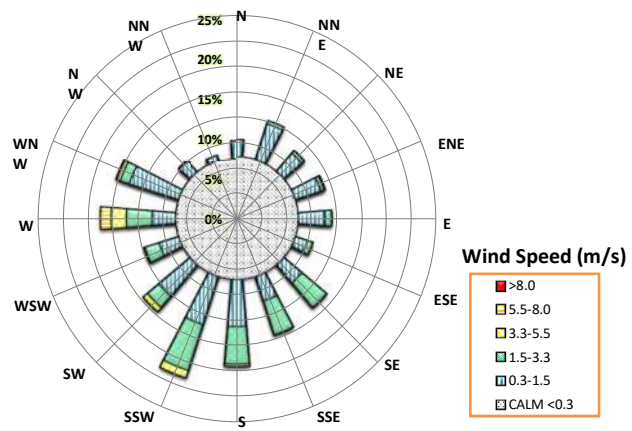

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	2.15%	0.00%	0.00%	0.00%	0.00%	**2.15%**
NNE	4.70%	0.40%	0.00%	0.00%	0.00%	**5.11%**
NE	2.96%	0.40%	0.00%	0.00%	0.00%	**3.36%**
ENE	3.36%	0.40%	0.13%	0.00%	0.00%	**3.90%**
E	3.36%	0.81%	0.00%	0.00%	0.00%	**4.17%**
ESE	1.61%	0.67%	0.00%	0.00%	0.00%	**2.28%**
SE	2.96%	4.03%	0.00%	0.00%	0.00%	**6.99%**
SSE	3.23%	4.44%	0.00%	0.00%	0.00%	**7.66%**
S	5.91%	4.70%	0.27%	0.00%	0.00%	**10.89%**
SSW	6.32%	6.05%	0.94%	0.00%	0.00%	**13.31%**
SW	5.11%	1.88%	0.67%	0.00%	0.00%	**7.66%**
WSW	2.55%	1.88%	0.13%	0.00%	0.00%	**4.57%**
W	2.96%	3.23%	1.88%	1.34%	0.00%	**9.41%**
WNW	6.45%	1.21%	0.40%	0.13%	0.00%	**8.20%**
NW	1.75%	0.13%	0.00%	0.00%	0.00%	**1.88%**
NNW	0.81%	0.00%	0.00%	0.00%	0.00%	**0.81%**
	56.18%	30.24%	4.44%	1.48%	0.00%	92.34%

No. of Monitored Hours	744	Hours	No. of Calm	57	Hours
No. of Monitored Days	31	Days	Calm (%)	7.66%	
Missing Data	0	Hours	Average Wind Speed	1.42	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	7.20	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	SSW	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : May

MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 May 26	36	25	1	1 - 2	1 - 5	18 - 58
2 May 26	28	24	1	1 - 2	1 - 6	12 - 49
3 May 26	37	26	1	1 - 2	1 - 10	9 - 44
4 May 26	31	24	1	1 - 2	1 - 6	8 - 41
5 May 26	23	16	1	1 - 2	1 - 7	13 - 59
6 May 26	25	22	1	1 - 2	2 - 8	6 - 50
7 May 26	26	19	1	1 - 2	2 - 7	7 - 44
8 May 26	27	18	1	1 - 2	2 - 7	11 - 49
9 May 26	34	27	1	1 - 2	2 - 9	19 - 67
10 May 26	30	25	1	1 - 2	2 - 8	19 - 59
11 May 26	33	26	1	1 - 2	1 - 7	11 - 53
12 May 26	28	19	1	1	2 - 6	11 - 34
13 May 26	21	14	1	1	2 - 7	5 - 32
14 May 26	24	16	1	1	2 - 7	5 - 32
15 May 26	27	15	1	1 - 2	2 - 6	5 - 31
16 May 26	21	14	1	1 - 2	2 - 6	5 - 40
17 May 26	15	10	1	1	0 - 5	6 - 30
18 May 26	20	14	1	1	1 - 5	8 - 32
19 May 26	24	15	1	1 - 2	1 - 5	8 - 32
20 May 26	25	18	1	0 - 1	2 - 6	10 - 38
21 May 26	30	24	0	0	1 - 5	5 - 29
22 May 26	26	19	0	0	2 - 5	6 - 32
23 May 26	22	20	0	0	2 - 7	7 - 38
24 May 26	20	12	0	0	2 - 5	7 - 33
25 May 26	25	16	0	0	2 - 6	5 - 32
26 May 26	28	20	0	0	2 - 7	5 - 37
27 May 26	18	12	0	0	2 - 5	8 - 41
28 May 26	28	19	0	0	2 - 9	6 - 35
29 May 26	31	23	0	0	2 - 9	5 - 36
30 May 26	27	20	0	0	1 - 6	6 - 44
31 May 26	24	19	0	0	1 - 5	7 - 41
Range	15 - 37	10 - 27	0 - 1	0 - 2	0 - 10	5 - 67
Number of times (exceeded standard)	0	0	0	0	0	0
Total Monitoring Day	31	31	31	31	31	31
Total Monitoring Hour	742	744	709	709	710	710
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-

1) **Standards** = Ambient Air Quality Standards of the National Environment Board
2) **TSP** = Total Suspended Particulate
3) **PM-10** = Particulate Matter less than 10 μm
4) **SO_2** = Sulfur Dioxide
5) **NO_2** = Nitrogen Dioxide
6) **N/A** = Data not Available
7) ***** = Exeeding air quality standard
8) **-** = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : May


MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 May 26	25.6	35.7	30.1	48	99	73	1,004	1,009	1,007	0.0
2 May 26	26.7	37.5	31.3	38	99	68	1,003	1,008	1,006	0.0
3 May 26	26.7	38.1	31.4	35	99	70	1,002	1,008	1,006	0.0
4 May 26	27.2	37.1	31.6	44	99	74	1,004	1,009	1,006	0.0
5 May 26	23.0	35.9	29.4	45	100	80	1,004	1,009	1,007	68.2
6 May 26	26.5	36.9	31.2	42	100	76	1,003	1,008	1,005	0.0
7 May 26	27.5	37.1	31.5	41	100	75	1,003	1,007	1,005	0.0
8 May 26	26.7	37.3	30.6	43	100	77	1,003	1,008	1,006	0.0
9 May 26	26.1	35.3	30.0	51	100	83	1,003	1,009	1,006	0.6
10 May 26	26.3	36.6	30.7	42	100	78	1,003	1,008	1,006	0.0
11 May 26	27.1	35.4	30.6	52	100	80	1,004	1,008	1,006	0.4
12 May 26	25.4	32.5	28.2	59	100	90	1,004	1,009	1,006	2.6
13 May 26	25.5	35.9	29.3	50	100	86	1,001	1,007	1,004	5.8
14 May 26	26.1	35.7	30.0	52	100	84	1,001	1,006	1,004	0.2
15 May 26	26.0	35.3	29.3	49	100	88	1,002	1,006	1,004	21.8
16 May 26	26.0	35.0	29.1	51	100	86	1,001	1,005	1,004	20.0
17 May 26	26.1	35.1	30.4	49	100	73	1,000	1,005	1,003	0.0
18 May 26	25.9	34.5	30.2	51	100	74	1,000	1,003	1,002	0.0
19 May 26	26.4	32.3	28.8	62	99	82	999	1,004	1,002	0.0
20 May 26	24.2	34.5	28.8	47	100	82	999	1,003	1,002	43.8
21 May 26	25.0	35.3	29.1	52	100	87	1,002	1,006	1,004	0.6
22 May 26	26.2	36.2	30.4	47	100	81	1,004	1,008	1,006	0.0
23 May 26	26.7	37.0	30.8	47	100	82	1,004	1,009	1,007	0.0
24 May 26	27.2	36.5	31.1	49	100	78	1,005	1,009	1,007	7.8
25 May 26	24.7	37.3	29.6	46	100	85	1,004	1,008	1,007	20.4
26 May 26	25.9	35.9	29.2	50	100	88	1,004	1,007	1,006	1.4
27 May 26	26.1	37.6	30.9	42	100	77	1,002	1,008	1,006	0.0
28 May 26	27.1	36.9	30.8	47	100	79	1,003	1,008	1,006	0.0
29 May 26	26.0	36.6	29.7	45	100	84	1,003	1,008	1,006	0.8
30 May 26	26.1	35.4	29.6	45	100	79	1,003	1,008	1,006	0.0
31 May 26	25.7	36.6	30.0	47	100	80	1,003	1,008	1,006	0.0
Total	23.0	38.1	30.1	35	100	80	999	1,009	1,005	194.4
Day	31			31			31			31
Hours	744			744			744			744

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/May/2026 STATION : Ban Chao Nua

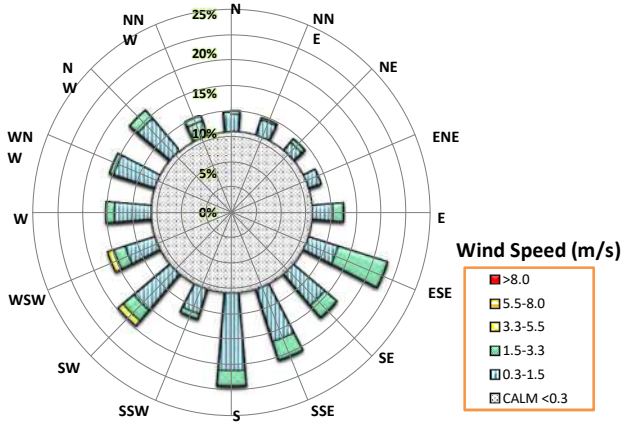

Wind Sector	Wind Speed (m/s)					
	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	2.15%	0.40%	0.00%	0.00%	0.00%	2.55%
NNE	2.02%	0.27%	0.00%	0.00%	0.00%	2.28%
NE	1.34%	0.54%	0.00%	0.00%	0.00%	1.88%
ENE	1.61%	0.00%	0.00%	0.00%	0.00%	1.61%
E	2.55%	1.34%	0.00%	0.00%	0.00%	3.90%
ESE	3.90%	6.45%	0.00%	0.00%	0.00%	10.35%
SE	5.11%	2.02%	0.00%	0.00%	0.00%	7.12%
SSE	6.85%	2.42%	0.00%	0.00%	0.00%	9.27%
S	9.68%	1.88%	0.13%	0.00%	0.00%	11.69%
SSW	3.23%	0.67%	0.00%	0.00%	0.00%	3.90%
SW	5.91%	1.75%	0.81%	0.00%	0.00%	8.47%
WSW	3.90%	1.48%	0.81%	0.00%	0.00%	6.18%
W	4.57%	1.08%	0.00%	0.00%	0.00%	5.65%
WNW	5.38%	0.54%	0.00%	0.00%	0.00%	5.91%
NW	5.24%	1.34%	0.00%	0.00%	0.00%	6.59%
NNW	1.88%	0.67%	0.00%	0.00%	0.00%	2.55%
	65.32%	22.85%	1.75%	0.00%	0.00%	89.92%

No. of Monitored Hours	744	Hours	No. of Calm	75	Hours
No. of Monitored Days	31	Days	Calm (%)	10.08%	
Missing Data	0	Hours	Average Wind Speed	1.11	m/s
No. of Valid Data	744	Hours	Maximum Wind Speed	4.40	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	S	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : June

MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Concentration					
	TSP (µg/m³)	PM-10 (µg/m³)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Jun 26	13	12	1	1	1 - 8	7 - 45
2 Jun 26	18	16	1	1	1 - 8	3 - 50
3 Jun 26	14	13	1	1 - 2	1 - 7	5 - 44
4 Jun 26	11	10	1	1	1 - 8	4 - 40
5 Jun 26	16	13	1	1	1 - 6	13 - 40
6 Jun 26	13	12	1	1	1 - 6	10 - 37
7 Jun 26	13	12	1	1	1 - 6	7 - 42
8 Jun 26	17	15	1	1	2 - 8	2 - 31
9 Jun 26	18	17	1	1	1 - 9	1 - 32
10 Jun 26	18	13	1	1	2 - 10	2 - 26
11 Jun 26	13	12	1	1	2 - 8	4 - 38
12 Jun 26	16	11	1	1	1 - 7	5 - 39
13 Jun 26	16	14	1	1	1 - 17	4 - 44
14 Jun 26	21	19	1	1	1 - 18	4 - 39
15 Jun 26	21	19	1	1	2 - 9	4 - 41
16 Jun 26	17	15	1	1 - 2	1 - 6	4 - 36
17 Jun 26	15	13	1	1	1 - 7	1 - 29
18 Jun 26	16	14	1	1	1 - 9	4 - 24
19 Jun 26	29	12	1	1 - 2	1 - 7	3 - 29
20 Jun 26	22	13	1	1	2 - 7	4 - 39
21 Jun 26	13	13	1	1	1 - 6	4 - 37
22 Jun 26	21	17	1	1	1 - 5	4 - 29
23 Jun 26	N/A	16	1	1	1 - 6	5 - 30
24 Jun 26	16	10	1	1	1 - 6	5 - 31
25 Jun 26	14	13	1	1 - 2	2 - 5	4 - 35
26 Jun 26	15	14	1	1 - 2	1 - 11	3 - 36
27 Jun 26	16	15	1	1 - 2	1 - 9	3 - 39
28 Jun 26	12	10	1	1 - 2	1 - 8	6 - 34
29 Jun 26	14	10	1	1	1 - 5	4 - 27
30 Jun 26	12	11	1	1	2 - 7	9 - 42
Range	11 - 29	10 - 19	1	1 - 2	1 - 18	1 - 50
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	29	30	30	30	30	30
Monitoring Hour	663	709	685	685	685	685
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 µm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : June


MONITORING STATION : Ban Don Mod Tanoi YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Jun 26	25.6	35.3	28.9	50	100	87	1,005	1,009	1,007	4.6
2 Jun 26	25.6	37.6	30.3	43	100	77	1,002	1,007	1,005	0.2
3 Jun 26	25.5	36.0	30.3	47	100	77	1,000	1,005	1,003	0.0
4 Jun 26	26.6	35.2	28.9	52	100	88	1,001	1,005	1,003	8.4
5 Jun 26	25.8	34.6	29.6	51	100	80	1,002	1,006	1,004	0.4
6 Jun 26	26.8	33.3	29.2	60	99	82	1,004	1,008	1,006	0.0
7 Jun 26	26.0	34.0	29.3	60	99	84	1,005	1,009	1,007	0.0
8 Jun 26	26.4	34.5	29.1	57	100	90	1,004	1,008	1,006	22.8
9 Jun 26	26.0	33.9	28.9	60	100	94	1,004	1,008	1,006	3.4
10 Jun 26	24.3	35.3	28.5	53	100	87	1,005	1,009	1,007	20.0
11 Jun 26	24.2	34.9	27.9	52	100	87	1,007	1,012	1,009	22.0
12 Jun 26	23.5	35.4	27.9	52	100	87	1,008	1,013	1,011	9.6
13 Jun 26	24.9	35.5	29.1	51	100	82	1,006	1,012	1,009	0.2
14 Jun 26	25.8	36.4	30.3	46	100	77	1,005	1,009	1,008	0.0
15 Jun 26	26.6	36.9	30.4	47	100	79	1,005	1,009	1,007	0.0
16 Jun 26	26.1	36.6	29.7	43	100	81	1,006	1,010	1,008	19.8
17 Jun 26	25.9	36.5	29.8	42	100	79	1,006	1,010	1,008	0.0
18 Jun 26	25.9	36.3	28.9	45	100	84	1,007	1,010	1,008	0.4
19 Jun 26	23.6	35.7	27.7	48	100	87	1,006	1,010	1,008	47.4
20 Jun 26	24.4	32.8	27.9	64	100	89	1,006	1,010	1,008	0.2
21 Jun 26	23.5	36.5	28.3	47	100	85	1,007	1,010	1,009	8.4
22 Jun 26	24.5	36.2	29.7	46	100	76	1,005	1,010	1,008	0.2
23 Jun 26	26.2	35.3	30.1	49	99	74	1,004	1,009	1,007	0.0
24 Jun 26	25.4	37.1	30.1	47	100	78	1,003	1,008	1,006	3.0
25 Jun 26	25.8	35.9	29.5	52	100	83	1,004	1,009	1,006	0.6
26 Jun 26	25.0	34.5	29.0	54	100	84	1,004	1,008	1,007	0.8
27 Jun 26	25.4	36.0	30.1	49	100	77	1,004	1,007	1,006	0.0
28 Jun 26	25.4	34.5	28.4	54	100	88	1,004	1,007	1,006	20.4
29 Jun 26	25.3	33.7	28.7	55	100	81	1,003	1,006	1,005	6.8
30 Jun 26	26.2	34.5	29.5	51	99	74	1,004	1,006	1,005	0.2
Total	23.5	37.6	29.2	42	100	83	1,000	1,013	1,007	199.8
Day	30			30			30			30
Hours	720			720			720			720

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-31/May/2026	STATION : Ban Don Mod Tanoi

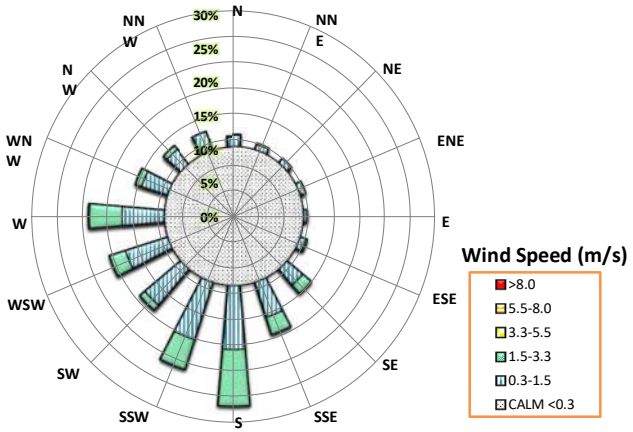

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	1.67%	0.14%	0.00%	0.00%	0.00%	1.81%
NNE	0.83%	0.14%	0.00%	0.00%	0.00%	0.97%
NE	0.83%	0.00%	0.00%	0.00%	0.00%	0.83%
ENE	0.83%	0.00%	0.00%	0.00%	0.00%	0.83%
E	0.56%	0.00%	0.00%	0.00%	0.00%	0.56%
ESE	0.83%	0.28%	0.00%	0.00%	0.00%	1.11%
SE	3.06%	1.67%	0.00%	0.00%	0.00%	4.72%
SSE	5.42%	2.64%	0.00%	0.00%	0.00%	8.06%
S	9.44%	8.33%	0.00%	0.00%	0.00%	17.78%
SSW	8.89%	4.58%	0.00%	0.00%	0.00%	13.47%
SW	6.94%	0.97%	0.00%	0.00%	0.00%	7.92%
WSW	6.53%	2.50%	0.00%	0.00%	0.00%	9.03%
W	6.25%	4.86%	0.14%	0.00%	0.00%	11.25%
WNW	4.03%	0.97%	0.00%	0.00%	0.00%	5.00%
NW	2.64%	0.69%	0.00%	0.00%	0.00%	3.33%
NNW	3.06%	0.00%	0.00%	0.00%	0.00%	3.06%
	61.81%	27.78%	0.14%	0.00%	0.00%	89.72%

No. of Monitored Hours	720	Hours	No. of Calm	74	Hours
No. of Monitored Days	30	Days	Calm (%)	10.28%	
Missing Data	0	Hours	Average Wind Speed	1.13	m/s
No. of Valid Data	720	Hours	Maximum Wind Speed	3.50	m/s
			Prevailing Wind Direction	S	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : June

MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Jun 26	27	15	2	2	2 - 7	N/A
2 Jun 26	29	15	2	2 - 3	2 - 9	N/A
3 Jun 26	26	13	2	2	2 - 7	N/A
4 Jun 26	25	13	3	2 - 3	2 - 11	9 - 44
5 Jun 26	28	13	3	2 - 3	2 - 5	19 - 43
6 Jun 26	27	12	2	2	2 - 6	16 - 40
7 Jun 26	28	13	2	2 - 3	2 - 5	13 - 48
8 Jun 26	30	18	2	2 - 3	2 - 7	8 - 35
9 Jun 26	33	17	2	2 - 3	2 - 11	6 - 27
10 Jun 26	28	13	2	2 - 3	2 - 9	9 - 45
11 Jun 26	26	13	2	2 - 3	2 - 9	10 - 44
12 Jun 26	24	12	2	2 - 3	1 - 7	11 - 51
13 Jun 26	28	12	3	2 - 3	2 - 10	9 - 41
14 Jun 26	27	16	3	2 - 3	1 - 10	9 - 40
15 Jun 26	32	16	3	3 - 3	2 - 8	10 - 43
16 Jun 26	28	14	3	2 - 4	2 - 11	10 - 36
17 Jun 26	28	16	2	2 - 3	1 - 7	9 - 26
18 Jun 26	30	15	3	2 - 3	1 - 6	9 - 27
19 Jun 26	30	14	2	2 - 3	1 - 8	9 - 29
20 Jun 26	29	17	3	2 - 4	3 - 8	8 - 43
21 Jun 26	27	14	3	2 - 3	2 - 12	9 - 40
22 Jun 26	30	17	3	2 - 4	1 - 10	9 - 30
23 Jun 26	30	16	3	3 - 5	2 - 10	8 - 31
24 Jun 26	27	12	3	2 - 4	1 - 6	11 - 39
25 Jun 26	29	11	2	2 - 3	2 - 7	9 - 43
26 Jun 26	30	16	3	2 - 3	2 - 15	9 - 37
27 Jun 26	30	15	3	2 - 3	2 - 12	8 - 33
28 Jun 26	24	12	3	2 - 3	2 - 10	9 - 34
29 Jun 26	22	8	3	2 - 3	2 - 11	9 - 31
30 Jun 26	22	11	3	2 - 3	2 - 8	13 - 47
Range	22 - 33	8 - 18	2	2 - 5	1 - 15	6 - 51
Number of times (exceeded standard)	0	0	0	0	0	0
Total Monitoring Day	30	30	30	30	30	27
Total Monitoring Hour	709	719	689	689	688	607
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-
1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : June


MONITORING STATION : Wat Bang Gado YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Jun 26	25.3	35.4	28.9	52	96	80	1,005	1,009	1,007	3.0
2 Jun 26	26.3	36.6	30.1	43	94	73	1,002	1,008	1,005	0.0
3 Jun 26	26.2	35.2	30.1	53	93	73	1,000	1,005	1,004	0.0
4 Jun 26	26.7	33.7	28.9	57	91	79	1,002	1,005	1,003	0.4
5 Jun 26	26.4	34.1	29.7	52	88	72	1,002	1,006	1,004	0.2
6 Jun 26	27.1	32.6	29.1	60	82	74	1,004	1,008	1,006	0.0
7 Jun 26	26.4	33.2	29.4	62	87	76	1,005	1,009	1,007	0.0
8 Jun 26	26.9	34.4	29.7	58	92	79	1,004	1,008	1,006	1.4
9 Jun 26	26.7	33.7	29.1	57	94	83	1,004	1,008	1,006	7.4
10 Jun 26	25.2	34.8	28.6	54	95	81	1,005	1,009	1,007	8.8
11 Jun 26	24.3	33.7	27.8	55	98	84	1,007	1,012	1,009	28.6
12 Jun 26	23.2	34.7	27.9	54	99	84	1,008	1,013	1,011	42.6
13 Jun 26	25.2	35.0	29.4	53	98	78	1,006	1,012	1,009	0.2
14 Jun 26	26.4	35.7	30.5	48	94	71	1,005	1,009	1,008	0.0
15 Jun 26	26.5	35.6	30.3	50	90	73	1,005	1,009	1,008	0.0
16 Jun 26	26.7	36.0	29.9	44	96	74	1,006	1,010	1,008	1.6
17 Jun 26	26.4	35.9	30.3	42	95	72	1,006	1,010	1,009	0.0
18 Jun 26	26.6	35.2	28.9	48	91	76	1,007	1,010	1,009	0.2
19 Jun 26	24.4	35.3	28.0	51	97	83	1,006	1,011	1,008	31.0
20 Jun 26	25.6	32.3	28.4	62	96	80	1,006	1,010	1,009	0.0
21 Jun 26	24.3	35.9	28.6	46	98	78	1,007	1,011	1,009	18.8
22 Jun 26	25.3	35.0	30.0	50	96	71	1,005	1,010	1,008	0.2
23 Jun 26	26.3	34.7	29.9	50	80	68	1,004	1,009	1,007	1.4
24 Jun 26	24.1	36.1	29.7	49	98	73	1,003	1,008	1,006	25.2
25 Jun 26	25.9	35.5	29.3	54	96	77	1,004	1,009	1,006	0.2
26 Jun 26	25.6	35.2	28.9	53	90	76	1,004	1,008	1,007	0.0
27 Jun 26	25.8	34.9	30.0	52	92	73	1,004	1,008	1,006	0.0
28 Jun 26	26.4	34.3	29.0	54	92	77	1,004	1,007	1,006	0.2
29 Jun 26	26.3	33.3	28.9	56	88	73	1,003	1,007	1,006	2.6
30 Jun 26	26.3	33.8	29.6	51	81	67	1,004	1,007	1,006	0.0
Total	23.2	36.6	29.3	42	99	76	1,000	1,013	1,007	174.0
Day	30			30			30			30
Hours	720			720			720			720

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-30/June/2026 STATION : Wat Bang Gado

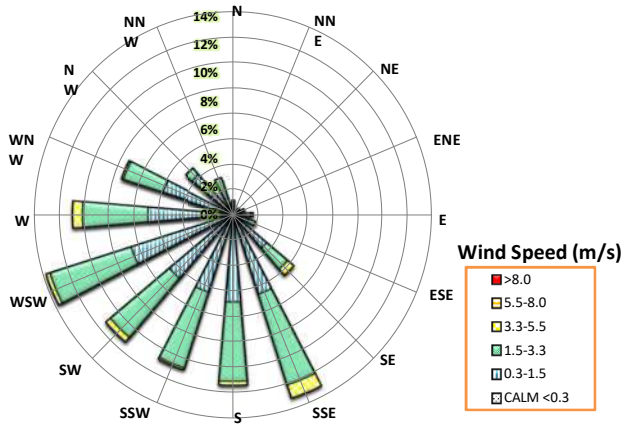

Wind Sector	Wind Speed (m/s)					
	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	0.97%	0.00%	0.00%	0.00%	0.00%	**0.97%**
NNE	0.28%	0.00%	0.00%	0.00%	0.00%	**0.28%**
NE	0.56%	0.00%	0.00%	0.00%	0.00%	**0.56%**
ENE	0.69%	0.14%	0.00%	0.00%	0.00%	**0.83%**
E	1.25%	0.14%	0.00%	0.00%	0.00%	**1.39%**
ESE	1.11%	0.56%	0.00%	0.00%	0.00%	**1.67%**
SE	3.06%	1.94%	0.56%	0.00%	0.00%	**5.56%**
SSE	5.83%	6.67%	0.97%	0.00%	0.00%	**13.47%**
S	6.11%	5.56%	0.28%	0.00%	0.00%	**11.94%**
SSW	5.69%	5.56%	0.14%	0.00%	0.00%	**11.39%**
SW	5.83%	5.42%	0.42%	0.00%	0.00%	**11.67%**
WSW	7.50%	5.97%	0.28%	0.00%	0.00%	**13.75%**
W	5.97%	4.58%	0.69%	0.00%	0.00%	**11.25%**
WNW	5.14%	2.92%	0.14%	0.00%	0.00%	**8.19%**
NW	3.75%	0.56%	0.00%	0.00%	0.00%	**4.31%**
NNW	1.25%	1.53%	0.00%	0.00%	0.00%	**2.78%**
	55.00%	**41.53%**	**3.47%**	**0.00%**	**0.00%**	**100.00%**

No. of Monitored Hours	720	Hours	No. of Calm	0	Hours
No. of Monitored Days	30	Days	Calm (%)	0.00%	
Missing Data	0	Hours	Average Wind Speed	1.62	m/s
No. of Valid Data	720	Hours	Maximum Wind Speed	4.50	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction		WSW

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : June

MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr. Avg.	24-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Jun 26	16	15	2	2	2 - 12	15 - 58
2 Jun 26	20	18	2	2	3 - 14	4 - 80
3 Jun 26	18	15	2	2 - 3	2 - 13	5 - 60
4 Jun 26	16	14	2	2	2 - 20	8 - 58
5 Jun 26	16	11	2	2	2 - 10	16 - 56
6 Jun 26	14	12	2	2	2 - 7	17 - 49
7 Jun 26	13	11	2	2	2 - 9	15 - 51
8 Jun 26	21	17	2	2	2 - 13	4 - 39
9 Jun 26	20	17	2	2	2 - 12	3 - 39
10 Jun 26	17	14	2	2	2 - 14	3 - 47
11 Jun 26	15	14	1	1 - 2	1 - 17	4 - 43
12 Jun 26	15	11	2	1 - 2	2 - 10	8 - 52
13 Jun 26	18	13	2	1 - 2	2 - 11	8 - 48
14 Jun 26	19	15	1	1 - 2	1 - 7	9 - 38
15 Jun 26	18	16	1	1 - 2	2 - 8	9 - 46
16 Jun 26	21	15	1	1 - 2	1 - 9	9 - 33
17 Jun 26	19	15	2	1 - 2	1 - 9	8 - 32
18 Jun 26	21	14	2	1 - 2	1 - 9	8 - 30
19 Jun 26	19	13	1	1 - 2	2 - 9	8 - 32
20 Jun 26	21	15	2	1 - 2	4 - 8	9 - 54
21 Jun 26	17	15	2	2	2 - 11	9 - 40
22 Jun 26	20	15	2	2	1 - 9	9 - 33
23 Jun 26	20	14	2	2 - 3	2 - 8	10 - 31
24 Jun 26	13	10	2	2 - 3	1 - 7	11 - 38
25 Jun 26	16	12	2	2	2 - 7	8 - 43
26 Jun 26	16	12	2	2 - 5	1 - 17	8 - 39
27 Jun 26	20	15	2	2 - 4	1 - 14	8 - 39
28 Jun 26	15	10	2	2 - 4	1 - 8	9 - 37
29 Jun 26	11	6	2	2 - 3	2 - 8	13 - 34
30 Jun 26	11	7	2	2 - 3	2 - 9	14 - 49
Range	11 - 21	6 - 18	1 - 2	1 - 5	1 - 20	3 - 80
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	30	30	30	30	30	30
Monitoring Hour	716	716	689	689	688	689
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :- 1) Standards = Ambient Air Quality Standards of the National Environment Board
2) TSP = Total Suspended Particulate
3) PM-10 = Particulate Matter less than 10 μm
4) SO_2 = Sulfur Dioxide
5) NO_2 = Nitrogen Dioxide
6) N/A = Data not Available
7) * = Exeeding air quality standard
8) - = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : June


MONITORING STATION : Ban Klong Klae YEAR : 2026

Date	Temperature (°C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Jun 26	25.7	35.3	29.4	50	94	76	1,004	1,008	1,007	1.8
2 Jun 26	26.5	36.3	30.5	44	93	70	1,001	1,007	1,005	0.0
3 Jun 26	26.2	36.0	30.3	50	91	71	1,000	1,005	1,003	0.0
4 Jun 26	26.0	34.8	28.7	53	99	82	1,001	1,004	1,003	30.8
5 Jun 26	26.0	34.4	29.8	54	90	73	1,002	1,005	1,004	0.8
6 Jun 26	27.2	32.5	29.1	63	84	75	1,004	1,008	1,006	0.0
7 Jun 26	26.2	34.2	29.5	58	86	75	1,004	1,008	1,007	0.2
8 Jun 26	27.1	34.1	29.9	57	93	78	1,004	1,008	1,006	0.8
9 Jun 26	27.2	34.4	30.1	56	94	76	1,004	1,007	1,005	0.0
10 Jun 26	24.7	36.1	29.1	50	99	80	1,004	1,009	1,006	19.0
11 Jun 26	25.0	34.9	28.4	52	97	82	1,007	1,012	1,009	19.4
12 Jun 26	23.5	35.2	28.2	53	99	84	1,008	1,012	1,010	27.6
13 Jun 26	25.4	35.3	29.7	53	99	77	1,006	1,012	1,009	0.0
14 Jun 26	26.4	35.4	30.8	50	93	70	1,004	1,009	1,007	0.0
15 Jun 26	26.5	37.6	30.9	46	86	68	1,005	1,009	1,007	0.0
16 Jun 26	26.4	37.5	30.6	41	93	70	1,005	1,010	1,008	0.8
17 Jun 26	27.1	36.5	30.6	42	92	69	1,005	1,010	1,008	0.2
18 Jun 26	26.4	35.4	29.2	46	91	74	1,006	1,009	1,008	2.8
19 Jun 26	25.3	36.5	28.4	44	96	80	1,006	1,010	1,008	6.2
20 Jun 26	25.6	32.3	28.7	60	95	77	1,006	1,009	1,008	0.4
21 Jun 26	25.1	35.8	28.8	47	95	76	1,006	1,010	1,009	7.8
22 Jun 26	25.6	36.6	30.3	42	93	68	1,005	1,010	1,008	0.2
23 Jun 26	26.4	35.5	30.7	46	80	62	1,004	1,008	1,006	0.0
24 Jun 26	26.8	37.7	30.9	44	92	67	1,003	1,008	1,006	1.8
25 Jun 26	26.7	36.6	30.2	49	92	71	1,003	1,008	1,006	0.0
26 Jun 26	26.3	34.6	29.6	53	86	70	1,004	1,008	1,006	0.8
27 Jun 26	26.4	35.8	30.7	49	86	67	1,003	1,007	1,006	0.2
28 Jun 26	26.4	35.1	29.0	52	93	76	1,003	1,007	1,005	6.8
29 Jun 26	26.5	34.4	29.9	49	83	65	1,003	1,006	1,005	0.2
30 Jun 26	28.2	34.7	30.6	45	66	58	1,004	1,006	1,005	0.0
Total	23.5	37.7	29.8	41	99	73	1,000	1,012	1,006	128.6
Day	30			30			30			30
Hours	720			720			720			720

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-30/June/2026 | **STATION : Ban Klong Klae**

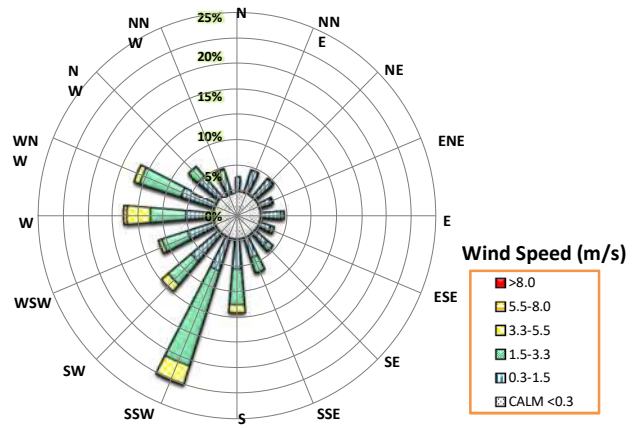

Wind Speed (m/s)						
Wind Sector	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	1.81%	0.00%	0.00%	0.00%	0.00%	**1.81%**
NNE	2.92%	0.00%	0.00%	0.00%	0.00%	**2.92%**
NE	2.92%	0.14%	0.00%	0.00%	0.00%	**3.06%**
ENE	1.67%	0.14%	0.00%	0.00%	0.00%	**1.81%**
E	2.50%	0.42%	0.00%	0.00%	0.00%	**2.92%**
ESE	1.53%	0.42%	0.00%	0.00%	0.00%	**1.94%**
SE	2.08%	0.83%	0.00%	0.00%	0.00%	**2.92%**
SSE	2.64%	1.94%	0.00%	0.00%	0.00%	**4.58%**
S	3.75%	4.44%	0.97%	0.00%	0.00%	**9.17%**
SSW	4.31%	12.36%	2.36%	0.14%	0.00%	**19.17%**
SW	4.58%	3.75%	1.11%	0.00%	0.00%	**9.44%**
WSW	3.61%	3.33%	0.42%	0.00%	0.00%	**7.36%**
W	3.47%	4.44%	2.92%	0.42%	0.00%	**11.25%**
WNW	4.44%	5.42%	0.69%	0.00%	0.00%	**10.56%**
NW	3.47%	1.53%	0.00%	0.00%	0.00%	**5.00%**
NNW	3.06%	0.14%	0.00%	0.00%	0.00%	**3.19%**
	48.75%	39.31%	8.47%	0.56%	0.00%	97.08%

No. of Monitored Hours	720	Hours	No. of Calm	21	Hours
No. of Monitored Days	30	Days	Calm (%)	2.92%	
Missing Data	0	Hours	Average Wind Speed	1.70	m/s
No. of Valid Data	720	Hours	Maximum Wind Speed	6.80	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	SSW	

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

AMBIENT AIR QUALITY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. MONTH : June

MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Concentration					
	TSP ($\mu g/m^3$)	PM-10 ($\mu g/m^3$)	SO_2 (ppb)		NO_2 (ppb)	O_3 (ppb)
	24-Hr Avg.	24-Hr Avg.	24-Hr Avg.	1-Hr. Avg.	1-Hr. Avg.	1-Hr. Avg.
1 Jun 26	21	14	0	0	1 - 6	9 - 36
2 Jun 26	20	15	0	0	1 - 5	6 - 38
3 Jun 26	22	12	0	0	1 - 4	6 - 36
4 Jun 26	22	11	0	0	1 - 7	7 - 34
5 Jun 26	20	15	0	0	1 - 5	12 - 32
6 Jun 26	19	12	0	0	1 - 4	12 - 31
7 Jun 26	19	13	0	0	1 - 6	9 - 35
8 Jun 26	24	18	1	0 - 2	2 - 5	7 - 28
9 Jun 26	28	18	2	2	1 - 6	9 - 31
10 Jun 26	22	14	2	2	1 - 6	8 - 34
11 Jun 26	15	12	2	2	1 - 6	8 - 37
12 Jun 26	19	11	2	2	1 - 4	8 - 34
13 Jun 26	22	15	2	2	1 - 6	8 - 29
14 Jun 26	24	16	2	2	1 - 5	8 - 27
15 Jun 26	26	17	2	2	2 - 4	7 - 32
16 Jun 26	22	15	2	2	1 - 4	8 - 28
17 Jun 26	20	13	2	2	1 - 5	7 - 23
18 Jun 26	20	13	2	1 - 2	1 - 4	7 - 20
19 Jun 26	21	12	2	1 - 2	1 - 4	7 - 23
20 Jun 26	24	15	2	1 - 2	2 - 6	7 - 31
21 Jun 26	21	12	2	1 - 2	0 - 4	9 - 27
22 Jun 26	20	15	2	1 - 2	0 - 5	7 - 23
23 Jun 26	21	14	2	1 - 2	1 - 4	9 - 24
24 Jun 26	17	12	2	1 - 2	1 - 3	8 - 26
25 Jun 26	20	13	2	2	1 - 4	8 - 29
26 Jun 26	18	14	2	2	1 - 7	8 - 27
27 Jun 26	26	16	2	2	1 - 6	7 - 27
28 Jun 26	19	10	2	1 - 2	1 - 6	8 - 27
29 Jun 26	17	11	2	1 - 2	1 - 4	8 - 24
30 Jun 26	16	10	2	2	1 - 5	12 - 33
Range	15 - 28	10 - 18	0 - 2	0 - 2	0 - 7	6 - 38
Number of times (exceeded standard)	0	0	0	0	0	0
Total Day	30	30	30	30	30	30
Monitoring Hour	720	719	687	687	687	686
Ambient Air Quality Standard	200	100	50	100	120	100

Remark :-

1) **Standards** = Ambient Air Quality Standards of the National Environment Board
2) **TSP** = Total Suspended Particulate
3) **PM-10** = Particulate Matter less than 10 μm
4) **SO_2** = Sulfur Dioxide
5) **NO_2** = Nitrogen Dioxide
6) **N/A** = Data not Available
7) ***** = Exeeding air quality standard
8) **-** = Not Measurement

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

MONTHLY REPORT

METEOROLOGY MONITORING RESULT

PROJECT : Ratchaburi Electricity Generating Co.,Ltd. Month : June


MONITORING STATION : Ban Chao Nua YEAR : 2026

Date	Temperature (° C)			Relative Humidity (%)			Pressure (mb)			Rain Gauge
	Min.	Max.	Avg.	Min.	Max.	Avg.	Min.	Max.	Avg.	Sum. (mm)
1 Jun 26	25.4	34.8	29.1	52	100	86	1,004	1,008	1,006	0.6
2 Jun 26	26.2	36.3	30.3	44	100	78	1,001	1,006	1,004	0.0
3 Jun 26	25.8	36.2	30.4	49	100	78	1,000	1,004	1,003	0.0
4 Jun 26	26.6	35.2	28.9	52	100	89	1,000	1,003	1,002	11.8
5 Jun 26	25.8	34.9	29.7	50	100	81	1,001	1,005	1,003	1.0
6 Jun 26	26.9	33.7	29.3	59	99	84	1,003	1,007	1,005	0.0
7 Jun 26	25.9	34.2	29.3	59	100	85	1,003	1,008	1,006	0.0
8 Jun 26	26.7	35.3	29.6	55	100	90	1,003	1,007	1,005	26.0
9 Jun 26	26.2	34.8	29.1	58	100	94	1,003	1,006	1,005	9.2
10 Jun 26	24.5	35.9	28.7	52	100	88	1,003	1,008	1,006	29.4
11 Jun 26	24.1	34.1	27.8	54	100	89	1,006	1,011	1,008	34.4
12 Jun 26	23.0	34.9	27.9	54	100	87	1,007	1,011	1,010	23.8
13 Jun 26	25.1	36.1	29.4	49	100	82	1,005	1,011	1,008	0.0
14 Jun 26	25.9	35.7	30.5	48	100	77	1,004	1,008	1,006	0.0
15 Jun 26	26.4	37.1	30.3	46	100	81	1,004	1,008	1,006	0.0
16 Jun 26	25.9	37.4	29.8	41	100	81	1,005	1,009	1,007	25.0
17 Jun 26	26.2	36.1	30.0	42	100	80	1,005	1,009	1,007	0.0
18 Jun 26	26.0	35.5	28.9	48	100	85	1,006	1,009	1,007	0.6
19 Jun 26	23.8	34.8	27.7	52	100	88	1,005	1,009	1,007	69.6
20 Jun 26	24.9	32.0	28.1	65	100	90	1,005	1,009	1,007	0.6
21 Jun 26	23.2	36.1	28.3	47	100	86	1,005	1,009	1,008	49.2
22 Jun 26	25.0	36.1	29.8	47	100	76	1,004	1,009	1,007	0.4
23 Jun 26	26.5	35.5	30.1	49	99	75	1,003	1,007	1,005	0.0
24 Jun 26	24.7	37.4	30.0	46	100	79	1,002	1,007	1,005	3.6
25 Jun 26	25.8	35.9	29.7	52	100	84	1,003	1,007	1,005	0.4
26 Jun 26	25.5	35.5	29.2	54	100	84	1,003	1,007	1,005	0.0
27 Jun 26	25.5	35.6	30.3	50	100	78	1,002	1,006	1,005	0.0
28 Jun 26	25.7	35.5	28.9	52	100	87	1,002	1,006	1,005	14.4
29 Jun 26	25.9	34.0	29.0	55	100	80	1,002	1,005	1,004	11.0
30 Jun 26	26.9	34.4	29.8	50	94	70	1,003	1,005	1,004	0.0
Total	23.0	37.4	29.3	41	100	83	1,000	1,011	1,006	311.0
Day	30			30			30			30
Hours	720			720			717			717

Remarks :- P = Power Fail ,F = Equipment Fail , N/A = Data not Available

บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
Ratchaburi Electricity Generating Co.,Ltd.

Date/Month/Year : 1-30/June/2026 STATION : Ban Chao Nua

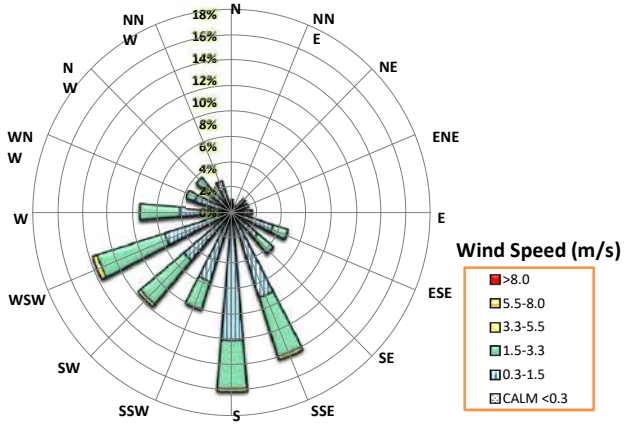

Wind Sector	Wind Speed (m/s)					
	0.3-1.5	1.5-3.3	3.3-5.5	5.5-8.0	>8.0	ALL
N	1.11%	0.00%	0.00%	0.00%	0.00%	1.11%
NNE	0.42%	0.14%	0.00%	0.00%	0.00%	0.56%
NE	1.53%	0.00%	0.00%	0.00%	0.00%	1.53%
ENE	1.25%	0.28%	0.00%	0.00%	0.00%	1.53%
E	1.67%	0.14%	0.00%	0.00%	0.00%	1.81%
ESE	3.89%	1.39%	0.00%	0.00%	0.00%	5.28%
SE	3.06%	1.81%	0.00%	0.00%	0.00%	4.86%
SSE	8.06%	5.56%	0.28%	0.00%	0.00%	13.89%
S	11.53%	4.31%	0.28%	0.00%	0.00%	16.11%
SSW	6.53%	2.64%	0.00%	0.00%	0.00%	9.17%
SW	5.69%	5.14%	0.28%	0.00%	0.00%	11.11%
WSW	6.39%	6.39%	0.42%	0.00%	0.00%	13.19%
W	4.72%	3.61%	0.00%	0.00%	0.00%	8.33%
WNW	3.47%	0.83%	0.00%	0.00%	0.00%	4.31%
NW	3.33%	0.83%	0.00%	0.00%	0.00%	4.17%
NNW	3.06%	0.00%	0.00%	0.00%	0.00%	3.06%
	65.69%	33.06%	1.25%	0.00%	0.00%	100.00%

No. of Monitored Hours	720	Hours	No. of Calm	0	Hours
No. of Monitored Days	30	Days	Calm (%)	0.00%	
Missing Data	0	Hours	Average Wind Speed	1.32	m/s
No. of Valid Data	720	Hours	Maximum Wind Speed	4.00	m/s
Wind Rose by : Air Quality and Noise Section : 2020/05			Prevailing Wind Direction	S	

เอกสารแนบที่ 3-2

ใบรายงานผลการตรวจสอบความถูกต้องด้วยระบบ AAQMS


บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of NO_x Analyzer

Station	: Ban Don Mot Tanoi	Date	: 10 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 13:30-14:30
$NO-NO_2-NO_x$ Analyzer			
Brand	: Thermo Scientific	Model	: 42iQ-BNAAN
Range	: 0-500 ppb	Serial No.	: 12609644592
Calibrator (Dilution System)			
Brand	: Teledyne	Model	: 700
Last Cal. Date	: 01 September 2025	Serial No.	: 911
Reference Standard Gas			
Standard Gas	: Nitric Oxide (NO)	Cylinder No.	: D878356
Expiration Date	: 21 April 2029	Cylinder Conc.	: 53.0 ppm

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	1.3	1.30	-
1	100.0	9.5	5000	101.5	1.50	1.50
2	200.0	18.9	5000	202.0	2.00	1.00
3	300.0	28.5	5000	301.0	1.00	0.33
4	400.0	38.0	5000	398.0	-2.00	0.50
Slope =	0.9929	Intercept =	2.1800	Average Difference (%) (Pass) =		0.8333
% Slope =	-0.7100	% Intercept =	0.4360	Correlation Coefficiency =		1.0000
	(Pass)		(Pass)	% Correlation Coefficiency (Pass) =		-0.0027

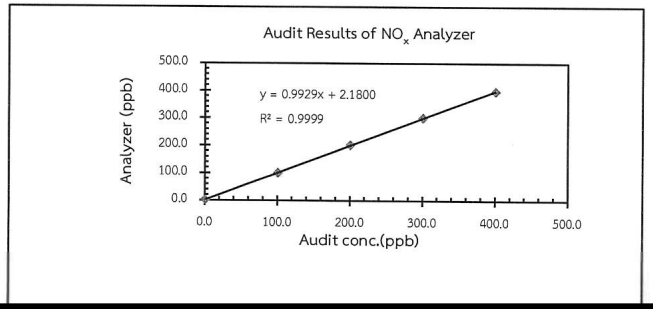

Site Operator

Technical Supervisor


บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of SO_2 Analyzer

Station	: Ban Don Mot Tanoi	Date	: 10 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 11:00-12:00
SO_2 Analyzer			
Brand	: Thermo Scientific	Model	: 43iQ-BNA
Range	: 0-500 ppb	Serial No.	: 12606944595
Calibrator (Dilution System)			
Brand	: Teledyne	Model	: 700
Last Cal. Date	: 01 September 2025	Serial No.	: 911
Reference Standard Gas			
Standard Gas	: Sulphur Dioxide (SO_2)	Cylinder No.	: D878356
Expiration Date	: 21 April 2029	Cylinder Conc.	: 48.9 ppm

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	1.2	1.20	-
1	100.0	10.2	5000	102.3	2.30	2.30
2	200.0	20.5	5000	203.0	3.00	1.50
3	300.0	30.9	5000	301.0	1.00	0.33
4	400.0	41.2	5000	400.0	0.00	0.00
Slope =	0.9963	Intercept =	2.2400	Average Difference (%) (Pass) =		1.0333
% Slope =	-0.3700	% Intercept =	0.4480	Correlation Coefficiency =		1.0000
	(Pass)		(Pass)	% Correlation Coefficiency (Pass) =		-0.0026

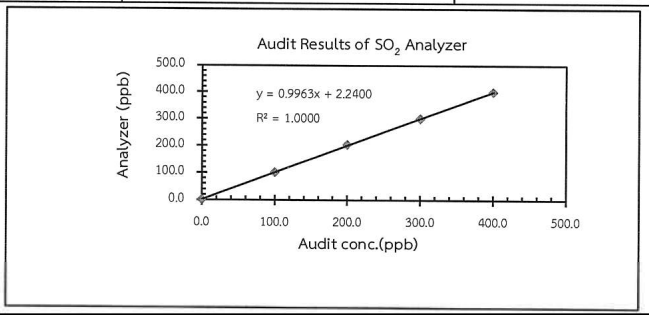

[redacted]

Site Operator


Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of O_3 Analyzer			
Station	: Ban Don Mot Tanoi	Date	: 10 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 10:00-11:00
O_3 Analyzer			
Brand	: Thermo Scientific	Model	: 49I-B2NCA
Range	: 0-500 ppb	Serial No.	: 1162850020
Calibrator (Ozone Gen.)			
Brand	: Teledyne	Model	: T703
Last Cal. Date	: 01 September 2025	Serial No.	: 412

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	0.8	0.80	-
1	100.0	10.0	5000	97.7	-2.30	2.30
2	200.0	20.1	5000	197.9	-2.10	1.05
3	300.0	30.2	5000	298.0	-2.00	0.67
4	400.0	40.3	5000	402.0	2.00	0.50
Slope =	1.0027	Intercept =	-1.2600	Average Difference (%) (Pass) =		1.1292
% Slope =	0.2700 (Pass)	% Intercept =	-0.2520 (Pass)	Correlation Coefficiency =		1.0000
				% Correlation Coefficiency (Pass) =		-0.0043

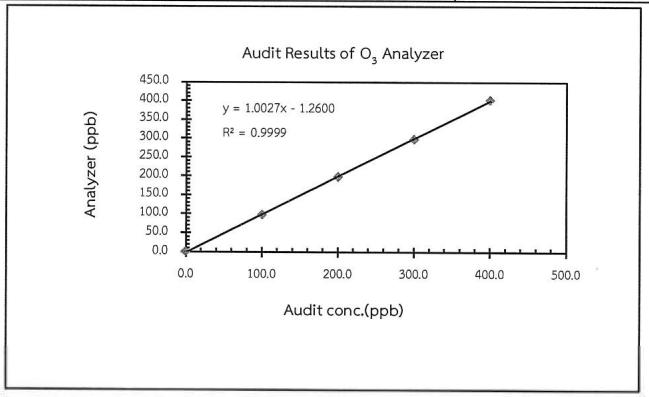

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of TSP Analyzer			
Station	: Ban Don Mot Tanoi	Date	: 10 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 13:10-13:20
TSP Analyzer			
Brand	: Thermo Scientific	Model	: 5014i/5030i
Method	: Beta Ray	Serial No.	: CM16461002
Calibrator (Dry Cal Primary Flow Meter)			
Brand	: Bios Defender	Model	: Defender 510-H
Last Cal. Date	: 12 September 2025	Serial No.	: 136164

Data	Monitor Flow Rate (Lit/min)	Audit Std. Flow Rate (Lit/min)	Difference	% Difference
1	16.7	16.68	0.02	0.11
2	16.7	16.67	0.04	0.21
3	16.7	16.65	0.05	0.28
4	16.7	16.66	0.04	0.23
5	16.7	16.65	0.05	0.29
6	16.7	16.67	0.03	0.17
7	16.7	16.66	0.04	0.23
8	16.7	16.67	0.03	0.18
9	16.7	16.65	0.05	0.33
10	16.7	16.68	0.02	0.15
Average =	16.7	16.66	0.04	0.22
Average Difference (%) (Pass) =				0.22

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of PM10 Analyzer			
Station	: Ban Don Mot Tanoi	Date	: 10 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 13:30-13:40
PM10 Analyzer			
Brand	: Thermo Scientific	Model	: 5014i/5030i
Method	: Beta Ray	Serial No.	: CM16471015
Calibrator (Dry Cal Primary Flow Meter)			
Brand	: Bios Defender	Model	: Defender 510-H
Last Cal. Date	: 12 September 2025	Serial No.	: 136164

Data	Monitor Flow Rate (Lit/min)	Audit Std. Flow Rate (Lit/min)	Difference	% Difference
1	16.7	16.67	0.03	0.17
2	16.7	16.68	0.02	0.15
3	16.7	16.66	0.04	0.25
4	16.7	16.68	0.02	0.10
5	16.7	16.67	0.03	0.16
6	16.7	16.65	0.05	0.28
7	16.7	16.67	0.03	0.17
8	16.7	16.68	0.02	0.14
9	16.7	16.67	0.03	0.17
10	16.7	16.69	0.01	0.08
Average =	16.7	16.67	0.03	0.17
Average Difference (%) (Pass) =				0.17

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Wind Speed			
Station	: Ban Don Mot Tanoi	Date	: 10-11 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 11:00-11:00 (24 Hr)
Wind Speed (Station)			
Brand	: LSI LASTEM	Model	: DNA 821
Method	: Wind Speed Sensor	Serial No.	: 24090146
Wind Speed (Reference Instrument)			
Brand	: Young Wind Monitor	Model	: 05103
Method	: Wind Direction Sensor	Serial No.	: 68983

Data	Date	Time	Wind Speed (Station) (m/s)	Wind Speed (Ref.) (m/s)	Difference (m/s)
1	10/06/2026	11:00	1.4	1.6	0.2
2	10/06/2026	12:00	1.5	1.2	-0.3
3	10/06/2026	13:00	2.2	2.6	0.4
4	10/06/2026	14:00	2.3	2.8	0.5
5	10/06/2026	15:00	2.7	2.9	0.2
6	10/06/2026	16:00	2.2	2.5	0.3
7	10/06/2026	17:00	1.0	1.2	0.2
8	10/06/2026	18:00	1.2	1.5	0.3
9	10/06/2026	19:00	1.4	1.9	0.5
10	10/06/2026	20:00	1.1	1.5	0.4
11	10/06/2026	21:00	1.2	1.1	-0.1
12	10/06/2026	22:00	0.8	0.9	0.1
13	10/06/2026	23:00	0.8	1.1	0.3
14	11/06/2026	00:00	0.4	0.5	0.1
15	11/06/2026	01:00	0.6	0.8	0.2
16	11/06/2026	02:00	0.6	0.9	0.3
17	11/06/2026	03:00	0.5	0.8	0.3
18	11/06/2026	04:00	0.3	0.9	0.6
19	11/06/2026	05:00	0.2	0.5	0.3
20	11/06/2026	06:00	0.7	0.9	0.2
21	11/06/2026	07:00	1.4	1.7	0.3
22	11/06/2026	08:00	1.5	1.9	0.4
23	11/06/2026	09:00	1.6	1.7	0.1
24	11/06/2026	10:00	1.6	1.9	0.3
Average =			1.2	1.5	0.3
Average Difference (m/s) (Pass) =					0.25

[redacted]

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Wind Direction

Station	: Ban Don Mot Tanoi	Date	: 10-11 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 11:00-11:00 (24 Hr)

Wind Direction (Station)

Brand	: LSI LASTEM	Model	: DNA 821
Method	: Wind Direction Sensor	Serial No.	: 24090146

Wind Direction (Reference Instrument)

Brand	: Young Wind Monitor	Model	: 05103
Method	: Wind Direction Sensor	Serial No.	: 68983

Data	Date	Time	Wind Direction (Station) (degree)	Wind Direction (Ref.) (degree)	Difference (degree)
1	10/06/2026	11:00	238	245	7
2	10/06/2026	12:00	190	195	5
3	10/06/2026	13:00	191	194	3
4	10/06/2026	14:00	169	174	5
5	10/06/2026	15:00	207	210	3
6	10/06/2026	16:00	117	116	-1
7	10/06/2026	17:00	152	150	-2
8	10/06/2026	18:00	161	167	6
9	10/06/2026	19:00	170	168	-2
10	10/06/2026	20:00	179	173	-6
11	10/06/2026	21:00	177	182	5
12	10/06/2026	22:00	183	185	2
13	10/06/2026	23:00	198	194	-4
14	11/06/2026	00:00	228	229	1
15	11/06/2026	01:00	207	205	-2
16	11/06/2026	02:00	199	202	3
17	11/06/2026	03:00	162	167	5
18	11/06/2026	04:00	103	109	6
19	11/06/2026	05:00	171	178	7
20	11/06/2026	06:00	165	173	8
21	11/06/2026	07:00	175	180	5
22	11/06/2026	08:00	193	197	4
23	11/06/2026	09:00	167	172	5
24	11/06/2026	10:00	182	189	7
		Average =	179	181	3
			Average Difference (degree) (Pass) =		2.92

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Air Temperature

Station	: Ban Don Mot Tanoi	Date	: 10-11 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 11:00-11:00 (24 Hr)

Air Temperature (Station)

Brand	: LSI LASTEM	Model	: DMA 875
Method	: Temperature Sensor	Serial No.	: 24090275

Air Temperature (Reference Instrument)

Brand	: NRG Systems (Weather Station)	Model	: LR20 (110S)
Method	: Temperature Sensor	Serial No.	: 30905581 (T001-19)

Data	Date	Time	Air Temp. (Station) (°C)	Air Temp. (Ref.) (°C)	Difference (°C)
1	10/06/2026	11:00	34.2	34.6	0.4
2	10/06/2026	12:00	34.1	34.4	0.3
3	10/06/2026	13:00	35.3	35.3	0.0
4	10/06/2026	14:00	35.1	35.4	0.3
5	10/06/2026	15:00	25.9	26.0	0.1
6	10/06/2026	16:00	24.3	24.5	0.2
7	10/06/2026	17:00	25.2	25.1	-0.1
8	10/06/2026	18:00	25.6	25.4	-0.2
9	10/06/2026	19:00	25.7	25.3	-0.4
10	10/06/2026	20:00	25.9	25.4	-0.5
11	10/06/2026	21:00	26.0	25.7	-0.3
12	10/06/2026	22:00	26.1	25.4	-0.7
13	10/06/2026	23:00	26.0	25.8	-0.2
14	11/06/2026	00:00	25.8	25.2	-0.6
15	11/06/2026	01:00	25.7	25.8	0.1
16	11/06/2026	02:00	25.6	25.9	0.3
17	11/06/2026	03:00	25.4	25.6	0.2
18	11/06/2026	04:00	25.5	25.2	-0.3
19	11/06/2026	05:00	25.5	25.1	-0.4
20	11/06/2026	06:00	25.9	25.4	-0.5
21	11/06/2026	07:00	29.7	29.5	-0.2
22	11/06/2026	08:00	30.6	30.8	0.2
23	11/06/2026	09:00	32.5	32.9	0.4
24	11/06/2026	10:00	34.3	34.6	0.3
		Average =	28.2	28.1	-0.1
			Average Difference (°C) (Pass) =		-0.07

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69

36/10/68

Audit Results of Relative Humidity

Station	: Ban Don Mot Tanoi	Date	: 10-11 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 11:00-11:00 (24 Hr)

Relative Humidity (Station)

Brand	: LSI LASTEM	Model	: DMA 875
Method	: Relative Humidity Sensor	Serial No.	: 24090275

Relative Humidity (Reference Instrument)

Brand	: NRG Systems (Weather Station)	Model	: LR20 (RH-5X)
Method	: Relative Humidity Sensor	Serial No.	: 30905581 (RH001-19)

Data	Date	Time	Relative Humidity (Station) (%)	Relative Humidity (Ref.) (%)	Difference (%)
1	10/06/2026	11:00	56	57	1
2	10/06/2026	12:00	56	54	-2
3	10/06/2026	13:00	53	50	-3
4	10/06/2026	14:00	56	52	-4
5	10/06/2026	15:00	95	93	-2
6	10/06/2026	16:00	100	96	-4
7	10/06/2026	17:00	100	98	-2
8	10/06/2026	18:00	100	97	-3
9	10/06/2026	19:00	100	98	-2
10	10/06/2026	20:00	100	97	-3
11	10/06/2026	21:00	100	98	-2
12	10/06/2026	22:00	100	96	-4
13	10/06/2026	23:00	100	97	-3
14	11/06/2026	00:00	100	98	-2
15	11/06/2026	01:00	100	97	-3
16	11/06/2026	02:00	100	96	-4
17	11/06/2026	03:00	100	95	-5
18	11/06/2026	04:00	100	96	-4
19	11/06/2026	05:00	100	95	-5
20	11/06/2026	06:00	100	94	-6
21	11/06/2026	07:00	87	86	-1
22	11/06/2026	08:00	70	75	5
23	11/06/2026	09:00	61	68	7
24	11/06/2026	10:00	53	59	6
		Average =	87	85	-2
			Average Difference (%) (Pass) =		-1.88

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69

36/10/68

Audit Results of Barometric Pressure

Station	: Ban Don Mot Tanoi	Date	: 10-11 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 11:00-11:00 (24 Hr)

Barometric Pressure (Station)

Brand	: LSI LASTEM	Model	: DQA 801
Method	: Barometric Pressure Sensor	Serial No.	: 24070782

Barometric Pressure (Reference Instrument)

Brand	: NRG Systems (Weather Station)	Model	: LR20 (BP-20)
Method	: Relative Humidity Sensor	Serial No.	: 30905581 (180512766)

Data	Date	Time	Barometric Pressure (Station) (mbar)	Barometric Pressure (Ref.) (mbar)	Difference (mbar)
1	10/06/2026	11:00	1007.0	1006.8	-0.2
2	10/06/2026	12:00	1007.0	1006.7	-0.3
3	10/06/2026	13:00	1006.0	1006.9	0.9
4	10/06/2026	14:00	1005.0	1006.3	1.3
5	10/06/2026	15:00	1006.0	1007.4	1.4
6	10/06/2026	16:00	1005.0	1006.6	1.6
7	10/06/2026	17:00	1005.0	1006.1	1.1
8	10/06/2026	18:00	1006.0	1007.5	1.5
9	10/06/2026	19:00	1007.0	1008.4	1.4
10	10/06/2026	20:00	1008.0	1009.3	1.3
11	10/06/2026	21:00	1009.0	1010.1	1.1
12	10/06/2026	22:00	1009.0	1010.6	1.6
13	10/06/2026	23:00	1009.0	1009.5	0.5
14	11/06/2026	00:00	1008.0	1009.1	1.1
15	11/06/2026	01:00	1008.0	1008.7	0.7
16	11/06/2026	02:00	1007.0	1007.2	0.2
17	11/06/2026	03:00	1007.0	1006.8	-0.2
18	11/06/2026	04:00	1008.0	1007.5	-0.5
19	11/06/2026	05:00	1008.0	1008.4	0.4
20	11/06/2026	06:00	1009.0	1009.9	0.9
21	11/06/2026	07:00	1009.0	1010.6	1.6
22	11/06/2026	08:00	1010.0	1010.4	0.4
23	11/06/2026	09:00	1010.0	1010.7	0.7
24	11/06/2026	10:00	1010.0	1010.6	0.6
		Average =	1007.6	1008.4	0.8
			Average Difference (mbar) (Pass) =		0.80

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69

36/10/68

Audit Results of Rain Gauge			
Station	: Ban Don Mot Tanoi	Date	: 10 June 2026
Location	: 47P UTM 0601523E , 1502637N	Time	: 15:30-15:50
Rain Gauge (Station)			
Brand	: LSI LASTEM	Model	: DQA 230.1
Method	: Rain Gauge (Tipping Bucket)	Serial No.	: 24100019
Diameter	: 200 mm.	Collector Surface	: 324 cm^2


Calibrator (Volumetric Burette)

Data	Audit (Tipping Bucket A) (mL/TIP)	Audit (Tipping Bucket B) (mL/TIP)	Difference (mL/TIP)
1	6.5	6.4	0.1
2	6.4	6.6	-0.2
3	6.7	6.5	0.2
4	6.9	6.8	0.1
5	6.6	6.5	0.1
6	6.7	6.8	-0.1
7	6.9	6.7	0.2
8	6.8	6.9	-0.1
9	6.9	6.7	0.2
10	6.6	6.8	-0.2
(Average)	6.7	6.7	0.03
Average(mm/TIP) =	0.21	0.21	-
Average(mm/TIP) Total =	0.2		(Pass)


[redacted]

Site Operator

Technical Supervisor

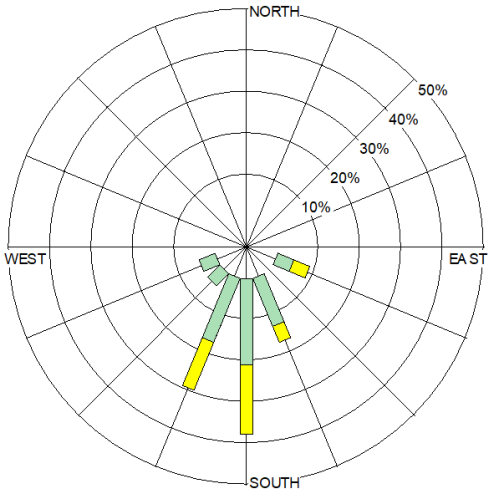

REFERENCE INSTRUMENT

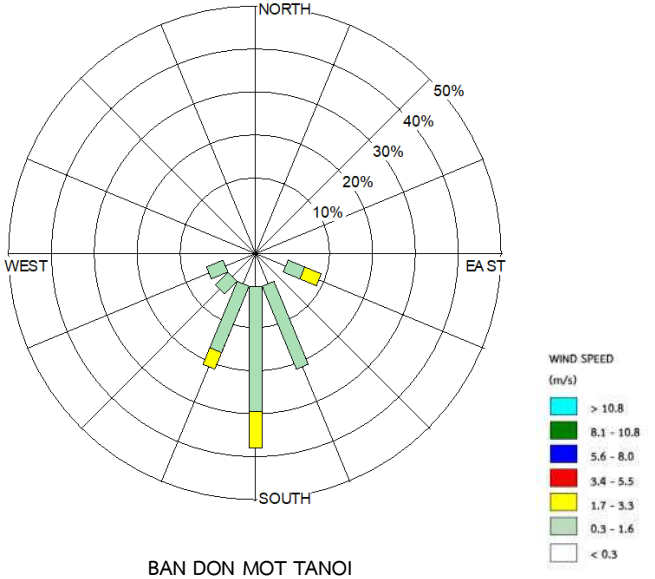

BAN DON MOT TANOI

ผังแสดงความเร็วและทิศทางลม ระหว่างวันที่ 10-11 มิถุนายน 2569

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com


BY027/06/69

36/10/68

Audit Results of NO_x Analyzer

Station	: Ban Bang Kra Do	Date	: 09 June 2026
Location	: 47P UTM 0597559E , 1509571N	Time	: 11:00-12:00
$NO-NO_2-NO_x$ Analyzer			
Brand	: Thermo Scientific	Model	: 421Q-BNAAN
Range	: 0-500 ppb	Serial No.	: 12606944593
Calibrator (Dilution System)			
Brand	: Teledyne	Model	: 700
Last Cal. Date	: 01 September 2025	Serial No.	: 911
Reference Standard Gas			
Standard Gas	: Nitric Oxide (NO)	Cylinder No.	: D878356
Expiration Date	: 21 April 2029	Cylinder Conc.	: 53.0 ppm

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	1.8	1.80	-
1	101.0	9.5	5000	103.8	2.80	2.77
2	201.0	19.0	5000	205.0	4.00	1.99
3	301.0	28.6	5000	299.0	-2.00	0.66
4	400.0	38.0	5000	401.0	1.00	0.25
Slope =	0.9936	Intercept =	2.8033	Average Difference (%) (Pass) =		1.4192
% Slope =	-0.6400	% Intercept =	0.5607	Correlation Coefficiency =		0.9999
	(Pass)		(Pass)	% Correlation Coefficiency (Pass) =		-0.0065

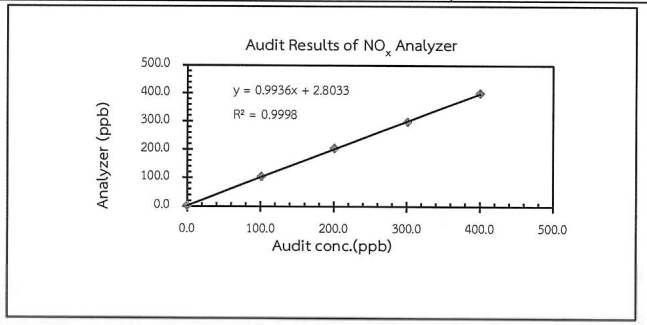

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com


BY027/06/69

36/10/68

Audit Results of SO_2 Analyzer

Station	: Ban Bang Kra Do	Date	: 09 June 2026
Location	: 47P UTM 0597559E , 1509571N	Time	: 10:00-11:00
SO_2 Analyzer			
Brand	: Thermo Scientific	Model	: 43IQ-CNA
Range	: 0-500 ppb	Serial No.	: 12434436947
Calibrator (Dilution System)			
Brand	: Teledyne	Model	: 700
Last Cal. Date	: 01 September 2025	Serial No.	: 911
Reference Standard Gas			
Standard Gas	: Sulphur Dioxide (SO_2)	Cylinder No.	: D878356
Expiration Date	: 21 April 2029	Cylinder Conc.	: 48.9 ppm

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	1.8	1.80	-
1	101.0	10.3	5000	102.5	1.50	1.49
2	201.0	20.6	5000	203.0	2.00	1.00
3	301.0	31.0	5000	303.0	2.00	0.66
4	401.0	41.3	5000	401.0	0.00	0.00
Slope =	0.9969	Intercept =	2.0807	Average Difference (%) (Pass) =		0.7862
% Slope =	-0.3100	% Intercept =	0.4161	Correlation Coefficiency =		1.0000
	(Pass)		(Pass)	% Correlation Coefficiency (Pass) =		-0.0018

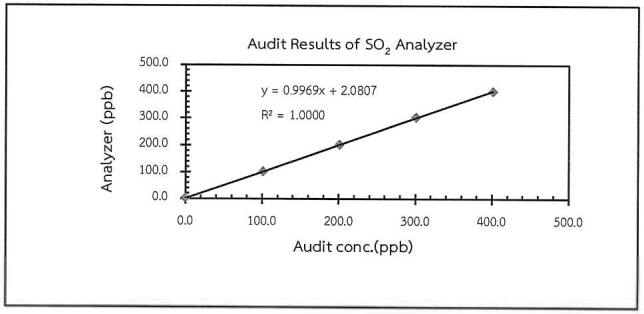

Site Operator


Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of O_3 Analyzer			
Station	: Ban Bang Kra Do	Date	: 09 June 2026
Location	: 47P UTM 0597559E , 1509571N	Time	: 10:00-11:00
O_3 Analyzer			
Brand	: Thermo Scientific	Model	: 49I-B2NAB
Range	: 0-500 ppb	Serial No.	: 1315758000
Calibrator (Ozone Gen.)			
Brand	: Teledyne	Model	: T703
Last Cal. Date	: 01 September 2025	Serial No.	: 412

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	0.2	0.20	-
1	99.0	9.9	5000	99.4	0.40	0.40
2	200.0	20.1	5000	199.6	-0.40	0.20
3	300.0	30.2	5000	302.0	2.00	0.67
4	401.0	40.4	5000	402.0	1.00	0.25
Slope =	1.0032	Intercept =	0.0026	Average Difference (%) (Pass) =		0.3800
% Slope =	0.3200 (Pass)	% Intercept =	0.0005 (Pass)	Correlation Coefficiency =		1.0000
				% Correlation Coefficiency (Pass) =		-0.0006

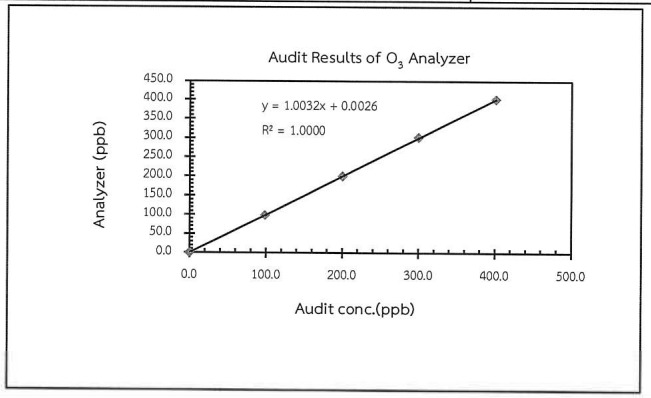

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of TSP Analyzer			
Station	: Ban Bang Kra Do	Date	: 09 June 2026
Location	: 47P UTM 0597559E , 1509571N	Time	: 14:10-14:20
TSP Analyzer			
Brand	: Thermo Scientific	Model	: 5014i (in26-004-2)
Method	: Beta Ray	Serial No.	: CM13211004
Calibrator (Dry Cal Primary Flow Meter)			
Brand	: Bios Defender	Model	: Defender 510-H
Last Cal. Date	: 12 September 2025	Serial No.	: 136164

Data	Monitor Flow Rate (Lit/min)	Audit Std. Flow Rate (Lit/min)	Difference	% Difference
1	16.7	16.68	0.02	0.11
2	16.7	16.69	0.01	0.04
3	16.7	16.67	0.03	0.17
4	16.7	16.68	0.02	0.14
5	16.7	16.67	0.03	0.19
6	16.7	16.68	0.02	0.14
7	16.7	16.67	0.04	0.21
8	16.7	16.68	0.02	0.11
9	16.7	16.67	0.03	0.17
10	16.7	16.68	0.02	0.14
Average =	16.7	16.68	0.02	0.14
		Average Difference (%) (Pass) =		0.14

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69

36/10/68

Audit Results of PM10 Analyzer			
Station : Ban Bang Kra Do		Date : 09 June 2026	
Location : 47P UTM 0597559E , 1509571N		Time : 13:50-14:00	
PM10 Analyzer			
Brand : Thermo Scientific		Model : 5014i (in26-004-1)	
Method : Beta Ray		Serial No. : CM13211003	
Calibrator (Dry Cal Primary Flow Meter)			
Brand : Bios Defender		Model : Defender 510-H	
Last Cal. Date : 12 September 2025		Serial No. : 136164	

Data	Monitor Flow Rate (Lit/min)	Audit Std. Flow Rate (Lit/min)	Difference	% Difference
1	16.7	16.67	0.03	0.17
2	16.7	16.68	0.02	0.10
3	16.7	16.65	0.05	0.33
4	16.7	16.67	0.03	0.20
5	16.7	16.66	0.04	0.26
6	16.7	16.69	0.02	0.09
7	16.7	16.68	0.02	0.11
8	16.7	16.67	0.03	0.16
9	16.7	16.68	0.02	0.15
10	16.7	16.67	0.03	0.17
Average =	16.7	16.67	0.03	0.17
		Average Difference (%) (Pass) =		0.17

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69

36/10/68

Audit Results of Wind Speed			
Station : Ban Bang Kra Do		Date : 09-10 June 2026	
Location : 47P UTM 0597559E , 1509571N		Time : 10:00-10:00 (24 Hr)	
Wind Speed (Station)			
Brand : LSI LASTEM		Model : DNA 821	
Method : Wind Speed Sensor		Serial No. : 24070540	
Wind Speed (Reference Instrument)			
Brand : Young Wind Monitor		Model : 05103	
Method : Wind Speed Sensor		Serial No. : 68983	

Data	Date	Time	Wind Speed (Station) (m/s)	Wind Speed (Ref.) (m/s)	Difference (m/s)
1	09/06/2026	10:00	2.5	2.8	0.3
2	09/06/2026	11:00	3.0	3.2	0.2
3	09/06/2026	12:00	3.3	3.6	0.3
4	09/06/2026	13:00	1.5	1.7	0.2
5	09/06/2026	14:00	1.5	1.4	-0.1
6	09/06/2026	15:00	1.3	1.5	0.2
7	09/06/2026	16:00	1.2	1.3	0.1
8	09/06/2026	17:00	1.2	1.6	0.4
9	09/06/2026	18:00	1.6	1.9	0.3
10	09/06/2026	19:00	1.4	1.6	0.2
11	09/06/2026	20:00	0.7	1.0	0.3
12	09/06/2026	21:00	0.4	0.9	0.5
13	09/06/2026	22:00	0.5	0.8	0.3
14	09/06/2026	23:00	0.4	0.7	0.3
15	10/06/2026	00:00	1.1	1.3	0.2
16	10/06/2026	01:00	0.9	1.0	0.1
17	10/06/2026	02:00	1.2	1.5	0.3
18	10/06/2026	03:00	1.9	1.8	-0.1
19	10/06/2026	04:00	1.5	1.9	0.4
20	10/06/2026	05:00	0.9	1.2	0.3
21	10/06/2026	06:00	0.6	1.0	0.4
22	10/06/2026	07:00	1.1	1.3	0.2
23	10/06/2026	08:00	1.5	1.8	0.3
24	10/06/2026	09:00	1.8	1.9	0.1
		Average =	1.4	1.6	0.2
			Average Difference (m/s) (Pass) =		0.24

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Wind Direction

Station	: Ban Bang Kra Do	Date	: 09-10 June 2026
Location	: 47P UTM 0597559E , 1509571N	Time	: 10:00-10:00 (24 Hr)
Wind Direction (Station)			
Brand	: LSI LASTEM	Model	: DNA 821
Method	: Wind Direction Sensor	Serial No.	: 24070540
Wind Direction (Reference Instrument)			
Brand	: Young Wind Monitor	Model	: 05103
Method	: Wind Direction Sensor	Serial No.	: 68983

Data	Date	Time	Wind Direction (Station) (degree)	Wind Direction (Ref.) (degree)	Difference (degree)
1	09/06/2026	10:00	202	205	3
2	09/06/2026	11:00	240	247	7
3	09/06/2026	12:00	227	225	-2
4	09/06/2026	13:00	275	278	3
5	09/06/2026	14:00	55	60	5
6	09/06/2026	15:00	124	131	7
7	09/06/2026	16:00	161	167	6
8	09/06/2026	17:00	244	248	4
9	09/06/2026	18:00	180	178	-2
10	09/06/2026	19:00	130	125	-5
11	09/06/2026	20:00	318	311	-7
12	09/06/2026	21:00	218	220	2
13	09/06/2026	22:00	212	215	3
14	09/06/2026	23:00	242	246	4
15	10/06/2026	00:00	231	238	7
16	10/06/2026	01:00	209	210	1
17	10/06/2026	02:00	188	192	4
18	10/06/2026	03:00	155	160	5
19	10/06/2026	04:00	149	150	1
20	10/06/2026	05:00	100	105	5
21	10/06/2026	06:00	316	315	-1
22	10/06/2026	07:00	220	215	-5
23	10/06/2026	08:00	151	153	2
24	10/06/2026	09:00	180	185	5
		Average =	197	199	2
		Average Difference (degree) (Pass) =			2.17

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Air Temperature

Station	: Ban Bang Kra Do	Date	: 09-10 June 2026
Location	: 47P UTM 0597559E , 1509571N	Time	: 10:00-10:00 (24 Hr)
Air Temperature (Station)			
Brand	: LSI LASTEM	Model	: DMA 875
Method	: Temperature Sensor	Serial No.	: 24090281
Air Temperature (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (110S)
Method	: Temperature Sensor	Serial No.	: 30905581 (T001-19)

Data	Date	Time	Air Temp. (Station) (°C)	Air Temp. (Ref.) (°C)	Difference (°C)
1	09/06/2026	10:00	33.0	33.4	0.4
2	09/06/2026	11:00	33.7	33.5	-0.2
3	09/06/2026	12:00	32.2	32.8	0.6
4	09/06/2026	13:00	28.1	28.6	0.5
5	09/06/2026	14:00	29.4	29.7	0.3
6	09/06/2026	15:00	29.6	30.1	0.5
7	09/06/2026	16:00	29.9	30.3	0.4
8	09/06/2026	17:00	30.1	30.4	0.3
9	09/06/2026	18:00	29.7	30.4	0.7
10	09/06/2026	19:00	29.1	29.5	0.4
11	09/06/2026	20:00	28.3	28.8	0.5
12	09/06/2026	21:00	28.3	28.7	0.4
13	09/06/2026	22:00	28.4	29.0	0.6
14	09/06/2026	23:00	28.0	28.7	0.7
15	10/06/2026	00:00	27.9	28.2	0.3
16	10/06/2026	01:00	27.5	28.1	0.6
17	10/06/2026	02:00	27.3	27.8	0.5
18	10/06/2026	03:00	27.2	27.8	0.6
19	10/06/2026	04:00	26.9	27.3	0.4
20	10/06/2026	05:00	26.5	27.0	0.5
21	10/06/2026	06:00	26.7	27.1	0.4
22	10/06/2026	07:00	28.8	29.0	0.2
23	10/06/2026	08:00	30.6	30.4	-0.2
24	10/06/2026	09:00	32.4	32.7	0.3
		Average =	29.2	29.6	0.4
		Average Difference (°C) (Pass) =			0.40

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Relative Humidity			
Station	: Ban Bang Kra Do	Date	: 09-10 June 2026
Location	: 47P UTM 0597559E , 1509571N	Time	: 10:00-10:00 (24 Hr)
Relative Humidity (Station)			
Brand	: LSI LASTEM	Model	: DMA 875
Method	: Relative Humidity Sensor	Serial No.	: 24090281
Relative Humidity (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (RH-5X)
Method	: Relative Humidity Sensor	Serial No.	: 30905581 (RH001-19)

Data	Date	Time	Relative Humidity (Station) (%)	Relative Humidity (Ref.) * (%)	Difference (%)
1	09/06/2026	10:00	61	60	-1
2	09/06/2026	11:00	57	54	-3
3	09/06/2026	12:00	64	67	3
4	09/06/2026	13:00	88	83	-5
5	09/06/2026	14:00	85	92	7
6	09/06/2026	15:00	84	82	-2
7	09/06/2026	16:00	83	87	4
8	09/06/2026	17:00	77	84	7
9	09/06/2026	18:00	75	81	6
10	09/06/2026	19:00	84	90	6
11	09/06/2026	20:00	89	93	4
12	09/06/2026	21:00	90	91	1
13	09/06/2026	22:00	88	86	-2
14	09/06/2026	23:00	90	87	-3
15	10/06/2026	00:00	87	85	-2
16	10/06/2026	01:00	88	90	2
17	10/06/2026	02:00	92	93	1
18	10/06/2026	03:00	87	90	3
19	10/06/2026	04:00	87	93	6
20	10/06/2026	05:00	89	90	1
21	10/06/2026	06:00	90	92	2
22	10/06/2026	07:00	79	84	5
23	10/06/2026	08:00	71	75	4
24	10/06/2026	09:00	62	67	5
		Average =	81	83	2
			Average Difference (%) (Pass) =		2.04

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Barometric Pressure			
Station	: Ban Bang Kra Do	Date	: 09-10 June 2026
Location	: 47P UTM 0597559E , 1509571N	Time	: 10:00-10:00 (24 Hr)
Barometric Pressure (Station)			
Brand	: LSI LASTEM	Model	: DQA 801
Method	: Barometric Pressure Sensor	Serial No.	: 24070783
Barometric Pressure (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (BP-20)
Method	: Relative Humidity Sensor	Serial No.	: 30905581 (180512766)

Data	Date	Time	Barometric Pressure (Station) (mbar)	Barometric Pressure (Ref.) (mbar)	Difference (mbar)
1	09/06/2026	10:00	1007.0	1008.2	1.2
2	09/06/2026	11:00	1007.0	1008.5	1.5
3	09/06/2026	12:00	1006.0	1007.8	1.8
4	09/06/2026	13:00	1006.0	1006.5	0.5
5	09/06/2026	14:00	1005.0	1005.9	0.9
6	09/06/2026	15:00	1005.0	1006.2	1.2
7	09/06/2026	16:00	1004.0	1005.7	1.7
8	09/06/2026	17:00	1005.0	1006.3	1.3
9	09/06/2026	18:00	1005.0	1006.2	1.2
10	09/06/2026	19:00	1006.0	1006.5	0.5
11	09/06/2026	20:00	1006.0	1006.8	0.8
12	09/06/2026	21:00	1007.0	1006.1	-0.9
13	09/06/2026	22:00	1008.0	1007.4	-0.6
14	09/06/2026	23:00	1008.0	1007.9	-0.1
15	10/06/2026	00:00	1007.0	1007.5	0.5
16	10/06/2026	01:00	1006.0	1006.6	0.6
17	10/06/2026	02:00	1006.0	1006.4	0.4
18	10/06/2026	03:00	1005.0	1006.1	1.1
19	10/06/2026	04:00	1005.0	1005.7	0.7
20	10/06/2026	05:00	1005.0	1005.9	0.9
21	10/06/2026	06:00	1006.0	1006.5	0.5
22	10/06/2026	07:00	1008.0	1007.8	-0.2
23	10/06/2026	08:00	1008.0	1008.4	0.4
24	10/06/2026	09:00	1008.0	1008.5	0.5
		Average =	1006.2	1006.9	0.7
			Average Difference (mbar) (Pass) =		0.68

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Rain Gauge			
Station	: Ban Bang Kra Do	Date	: 09 June 2026
Location	: 47P UTM 0597559E , 1509571N	Time	: 13:10-13:30
Rain Gauge (Station)			
Brand	: LSI LASTEM	Model	: DQA 230.1
Method	: Rain Gauge (Tipping Bucket)	Serial No.	: 21120166
Diameter	: 200 mm.	Collector Surface	: 324 cm^2


Calibrator (Volumetric Burette)

Data	Audit (Tipping Bucket A) (mL/TIP)	Audit (Tipping Bucket B) (mL/TIP)	Difference (mL/TIP)
1	6.9	7.0	-0.1
2	6.8	6.7	0.1
3	6.9	7.0	-0.1
4	6.8	6.6	0.2
5	7.0	6.9	0.1
6	6.9	6.7	0.2
7	7.0	6.8	0.2
8	6.9	6.7	0.2
9	6.8	6.9	-0.1
10	6.7	6.8	-0.1
(Average)	6.9	6.8	0.06
Average(mm/TIP) =	0.21	0.21	-
Average(mm/TIP) Total =	0.2		(Pass)


[redacted]

Site Operator

Technical Supervisor

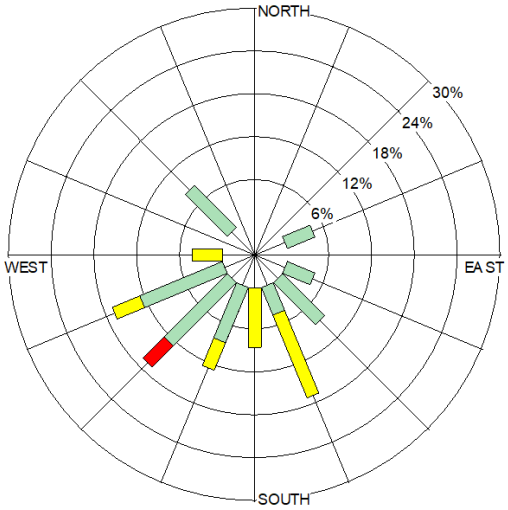

REFERENCE INSTRUMENT

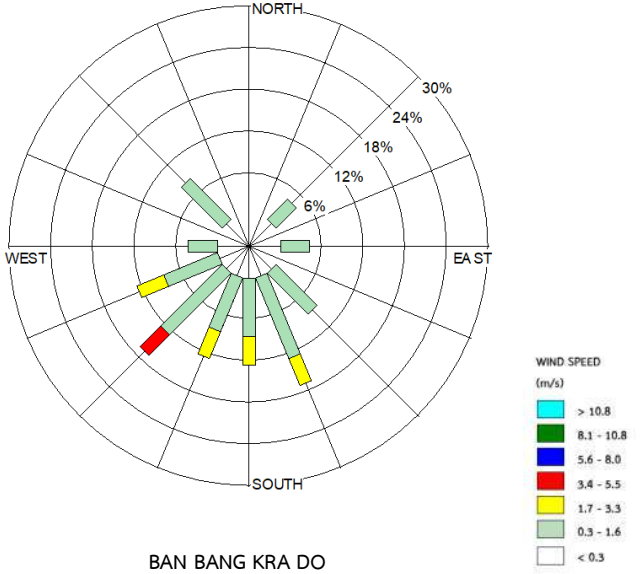

BAN BANG KRA DO


ผังแสดงความเร็วและทิศทางลม ระหว่างวันที่ 9-10 มิถุนายน 2569

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of NO_x Analyzer			
Station	: Ban Khlong khae	Date	: 11 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 11:00-12:00
$NO-NO_2-NO_x$ Analyzer			
Brand	: Thermo Scientific	Model	: 42IQ-BNAAN
Range	: 0-500 ppb	Serial No.	: 12521842312
Calibrator (Dilution System)			
Brand	: Teledyne	Model	: 700
Last Cal. Date	: 01 September 2025	Serial No.	: 911
Reference Standard Gas			
Standard Gas	: Nitric Oxide (NO)	Cylinder No.	: D878356
Expiration Date	: 21 April 2029	Cylinder Conc.	: 53.0 ppm

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	1.5	1.50	-
1	100.0	9.5	5000	100.1	0.10	0.10
2	200.0	18.9	5000	199.8	-0.20	0.10
3	300.0	28.5	5000	301.0	1.00	0.33
4	400.0	38.0	5000	399.0	-1.00	0.25
Slope =	0.9959	Intercept =	1.1000	Average Difference (%) (Pass) =		0.1958
% Slope =	-0.4100	% Intercept =	0.2200	Correlation Coefficiency =		1.0000
	(Pass)		(Pass)	% Correlation Coefficiency (Pass) =		-0.0009

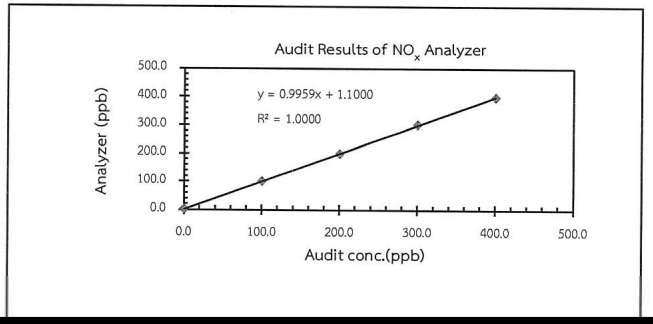

[redacted]

Site Operator


Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of SO_2 Analyzer			
Station	: Ban Khlong khae	Date	: 11 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 10:00-11:00
SO_2 Analyzer			
Brand	: Thermo Scientific	Model	: 43IQ-BNA
Range	: 0-500 ppb	Serial No.	: 12521842313
Calibrator (Dilution System)			
Brand	: Teledyne	Model	: 700
Last Cal. Date	: 01 September 2025	Serial No.	: 911
Reference Standard Gas			
Standard Gas	: Sulphur Dioxide (SO_2)	Cylinder No.	: D878356
Expiration Date	: 21 April 2029	Cylinder Conc.	: 48.9 ppm

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	1.5	1.50	-
1	100.0	10.2	5000	102.4	2.40	2.40
2	200.0	20.5	5000	201.0	1.00	0.50
3	300.0	30.9	5000	302.0	2.00	0.67
4	400.0	41.2	5000	401.0	1.00	0.25
Slope =	0.9986	Intercept =	1.8600	Average Difference (%) (Pass) =		0.9542
% Slope =	-0.1400	% Intercept =	0.3720	Correlation Coefficiency =		1.0000
	(Pass)		(Pass)	% Correlation Coefficiency (Pass) =		-0.0014

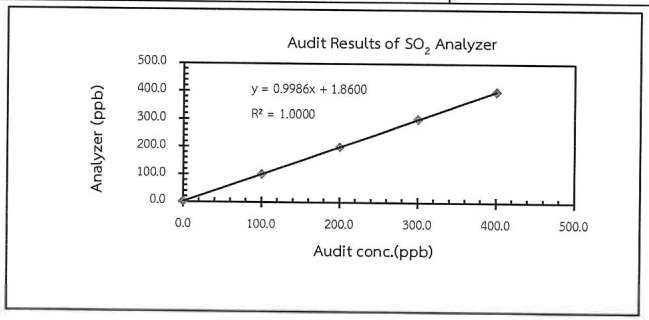

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003


บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of O_3 Analyzer

Station	: Ban Khlong khae	Date	: 11 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 10:00-11:00
O_3 Analyzer			
Brand	: Thermo Scientific	Model	: 49I-B2NCA
Range	: 0-500 ppb	Serial No.	: 1162850019
Calibrator (Ozone Gen.)			
Brand	: Teledyne	Model	: T703
Last Cal. Date	: 01 September 2025	Serial No.	: 412

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	0.6	0.60	-
1	100.0	10.0	5000	101.8	1.80	1.80
2	200.0	20.1	5000	200.0	0.00	0.00
3	300.0	30.2	5000	301.0	1.00	0.33
4	400.0	40.3	5000	403.0	3.00	0.75
Slope =	1.0040	Intercept =	0.4800	Average Difference (%) (Pass) =		0.7208
% Slope =	0.4000 (Pass)	% Intercept =	0.0960 (Pass)	Correlation Coefficiency =		1.0000
				% Correlation Coefficiency (Pass) =		-0.0010

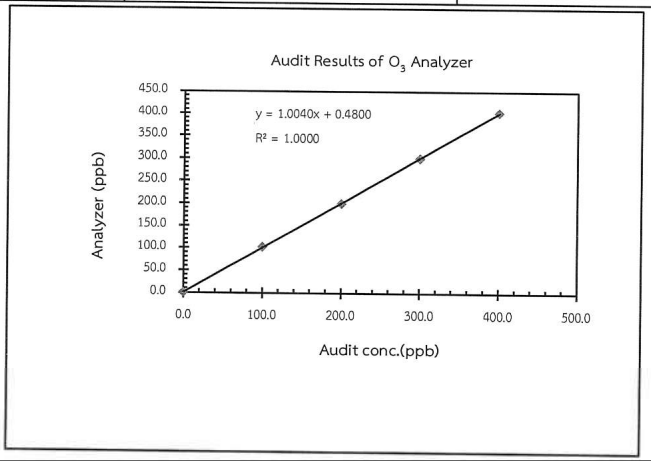

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of TSP Analyzer

Station	: Ban Khlong khae	Date	: 11 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 14:00-14:10
TSP Analyzer			
Brand	: Thermo Scientific	Model	: 5014i/5030i
Method	: Beta Ray	Serial No.	: CM16461001
Calibrator (Dry Cal Primary Flow Meter)			
Brand	: Bios Defender	Model	: Defender 510-H
Last Cal. Date	: 12 September 2025	Serial No.	: 136164

Data	Monitor Flow Rate (Lit/min)	Audit Std. Flow Rate (Lit/min)	Difference	% Difference
1	16.7	16.81	-0.11	-0.66
2	16.7	16.78	-0.08	-0.45
3	16.7	16.72	-0.02	-0.13
4	16.7	16.75	-0.05	-0.31
5	16.7	16.80	-0.10	-0.61
6	16.7	16.76	-0.06	-0.35
7	16.7	16.78	-0.08	-0.49
8	16.7	16.75	-0.05	-0.32
9	16.7	16.72	-0.02	-0.14
10	16.7	16.74	-0.04	-0.26
Average =	16.7	16.76	-0.06	-0.37
		Average Difference (%) (Pass) =		-0.37

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of PM10 Analyzer			
Station	: Ban Khlong khae	Date	: 11 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 13:40-13:50
PM10 Analyzer			
Brand	: Thermo Scientific	Model	: 5014i/5030i
Method	: Beta Ray	Serial No.	: CM16471014
Calibrator (Dry Cal Primary Flow Meter)			
Brand	: Bios Defender	Model	: Defender 510-H
Last Cal. Date	: 12 September 2025	Serial No.	: 136164

Data	Monitor Flow Rate (Lit/min)	Audit Std. Flow Rate (Lit/min)	Difference	% Difference
1	16.7	16.72	-0.02	-0.13
2	16.7	16.71	-0.01	-0.08
3	16.7	16.73	-0.03	-0.20
4	16.7	16.68	0.02	0.11
5	16.7	16.69	0.01	0.05
6	16.7	16.67	0.03	0.16
7	16.7	16.71	-0.01	-0.07
8	16.7	16.68	0.02	0.11
9	16.7	16.74	-0.04	-0.26
10	16.7	16.76	-0.06	-0.37
Average =	16.7	16.71	-0.01	-0.07
		Average Difference (%) (Pass) =		-0.07

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Wind Speed			
Station	: Ban Khlong khae	Date	: 11-12 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 12:00-12:00 (24 Hr)
Wind Speed (Station)			
Brand	: LSI LASTEM	Model	: DNA 821
Method	: Wind Speed Sensor	Serial No.	: 24070534
Wind Speed (Reference Instrument)			
Brand	: Young Wind Monitor	Model	: 05103
Method	: Wind Direction Sensor	Serial No.	: 68983

Data	Date	Time	Wind Speed (Station) (m/s)	Wind Speed (Ref.) (m/s)	Difference (m/s)
1	11/06/2026	12:00	2.2	2.4	0.2
2	11/06/2026	13:00	1.6	1.9	0.3
3	11/06/2026	14:00	2.7	2.8	0.1
4	11/06/2026	15:00	2.3	2.5	0.2
5	11/06/2026	16:00	1.3	1.6	0.3
6	11/06/2026	17:00	1.4	1.8	0.4
7	11/06/2026	18:00	0.7	0.9	0.2
8	11/06/2026	19:00	1.0	1.3	0.3
9	11/06/2026	20:00	1.3	1.5	0.2
10	11/06/2026	21:00	2.4	2.3	-0.1
11	11/06/2026	22:00	2.6	2.4	-0.2
12	11/06/2026	23:00	1.5	1.6	0.1
13	12/06/2026	00:00	0.5	0.9	0.4
14	12/06/2026	01:00	1.2	1.5	0.3
15	12/06/2026	02:00	1.7	1.9	0.2
16	12/06/2026	03:00	0.9	1.2	0.3
17	12/06/2026	04:00	1.1	1.5	0.4
18	12/06/2026	05:00	1.2	1.7	0.5
19	12/06/2026	06:00	1.6	1.8	0.2
20	12/06/2026	07:00	1.3	1.9	0.6
21	12/06/2026	08:00	2.7	3.0	0.3
22	12/06/2026	09:00	2.5	2.6	0.1
23	12/06/2026	10:00	2.1	2.4	0.3
24	12/06/2026	11:00	1.6	2.0	0.4
		Average =	1.6	1.9	0.3
			Average Difference (m/s) (Pass) =		0.25

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Wind Direction

Station	: Ban Khlong khae	Date	: 11-12 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 12:00-12:00 (24 Hr)
Wind Direction (Station)			
Brand	: LSI LASTEM	Model	: DNA 821
Method	: Wind Direction Sensor	Serial No.	: 24070534
Wind Direction (Reference Instrument)			
Brand	: Young Wind Monitor	Model	: 05103
Method	: Wind Direction Sensor	Serial No.	: 68983

Data	Date	Time	Wind Direction (Station) (degree)	Wind Direction (Ref.) (degree)	Difference (degree)
1	11/06/2026	12:00	229	225	-4
2	11/06/2026	13:00	168	170	2
3	11/06/2026	14:00	181	185	4
4	11/06/2026	15:00	154	157	3
5	11/06/2026	16:00	145	146	1
6	11/06/2026	17:00	155	157	2
7	11/06/2026	18:00	146	150	4
8	11/06/2026	19:00	78	80	2
9	11/06/2026	20:00	150	151	1
10	11/06/2026	21:00	206	209	3
11	11/06/2026	22:00	200	205	5
12	11/06/2026	23:00	182	178	-4
13	12/06/2026	00:00	79	85	6
14	12/06/2026	01:00	221	219	-2
15	12/06/2026	02:00	208	205	-3
16	12/06/2026	03:00	217	223	6
17	12/06/2026	04:00	224	227	3
18	12/06/2026	05:00	188	190	2
19	12/06/2026	06:00	216	220	4
20	12/06/2026	07:00	209	212	3
21	12/06/2026	08:00	196	195	-1
22	12/06/2026	09:00	201	208	7
23	12/06/2026	10:00	186	190	4
24	12/06/2026	11:00	228	233	5
		Average =	182	184	2
		Average Difference (degree) (Pass) =			2.21

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Air Temperature

Station	: Ban Khlong khae	Date	: 11-12 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 12:00-12:00 (24 Hr)
Air Temperature (Station)			
Brand	: LSI LASTEM	Model	: DMA 875
Method	: Temperature Sensor	Serial No.	: 24090284
Air Temperature (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (110S)
Method	: Temperature Sensor	Serial No.	: 30905581 (T001-19)

Data	Date	Time	Air Temp. (Station) (°C)	Air Temp. (Ref.) (°C)	Difference (°C)
1	11/06/2026	12:00	34.0	34.3	0.3
2	11/06/2026	13:00	34.4	34.6	0.2
3	11/06/2026	14:00	33.2	33.8	0.6
4	11/06/2026	15:00	26.6	26.9	0.3
5	11/06/2026	16:00	25.0	25.7	0.7
6	11/06/2026	17:00	25.2	25.4	0.2
7	11/06/2026	18:00	25.5	26.0	0.5
8	11/06/2026	19:00	25.5	25.8	0.3
9	11/06/2026	20:00	25.7	25.9	0.2
10	11/06/2026	21:00	26.3	26.7	0.4
11	11/06/2026	22:00	26.4	26.6	0.2
12	11/06/2026	23:00	26.1	26.8	0.7
13	12/06/2026	00:00	25.8	26.0	0.2
14	12/06/2026	01:00	26.2	26.5	0.3
15	12/06/2026	02:00	26.1	26.7	0.6
16	12/06/2026	03:00	26.0	26.3	0.3
17	12/06/2026	04:00	25.9	26.0	0.1
18	12/06/2026	05:00	25.9	26.4	0.5
19	12/06/2026	06:00	26.1	26.7	0.6
20	12/06/2026	07:00	27.6	27.8	0.2
21	12/06/2026	08:00	29.7	30.4	0.7
22	12/06/2026	09:00	30.9	31.2	0.3
23	12/06/2026	10:00	32.5	32.9	0.4
24	12/06/2026	11:00	33.7	33.5	-0.2
		Average =	27.9	28.3	0.4
		Average Difference (°C) (Pass) =			0.36

(Kitti Chualwan)
Site Operator

(Peera Detudom)
Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Relative Humidity

Station	: Ban Khlong khae	Date	: 11-12 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 12:00-12:00 (24 Hr)
Relative Humidity (Station)			
Brand	: LSI LASTEM	Model	: DMA 875
Method	: Relative Humidity Sensor	Serial No.	: 24090284
Relative Humidity (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (RH-5X)
Method	: Relative Humidity Sensor	Serial No.	: 30905581 (RH001-19)

Data	Date	Time	Relative Humidity (Station) (%)	Relative Humidity (Ref.) (%)	Difference (%)
1	11/06/2026	12:00	55	60	5
2	11/06/2026	13:00	56	63	7
3	11/06/2026	14:00	63	62	-1
4	11/06/2026	15:00	91	94	3
5	11/06/2026	16:00	95	97	2
6	11/06/2026	17:00	97	95	-2
7	11/06/2026	18:00	97	98	1
8	11/06/2026	19:00	97	95	-2
9	11/06/2026	20:00	97	97	0
10	11/06/2026	21:00	95	94	-1
11	11/06/2026	22:00	93	97	4
12	11/06/2026	23:00	94	96	2
13	12/06/2026	00:00	96	97	1
14	12/06/2026	01:00	95	94	-1
15	12/06/2026	02:00	96	97	1
16	12/06/2026	03:00	96	95	-1
17	12/06/2026	04:00	97	98	1
18	12/06/2026	05:00	97	96	-1
19	12/06/2026	06:00	96	94	-2
20	12/06/2026	07:00	88	92	4
21	12/06/2026	08:00	75	81	6
22	12/06/2026	09:00	69	73	4
23	12/06/2026	10:00	62	65	3
24	12/06/2026	11:00	57	59	2
		Average =	86	87	1
			Average Difference (%) (Pass) =		1.46

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Barometric Pressure

Station	: Ban Khlong khae	Date	: 11-12 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 12:00-12:00 (24 Hr)
Barometric Pressure (Station)			
Brand	: LSI LASTEM	Model	: DQA 801
Method	: Barometric Pressure Sensor	Serial No.	: 24070781
Barometric Pressure (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (BP-20)
Method	: Relative Humidity Sensor	Serial No.	: 30905581 (180512766)

Data	Date	Time	Barometric Pressure (Station) (mbar)	Barometric Pressure (Ref.) (mbar)	Difference (mbar)
1	11/06/2026	12:00	1009.0	1009.5	0.5
2	11/06/2026	13:00	1008.0	1009.3	1.3
3	11/06/2026	14:00	1007.0	1008.1	1.1
4	11/06/2026	15:00	1007.0	1008.7	1.7
5	11/06/2026	16:00	1008.0	1008.4	0.4
6	11/06/2026	17:00	1008.0	1008.6	0.6
7	11/06/2026	18:00	1009.0	1009.2	0.2
8	11/06/2026	19:00	1009.0	1009.7	0.7
9	11/06/2026	20:00	1010.0	1010.5	0.5
10	11/06/2026	21:00	1011.0	1010.8	-0.2
11	11/06/2026	22:00	1012.0	1011.4	-0.6
12	11/06/2026	23:00	1012.0	1011.2	-0.8
13	12/06/2026	00:00	1011.0	1010.7	-0.3
14	12/06/2026	01:00	1010.0	1010.3	0.3
15	12/06/2026	02:00	1010.0	1010.4	0.4
16	12/06/2026	03:00	1011.0	1011.2	0.2
17	12/06/2026	04:00	1011.0	1010.5	-0.5
18	12/06/2026	05:00	1011.0	1010.3	-0.7
19	12/06/2026	06:00	1011.0	1011.2	0.2
20	12/06/2026	07:00	1012.0	1011.5	-0.5
21	12/06/2026	08:00	1012.0	1010.9	-1.1
22	12/06/2026	09:00	1012.0	1011.3	-0.7
23	12/06/2026	10:00	1012.0	1011.7	-0.3
24	12/06/2026	11:00	1011.0	1010.6	-0.4
		Average =	1010.2	1010.3	0.1
				Average Difference (mbar) (Pass) =	0.08

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Rain Gauge			
Station	: Ban Khlong khae	Date	: 11 June 2026
Location	: 47P UTM 0591646E , 1496895N	Time	: 13:10-13:30
Rain Gauge (Station)			
Brand	: LSI LASTEM	Model	: DOA 230.1
Method	: Rain Gauge (Tipping Bucket)	Serial No.	: 24100021
Diameter	: 200 mm.	Collector Surface	: 324 cm^2


Calibrator (Volumetric Burette)

Data	Audit (Tipping Bucket A) (mL/TIP)	Audit (Tipping Bucket B) (mL/TIP)	Difference (mL/TIP)
1	7.1	7.0	0.1
2	7.0	6.8	0.2
3	7.1	6.9	0.2
4	6.9	6.8	0.1
5	6.8	6.9	-0.1
6	6.7	6.6	0.1
7	6.8	6.9	-0.1
8	7.0	6.8	0.2
9	6.9	6.7	0.2
10	7.0	6.9	0.1
(Average)	6.9	6.8	0.10
Average(mm/TIP) =	0.21	0.21	-
Average(mm/TIP) Total =	0.2		(Pass)


[redacted]

Site Operator

Technical Supervisor

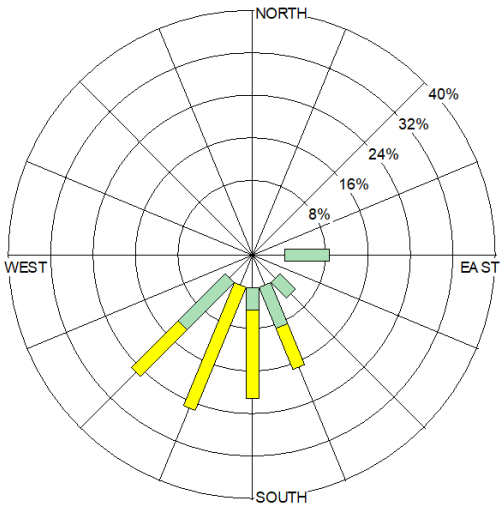

REFERENCE INSTRUMENT

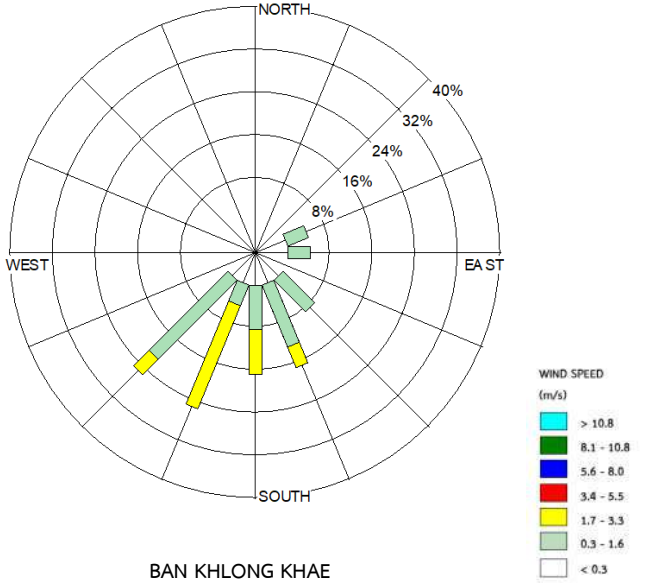

BAN KHLONG KHAE


ผังแสดงความเร็วและทิศทางลม ระหว่างวันที่ 11-12 มิถุนายน 2569

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of NO_x Analyzer			
Station : Ban Chao Nuea		Date : 08 June 2026	
Location : 47P UTM 0597517E , 1503683N		Time : 14:30-15:30	
$NO-NO_2-NO_x$ Analyzer			
Brand : Thermo Scientific		Model : 42I-BZMSDAA	
Range : 0-500 ppb		Serial No. : CM23367032	
Calibrator (Dilution System)			
Brand : Teledyne		Model : 700	
Last Cal. Date : 01 September 2025		Serial No. : 911	
Reference Standard Gas			
Standard Gas : Nitric Oxide (NO)		Cylinder No. : D878356	
Expiration Date : 21 April 2029		Cylinder Conc. : 53.0 ppm	

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	1.8	1.80	-
1	99.0	9.4	5000	99.6	0.60	0.61
2	200.0	18.9	5000	200.0	0.00	0.00
3	300.0	28.5	5000	302.0	2.00	0.67
4	400.0	38.0	5000	399.0	-1.00	0.25
Slope =	0.9958	Intercept =	1.5173	Average Difference (%) (Pass) =		0.3807
% Slope =	-0.4200	% Intercept =	0.3035	Correlation Coefficiency =		1.0000
	(Pass)		(Pass)	% Correlation Coefficiency (Pass) =		-0.0019

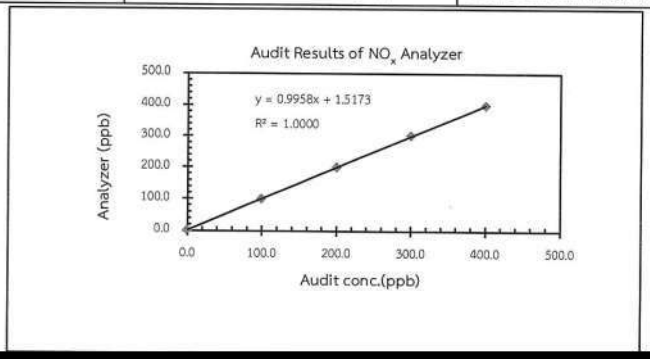

[redacted]

Site Operator


Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of SO_2 Analyzer			
Station : Ban Chao Nuea		Date : 08 June 2026	
Location : 47P UTM 0597517E , 1503683N		Time : 13:30-14:30	
SO_2 Analyzer			
Brand : Thermo Scientific		Model : 43IQ-BNA	
Range : 0-500 ppb		Serial No. : 12606944594	
Calibrator (Dilution System)			
Brand : Teledyne		Model : 700	
Last Cal. Date : 01 September 2025		Serial No. : 911	
Reference Standard Gas			
Standard Gas : Sulphur Dioxide (SO_2)		Cylinder No. : D878356	
Expiration Date : 21 April 2029		Cylinder Conc. : 48.9 ppm	

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	1.2	1.20	-
1	101.0	10.3	5000	102.5	1.50	1.49
2	201.0	20.6	5000	202.0	1.00	0.50
3	301.0	31.0	5000	304.0	3.00	1.00
4	400.0	41.2	5000	399.0	-1.00	0.25
Slope =	0.9971	Intercept =	1.7176	Average Difference (%) (Pass) =		0.8073
% Slope =	-0.2900	% Intercept =	0.3435	Correlation Coefficiency =		1.0000
	(Pass)		(Pass)	% Correlation Coefficiency (Pass) =		-0.0027

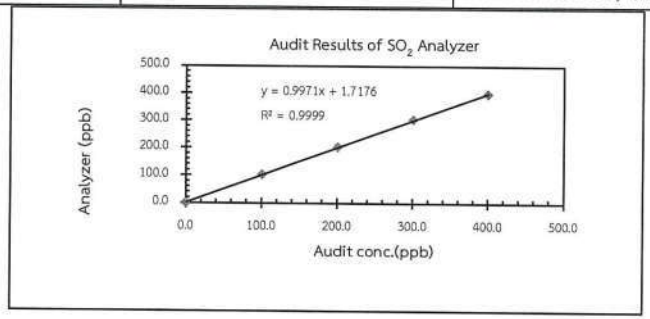

Site Operator


Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of O_3 Analyzer			
Station	: Ban Chao Nuea	Date	: 08 June 2026
Location	: 47P UTM 0597517E , 1503683N	Time	: 13:30-14:30
O_3 Analyzer			
Brand	: Thermo Scientific	Model	: 49I-B2NAB
Range	: 0-500 ppb	Serial No.	: 1315757999
Calibrator (Ozone Gen.)			
Brand	: Teledyne	Model	: T703
Last Cal. Date	: 01 September 2025	Serial No.	: 412

Point No	Calibrator Setting (Standard Condition)			Analyzer Response/ Recording Data		
	Audit conc. [x]	Gas Flow	Zero Air Flow	Analyzer [Y]	Output Difference	
	(ppb)	(ml/min)	(ml/min)	(ppb)	(ppb)	(%)
ZERO	0.0	-	5000	0.5	0.50	-
1	100.0	10.0	5000	99.2	-0.80	0.80
2	200.0	20.1	5000	199.4	-0.60	0.30
3	300.0	30.2	5000	299.0	-1.00	0.33
4	400.0	40.3	5000	399.0	-1.00	0.25
Slope =	0.9968	Intercept =	0.0600	Average Difference (%) (Pass) =		0.4208
% Slope =	-0.3200	% Intercept =	0.0120	Correlation Coefficiency =		1.0000
	(Pass)		(Pass)	% Correlation Coefficiency (Pass) =		-0.0001

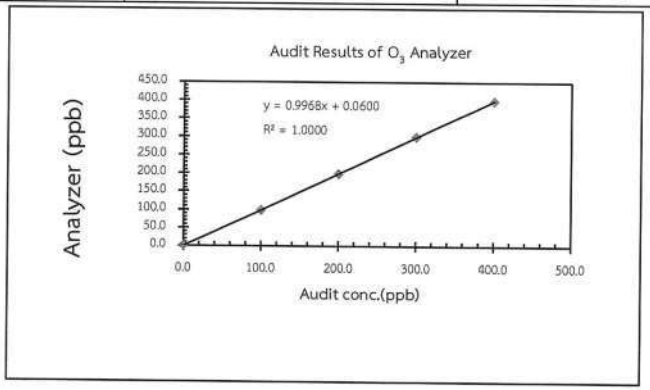

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of TSP Analyzer			
Station	: Ban Chao Nuea	Date	: 08 June 2026
Location	: 47P UTM 0597517E , 1503683N	Time	: 13:10-13:20
TSP Analyzer			
Brand	: Thermo Scientific	Model	: 5014i-B8CAA
Method	: Beta Ray	Serial No.	: CM24438002
Calibrator (Dry Cal Primary Flow Meter)			
Brand	: Bios Defender	Model	: Defender 510-H
Last Cal. Date	: 12 September 2025	Serial No.	: 136164

Data	Monitor Flow Rate (Lit/min)	Audit Std. Flow Rate (Lit/min)	Difference	% Difference
1	16.7	16.69	0.01	0.05
2	16.7	16.68	0.02	0.10
3	16.7	16.69	0.01	0.05
4	16.7	16.67	0.03	0.17
5	16.7	16.69	0.02	0.09
6	16.7	16.68	0.02	0.14
7	16.7	16.69	0.01	0.08
8	16.7	16.66	0.04	0.25
9	16.7	16.68	0.02	0.10
10	16.7	16.67	0.03	0.20
Average =	16.7	16.68	0.02	0.12
		Average Difference (%) (Pass) =		0.12

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of PM10 Analyzer			
Station	: Ban Chao Nuea	Date	: 08 June 2026
Location	: 47P UTM 0597517E , 1503683N	Time	: 13:30-13:40
PM10 Analyzer			
Brand	: Thermo Scientific	Model	: 5014i-BBEAA
Method	: Beta Ray	Serial No.	: CM24438001
Calibrator (Dry Cal Primary Flow Meter)			
Brand	: Bios Defender	Model	: Defender 510-H
Last Cal. Date	: 12 September 2025	Serial No.	: 136164

Data	Monitor Flow Rate (Lit/min)	Audit Std. Flow Rate (Lit/min)	Difference	% Difference
1	16.7	16.65	0.05	0.29
2	16.7	16.66	0.04	0.22
3	16.7	16.65	0.05	0.28
4	16.7	16.67	0.03	0.17
5	16.7	16.68	0.02	0.10
6	16.7	16.69	0.01	0.08
7	16.7	16.68	0.02	0.13
8	16.7	16.67	0.03	0.17
9	16.7	16.68	0.02	0.13
10	16.7	16.66	0.04	0.23
Average =	16.7	16.67	0.03	0.18
		Average Difference (%) (Pass) =		0.18

[redacted]

Site Operator

[redacted] (Peera Detudom)
Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Wind Speed			
Station	: Ban Chao Nuea	Date	: 08-09 June 2026
Location	: 47P UTM 0597517E , 1503683N	Time	: 14:00-14:00 (24 Hr)
Wind Speed (Station)			
Brand	: LSI LASTEM	Model	: DNA 821
Method	: Wind Speed Sensor	Serial No.	: -
Wind Speed (Reference Instrument)			
Brand	: Young Wind Monitor	Model	: 05103
Method	: Wind Speed Sensor	Serial No.	: 57243

Data	Date	Time	Wind Speed (Station) (m/s)	Wind Speed (Ref.) (m/s)	Difference (m/s)
1	08/06/2026	14:00	1.6	2.0	0.4
2	08/06/2026	15:00	1.1	1.3	0.2
3	08/06/2026	16:00	1.1	1.4	0.3
4	08/06/2026	17:00	1.1	1.5	0.4
5	08/06/2026	18:00	1.2	1.1	-0.1
6	08/06/2026	19:00	1.0	1.4	0.4
7	08/06/2026	20:00	0.6	0.9	0.3
8	08/06/2026	21:00	0.7	0.5	-0.2
9	08/06/2026	22:00	0.5	0.8	0.3
10	08/06/2026	23:00	0.3	0.4	0.1
11	09/06/2026	00:00	0.3	0.5	0.2
12	09/06/2026	01:00	0.6	1.0	0.4
13	09/06/2026	02:00	0.6	0.9	0.3
14	09/06/2026	03:00	1.0	1.1	0.1
15	09/06/2026	04:00	0.8	1.0	0.2
16	09/06/2026	05:00	0.5	0.4	-0.1
17	09/06/2026	06:00	1.0	1.3	0.3
18	09/06/2026	07:00	1.4	1.2	-0.2
19	09/06/2026	08:00	1.4	1.5	0.1
20	09/06/2026	09:00	1.5	1.7	0.2
21	09/06/2026	10:00	2.1	2.4	0.3
22	09/06/2026	11:00	2.0	2.5	0.5
23	09/06/2026	12:00	1.7	2.1	0.4
24	09/06/2026	13:00	1.2	1.3	0.1
		Average =	1.1	1.3	0.2
			Average Difference (m/s) (Pass) =		0.20

[redacted]

Site Operator

[redacted] (Peera Detudom)
Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69

36/10/68

Audit Results of Wind Direction

Station	: Ban Chao Nuea	Date	: 08-09 June 2026
Location	: 47P UTM 0597517E , 1503683N	Time	: 14:00-14:00 (24 Hr)
Wind Direction (Station)			
Brand	: LASTEM	Model	: DNA 821
Method	: Wind Direction Sensor	Serial No.	: -
Wind Direction (Reference Instrument)			
Brand	: Young Wind Monitor	Model	: 05103
Method	: Wind Speed Sensor	Serial No.	: 57243

Data	Date	Time	Wind Direction (Station) (degree)	Wind Direction (Ref.) (degree)	Difference (degree)
1	08/06/2026	14:00	70	77	7
2	08/06/2026	15:00	153	158	5
3	08/06/2026	16:00	166	165	-1
4	08/06/2026	17:00	167	174	7
5	08/06/2026	18:00	174	179	5
6	08/06/2026	19:00	176	180	4
7	08/06/2026	20:00	161	167	6
8	08/06/2026	21:00	155	150	-5
9	08/06/2026	22:00	181	186	5
10	08/06/2026	23:00	247	242	-5
11	09/06/2026	00:00	123	129	6
12	09/06/2026	01:00	164	167	3
13	09/06/2026	02:00	179	183	4
14	09/06/2026	03:00	170	173	3
15	09/06/2026	04:00	176	175	-1
16	09/06/2026	05:00	186	187	1
17	09/06/2026	06:00	183	189	6
18	09/06/2026	07:00	181	188	7
19	09/06/2026	08:00	190	192	2
20	09/06/2026	09:00	167	171	4
21	09/06/2026	10:00	203	205	2
22	09/06/2026	11:00	228	225	-3
23	09/06/2026	12:00	120	127	7
24	09/06/2026	13:00	336	330	-6
		Average =	177	180	3
			Average Difference (degree) (Pass) =		2.63

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69

36/10/68

Audit Results of Air Temperature

Station	: Ban Chao Nuea	Date	: 08-09 June 2026
Location	: 47P UTM 0597517E , 1503683N	Time	: 14:00-14:00 (24 Hr)
Air Temperature (Station)			
Brand	: LASTEM	Model	: DMA 875
Method	: Temperature Sensor	Serial No.	: -
Air Temperature (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (110S)
Method	: Temperature Sensor	Serial No.	: 428007169 (T002-19)

Data	Date	Time	Air Temp. (Station) (°C)	Air Temp. (Ref.) (°C)	Difference (°C)
1	08/06/2026	14:00	26.8	26.5	-0.3
2	08/06/2026	15:00	28.7	28.6	-0.1
3	08/06/2026	16:00	30.5	30.3	-0.2
4	08/06/2026	17:00	30.5	30.5	0.0
5	08/06/2026	18:00	29.7	29.9	0.2
6	08/06/2026	19:00	28.9	29.0	0.1
7	08/06/2026	20:00	28.4	28.7	0.3
8	08/06/2026	21:00	28.2	28.6	0.4
9	08/06/2026	22:00	28.0	28.5	0.5
10	08/06/2026	23:00	27.5	27.8	0.3
11	09/06/2026	00:00	27.2	27.9	0.7
12	09/06/2026	01:00	27.1	27.0	-0.1
13	09/06/2026	02:00	27.0	27.4	0.4
14	09/06/2026	03:00	26.7	26.8	0.1
15	09/06/2026	04:00	26.4	26.6	0.2
16	09/06/2026	05:00	26.2	26.9	0.7
17	09/06/2026	06:00	26.6	26.7	0.1
18	09/06/2026	07:00	29.1	29.5	0.4
19	09/06/2026	08:00	31.1	31.3	0.2
20	09/06/2026	09:00	33.1	32.8	-0.3
21	09/06/2026	10:00	34.8	34.6	-0.2
22	09/06/2026	11:00	34.4	34.3	-0.1
23	09/06/2026	12:00	29.7	30.1	0.4
24	09/06/2026	13:00	29.1	29.7	0.6
		Average =	29.0	29.2	0.2
			Average Difference (°C) (Pass) =		0.18

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

Audit Results of Relative Humidity			
Station	: Ban Chao Nuea	Date	: 08-09 June 2026
Location	: 47P UTM 0597517E , 1503683N	Time	: 14:00-14:00 (24 Hr)
Relative Humidity (Station)			
Brand	: LASTEM	Model	: DMA 875
Method	: Relative Humidity Sensor	Serial No.	: -
Relative Humidity (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (RH-5X)
Method	: Relative Humidity Sensor	Serial No.	: 428007169 (RH002-19)

Data	Date	Time	Relative Humidity (Station) (%)	Relative Humidity (Ref.) (%)	Difference (%)
1	08/06/2026	14:00	100	96	-4
2	08/06/2026	15:00	100	97	-3
3	08/06/2026	16:00	99	95	-4
4	08/06/2026	17:00	99	96	-3
5	08/06/2026	18:00	99	94	-5
6	08/06/2026	19:00	100	96	-4
7	08/06/2026	20:00	100	97	-3
8	08/06/2026	21:00	100	96	-4
9	08/06/2026	22:00	100	95	-5
10	08/06/2026	23:00	100	96	-4
11	09/06/2026	00:00	100	97	-3
12	09/06/2026	01:00	100	95	-5
13	09/06/2026	02:00	100	94	-6
14	09/06/2026	03:00	100	96	-4
15	09/06/2026	04:00	100	97	-3
16	09/06/2026	05:00	100	95	-5
17	09/06/2026	06:00	100	94	-6
18	09/06/2026	07:00	98	93	-5
19	09/06/2026	08:00	84	90	6
20	09/06/2026	09:00	69	74	5
21	09/06/2026	10:00	58	60	2
22	09/06/2026	11:00	58	64	6
23	09/06/2026	12:00	93	95	2
24	09/06/2026	13:00	99	96	-3
		Average =	94	92	-2
			Average Difference (%) (Pass) =		-2.42

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Barometric Pressure			
Station	: Ban Chao Nuea	Date	: 08-09 June 2026
Location	: 47P UTM 0597517E , 1503683N	Time	: 14:00-14:00 (24 Hr)
Barometric Pressure (Station)			
Brand	: LASTEM	Model	: DQA 801
Method	: Barometric Pressure Sensor	Serial No.	: -
Barometric Pressure (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (BP-20)
Method	: Barometric Pressure Sensor	Serial No.	: 428007169 (180512766)

Data	Date	Time	Barometric Pressure (Station) (mbar)	Barometric Pressure (Ref.) (mbar)	Difference (mbar)
1	08/06/2026	14:00	1004.0	1005.1	1.1
2	08/06/2026	15:00	1004.0	1004.5	0.5
3	08/06/2026	16:00	1003.0	1003.8	0.8
4	08/06/2026	17:00	1003.0	1004.6	1.6
5	08/06/2026	18:00	1004.0	1005.2	1.2
6	08/06/2026	19:00	1004.0	1004.5	0.5
7	08/06/2026	20:00	1005.0	1005.9	0.9
8	08/06/2026	21:00	1006.0	1006.8	0.8
9	08/06/2026	22:00	1006.0	1006.4	0.4
10	08/06/2026	23:00	1006.0	1006.5	0.5
11	09/06/2026	00:00	1006.0	1005.8	-0.2
12	09/06/2026	01:00	1005.0	1005.3	0.3
13	09/06/2026	02:00	1005.0	1005.7	0.7
14	09/06/2026	03:00	1004.0	1004.9	0.9
15	09/06/2026	04:00	1004.0	1004.5	0.5
16	09/06/2026	05:00	1004.0	1004.7	0.7
17	09/06/2026	06:00	1004.0	1005.2	1.2
18	09/06/2026	07:00	1005.0	1004.8	-0.2
19	09/06/2026	08:00	1006.0	1005.4	-0.6
20	09/06/2026	09:00	1006.0	1006.3	0.3
21	09/06/2026	10:00	1006.0	1006.7	0.7
22	09/06/2026	11:00	1005.0	1005.8	0.8
23	09/06/2026	12:00	1005.0	1004.7	-0.3
24	09/06/2026	13:00	1004.0	1005.5	1.5
		Average =	1004.8	1005.4	0.6
				Average Difference (mbar) (Pass) =	0.61

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69

36/10/68


Audit Results of Rain Gauge			
Station	: Ban Chao Nuea	Date	: 08 June 2026
Location	: 47P UTM 0597517E , 1503683N	Time	: 14:20-14:40
Rain Gauge (Station)			
Brand	: LSI LASTEM	Model	: DQA 230.1
Method	: Rain Gauge (Tipping Bucket)	Serial No.	: -
Diameter	: 200 mm.	Collector Surface	: 324 cm^2
Calibrator (Volumetric Burette)			

Data	Audit (Tipping Bucket A) (mL/TIP)	Audit (Tipping Bucket B) (mL/TIP)	Difference (mL/TIP)
1	7.0	7.1	-0.1
2	7.1	7.0	0.1
3	7.0	7.1	-0.1
4	6.9	6.7	0.2
5	7.0	6.9	0.1
6	6.8	6.8	0.0
7	6.9	7.0	-0.1
8	7.0	6.8	0.2
9	7.1	6.9	0.2
10	6.9	6.8	0.1
(Average)	7.0	6.9	0.06
Average(mm/TIP) =	0.22	0.21	-
Average(mm/TIP) Total =	0.2		(Pass)


[redacted]

Site Operator

Technical Supervisor

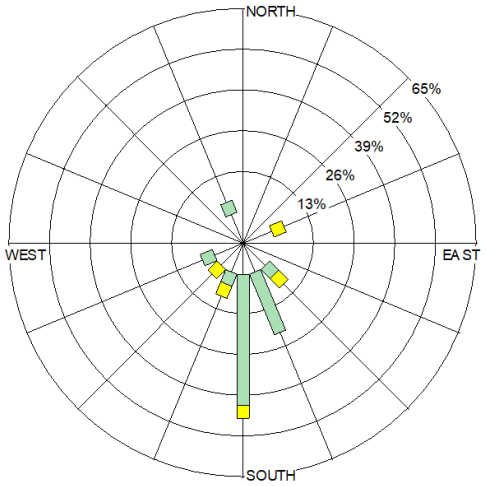

REFERENCE INSTRUMENT

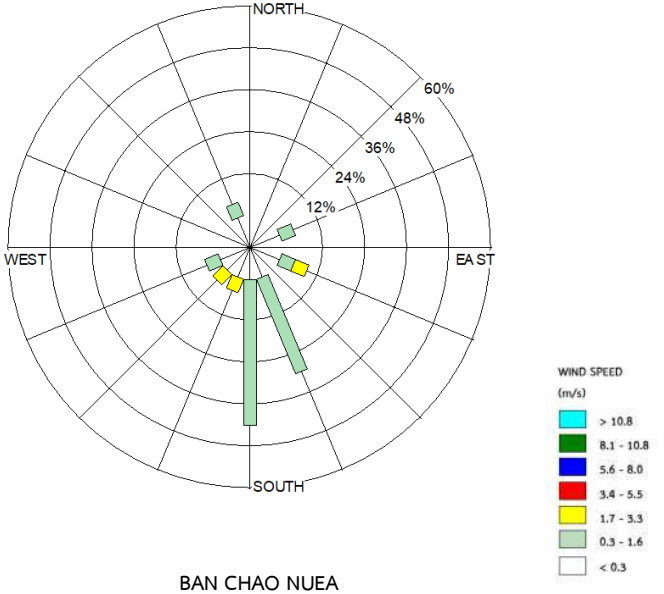

BAN CHAO NUEA

ผังแสดงความเร็วและทิศทางลม ระหว่างวันที่ 8-9 มิถุนายน 2569

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/6/69
36/10/68

Audit Results of Wind Speed

Station	: Meteorological Station	Date	: 10-11 June 2026
Location	: 47P UTM 0596024E , 1503443N	Time	: 13:00-13:00 (24 Hr)

Wind Speed (Station)

Brand	: LSI LASTEM	Model	: DNA-827
Method	: Wind Speed Sensor	Serial No.	: -

Wind Speed (Reference Instrument)

Brand	: Young Wind Monitor	Model	: 05103
Method	: Wind Speed Sensor	Serial No.	: 57243

Data	Date	Time	Wind Speed (Station) (m/s)	Wind Speed (Ref.) (m/s)	Difference (m/s)
1	10/06/2026	13:00	2.8	2.6	-0.2
2	10/06/2026	14:00	3.0	3.1	0.1
3	10/06/2026	15:00	2.8	3.0	0.2
4	10/06/2026	16:00	1.3	1.7	0.4
5	10/06/2026	17:00	0.6	0.9	0.3
6	10/06/2026	18:00	0.6	0.8	0.2
7	10/06/2026	19:00	1.2	1.5	0.3
8	10/06/2026	20:00	1.7	1.5	-0.2
9	10/06/2026	21:00	0.8	1.0	0.2
10	10/06/2026	22:00	0.9	0.7	-0.2
11	10/06/2026	23:00	1.1	1.3	0.2
12	11/06/2026	00:00	0.4	0.7	0.3
13	11/06/2026	01:00	0.7	1.1	0.4
14	11/06/2026	02:00	1.1	0.9	-0.2
15	11/06/2026	03:00	0.8	0.7	-0.1
16	11/06/2026	04:00	0.5	0.6	0.1
17	11/06/2026	05:00	0.3	0.5	0.2
18	11/06/2026	06:00	0.6	0.9	0.3
19	11/06/2026	07:00	1.6	1.8	0.2
20	11/06/2026	08:00	1.8	2.2	0.4
21	11/06/2026	09:00	1.7	2.0	0.3
22	11/06/2026	10:00	1.6	1.5	-0.1
23	11/06/2026	11:00	2.1	2.3	0.2
24	11/06/2026	12:00	1.7	2.1	0.4
		Average =	1.3	1.5	0.2
			Average Difference (m/s) (Pass) =		0.15

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/6/69
36/10/68

Audit Results of Wind Direction

Station	: Meteorological Station	Date	: 10-11 June 2026
Location	: 47P UTM 0596024E , 1503443N	Time	: 13:00-13:00 (24 Hr)

Wind Direction (Station)

Brand	: LSI LASTEM	Model	: DNA-827
Method	: Wind Direction Sensor	Serial No.	: -

Wind Direction (Reference Instrument)

Brand	: Young Wind Monitor	Model	: 05103
Method	: Wind Speed Sensor	Serial No.	: 57243

Data	Date	Time	Wind Direction (Station) (degree)	Wind Direction (Ref.) (degree)	Difference (degree)
1	10/06/2026	13:00	186	190	4
2	10/06/2026	14:00	227	230	3
3	10/06/2026	15:00	141	148	7
4	10/06/2026	16:00	102	107	5
5	10/06/2026	17:00	156	150	-6
6	10/06/2026	18:00	164	167	3
7	10/06/2026	19:00	164	160	-4
8	10/06/2026	20:00	178	175	-3
9	10/06/2026	21:00	173	173	0
10	10/06/2026	22:00	185	182	-3
11	10/06/2026	23:00	196	190	-6
12	11/06/2026	00:00	212	216	4
13	11/06/2026	01:00	188	185	-3
14	11/06/2026	02:00	188	182	-6
15	11/06/2026	03:00	164	171	7
16	11/06/2026	04:00	92	95	3
17	11/06/2026	05:00	146	152	6
18	11/06/2026	06:00	164	160	-4
19	11/06/2026	07:00	171	175	4
20	11/06/2026	08:00	165	170	5
21	11/06/2026	09:00	135	137	2
22	11/06/2026	10:00	172	178	6
23	11/06/2026	11:00	194	190	-4
24	11/06/2026	12:00	136	140	4
		Average =	167	168	1
			Average Difference (degree) (Pass) =		1.00

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/6/69

36/10/68

Audit Results of Air Temperature

Station	: Meteorological Station	Date	: 10-11 June 2026
Location	: 47P UTM 0596024E , 1503443N	Time	: 13:00-13:00 (24 Hr)
Air Temperature (Station)			
Brand	: LSI LASTEM	Model	: DMA-875
Method	: Temperature Sensor	Serial No.	: -
Air Temperature (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (110S)
Method	: Temperature Sensor	Serial No.	: 428007169 (T002-19)

Data	Date	Time	Air Temp. (Station) (°C)	Air Temp. (Ref.) (°C)	Difference (°C)
1	10/06/2026	13:00	34.7	34.3	-0.4
2	10/06/2026	14:00	32.6	32.4	-0.2
3	10/06/2026	15:00	25.1	25.6	0.5
4	10/06/2026	16:00	24.5	25.1	0.6
5	10/06/2026	17:00	25.2	25.7	0.5
6	10/06/2026	18:00	25.7	26.4	0.7
7	10/06/2026	19:00	26.2	26.8	0.6
8	10/06/2026	20:00	26.3	26.7	0.4
9	10/06/2026	21:00	26.3	26.8	0.5
10	10/06/2026	22:00	26.3	26.5	0.2
11	10/06/2026	23:00	26.4	26.9	0.5
12	11/06/2026	00:00	26.6	27.0	0.4
13	11/06/2026	01:00	26.4	26.7	0.3
14	11/06/2026	02:00	26.2	26.4	0.2
15	11/06/2026	03:00	26.1	26.7	0.6
16	11/06/2026	04:00	26.0	26.5	0.5
17	11/06/2026	05:00	26.0	26.7	0.7
18	11/06/2026	06:00	26.2	26.8	0.6
19	11/06/2026	07:00	28.5	28.8	0.3
20	11/06/2026	08:00	30.0	29.7	-0.3
21	11/06/2026	09:00	31.7	31.3	-0.4
22	11/06/2026	10:00	33.0	32.8	-0.2
23	11/06/2026	11:00	33.4	33.7	0.3
24	11/06/2026	12:00	32.8	33.2	0.4
		Average =	28.0	28.3	0.3
				Average Difference (°C) (Pass)	

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/6/69

36/10/68

Audit Results of Relative Humidity

Station	: Meteorological Station	Date	: 10-11 June 2026
Location	: 47P UTM 0596024E , 1503443N	Time	: 13:00-13:00 (24 Hr)
Relative Humidity (Station)			
Brand	: LSI LASTEM	Model	: DMA-875
Method	: Relative Humidity Sensor	Serial No.	: -
Relative Humidity (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (RH-5X)
Method	: Relative Humidity Sensor	Serial No.	: 428007169 (RH002-19)

Data	Date	Time	Relative Humidity (Station) (%)	Relative Humidity (Ref.) (%)	Difference (%)
1	10/06/2026	13:00	57	59	2
2	10/06/2026	14:00	69	68	-1
3	10/06/2026	15:00	99	94	-5
4	10/06/2026	16:00	99	95	-4
5	10/06/2026	17:00	99	96	-3
6	10/06/2026	18:00	99	95	-4
7	10/06/2026	19:00	99	97	-2
8	10/06/2026	20:00	99	96	-3
9	10/06/2026	21:00	99	95	-4
10	10/06/2026	22:00	99	96	-3
11	10/06/2026	23:00	99	95	-4
12	11/06/2026	00:00	99	97	-2
13	11/06/2026	01:00	99	96	-3
14	11/06/2026	02:00	99	97	-2
15	11/06/2026	03:00	99	95	-4
16	11/06/2026	04:00	99	96	-3
17	11/06/2026	05:00	99	95	-4
18	11/06/2026	06:00	99	94	-5
19	11/06/2026	07:00	99	93	-6
20	11/06/2026	08:00	88	90	2
21	11/06/2026	09:00	71	74	3
22	11/06/2026	10:00	61	62	1
23	11/06/2026	11:00	58	64	6
24	11/06/2026	12:00	62	65	3
		Average =	90	88	-2
				Average Difference (%) (Pass)	

[redacted]

Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/6/69
36/10/68

Audit Results of Barometric Pressure			
Station	: Meteorological Station	Date	: 10-11 June 2026
Location	: 47P UTM 0596024E , 1503443N	Time	: 13:00-13:00 (24 Hr)
Barometric Pressure (Station)			
Brand	: LSI LASTEM	Model	: -
Method	: Barometric Pressure Sensor	Serial No.	: CP1512199
Barometric Pressure (Reference Instrument)			
Brand	: NRG Systems (Weather Station)	Model	: LR20 (BP-20)
Method	: Barometric Pressure Sensor	Serial No.	: 428007169 (180512766)

Data	Date	Time	Barometric Pressure (Station) (mbar)	Barometric Pressure (Ref.) (mbar)	Difference (mbar)
1	10/06/2026	13:00	1008.0	1008.5	0.5
2	10/06/2026	14:00	1007.0	1007.6	0.6
3	10/06/2026	15:00	1008.0	1008.8	0.8
4	10/06/2026	16:00	1008.0	1007.9	-0.1
5	10/06/2026	17:00	1008.0	1008.2	0.2
6	10/06/2026	18:00	1008.0	1008.4	0.4
7	10/06/2026	19:00	1009.0	1009.2	0.2
8	10/06/2026	20:00	1010.0	1010.4	0.4
9	10/06/2026	21:00	1010.0	1010.6	0.6
10	10/06/2026	22:00	1011.0	1011.2	0.2
11	10/06/2026	23:00	1010.0	1010.9	0.9
12	11/06/2026	00:00	1010.0	1010.4	0.4
13	11/06/2026	01:00	1010.0	1010.8	0.8
14	11/06/2026	02:00	1009.0	1009.6	0.6
15	11/06/2026	03:00	1009.0	1009.2	0.2
16	11/06/2026	04:00	1009.0	1009.8	0.8
17	11/06/2026	05:00	1010.0	1010.1	0.1
18	11/06/2026	06:00	1010.0	1010.7	0.7
19	11/06/2026	07:00	1011.0	1010.5	-0.5
20	11/06/2026	08:00	1011.0	1010.8	-0.2
21	11/06/2026	09:00	1011.0	1011.2	0.2
22	11/06/2026	10:00	1011.0	1011.4	0.4
23	11/06/2026	11:00	1011.0	1010.7	-0.3
24	11/06/2026	12:00	1010.0	1010.5	0.5
		Average =	1009.5	1009.9	0.4
			Average Difference (mbar) (Pass) =		0.35

[redacted]

Site Operator

Technical Supervisor

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel: (662) 939-4370 (Automatic 5 Lines) Fax: (662) 513-4221 E-mail: sale@spscon.com

BY027/06/69
36/10/68

Audit Results of Rain Gauge			
Station	: Meteorological Station	Date	: 10 June 2026
Location	: 47P UTM 0596024E , 1503443N	Time	: 14:00-14:20
Rain Gauge (Station)			
Brand	: LSI LASTEM	Model	: DQA 130#C
Method	: Rain Gauge (Tipping Bucket)	Serial No.	: -
Diameter	: 200 mm.	Collector Surface	: 324 cm^2


Calibrator (Volumetric Burette)			
Data	Audit (Tipping Bucket A) (mL/TIP)	Audit (Tipping Bucket B) (mL/TIP)	Difference (mL/TIP)
1	7.0	6.9	0.1
2	6.9	7.1	-0.2
3	7.0	6.8	0.2
4	6.8	6.9	-0.1
5	7.0	6.8	0.2
6	7.1	7.0	0.1
7	6.9	6.8	0.1
8	7.1	6.9	0.2
9	6.8	7.0	-0.2
10	6.9	6.8	0.1
(Average)	7.0	6.9	0.05
Average(mm/TIP) =	0.21	0.21	-
Average(mm/TIP) Total =	0.2		(Pass)

[redacted]


Site Operator

Technical Supervisor

FRS01/10-11-15/R024/Audit(AAQMS)2003

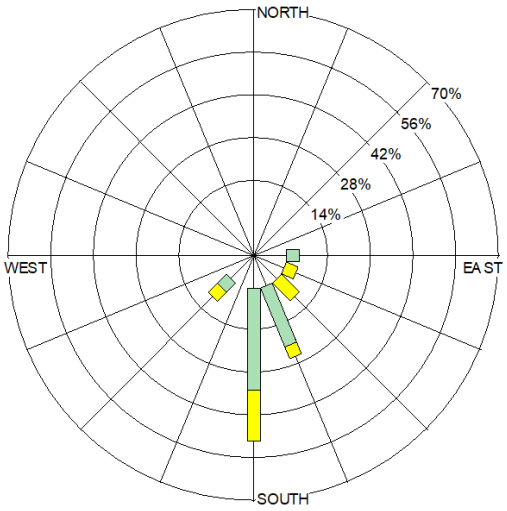

REFERENCE INSTRUMENT

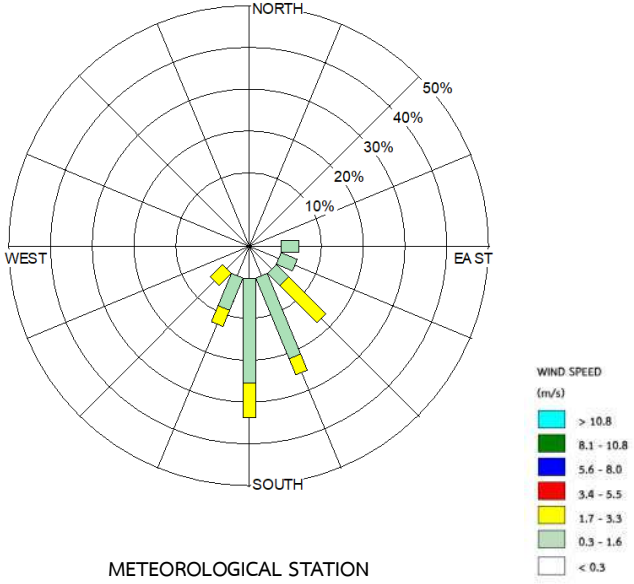

METEOROLOGICAL STATION

ผังแสดงความเร็วและทิศทางลม ระหว่างวันที่ 10-11 มิถุนายน 2569

เอกสารแนบที่ 3-3

ใบรายงานผลการตรวจวัดระดับเสียงในบรรยากาศ

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY008/02/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2569
วันที่ตรวจวัด : 3-10 กุมภาพันธ์ 2569
วันที่ออกรายงาน : 13 กุมภาพันธ์ 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

เวลา	บริเวณบ้านสามเรือน เดือนกุมภาพันธ์ 2569								ค่ามาตรฐาน
	วันที่ 3-4		วันที่ 4-5		วันที่ 5-6		วันที่ 6-7		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
12:00-13:00	61.8	56.7	55.2	53.4	61.6	59.3	58.8	54.0	-
13:00-14:00	66.2	55.6	63.8	55.8	65.5	56.0	60.2	51.2	-
14:00-15:00	59.6	50.5	62.2	59.3	60.3	59.3	53.5	48.9	-
15:00-16:00	51.3	51.0	65.4	55.6	65.6	63.0	55.3	51.3	-
16:00-17:00	65.2	44.1	68.4	52.1	69.4	57.1	57.9	51.2	-
17:00-18:00	66.0	43.0	53.3	41.5	62.1	46.1	57.1	56.5	-
18:00-19:00	51.6	40.1	45.7	40.8	49.5	42.1	63.6	59.8	-
19:00-20:00	43.8	40.6	41.7	41.4	43.1	41.2	60.7	43.3	-
20:00-21:00	43.5	42.2	42.8	41.2	42.7	40.8	44.5	41.0	-
21:00-22:00	47.5	41.5	46.1	41.7	42.6	40.9	41.6	41.2	-
22:00-23:00	47.8	40.5	42.0	41.0	41.2	41.0	42.8	41.9	-
23:00-00:00	46.9	40.1	44.4	41.5	47.8	43.7	42.7	41.6	-
00:00-01:00	46.5	41.8	45.5	44.2	49.8	41.1	44.4	42.5	-
01:00-02:00	41.8	41.6	54.1	41.4	46.9	41.6	44.7	42.3	-
02:00-03:00	50.2	41.5	47.0	43.9	43.3	43.0	45.9	42.7	-
03:00-04:00	47.5	46.5	50.8	46.1	49.1	45.9	46.4	42.6	-
04:00-05:00	54.7	45.8	56.2	50.1	52.0	50.2	49.3	45.8	-
05:00-06:00	56.8	43.4	59.5	50.0	56.4	51.7	53.4	48.2	-
06:00-07:00	58.7	46.5	56.1	55.6	58.3	54.7	57.2	53.2	-
07:00-08:00	60.2	45.1	62.5	56.4	61.6	56.3	59.4	56.8	-
08:00-09:00	61.6	44.2	63.3	55.0	68.4	54.4	67.0	58.5	-
09:00-10:00	62.4	44.4	60.7	54.9	59.2	55.4	65.0	63.1	-
10:00-11:00	63.7	44.3	61.6	55.1	61.3	53.5	69.3	61.2	-
11:00-12:00	62.0	41.3	61.3	55.5	60.2	52.7	62.6	60.2	-
L_{eq} 24 hr [dB(A)]	60.0	-	60.2	-	61.4	-	60.6	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	43.4	-	50.0	-	50.2	-	48.9	-	-
L_{max} [dB(A)]	107.5	-	110.7	-	108.4	-	109.8	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	62.3	-	62.7	-	63.0	-	61.8	-	-
-	Sound Level Meter Data								-
	Calibrate Sheet No.: Noise B 037/26				02 February 2026				
	SLM No.		Brand		Model		Serial No.		
	ST-C1-B10		SCARLET		ST-12D		10351483		
	Actual Reading [dB]								
	Before Adjustment				After Adjustment				
	93.9				93.9				

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น
ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์
13 / 02 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY008/02/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2567
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

วันที่ตรวจวัด : 3-10 กุมภาพันธ์ 2569
วันที่ออกรายงาน : 13 กุมภาพันธ์ 2569

เวลา	บริเวณบ้านสามเรือน เดือนกุมภาพันธ์ 2569						ค่ามาตรฐาน
	วันที่ 7-8		วันที่ 8-9		วันที่ 9-10		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
12:00-13:00	62.9	56.2	63.2	55.8	61.8	54.8	-
13:00-14:00	63.1	57.0	62.3	56.4	61.0	55.0	-
14:00-15:00	63.4	60.1	62.6	56.2	61.2	51.2	-
15:00-16:00	66.8	60.5	60.6	55.2	57.1	49.6	-
16:00-17:00	67.3	58.0	56.8	53.9	56.1	55.0	-
17:00-18:00	60.2	54.1	57.2	51.8	64.2	55.5	-
18:00-19:00	54.9	53.6	53.4	45.3	56.5	51.8	-
19:00-20:00	55.7	44.1	49.0	41.9	55.8	54.4	-
20:00-21:00	45.5	42.0	44.1	42.3	59.0	45.0	-
21:00-22:00	42.9	40.0	47.8	43.2	45.8	44.0	-
22:00-23:00	41.1	41.0	49.7	49.0	53.1	43.4	-
23:00-00:00	43.6	43.0	52.0	42.3	44.3	41.6	-
00:00-01:00	51.5	42.1	42.8	41.4	44.8	40.9	-
01:00-02:00	45.9	40.9	41.9	41.1	45.0	40.1	-
02:00-03:00	43.3	41.2	47.9	45.1	45.1	42.8	-
03:00-04:00	46.2	41.5	55.9	46.2	55.6	43.8	-
04:00-05:00	47.2	45.7	50.2	49.8	47.9	46.7	-
05:00-06:00	53.1	50.0	55.9	51.2	59.3	51.9	-
06:00-07:00	56.7	54.5	57.3	53.5	58.3	55.4	-
07:00-08:00	60.9	54.6	60.0	56.9	66.2	57.8	-
08:00-09:00	61.4	54.4	64.2	54.4	62.0	59.5	-
09:00-10:00	58.9	56.4	61.2	58.3	66.1	56.4	-
10:00-11:00	59.2	54.6	65.2	58.2	60.5	56.0	-
11:00-12:00	58.7	54.7	64.4	56.5	59.0	55.7	-
L_{eq} 24 hr [dB(A)]	60.0	-	59.4	-	59.9	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	53.6	-	51.2	-	51.8	-	-
L_{max} [dB(A)]	109.5	-	101.6	-	108.1	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	61.4	-	61.9	-	62.6	-	-

Sound Level Meter Data			
Calibrate Sheet No.: Noise B 037/26		02 February 2026	
SLM No.	Brand	Model	Serial No.
ST-C1-B10	SCARLET	ST-12D	10351483
Actual Reading [dB]			
Before Adjustment		After Adjustment	
93.9		93.9	

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น
ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์
13 / 02 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY008/02/69
34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

วันที่ตรวจวัด : 3-10 กุมภาพันธ์ 2569
วันที่ออกรายงาน : 13 กุมภาพันธ์ 2569

เวลา	บริเวณบ้านชาวเหนือ เดือนกุมภาพันธ์ 2569								ค่ามาตรฐาน
	วันที่ 3-4		วันที่ 4-5		วันที่ 5-6		วันที่ 6-7		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
12:00-13:00	51.3	45.2	50.1	46.2	54.9	45.4	53.8	43.3	-
13:00-14:00	51.1	46.6	53.0	45.7	50.9	44.0	49.6	46.9	-
14:00-15:00	52.9	43.5	52.6	46.2	50.9	46.6	53.8	44.5	-
15:00-16:00	50.5	44.7	52.7	47.9	52.7	47.9	53.7	45.5	-
16:00-17:00	50.9	47.5	54.3	45.8	53.9	47.5	52.3	49.6	-
17:00-18:00	54.3	45.6	52.0	48.5	53.9	44.2	56.6	50.7	-
18:00-19:00	52.2	44.0	54.9	45.1	51.1	42.2	57.5	50.9	-
19:00-20:00	50.7	45.7	51.0	42.3	49.2	42.8	52.8	41.5	-
20:00-21:00	52.1	43.0	48.7	47.8	47.1	45.5	47.7	40.5	-
21:00-22:00	48.8	40.4	54.0	47.7	53.9	44.4	44.7	41.0	-
22:00-23:00	46.8	44.4	54.5	49.6	46.3	45.6	47.4	41.7	-
23:00-00:00	50.9	47.0	55.9	46.2	53.4	44.8	45.6	43.2	-
00:00-01:00	53.6	43.6	50.8	41.3	51.0	41.0	50.0	41.5	-
01:00-02:00	44.9	42.8	43.7	41.5	42.1	41.1	48.0	41.1	-
02:00-03:00	43.0	40.0	46.2	40.7	41.7	41.4	44.0	40.6	-
03:00-04:00	40.4	40.1	43.3	41.8	45.5	41.3	41.2	40.2	-
04:00-05:00	43.6	42.1	47.4	41.0	43.8	41.8	54.1	49.5	-
05:00-06:00	48.7	45.3	49.3	47.7	51.5	43.3	55.0	48.2	-
06:00-07:00	52.1	50.6	54.3	47.3	53.5	50.4	53.5	45.2	-
07:00-08:00	60.2	50.4	54.2	45.4	56.6	49.4	51.3	43.7	-
08:00-09:00	53.5	48.1	51.7	42.2	54.5	45.5	49.8	48.0	-
09:00-10:00	54.3	46.1	49.1	45.6	51.2	45.4	60.8	53.3	-
10:00-11:00	52.3	45.1	52.6	47.9	50.9	46.9	60.2	44.6	-
11:00-12:00	49.8	41.0	54.7	46.0	53.6	45.6	49.0	42.7	-
L_{eq} 24 hr [dB(A)]	52.2	-	52.3	-	52.0	-	53.9	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	44.7	-	45.8	-	44.8	-	43.7	-	-
L_{max} [dB(A)]	91.7	-	82.9	-	83.0	-	88.6	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	56.4	-	58.2	-	56.8	-	58.2	-	-

-	Sound Level Meter Data				-
	Calibrate Sheet No.: Noise B_037/26		02 February 2026		
	SLM No.	Brand	Model	Serial No.	
	ST-C1-B15	SCARLET	ST-12D	10352314	
	Actual Reading [dB]				
	Before Adjustment		After Adjustment		
	93.9		93.9		

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น
ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์
13 / 02 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY008/02/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2567
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

วันที่ตรวจวัด : 3-10 กุมภาพันธ์ 2569
วันที่ออกรายงาน : 13 กุมภาพันธ์ 2569

เวลา	บริเวณบ้านชาวเหนือ						ค่ามาตรฐาน
	เดือนกุมภาพันธ์ 2569						
	วันที่ 7-8		วันที่ 8-9		วันที่ 9-10		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
12:00-13:00	49.2	45.2	51.3	44.9	53.1	43.3	-
13:00-14:00	50.0	46.2	51.9	45.3	49.8	46.3	-
14:00-15:00	52.9	45.8	51.4	47.3	57.4	47.9	-
15:00-16:00	52.7	46.4	53.4	49.2	54.5	48.8	-
16:00-17:00	52.6	47.9	55.5	46.1	54.4	47.1	-
17:00-18:00	54.7	44.0	52.7	50.6	54.0	46.2	-
18:00-19:00	50.7	42.5	57.6	44.3	52.6	49.7	-
19:00-20:00	48.8	42.7	50.4	43.1	56.7	51.8	-
20:00-21:00	48.9	41.4	49.6	41.3	58.8	46.1	-
21:00-22:00	48.0	40.3	48.2	41.7	53.0	43.1	-
22:00-23:00	45.6	40.5	42.3	41.6	44.8	43.9	-
23:00-00:00	41.1	40.1	43.7	41.0	54.2	51.1	-
00:00-01:00	46.2	40.3	51.3	49.2	58.0	48.7	-
01:00-02:00	41.0	40.9	55.9	43.0	52.7	41.2	-
02:00-03:00	46.2	41.9	44.6	41.5	42.9	41.1	-
03:00-04:00	42.6	41.1	44.2	42.5	46.9	43.1	-
04:00-05:00	55.9	47.8	45.1	44.2	48.2	44.8	-
05:00-06:00	51.8	48.2	51.2	46.7	51.8	45.6	-
06:00-07:00	54.2	46.3	53.4	47.0	52.6	43.9	-
07:00-08:00	52.1	45.9	53.1	52.4	50.7	45.7	-
08:00-09:00	51.2	43.4	58.8	48.1	51.8	43.3	-
09:00-10:00	50.3	44.8	54.4	48.9	49.9	45.1	-
10:00-11:00	51.3	46.3	53.2	45.1	61.7	53.2	-
11:00-12:00	52.4	43.4	51.3	42.6	59.3	51.7	-
L_{eq} 24 hr [dB(A)]	51.0	-	52.8	-	55.0	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	43.4	-	44.9	-	45.7	-	-
L_{max} [dB(A)]	82.0	-	90.0	-	83.4	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	56.9	-	57.5	-	59.6	-	-
-	Sound Level Meter Data						-
	Calibrate Sheet No.: Noise B_037/26		02 February 2026				
	SLM No.	Brand	Model	Serial No.			
	ST-C1-B15	SCARLET	ST-12D	10352314			
	Actual Reading [dB]						
	Before Adjustment		After Adjustment				
	93.9		93.9				

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น

ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์

13 / 02 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY008/02/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

วันที่ตรวจวัด : 3-10 กุมภาพันธ์ 2569
วันที่ออกรายงาน : 13 กุมภาพันธ์ 2569

เวลา	บริเวณที่ตั้งโรงไฟฟ้าราชบุรี เดือนกุมภาพันธ์ 2569								ค่ามาตรฐาน
	วันที่ 3-4		วันที่ 4-5		วันที่ 5-6		วันที่ 6-7		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
11:00-12:00	49.3	45.1	50.7	43.8	48.7	46.3	52.6	44.2	-
12:00-13:00	50.0	44.7	47.7	43.6	52.9	44.9	49.0	46.2	-
13:00-14:00	48.2	44.6	47.4	43.4	49.6	45.3	51.2	45.1	-
14:00-15:00	49.4	46.9	53.0	43.9	50.7	47.3	49.9	49.0	-
15:00-16:00	53.1	44.4	50.3	46.6	54.1	44.7	65.0	55.0	-
16:00-17:00	45.4	45.0	53.2	44.4	48.5	45.5	56.1	46.8	-
17:00-18:00	51.9	43.8	50.5	41.5	51.8	42.7	50.7	42.1	-
18:00-19:00	45.6	41.7	46.3	41.6	47.4	40.0	48.9	40.8	-
19:00-20:00	44.2	40.0	46.2	41.3	43.3	41.9	44.9	41.4	-
20:00-21:00	44.1	41.6	43.6	41.0	42.2	41.6	45.4	41.1	-
21:00-22:00	42.8	42.1	45.0	41.7	42.9	41.5	43.3	41.3	-
22:00-23:00	48.9	42.2	45.8	43.6	46.8	41.9	42.6	41.8	-
23:00-00:00	47.4	40.9	50.1	40.7	45.0	41.8	46.4	41.9	-
00:00-01:00	41.7	40.3	41.6	40.9	43.6	40.0	46.9	40.7	-
01:00-02:00	44.0	41.0	46.0	41.7	40.3	40.2	41.6	40.5	-
02:00-03:00	47.3	41.5	46.6	43.6	47.1	41.7	41.5	40.8	-
03:00-04:00	45.5	41.1	50.0	46.1	44.2	41.8	44.0	41.4	-
04:00-05:00	47.5	45.0	52.2	47.7	46.6	44.6	45.8	41.8	-
05:00-06:00	51.8	46.1	54.4	46.8	50.8	47.5	48.5	47.4	-
06:00-07:00	52.4	46.9	53.6	46.5	53.7	47.3	53.8	49.8	-
07:00-08:00	51.8	45.0	51.1	46.0	53.5	46.9	56.5	49.3	-
08:00-09:00	48.7	45.6	51.2	46.4	50.9	46.4	55.8	54.3	-
09:00-10:00	52.4	46.1	51.8	44.5	50.0	45.5	67.7	58.3	-
10:00-11:00	52.6	44.4	51.4	44.2	51.6	44.0	64.5	55.8	-
L_{eq} 24 hr [dB(A)]	49.3	-	50.3	-	49.7	-	57.8	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	44.4	-	43.6	-	44.0	-	42.1	-	-
L_{max} [dB(A)]	78.9	-	82.9	-	80.5	-	94.7	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	55.1	-	56.9	-	55.0	-	59.0	-	-
-	Sound Level Meter Data								-
	Calibrate Sheet No.: Noise B_037/26				02 February 2026				
	SLM No.		Brand		Model		Serial No.		
	ST-C1-B09		SCARLET		ST-12D		10351478		
	Actual Reading [dB]								
	Before Adjustment				After Adjustment				
	93.8				93.9				

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น
ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์

13 / 02 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY008/02/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2567
วันที่ตรวจวัด : 3-10 กุมภาพันธ์ 2569
วันที่ออกรายงาน : 13 กุมภาพันธ์ 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

เวลา	บริเวณที่ตั้งโรงไฟฟ้าราชบุรี เดือนกุมภาพันธ์ 2569						ค่ามาตรฐาน
	วันที่ 7-8		วันที่ 8-9		วันที่ 9-10		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
11:00-12:00	47.3	45.2	44.8	41.8	51.7	46.0	-
12:00-13:00	47.5	46.9	44.4	41.2	52.0	46.2	-
13:00-14:00	61.4	46.3	44.4	41.8	50.6	46.0	-
14:00-15:00	49.3	43.7	47.7	44.0	49.9	45.5	-
15:00-16:00	49.9	43.8	50.6	45.0	51.7	46.4	-
16:00-17:00	49.1	44.0	50.2	45.5	53.2	46.7	-
17:00-18:00	50.4	40.9	51.6	41.8	53.2	46.1	-
18:00-19:00	44.6	41.6	43.0	40.8	52.3	42.1	-
19:00-20:00	45.3	41.3	41.2	41.0	45.8	42.0	-
20:00-21:00	46.0	41.0	47.8	41.7	43.8	41.8	-
21:00-22:00	43.2	41.5	42.8	41.8	44.1	41.3	-
22:00-23:00	45.9	41.9	44.4	40.8	44.0	41.0	-
23:00-00:00	45.8	40.1	43.5	41.9	46.6	40.3	-
00:00-01:00	40.1	40.0	42.4	42.0	40.8	40.0	-
01:00-02:00	44.0	41.9	54.1	44.4	44.7	41.7	-
02:00-03:00	44.1	41.1	45.9	41.2	41.9	41.3	-
03:00-04:00	46.6	43.6	42.2	41.4	44.9	41.1	-
04:00-05:00	50.2	45.4	47.2	46.2	46.3	41.8	-
05:00-06:00	52.3	50.6	52.8	49.6	48.1	46.5	-
06:00-07:00	56.7	46.9	55.9	49.9	54.8	48.8	-
07:00-08:00	51.6	45.8	56.6	52.8	55.1	45.1	-
08:00-09:00	50.9	42.2	59.7	51.8	50.5	45.8	-
09:00-10:00	48.5	41.2	58.0	52.2	48.7	45.0	-
10:00-11:00	45.6	41.3	53.9	46.8	51.6	44.9	-
L_{eq} 24 hr [dB(A)]	51.4	-	52.1	-	50.3	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	41.9	-	41.9	-	44.9	-	-
L_{max} [dB(A)]	96.4	-	83.3	-	81.2	-	ไม่เกิน 115.0
L_{dr} [dB(A)]	56.9	-	57.3	-	55.0	-	-

-	Sound Level Meter Data				-
	Calibrate Sheet No.: Noise B 037/26		02 February 2026		
	SLM No.	Brand	Model	Serial No.	
	ST-C1-B09	SCARLET	ST-12D	10351478	
	Actual Reading [dB]				
	Before Adjustment		After Adjustment		
	93.8		93.9		

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น
ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์
13 / 02 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY225/05/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

วันที่ตรวจวัด : 14-21 พฤษภาคม 2569
วันที่ออกรายงาน : 2 มิถุนายน 2569

เวลา	บริเวณบ้านสามเรือน								ค่ามาตรฐาน
	เดือนพฤษภาคม 2569								
	วันที่ 14-15		วันที่ 15-16		วันที่ 16-17		วันที่ 17-18		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
11:00-12:00	55.1	48.8	47.7	43.9	56.5	48.2	55.5	47.2	-
12:00-13:00	55.7	47.3	50.7	45.2	54.2	47.6	55.8	49.3	-
13:00-14:00	54.7	46.6	51.6	46.5	50.9	45.3	56.7	47.4	-
14:00-15:00	53.8	45.7	53.3	48.8	49.2	44.1	53.6	45.1	-
15:00-16:00	51.5	42.1	55.5	48.2	51.0	43.9	52.4	45.8	-
16:00-17:00	47.2	41.9	53.3	47.6	50.3	42.1	53.2	48.8	-
17:00-18:00	48.5	43.5	53.6	46.8	48.8	43.6	49.6	48.8	-
18:00-19:00	51.5	43.9	51.4	43.2	44.1	41.3	50.2	48.2	-
19:00-20:00	50.7	41.3	49.7	44.0	43.5	41.3	48.6	46.8	-
20:00-21:00	44.0	40.2	50.9	43.6	41.9	40.4	47.5	43.8	-
21:00-22:00	45.1	40.1	47.2	42.8	40.8	39.0	45.1	41.8	-
22:00-23:00	41.4	40.2	46.9	40.6	42.9	37.3	43.6	40.9	-
23:00-00:00	41.3	39.6	47.6	40.6	43.4	37.3	42.1	39.1	-
00:00-01:00	40.1	38.2	42.8	41.2	42.4	37.7	44.6	38.6	-
01:00-02:00	41.8	40.2	47.4	40.5	44.6	39.5	42.8	37.3	-
02:00-03:00	43.9	39.7	45.8	41.2	46.9	41.0	44.9	41.5	-
03:00-04:00	42.0	40.7	47.3	40.7	48.7	42.1	46.6	43.1	-
04:00-05:00	42.4	41.9	46.6	41.4	50.5	43.7	50.9	44.4	-
05:00-06:00	46.0	42.0	47.6	42.1	52.6	45.3	52.0	45.0	-
06:00-07:00	48.5	44.3	48.3	43.5	54.0	47.9	54.2	46.8	-
07:00-08:00	50.9	45.4	50.1	45.9	53.8	47.2	56.6	49.5	-
08:00-09:00	52.2	47.6	52.6	47.4	56.1	48.9	54.0	49.1	-
09:00-10:00	54.2	47.0	54.2	49.6	55.9	47.5	57.8	50.0	-
10:00-11:00	52.9	46.9	55.5	50.3	54.8	46.9	55.8	49.1	-
L_{eq} 24 hr [dB(A)]	50.6	-	51.1	-	51.5	-	52.8	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	42.0	-	43.6	-	43.6	-	45.8	-	-
L_{max} [dB(A)]	84.2	-	96.1	-	94.6	-	93.4	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	53.0	-	54.7	-	56.3	-	56.6	-	-

-	Sound Level Meter Data				-
	Calibrate Sheet No.: Noise B_257/26		13 May 2026		
	SLM No.	Brand	Model	Serial No.	
	ST-C1-B10	SCARLET	ST-12D	10351483	
	Actual Reading [dB]				
	Before Adjustment		After Adjustment		
	93.7		93.9		

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น

ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์

02 / 06 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY225/05/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2569
วันที่ตรวจวัด : 14-21 พฤษภาคม 2569
วันที่ออกรายงาน : 2 มิถุนายน 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

เวลา	บริเวณบ้านสามเรือน						ค่ามาตรฐาน
	เดือนพฤษภาคม 2569						
	วันที่ 18-19		วันที่ 19-20		วันที่ 20-21		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
11:00-12:00	50.1	44.1	55.1	47.9	57.5	47.5	-
12:00-13:00	51.0	45.8	54.8	46.8	55.3	45.5	-
13:00-14:00	52.1	45.4	53.4	45.9	52.5	45.2	-
14:00-15:00	50.5	46.2	50.6	43.3	50.8	42.7	-
15:00-16:00	52.4	47.7	47.4	42.7	47.7	44.0	-
16:00-17:00	54.6	48.2	48.3	43.1	50.6	45.2	-
17:00-18:00	54.7	48.8	51.5	44.5	49.5	44.6	-
18:00-19:00	57.3	49.3	49.0	43.4	50.9	43.2	-
19:00-20:00	55.5	47.4	46.5	41.7	43.6	41.8	-
20:00-21:00	50.6	45.5	46.2	41.4	43.6	41.2	-
21:00-22:00	47.3	43.8	43.4	38.8	42.6	40.7	-
22:00-23:00	44.0	41.0	40.3	38.2	42.2	39.2	-
23:00-00:00	41.8	38.9	42.7	40.5	46.0	39.4	-
00:00-01:00	40.7	39.5	42.1	39.4	42.1	40.1	-
01:00-02:00	42.2	37.6	40.1	38.0	42.3	39.7	-
02:00-03:00	41.9	39.7	42.6	39.0	42.2	38.0	-
03:00-04:00	42.1	37.6	44.5	40.1	40.4	39.5	-
04:00-05:00	42.9	38.2	46.1	42.3	42.6	40.3	-
05:00-06:00	44.6	39.7	48.9	43.0	48.0	42.3	-
06:00-07:00	46.3	40.7	49.4	45.2	51.1	43.3	-
07:00-08:00	49.5	41.6	51.6	46.7	49.5	42.5	-
08:00-09:00	48.1	42.1	53.3	47.2	51.0	44.1	-
09:00-10:00	48.0	43.7	55.0	48.9	52.8	45.7	-
10:00-11:00	51.6	45.5	56.2	48.3	50.1	44.1	-
L_{eq} 24 hr [dB(A)]	50.8	-	50.7	-	50.1	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	43.7	-	43.0	-	42.5	-	-
L_{max} [dB(A)]	92.8	-	96.0	-	93.1	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	52.8	-	53.6	-	53.5	-	-
-	Sound Level Meter Data						-
	Calibrate Sheet No.: Noise B 257/26				13 May 2026		
	SLM No.	Brand			Model	Serial No.	
	ST-C1-B10	SCARLET			ST-12D	10351483	
	Actual Reading [dB]						
	Before Adjustment				After Adjustment		
	93.7				93.9		

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น

ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted])

ผู้รับรองรายงานผลการวิเคราะห์

02 / 06 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY225/05/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2569
วันที่ตรวจวัด : 14-21 พฤษภาคม 2569
วันที่ออกรายงาน : 2 มิถุนายน 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

เวลา	บริเวณบ้านชาวเหนือ								ค่ามาตรฐาน
	เดือนพฤษภาคม 2569								
	วันที่ 14-15		วันที่ 15-16		วันที่ 16-17		วันที่ 17-18		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
12:00-13:00	55.1	49.8	55.0	50.9	56.4	50.6	54.1	50.3	-
13:00-14:00	53.1	47.6	53.8	48.7	56.0	49.6	53.2	50.0	-
14:00-15:00	52.0	46.8	52.1	45.5	56.2	48.8	52.3	49.9	-
15:00-16:00	53.7	45.2	52.4	47.4	57.3	49.6	52.6	49.4	-
16:00-17:00	51.6	45.6	51.0	45.7	57.1	50.4	53.6	48.5	-
17:00-18:00	51.0	44.8	50.2	43.8	56.7	49.9	54.3	47.9	-
18:00-19:00	53.5	43.5	50.7	47.7	55.6	48.4	53.5	50.2	-
19:00-20:00	53.1	45.7	52.2	45.6	54.9	46.5	53.1	48.1	-
20:00-21:00	52.1	42.2	52.6	43.8	54.7	45.8	52.9	45.7	-
21:00-22:00	51.8	40.8	49.9	40.3	55.0	46.2	50.0	44.4	-
22:00-23:00	50.9	44.4	49.3	39.8	52.4	47.9	49.1	42.1	-
23:00-00:00	49.8	38.1	49.4	40.2	51.2	45.5	48.2	40.8	-
00:00-01:00	48.5	41.9	48.1	43.6	50.6	44.7	48.9	41.5	-
01:00-02:00	47.4	39.7	49.9	40.5	49.7	43.3	49.6	40.7	-
02:00-03:00	45.6	40.3	51.5	43.2	47.3	42.5	46.3	39.5	-
03:00-04:00	46.7	37.1	50.8	46.7	48.2	40.9	44.6	38.3	-
04:00-05:00	46.4	40.6	48.6	42.5	47.7	42.1	47.0	42.9	-
05:00-06:00	49.8	42.9	47.4	41.7	49.7	40.4	49.9	40.4	-
06:00-07:00	48.2	45.8	50.2	40.7	48.2	40.9	50.2	45.1	-
07:00-08:00	47.8	45.3	49.8	41.9	49.7	43.9	50.9	46.2	-
08:00-09:00	46.4	43.6	48.6	41.6	50.3	45.6	49.8	42.9	-
09:00-10:00	49.9	44.7	48.5	41.8	50.5	47.5	50.3	47.0	-
10:00-11:00	50.8	46.8	47.8	40.9	51.4	49.0	50.6	48.8	-
11:00-12:00	50.0	44.8	49.5	44.1	51.8	50.2	49.8	49.1	-
L_{eq} 24 hr [dB(A)]	51.0	-	50.8	-	53.6	-	51.3	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	44.4	-	43.2	-	46.2	-	45.7	-	-
L_{max} [dB(A)]	98.6	-	97.9	-	93.9	-	95.1	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	55.6	-	56.3	-	57.4	-	55.7	-	-
-	Sound Level Meter Data								-
	Calibrate Sheet No.: B_257/26				13 May 2026				
	SLM No.		Brand		Model		Serial No.		
	ST-C1-B13		SCARLET		ST-12D		10351486		
	Actual Reading [dB]								
	Before Adjustment				After Adjustment				
	93.9				93.9				

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น
ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์
02 / 06 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY225/05/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

วันที่ตรวจวัด : 14-21 พฤษภาคม 2569
วันที่ออกรายงาน : 2 มิถุนายน 2569

เวลา	บริเวณบ้านชาวเหนือ						ค่ามาตรฐาน
	เดือนพฤษภาคม 2569						
	วันที่ 18-19		วันที่ 19-20		วันที่ 20-21		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
12:00-13:00	60.1	59.2	55.1	49.2	55.5	50.6	-
13:00-14:00	59.5	58.2	54.2	48.4	57.8	49.8	-
14:00-15:00	58.8	57.5	55.2	46.4	55.5	49.6	-
15:00-16:00	58.1	57.3	52.6	45.8	56.2	47.8	-
16:00-17:00	59.0	56.6	51.3	43.6	55.6	48.7	-
17:00-18:00	58.8	56.2	53.2	44.8	53.0	47.2	-
18:00-19:00	57.1	54.1	55.6	41.3	54.2	48.1	-
19:00-20:00	54.8	53.7	55.2	40.1	55.9	45.9	-
20:00-21:00	53.9	53.0	50.5	41.6	54.2	44.8	-
21:00-22:00	55.4	52.4	53.0	40.9	55.0	43.7	-
22:00-23:00	53.9	52.1	49.4	40.3	53.1	43.5	-
23:00-00:00	54.5	52.2	49.7	41.8	52.5	42.8	-
00:00-01:00	52.5	51.9	48.9	40.6	50.3	42.2	-
01:00-02:00	52.7	50.3	46.6	40.2	48.1	43.5	-
02:00-03:00	50.9	50.4	47.8	41.5	49.7	45.0	-
03:00-04:00	52.7	50.4	49.8	40.9	50.4	44.1	-
04:00-05:00	55.1	49.5	50.8	40.6	51.5	43.1	-
05:00-06:00	56.5	50.7	53.0	42.5	50.2	43.7	-
06:00-07:00	57.3	49.7	52.6	43.2	50.7	43.2	-
07:00-08:00	57.8	49.5	50.0	42.6	50.0	44.0	-
08:00-09:00	58.3	50.2	49.3	42.8	49.7	43.6	-
09:00-10:00	59.2	49.7	49.8	44.3	49.6	42.6	-
10:00-11:00	57.4	50.7	51.2	45.5	50.4	40.9	-
11:00-12:00	56.7	51.1	50.1	43.8	48.9	40.0	-
L_{eq} 24 hr [dB(A)]	57.0	-	52.1	-	53.3	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	51.9	-	42.5	-	43.7	-	-
L_{max} [dB(A)]	94.3	-	95.7	-	97.3	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	61.6	-	57.2	-	58.0	-	-
-	Sound Level Meter Data						-
	Calibrate Sheet No.: B_257/26			13 May 2026			
	SLM No.	Brand		Model		Serial No.	
	ST-C1-B13	SCARLET		ST-12D		10351486	
	Actual Reading [dB]						
	Before Adjustment			After Adjustment			
	93.9			93.9			

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น

ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์

02 / 06 / 69

RS/R024/26/MAY

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY225/05/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2569
วันที่ตรวจวัด : 14-21 พฤษภาคม 2569
วันที่ออกรายงาน : 2 มิถุนายน 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

เวลา	บริเวณที่ตั้งโรงไฟฟ้าราชบุรี								ค่ามาตรฐาน
	เดือนพฤษภาคม 2569								
	วันที่ 14-15		วันที่ 15-16		วันที่ 16-17		วันที่ 17-18		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
12:00-13:00	54.3	47.6	56.9	48.6	58.9	54.2	56.1	50.9	-
13:00-14:00	53.5	48.1	55.5	49.3	55.8	51.9	55.2	49.4	-
14:00-15:00	52.2	48.6	54.1	49.5	54.4	51.7	54.8	48.2	-
15:00-16:00	54.8	50.1	56.2	49.1	53.2	50.0	53.7	49.9	-
16:00-17:00	53.6	50.9	55.7	48.7	57.0	52.9	55.6	49.6	-
17:00-18:00	55.8	53.5	53.0	47.9	56.5	53.5	56.5	51.0	-
18:00-19:00	57.2	51.5	54.5	49.4	59.2	54.9	57.8	49.4	-
19:00-20:00	55.5	49.2	56.4	51.1	55.7	51.2	54.2	52.2	-
20:00-21:00	53.2	47.3	55.9	48.4	57.4	52.5	58.6	53.4	-
21:00-22:00	52.2	48.5	54.5	47.0	57.5	53.6	56.9	52.3	-
22:00-23:00	51.4	48.9	53.1	46.7	54.6	51.8	58.3	53.4	-
23:00-00:00	53.9	47.6	51.7	45.0	52.8	49.9	59.4	49.6	-
00:00-01:00	50.7	44.8	48.3	43.6	55.4	51.1	52.3	48.7	-
01:00-02:00	48.6	42.6	49.2	44.0	51.2	47.0	53.7	48.4	-
02:00-03:00	43.9	39.7	50.7	45.6	49.5	44.4	52.3	46.3	-
03:00-04:00	46.6	42.8	48.3	41.4	50.0	45.8	49.8	43.9	-
04:00-05:00	48.2	44.0	47.3	44.7	48.1	43.4	48.1	42.9	-
05:00-06:00	48.5	46.0	51.6	41.8	49.6	44.7	47.3	41.4	-
06:00-07:00	51.6	50.3	48.2	42.9	51.4	47.8	45.7	41.3	-
07:00-08:00	54.9	52.4	47.5	46.5	52.4	50.5	47.0	43.7	-
08:00-09:00	57.8	49.9	49.9	48.0	57.3	52.3	48.4	44.5	-
09:00-10:00	54.0	51.6	53.6	49.5	57.4	52.2	50.9	47.4	-
10:00-11:00	56.5	48.5	51.5	48.3	55.6	51.2	52.8	47.5	-
11:00-12:00	52.4	45.3	53.7	49.7	54.0	44.8	54.3	48.9	-
L_{eq} 24 hr [dB(A)]	53.6	-	53.4	-	55.3	-	54.8	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	48.5	-	47.9	-	51.2	-	48.7	-	-
L_{max} [dB(A)]	75.6	-	86.5	-	89.9	-	93.8	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	57.6	-	57.6	-	59.5	-	60.8	-	-

-	Sound Level Meter Data				-
	Calibrate Sheet No.: B_257/26		13 May 2026		
	SLM No.	Brand	Model	Serial No.	
	ST-C1-B19	SCARLET	ST-12D	0352320	
	Actual Reading [dB]				
	Before Adjustment		After Adjustment		
	93.9		93.9		

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น
ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์
02 / 06 / 69

บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด
S.P.S. CONSULTING SERVICE CO., LTD.
7 ซอยพหลโยธิน 24 ถนนพหลโยธิน แขวงจอมพล เขตจตุจักร กรุงเทพฯ 10900
7 Soi Phaholyothin 24, Phaholyothin Rd., Jompol, Chatuchak, Bangkok 10900
Tel : (662) 939-4370-72, Fax : (662) 513-4221, E-mail : sale@spscon.com., www.spscon.com

BY225/05/69

34/10/68

รายงานผลการตรวจวัดระดับเสียง

โครงการ : ติดตามตรวจสอบคุณภาพสิ่งแวดล้อม โครงการโรงไฟฟ้าราชบุรี ประจำปี 2569
วันที่ตรวจวัด : 14-21 พฤษภาคม 2569
วันที่ออกรายงาน : 2 มิถุนายน 2569
ที่ตั้งโครงการ : 128 หมู่ 6 ตำบลพิกุลทอง อำเภอเมือง จังหวัดราชบุรี
ชื่อ/ที่อยู่ลูกค้า : บริษัท ผลิตไฟฟ้าราชบุรี จำกัด
ผู้ตรวจวัด : บริษัท เอส.พี.เอส. คอนซัลติ้ง เซอร์วิส จำกัด

เวลา	บริเวณที่ตั้งโรงไฟฟ้าราชบุรี						ค่ามาตรฐาน
	เดือนพฤษภาคม 2569						
	วันที่ 18-19		วันที่ 19-20		วันที่ 20-21		
	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	L_{eq} 1 hr [dB(A)]	L_{90} [dB(A)]	
12:00-13:00	51.7	46.4	48.6	44.2	51.4	49.1	-
13:00-14:00	53.0	48.8	49.6	45.3	50.2	47.9	-
14:00-15:00	52.5	47.2	49.8	46.1	54.6	51.2	-
15:00-16:00	52.8	47.9	51.1	47.0	52.0	45.2	-
16:00-17:00	53.8	49.9	50.7	46.4	47.7	42.7	-
17:00-18:00	52.6	47.4	49.5	43.0	52.2	44.1	-
18:00-19:00	51.7	46.2	49.7	44.9	52.8	44.3	-
19:00-20:00	47.8	43.1	51.1	47.7	55.0	46.5	-
20:00-21:00	44.0	39.7	49.6	48.0	48.2	44.4	-
21:00-22:00	41.5	40.4	48.4	41.9	44.5	41.2	-
22:00-23:00	43.1	40.5	46.8	41.9	42.1	41.0	-
23:00-00:00	44.3	39.9	44.7	41.7	43.8	41.2	-
00:00-01:00	42.4	39.8	45.0	41.5	45.1	40.7	-
01:00-02:00	42.8	41.2	42.4	40.3	43.3	40.7	-
02:00-03:00	43.7	41.3	42.6	40.6	43.0	41.4	-
03:00-04:00	43.9	41.2	43.9	40.1	44.0	41.6	-
04:00-05:00	45.0	41.5	45.6	42.2	44.3	41.6	-
05:00-06:00	47.8	44.9	47.3	44.3	45.5	41.6	-
06:00-07:00	51.5	48.9	49.9	45.2	48.1	44.5	-
07:00-08:00	54.8	49.3	52.0	48.7	50.8	44.9	-
08:00-09:00	51.9	50.2	53.4	47.7	55.1	49.6	-
09:00-10:00	50.3	47.6	50.9	49.3	52.2	50.5	-
10:00-11:00	50.8	46.6	55.5	50.6	50.6	47.9	-
11:00-12:00	49.6	44.3	53.3	52.6	51.2	47.0	-
L_{eq} 24 hr [dB(A)]	50.2	-	50.0	-	50.4	-	ไม่เกิน 70.0
L_{90} 24 hr [dB(A)]	44.9	-	44.9	-	44.3	-	-
L_{max} [dB(A)]	93.2	-	95.0	-	91.5	-	ไม่เกิน 115.0
L_{dn} [dB(A)]	53.8	-	53.7	-	53.2	-	-
-	Sound Level Meter Data						-
	Calibrate Sheet No.: B_257/26			13 May 2026			
	SLM No.	Brand		Model		Serial No.	
	ST-C1-B19	SCARLET		ST-12D		0352320	
	Actual Reading [dB]						
	Before Adjustment			After Adjustment			
	93.9			93.9			

หมายเหตุ:

ค่ามาตรฐาน = ประกาศคณะกรรมการสิ่งแวดล้อมแห่งชาติ ฉบับที่ 15 (พ.ศ. 2540) เรื่อง กำหนดมาตรฐานระดับเสียงโดยทั่วไป

วิธีการตรวจวัด = เครื่องมือตรวจวัดระดับเสียง

เครื่องวัดเสียงทำการสอบเทียบโดยใช้ Acoustic Calibrator, ACO, Model 2127, S/N. 130006

ผลการตรวจวัดนี้รับรองเฉพาะช่วงเวลาที่ได้ทำการตรวจวัดเท่านั้น

ห้ามคัดถ่ายรายงานผลตรวจวัดเพียงบางส่วนโดยไม่ได้รับอนุญาตจากบริษัทเป็นลายลักษณ์อักษร

[redacted]

ผู้รับรองรายงานผลการวิเคราะห์

02 / 06 / 69
